


I.1  
5/21/02

**STS CONSULTANTS, LTD.**  
**Consulting Engineers and Environmental Scientists**  
**750 Corporate Woods Parkway**  
**Vernon Hills, Illinois 60061**  
**Phone: (847) 279-2500**  
**Fax: (847) 279-2510**

EPA Region 5 Records Ctr.



226916

**Date: May 21, 2002****Total Number of Pages, Including Cover: 3**

**FAX TRANSMITTAL COVER SHEET**  
**PLEASE DELIVER THE FOLLOWING PAGES**

**NAME: Fred Micke****COMPANY: USEPA****FAX NUMBER(S): 312-353-9176****FROM: Rich Berggreen**

**MESSAGE:** Fred, here is a copy of the current schedule for the 341 E. Ohio Street site. As we discussed, we are planning the training on June 5, Wednesday, with the actual on-site work to begin Thursday June 6. The schedule runs 62 days or approximately 12 weeks. We think the majority of the removal will be during the first 30 to 40 days, with the remainder being the surveying of the fill to identify and remove any material not evident from the ground surface. I understand Tim Ramsey has already forwarded this schedule to Mary Fulghum so you may have gotten or can expect to get a copy from Mary. Call with any questions.

**IF YOU DO NOT RECEIVE ALL PAGES, PLEASE CALL (847) 279-2500 IMMEDIATELY**  
**IMPORTANT:** This facsimile is intended only for the use of the individual(s) or entity to which it is addressed and may contain information that is privileged, confidential, and exempt from disclosure under applicable law. If the reader of this facsimile is not the intended recipient, you are hereby notified that any dissemination, distribution, or copying of this communication is strictly prohibited. If you have received this communication in error, please notify us immediately by telephone and return this facsimile to us at the above address via the United State Postal Service. Thank you.

STS USE ONLY:	OFFICE	DEPT	JOB/PROJECT	NO.
	TASK NO.			

GMO Site -  
STS Project No

ID	Task Name	Duration	Start	Finish	Jun '01	Jul '01	Aug '01	Sep '01	Oct '01	Nov '01
1	Receive Project Authorization	0 days	Tue 01/02/01	Tue 01/02/01						
2	<b>WORK PLAN DEVELOPMENT:</b>	<b>348 days</b>	<b>Mon 01/15/01</b>	<b>Wed 05/15/02</b>						
3	Develop Work Plan	60 days	Mon 01/15/01	Fri 04/06/01						
4	I.D. ROW & Onsite Utils.	15 days	Mon 01/15/01	Fri 02/02/01						
5	Time-Life Substructure As-Built Condition	15 days	Mon 01/15/01	Fri 02/02/01						
6	Draft Plan	28 days	Mon 01/15/01	Wed 02/21/01						
7	USEPA Review/Response	20 days	Tue 04/10/01	Mon 05/07/01						
8	Revise Plan & Submit Final Draft	15 days	Tue 05/08/01	Mon 05/28/01						
9	Agency Approval	47 days	Tue 05/29/01	Wed 05/15/02						
10										
11	<b>REMEDIATION BID PACKAGE:</b>	<b>274 days</b>	<b>Tue 05/08/01</b>	<b>Fri 05/24/02</b>						
12	Develop Documents	70 days	Tue 05/08/01	Mon 08/13/01						
13	Owners Review	15 days	Tue 06/19/01	Mon 07/09/01						
14	Review at 50%	10 days	Tue 06/19/01	Mon 07/02/01						
15	Review at 100 %	5 days	Tue 07/03/01	Mon 07/09/01						
16	Revise Bid Package	12 days	Tue 08/14/01	Wed 08/29/01						
17	Solicit Contractor Bids	10 days	Thu 08/30/01	Wed 09/12/01						
18	Review/Negotiation & Award Contract	29 days	Thu 09/13/01	Fri 05/24/02						
19										
20	<b>PERMITS/APPROVALS:</b>	<b>275 days</b>	<b>Tue 05/29/01</b>	<b>Mon 06/17/02</b>						
21	Department of Underground Approval	46 days	Tue 05/29/01	Tue 05/07/02						
22	<b>MWRDGC SDA Approval</b>	<b>14 days</b>	<b>Mon 05/06/02</b>	<b>Thu 05/23/02</b>						
23	Draft SDA Request	11 days	Mon 05/06/02	Mon 05/20/02						
24	Submit SDA to MWRDGC	0 days	Mon 05/20/02	Mon 05/20/02						
25	MWRDGC Approval	3 days	Tue 05/21/02	Thu 05/23/02						
26	<b>Chicago Department of Sewers Permit</b>	<b>81 days</b>	<b>Mon 02/25/02</b>	<b>Mon 06/17/02</b>						
27	Draft Permit Request	12 days	Mon 02/25/02	Tue 03/12/02						
28	Submit Permit Request	0 days	Thu 06/13/02	Thu 06/13/02						
29	Dept of Sewers Approval	2 days	Fri 06/14/02	Mon 06/17/02						
30	<b>Pesticide Contamination Resolution</b>	<b>163 days</b>	<b>Wed 08/01/01</b>	<b>Fri 03/15/02</b>						
31	Testing for Pesticides	67 days	Wed 08/01/01	Thu 11/01/01						
32	Obtain USEPA Concurrence	75 days	Mon 12/03/01	Fri 03/15/02						
33	Revise Work Plan	30 days	Mon 02/04/02	Fri 03/15/02						
34										
35	<b>CONSTRUCTION:</b>	<b>77 days</b>	<b>Thu 05/16/02</b>	<b>Fri 08/30/02</b>						
36	Clear Utilities	10 days	Mon 05/27/02	Fri 06/07/02						
37	H&S Training	1 day	Wed 06/05/02	Wed 06/05/02						
38	Mobilization/Site Preparation	15 days	Thu 05/16/02	Wed 06/05/02						
39	Implement Remediation Plan	62 days	Thu 06/06/02	Fri 08/30/02						
40										
41	<b>PROJECT CLOSE OUT:</b>	<b>130 days</b>	<b>Mon 09/02/02</b>	<b>Fri 02/28/03</b>						

Project: GMO Site  
Date: Fri 05/17/02

Task

Milestone

Rolled Up Split

Split

Summary

Rolled Up Milestone


Progress

Rolled Up Task

Rolled Up Progress

te - Schedule  
No. 25585-XG

'01	Nov '01	Dec '01	Jan '02	Feb '02	Mar '02	Apr '02	May '02	Jun '02	Jul '02	Aug '02	Sep '02	Oct '02	Nov '02	Dec '02	Jan '03	Feb '03	Mar '03
-----	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------	---------

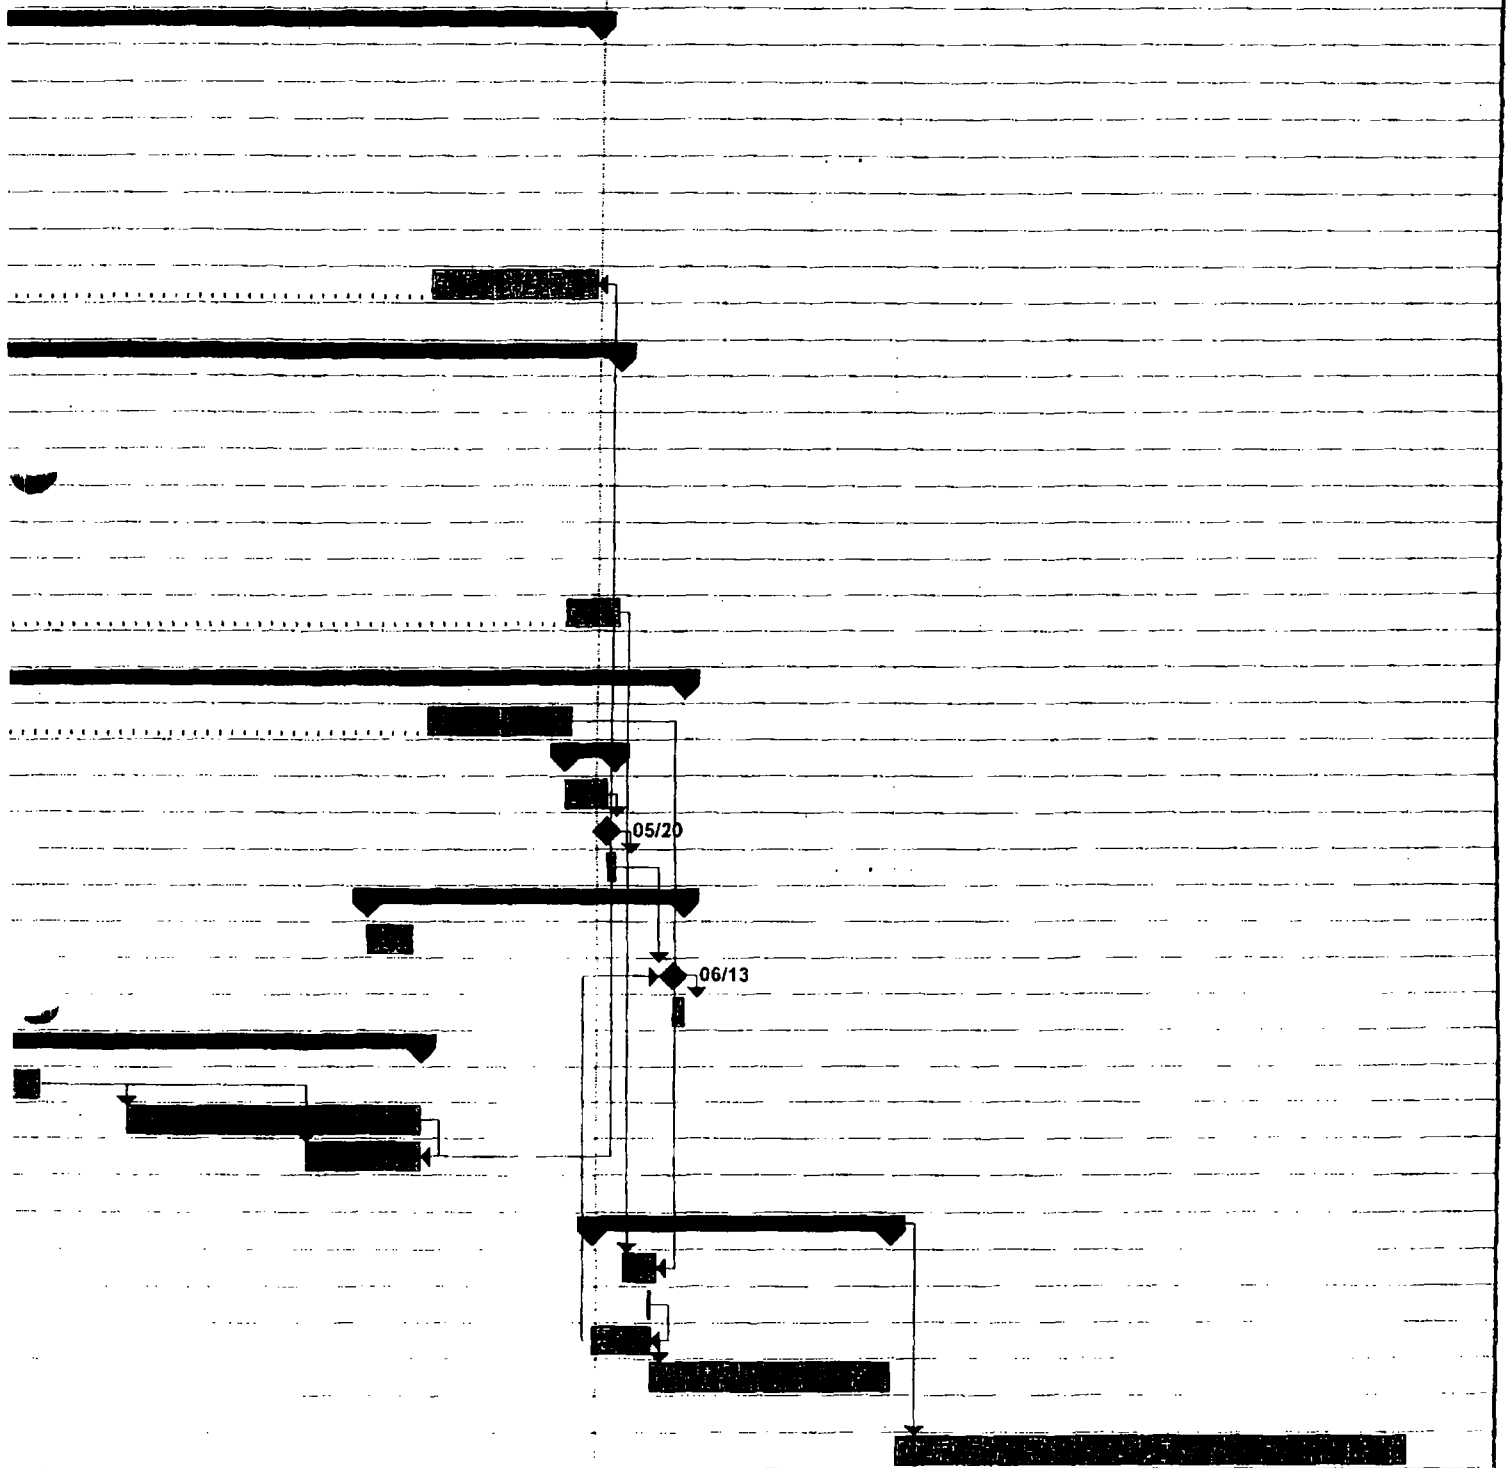

External Tasks

Deadline



Project Summary

External Milestone

