



Project Summary Report

SDMS Document ID



2027818

Contractor's Name: **Project Resources Inc.**
Contract Number: **W9128F-04-D-0029**
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	09OCT04	16OCT04	Report #	018
--------------	----------------	----------------	----------	------------

Project Safety Report

Days Worked To Date:	121	Date of Last Accident:	8/12/04
Project Man-hours To Date:	33,296.75	Hours Worked w/o Accident:	14,582.00
Comments/Issues: None.			

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		80
Property Close-Out	31OCT05	15MAR05		30JUN04*	30JAN04		40
Final Report	01DEC04	15JAN05					0
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		50

* These dates are actual dates.

Conditions/Events which have/may result in delayed progress

- **None.**

Current Project Activities

- Property owners were contacted and completion appointments were scheduled.
- Thirteen properties remediated to backfill this week for a total of 156 properties.
- Seven completion appointments completed.
- Digital copies of property files were created and property completion packets composed.
- Final letters were mailed out to property owners for properties remediated through June 30, 2004 (230 letters).
- NE Denver Housing has completed conducting the lead-based paint assessment of the first fifteen homes.
- Community meeting was held at the Swansea Recreation Center October 14, 2004. Ms. Smith of PRI attended the meeting. A future meeting is planned for 1/05 and Ms. Smith has been requested to present on the lead-based paint assessments and abatement process at that time.
- Weekly meeting with Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on Wednesday, October 13, 2004.

Upcoming Project Activities


- Ten properties scheduled for remediation next week.
- A meeting is scheduled with NE Denver Housing on 10/21 to review the results of the fifteen lead-based paint assessments.

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	143	156	
Square Footage Excavated	SF	595,559	631,091*	

*Approximate totals

Project Photos

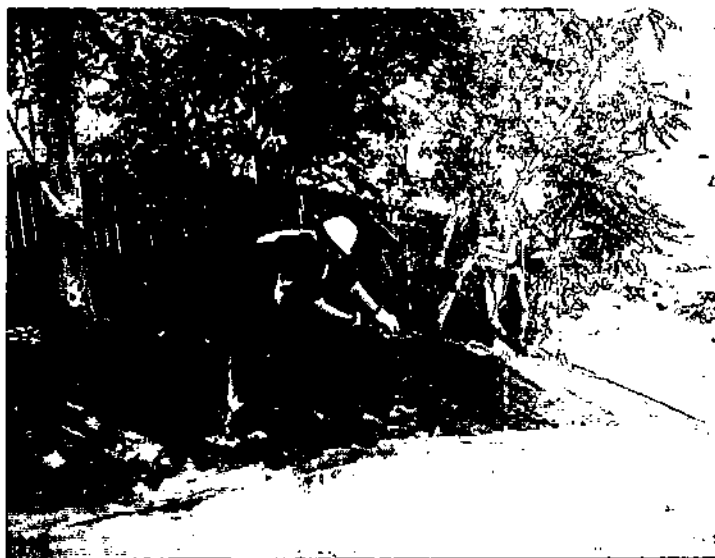

Additional Comments/Observations

☐ None

Signed: *Michelle Smith*

Date:

15OCT04
