


(b) (7)(E)


(b) (7)(E)

(b) (7)(E)

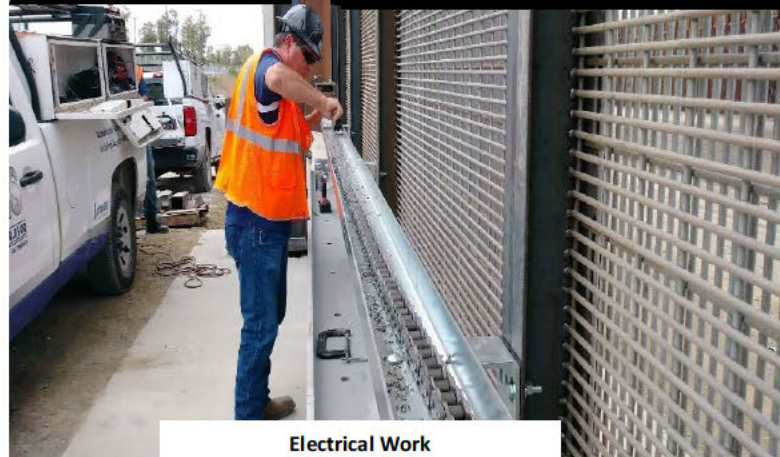

Electrical Work

(b) (7)(E)

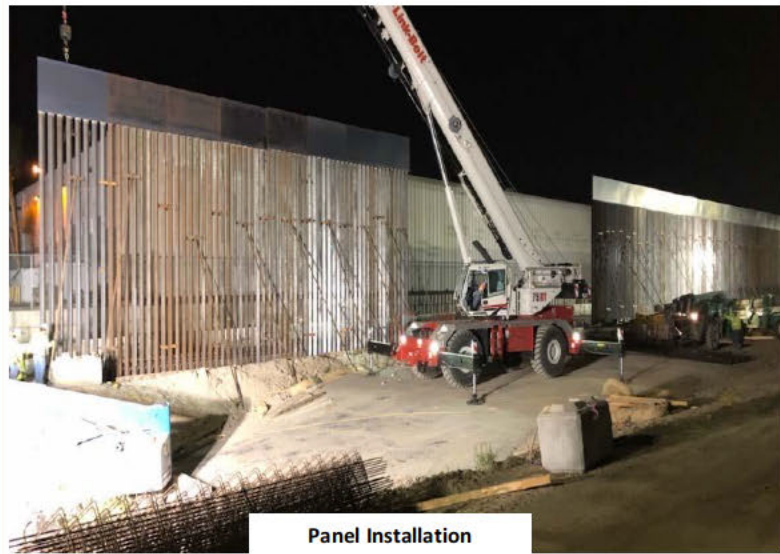

Panel Installation

Construction of FY18 San Diego SECONDARY Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)



Legacy Barrier Demolition


Construction of (b) (7)(E) Primary Replacement Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

(b) (7)(E)

07.16.2019 09:31

Installed Panels

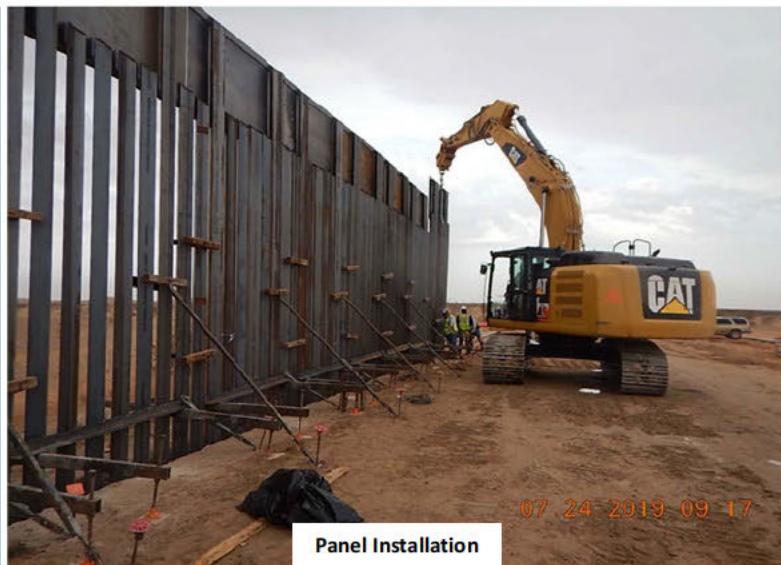

07.24.2019 09:17

Panel Installation

(b) (7)(E)

07.24.2019

Panel Installation



07.24.2019

Panel Installation

Construction of (b) (7)(E) Primary Replacement Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

U.S. Customs and Border Protection **FY 2017 - 2019 Investment Plan**

SW Border Overview*

Total Southwest Border: 1,954 mi

Existing Barrier: 654 mi No Barrier: 1,300 mi

PW to Replace: 221 mi PW Replace: 133 mi VB Conversion: 300 mi Primary Border Wall System: 864 mi Non Priority: 437 mi

Secondary Enforcement Zone: 771 mi

*totals may differ slightly due to rounding

	FY2017	(b) (7)(E)	Type	Barrier	Qty.	Planned	CBP Obligated	USACE Obligated
		(b) (7)(E)						
			TOTAL			\$341M	\$336.5M	\$286.5M
	FY2018	Up to (b) (7)(E)	Type	Barrier	Qty.	Enacted	CBP Obligated	USACE Obligated
		\$1.375B						
		(b) (7)(E)						
			TOTAL			\$1.375B	\$1.29B	\$827.3M
	FY2019	TBD Miles ~\$2B**	Type	Barrier	Qty.	Planned	CBP Obligated	USACE Obligated
		(b) (7)(E)						
			TOTAL			\$2B	\$1.46B	\$81.8M

****DHS Budget \$1375B, Treasury Forfeiture Funds (TFF) \$601M**

FOR OFFICIAL USE ONLY

7/26/19

FY17 ENACTED BUDGET PROJECTS (To date, ~39.5/40 Miles & 99% Complete)			
	Project Milestone	Milestone Date	Status
(b) (7)(E)			

*Construction Start denotes the start of the contractor's Period of Performance (POF). Actual construction start dates are unavailable until Contract is awarded.

~~FOR OFFICIAL USE ONLY~~ 7/26/19

NOTE: Subject to change based upon Acquisition Timelines

Milestones

= TBD

= 30+ Days Slip

= 1-30 Days Slip

= On Schedule

= Complete

FY18 ENACTED BUDGET PROJECTS – Continued

(b) (7)(E)

1/19/2018 – (b) (7)(E) – ARB Approved (b) (7)(E) of levee wall in (b) (7)(E) County, Texas and (b) (7)(E) of bollard wall in (b) (7)(E) County, Texas
9/6/2018 – (b) (7)(E) – ARB Approved (b) (7)(E) of existing secondary wall in San Diego Sector, along the international border adjacent to (b) (7)(E) Mexico and (b) (7)(E) of new secondary wall extending to the (b) (7)(E) that is without secondary wall

FY19 ENACTED BUDGET PROJECTS

(b) (7)(E)

4/30/2019 – (b) (7)(E) – Pending ARB Approval – (b) (7)(E) of Border Wall System in (b) (7)(E) Texas

*Construction Start denotes the start of the contractor's Period of Performance (POP)
Actual construction start dates are unavailable until Contract is awarded

FOR OFFICIAL USE ONLY 7/26/19

FY19 DoD SECTION 284 PROJECTS

(b) (7)(E)

NOTE: Subject to change based upon Acquisition Timelines

= Change From Prior Week

= TBD

= 30+ Days Slip

= 1-30 Days Slip

= On Schedule

= Complete

Real Estate

Project	Miles/# of Land Tracts**	Initial Land Ownership Determination	Appraisal/Valuation Complete	Real Estate Possession
---------	--------------------------	--------------------------------------	------------------------------	------------------------

FY18

(b) (7)(E)

**Construction Start denotes the start of the contractor's Period of Performance (POP)
Actual construction start dates are unavailable until Contract is awarded
*** of tracts may change as we proceed through the Real Estate Acquisition Process

FOR OFFICIAL USE ONLY 7/26/19

From: (b)(6);(b)(7)(C)
Sent: Monday, July 29, 2019 9:08 AM
To: MARTIN, JERRY B
Subject: weekly wall email to chiefs
Attachments: FW Border Wall Weekly (22-26 July).oft

Attached for your use.

(b)(6);(b)(7)(C)
Deputy Executive Director, Strategic Planning & Analysis
U.S. Border Patrol
Desk (b)(6);(b)(7)(C)
Mobile (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

To: BP Field Chief (b) (7)(E) BP Field Deputie (b) (7)(E)
Cc: HASTINGS, BRIAN (b)(6);(b)(7)(C)
SINGLETON, RUYNARD (b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

Subject: FW: Border Wall Weekly (22-26 July)
[溢漸坊圪汚滌彌抵換梯湯惟濠猪イ敗歩漠 畊袷\(-\)ゑ\(-\) 6撃7](#)
[単備獲枯敷彫愁菜寝牡彤十た例L56撃7](#)

Chiefs & Deputies,

As promised, below please find below and attached the Border Wall Weekly Report. Do not hesitate to reach out if you have questions or concerns.

VR,

Brian Martin
U.S. Border Patrol
Chief of Strategic Planning and Analysis
Washington, DC
O (b)(6);(b)(7)(C)
M

Executive Summary: To date, ~14 miles (18% and ~1.3 miles more than last week) of the FY18 new and replacement wall (~76-80 total miles) and ~39.5 miles (99%) of the FY17 replacement wall (~40 total miles) have been constructed.

FY 2017 Wall Program

- * San Diego Primary Replacement Project (~14 miles):
 - ~13.1 miles (36 more panels than last week), have been constructed as of July 24. The last panels are expected to be installed in the next two weeks. The total project is estimated to be approximately 13.2 miles, however, final measurement will be done upon completion. (Photos attached)
- * RGV Gates (35 gates):
 - Package 1 (b)(7)(E) gates i (b)(7)(E) County Construction is on-going a (b)(7)(E) gates. Construction completion is estimated for lat (b)(5) (Photos attached)
 - Packages 2 & (b)(7) gates i (b)(7)(E) County an (b)(7) gates i (b)(7)(E) Award remains anticipated f (b)(5).
 - ROE-S signed to date: 30 of 43 (70%)
 - Surveys complete: 32 of 43 (74%)
 - Appraisals complete: 0 of 43 (0%)
 - Offers-to-Sell Delivered: 0 of 43 (0%)
 - Accepted Offers-to-Sell: 0 of 43 (0%)

FY 2018 Wall Program

- * (b)(7)(E) Primary Replacemen (b)(7)(E)
 - (b)(7)(E) more than last week), have been constructed as of July 24. Construction completion is estimated fo (b)(5). (Photos attached)
 - (b)(7)(E) are under contract. The remainin (b)(7)(E) have yet to be awarde (b)(5)

* San Diego Secondary Replacement (~14 miles):

- ~5.4 miles (0.2 miles more than last week), have been constructed as of July 24. Panel construction completion for is estimated for January 2020. (Photos attached)

* San Diego (b) (7)(E) Primary Replacement (b) (7)(E)

- (b) (7)(E) more than last week), have been constructed as of July 24. Panel construction completion for is estimate (b) (5) (Photos attached)

* El Centro (b) (7)(E) Primary Replacement (b) (7)(E)

- The USACE has been working through real estate challenges arising from poor land ownership records from previous barrier construction. DOJ is working with the USACE and CBP on obtaining the necessary private tracts of land. DOJ's involvement will allow for real estate clearance to continue, but the timeline is currently unknown pending the court issuing declarations of taking. The next panel installation (b) (7)(E) is anticipated to start in (b) (5)

* Rio Grande Valley Levee Wall (RG (b) (7)(E) RGV (b) (7)(E)

- RG (b) (7)(E) USAC (b) (5)
(b) (5) USACE has agreed on a new approach to clear real estate 2 miles at a time in an effort to keep the project moving. All Offers-to-Sell have been sent to landowners and are currently in negotiations.

□ ROE-S signed to date: 34 of 34 (100%)

□ Surveys complete: 34 of 34 (100%)

□ Appraisals complete: 31 of 31 (100%) (only required for private tracts)

□ Offers-to-Sell Delivered: 31 of 31 (100%) (only required for private tracts)

- Some offers have been with land owners for over a month. Project designs are currently being developed and are not finalized. Many landowners have irrigation or drainage questions that CBP cannot answer with confidence as the design process is ongoing. Landowners are hesitant to sign without knowing the final plan for the property. CBP continues to engage landowners in an effort to incorporate any landowner concerns into the initial design phase to preclude court action, and move to offer acceptance in as many cases as possible.

□ Accepted Offers-to-Sell: 7 of 31 (23%) (an increase of 1 from last week)

- RG (b) (7)(E) Limited construction continues on the enforcement zone patrol road. CBP met this week to review the levee seepage mitigation design. IBWC comments are due back July 31. Once the final design is approved by all stakeholders, and real estate is cleared, levee wall construction will commence.

□ ROE-S signed to date: 19 of 19 (100%)

□ Surveys complete: 19 of 19 (100%)

□ Appraisals complete: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)

□ Offers-to-Sell Delivered: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)

□ Accepted Offers-to-Sell: 0 of 16 (0%)

* Rio Grande Valley Border Wall System (RGV (b) (7)(E) i (b) (7)(E) County):

- This project comprises the areas that require additional consultation with (b) (7)(E) County elected officials (as required by the FY19 appropriation language). USBP has received all proposed alignments. The proposals are currently undergoing hydraulic analysis and modeling which is now anticipated to be completed in late (b) (5), which will then be reviewed by RGV Sector to identify any operational gaps. USBP and USACE will then discuss the findings of the analysis with the cities in an effort to seek a consensus on alignments while meeting operational requirements and treaty obligations. These meetings are anticipated to occur with the cities in September. It is anticipated that this may continue past September 30, 2019, which was the deadline established in the FY19 appropriation language.

□ ROE-S signed to date: 136 of 155 (88%)

□ Surveys complete: 20 of 155 (13%)

□ Appraisals complete: 0 of 152 (0%) (only required for private tracts)

□ Offers-to-Sell Delivered: 0 of 152 (0%) (only required for private tracts)

□ Accepted Offers-to-Sell: 0 of 152 (0%)

FY 2019 Wall Program

* Rio Grande Valley Levee Wall (RGV (b) (7)(E))

- The contract award remains anticipate (b) (5). Construction start is anticipated for (b) (5), assuming availability of real estate.

□ ROE-S signed to date: 81 of 95 (85%)

□ Surveys complete: 88 of 95 (92%)

□ Appraisals complete: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)

□ Offers-to-Sell Delivered: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)

□ Accepted Offers-to-Sell: 0 of 85 (0%)

* Rio Grande Valley Border Wall System (RG (b) (7)(E))

- The Contractor is currently developing the construction schedule and design. Construction start is anticipated for September.
- USBP continues to work with the USACE on barrier coating. USBP will apprise leadership of the potential impacts of the costs in advance of its execution.
- This project is U.S. Fish and Wildlife property and is currently real estate cleared. Four private tracts will require easements for access during construction. The USACE is currently working to obtain access.

* Rio Grande Valley Border Wall System (Remainin (b) (7)(E))

- The RFP packages for the FY19 projects RG (b) (7)(E) and RG (b) (7)(E) are anticipated to advertise (b) (5) and RG (b) (7)(E) is on track for (b) (5). USACE has changed the acquisition strategy from the pre-qualified sources list (#3) to the Western MATOC.
- Real estate numbers have been updated for FY19, however as the alignments are finalized, these are subject to change.

□ RG (b) (7)(E) Border Wall System (b) (7)(E)

- * This award remains on hold with GAO Protest submitted by four companies. USACE has submitted the corrective action plan which the GAO appears to have accepted which should resolve the protest within 30-60 days.
- * ROE-S signed to date: 23 of 23 (100%)
- * Surveys complete: 0 of 23 (0%)
- * Appraisals complete: 0 of 21 (0%) (only required for private tracts)
- * Offers-to-Sell Delivered: 0 of 21 (0%) (only required for private tracts)

□ RG (b) (7)(E) Border Wall System (b) (7)(E)

- * ROE-S signed to date: 170 of 177 (96%) (an increase of 1 from last week)
- * ROE-S DTs filed: 4 (pending)
- * Surveys complete: 0 of 177 (0%)
- * Appraisals complete: 0 of 174 (0%) (only required for private tracts)
- * Offers-to-Sell Delivered: 0 of 174 (0%) (only required for private tracts)

□ RG (b) (7)(E) Border Wall System (b) (7)(E)

- * ROE-S signed to date: 75 of 89 (84%) (an increase of 1 from last week)
- * Surveys complete: 0 of 89 (0%)
- * Appraisals complete: 0 of 74 (0%) (only required for private tracts)
- * Offers-to-Sell Delivered: 0 of 74 (0%) (only required for private tracts)

□ RG (b) (7)(E) Border Wall System (b) (7)(E)

- * ROE-S signed to date: 113 of 145 (78%) (an increase of 8 from last week)
- * ROE-S DTs filed: 3 (pending)
- * Surveys complete: 16 of 145 (11%)
- * Appraisals complete: 0 of 145 (0%) (only required for private tracts)
- * Offers-to-Sell Delivered: 0 of 145 (0%) (only required for private tracts)

- * As approved in late FY18, USBP will be constructing model enforcement zone at the Border Patrol Academy in Artesia, New Mexico to execute effective deployment, test and evaluation activities. Construction will include approximately 300 feet of primary and 300 feet of secondary border barrier with various toppings at various heights.

○ Construction is estimated to start in earl (b) (5) and complete by the end o (b) (5)

Treasury Forfeiture Funds (TFF)

- * CBP continues to plan to be flexible in its execution of the TFF, including planning for the possible execution of

- USBP is currently scoping the projects in (b) (7)(E) and awaiting the hydrology and hydraulic analysis which is anticipated to be completed in late (b) (5).
- All Treasury Forfeiture Funds have been allocated to the Border Wall program as of July 25 in the amount of \$601M.

Acquisition

- * The Eastern MATOC (\$5B in capacity) award remains on hold with a GAO Protest submitted by four companies. USACE has submitted the corrective action plan (b) (5)

FY 2020 Wall Program

- * No update this week.

We Build the Wall Coordination

- * USBP is developing a checklist to evaluate both past and future border wall construction for donation acceptance. It is estimated that this checklist will be completed in mid-August for CBP and DHS leadership approval. USBP will then follow back up with the *We Build the Wall* organization and present the checklist at an in person meeting in late August.

DoD Coordination Update

- * **284 Counter-Narcotics Funding (approximately (b) (7)(E))**
 - All of the DoD-assisted projects are now subject to a permanent injunction issued by the Federal District Court for the Northern District of California on June 28, 2019. The District Court's injunction bars the Government from taking any action to construct border barrier using the funds DoD had identified for the projects in the Yuma, El Paso, El Centro, and Tucson Sectors. The Government has appealed the District Court's decision that DoD's transfer of funds was impermissible. The Government is also seeking a stay of the injunction pending its appeal of the District Court's decision.
 - The Supreme Court is anticipated to make a decision by the end of this week on the requested stay.
 - The border wall projects included in DHS's request for assistance remain high priority areas for the USBP in order to obtain operational control of the border. Therefore, while the Government will not be undertaking any construction activity for these projects using DoD funds in light of the injunction referenced above, CBP will continue its environmental planning efforts to include the completion of environmental surveys to identify and consider potential impacts to the proposed border wall project areas in the event these projects proceed under future funding. The environmental planning efforts for these projects are funded by CBP appropriations.
- * **2808 Military Construction Funding:** USBP is awaiting SECDEF's decision on the use of 10 U.S.C. § 2808 funds. SECDEF confirmed by U.S. Senate on July 23.

Media

- * Fox News "Trump has not built a single mile of new border fence, agency confirms"
<https://www.foxnews.com/politics/trump-has-not-built-a-single-mile-of-new-border-fence-agency-confirms>
- * Townhall "Good News: We've Finished 50 Miles of New Border Wall"
<https://townhall.com/tipsheet/mattvespa/2019/07/22/good-news-weve-finished-50-miles-of-new-border-wall-n2550410>

- * Breitbart “Exclusive: Completed Section of Trump’s New Wall Helping Secure Border, Says Agents”
<https://www.breitbart.com/border/2019/07/23/exclusive-completed-section-of-trumps-new-wall-helping-secure-border-say-agents/>
- * We Build the Wall is hosting a three day symposium on the topic of National and Border Security. Speakers include NBPC President Brandon Judd, Kris Kobach, Brian Kolfage, Steve Bannon, Tommy Fisher and more. Symposium at the Wall: Cartels, Trafficking and Asylum <https://thewallsymposium.com/>

WARNING: This document is ~~LAW ENFORCEMENT SENSITIVE~~ and is designated ~~FOR OFFICIAL USE ONLY (FOUO)~~. It contains information that may be exempt from public release under the Freedom of Information Act (5 USC 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with Department of Homeland Security policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need to know" without prior approval.

From: (b)(6);(b)(7)(C)
Sent: Monday, July 29, 2019 10:23 AM
To: (b)(6);(b)(7)(C)
Subject: RE: Border Wall Weekly (22-26 July)

Amazing.

(b)(6);(b)(7)(C)
(Contractor, ManTech Team)
Supporting the Chief Engineer, Office of Acquisition
U.S. Customs and Border Protection

.....
Cell: (b)(6);(b)(7)(C)

.....
1901 South Bell Street, Suit (b)(6);(b)(7)(C)
Arlington, Virginia 22202
(b)(6);(b)(7)(C)

From (b)(6);(b)(7)(C)
Sent: Monday, July 29, 2019 8:42 AM
To (b)(6);(b)(7)(C)
Subject: FW: Border Wall Weekly (22-26 July)

Gents, FYI...

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
Chief Engineer & Chief Risk Officer
U.S. Customs and Border Protection
Ofc: (b)(6);(b)(7)(C)
Cell
Email: (b)(6);(b)(7)(C)
Address: 1901 S. Bell Street
Arlington VA 20598

From (b)(6);(b)(7)(C)
Sent: Monday, July 29, 2019 8:12 AM
To: (b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)
(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)

Subject: FW: Border Wall Weekly (22-26 July)

SA

(b)(6);(b)(7)(C)

*Division Director
Acquisition Policy and Oversight (APO)
Office of Acquisition (OA/AGO)*

(b)(6);(b)(7)(C) (office)
(cell)
(fax)

(b)(6);(b)(7)(C)

From (b)(6);(b)(7)(C)

Sent: Saturday, July 27, 2019 10:00 AM

To: (b)(6);(b)(7)(C)

[Redacted body text]

(b)(6);(b)(7)(C)

Cc: BORDERWALLTASKS (b) (7)(E) PMOD Tasker (b) (7)(E)
Subject: Border Wall Weekly (22-26 July)

All,
Below is the Border Wall Weekly update that was sent yesterday to DHS HQ and CBP leadership.
Please note that RG (b) (7)(E) and (b) (7)(E) were NOT solicited by USACE yesterday and that is now anticipated for (b) (5).
Also, as you all are likely aware, the 284 stay has been lifted by the Supreme Court. Details
here: <https://apnews.com/5d893d388c254c7fa83a1570112ae90e>
Attached are the Border Wall card and updated photos.
Have a great weekend!
Thanks,
(b) (7)(E)

Executive Summary: To date, ~14 miles (18% and ~1.3 miles more than last week) of the FY18 new and replacement wall (~76-80 total miles) and ~39.5 miles (99%) of the FY17 replacement wall (~40 total miles) have been constructed.

FY 2017 Wall Program

- San Diego Primary Replacement Project (~14 miles):

- ~13.1 miles (36 more panels than last week), have been constructed as of July 24. The last panels are expected to be installed in the next two weeks. The total project is estimated to be approximately 13.2 miles, however, final measurement will be done upon completion. (Photos attached)
- RGV Gates (35 gates):
 - Package 1 (b) (7)(E) gates i (b) (7)(E) County Construction is on-going a (b) (7)(E) gates. Construction completion is estimated for la (b) (5). (Photos attached)
 - Packages 2 & 3 (b) (7)(E) gates i (b) (7)(E) County an (b) (7)(E) gates i (b) (7)(E) Award remains anticipated fo (b) (5).
 - ROE-S signed to date: 30 of 43 (70%)
 - Surveys complete: 32 of 43 (74%)
 - Appraisals complete: 0 of 43 (0%)
 - Offers-to-Sell Delivered: 0 of 43 (0%)
 - Accepted Offers-to-Sell: 0 of 43 (0%)

FY 2018 Wall Program

- (b) (7)(E) Primary Replacemen (b) (7)(E)
 - (b) (7)(E) more than last week), have been constructed as of July 24. Construction completion is estimated fo (b) (5). (Photos attached)
 - (b) (7)(E) are under contract. The remainin (b) (7)(E) have yet to be awarded (b) (5)
- San Diego Secondary Replacement (~14 miles):
 - ~5.4 miles (0.2 miles more than last week), have been constructed as of July 24. Panel construction completion for is estimated for January 2020. (Photos attached)
- San Dieg (b) (7)(E) Primary Replacemen (b) (7)(E)
 - (b) (7)(E) more than last week), have been constructed as of July 24. Panel construction completion for is estimate (b) (5) (Photos attached)
- El Centr (b) (7)(E) Primary Replacemen (b) (7)(E)
 - The USACE has been working through real estate challenges arising from poor land ownership records from previous barrier construction. DOJ is working with the USACE and CBP on obtaining the necessary private tracts of land. DOJ's involvement will allow for real estate clearance to continue, but the timeline is currently unknown pending the court issuing declarations of taking. The next panel installatio (b) (7)(E) is anticipated to start i (b) (5).
- Rio Grande Valley Levee Wall (RG (b) (7)(E) RGV (b) (7)(E)
 - RG (b) (7)(E) USAC (b) (5)
 - ROE-S signed to date: 34 of 34 (100%)
 - Surveys complete: 34 of 34 (100%)
 - Appraisals complete: 31 of 31 (100%) (only required for private tracts)

- Offers-to-Sell Delivered: 31 of 31 (100%) (only required for private tracts)
 - Some offers have been with land owners for over a month. Project designs are currently being developed and are not finalized. Many landowners have irrigation or drainage questions that CBP cannot answer with confidence as the design process is ongoing. Landowners are hesitant to sign without knowing the final plan for the property. CBP continues to engage landowners in an effort to incorporate any landowner concerns into the initial design phase to preclude court action, and move to offer acceptance in as many cases as possible.
- Accepted Offers-to-Sell: 7 of 31 (23%) (an increase of 1 from last week)
- RG (b) (7)(E) Limited construction continues on the enforcement zone patrol road. CBP met this week to review the levee seepage mitigation design. IBWC comments are due back July 31. Once the final design is approved by all stakeholders, and real estate is cleared, levee wall construction will commence.
 - ROE-S signed to date: 19 of 19 (100%)
 - Surveys complete: 19 of 19 (100%)
 - Appraisals complete: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)
 - Offers-to-Sell Delivered: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)
 - Accepted Offers-to-Sell: 0 of 16 (0%)
- Rio Grande Valley Border Wall System (RGV (b) (7)(E) i (b) (7)(E) County):
 - This project comprises the areas that require additional consultation with (b) (7)(E) County elected officials (as required by the FY19 appropriation language). USBP has received all proposed alignments. The proposals are currently undergoing hydraulic analysis and modeling which is now anticipated to be completed in lat (b) (5), which will then be reviewed by RGV Sector to identify any operational gaps. USBP and USACE will then discuss the findings of the analysis with the cities in an effort to seek a consensus on alignments while meeting operational requirements and treaty obligations. These meetings are anticipated to occur with the cities in September. It is anticipated that this may continue past September 30, 2019, which was the deadline established in the FY19 appropriation language.
 - ROE-S signed to date: 136 of 155 (88%)
 - Surveys complete: 20 of 155 (13%)
 - Appraisals complete: 0 of 152 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 152 (0%) (only required for private tracts)
 - Accepted Offers-to-Sell: 0 of 152 (0%)

FY 2019 Wall Program

- Rio Grande Valley Levee Wall (RGV (b) (7)(E))
 - The contract award remains anticipate (b) (5) Construction start is anticipated for (b) (5), assuming availability of real estate.
 - ROE-S signed to date: 81 of 95 (85%)
 - Surveys complete: 88 of 95 (92%)

- Appraisals complete: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)
 - Offers-to-Sell Delivered: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)
 - Accepted Offers-to-Sell: 0 of 85 (0%)
- Rio Grande Valley Border Wall System (RGV (b) (7)(E))
 - The Contractor is currently developing the construction schedule and design. Construction start is anticipated for September.
 - USBP continues to work with the USACE on barrier coating. USBP will apprise leadership of the potential impacts of the costs in advance of its execution.
 - This project is U.S. Fish and Wildlife property and is currently real estate cleared. Four private tracts will require easements for access during construction. The USACE is currently working to obtain access.
- Rio Grande Valley Border Wall System (Remainin (b) (7)(E))
 - The RFP packages for the FY19 projects RG (b) (7)(E) and RG (b) (7)(E) are anticipated to advertise (b) (5) and RG (b) (7)(E) is on track for (b) (5). USACE has changed the acquisition strategy from the pre-qualified sources list (#3) to the Western MATOC.
 - Real estate numbers have been updated for FY19, however as the alignments are finalized, these are subject to change.
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - This award remains on hold with GAO Protest submitted by four companies. USACE has submitted the corrective action plan which the GAO appears to have accepted which should resolve the protest within 30-60 days.
 - ROE-S signed to date: 23 of 23 (100%)
 - Surveys complete: 0 of 23 (0%)
 - Appraisals complete: 0 of 21 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 21 (0%) (only required for private tracts)
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - ROE-S signed to date: 170 of 177 (96%) (an increase of 1 from last week)
 - ROE-S DTs filed: 4 (pending)
 - Surveys complete: 0 of 177 (0%)
 - Appraisals complete: 0 of 174 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 174 (0%) (only required for private tracts)
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - ROE-S signed to date: 75 of 89 (84%) (an increase of 1 from last week)
 - Surveys complete: 0 of 89 (0%)
 - Appraisals complete: 0 of 74 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 74 (0%) (only required for private tracts)

- RGV ^{(b) (7)} Border Wall System (b) (7)(E)
 - ROE-S signed to date: 113 of 145 (78%) (an increase of 8 from last week)
 - ROE-S DTs filed: 3 (pending)
 - Surveys complete: 16 of 145 (11%)
 - Appraisals complete: 0 of 145 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 145 (0%) (only required for private tracts)
- As approved in late FY18, USBP will be constructing model enforcement zone at the Border Patrol Academy in Artesia, New Mexico to execute effective deployment, test and evaluation activities. Construction will include approximately 300 feet of primary and 300 feet of secondary border barrier with various toppings at various heights.
 - Construction is estimated to start in earl (b) (5) and complete by the end (b) (5).

Treasury Forfeiture Funds (TFF)

- CBP continues to plan to be flexible in its execution of the TFF, including planning for the possible execution o (b) (7)(E)
 - USBP is currently scoping the projects i (b) (7)(E) and awaiting the hydrology and hydraulic analysis which is anticipated to be completed in lat (b) (5).
 - All Treasury Forfeiture Funds have been allocated to the Border Wall program as of July 25 in the amount of \$601M.

Acquisition

- The Eastern MATOC (\$5B in capacity) award remains on hold with a GAO Protest submitted by four companies. USACE has submitted the corrective action pla (b) (5)

FY 2020 Wall Program

- No update this week.

***We Build the Wall* Coordination**

- USBP is developing a checklist to evaluate both past and future border wall construction for donation acceptance. It is estimated that this checklist will be completed in mid-August for CBP and DHS leadership approval. USBP will then follow back up with the *We Build the Wall* organization and present the checklist at an in person meeting in late August.

DoD Coordination Update

- **284 Counter-Narcotics Funding (approximatel (b) (7)(E)**
 - All of the DoD-assisted projects are now subject to a permanent injunction issued by the Federal District Court for the Northern District of California on June 28, 2019. The District Court's injunction bars the Government from taking any action to construct border barrier using the funds DoD had identified for the projects in the Yuma, El Paso, El Centro, and Tucson Sectors. The Government has appealed the District Court's decision that DoD's transfer of funds was impermissible. The Government is also seeking a stay of the injunction pending its appeal of the District Court's decision.
 - The Supreme Court is anticipated to make a decision by the end of this week on the requested stay.

- The border wall projects included in DHS's request for assistance remain high priority areas for the USBP in order to obtain operational control of the border. Therefore, while the Government will not be undertaking any construction activity for these projects using DoD funds in light of the injunction referenced above, CBP will continue its environmental planning efforts to include the completion of environmental surveys to identify and consider potential impacts to the proposed border wall project areas in the event these projects proceed under future funding. The environmental planning efforts for these projects are funded by CBP appropriations.
- **2808 Military Construction Funding:** USBP is awaiting SECDEF's decision on the use of 10 U.S.C. § 2808 funds. SECDEF confirmed by U.S. Senate on July 23.

Media

- Fox News "Trump has not built a single mile of new border fence, agency confirms"
<https://www.foxnews.com/politics/trump-has-not-built-a-single-mile-of-new-border-fence-agency-confirms>
- Townhall "Good News: We've Finished 50 Miles of New Border Wall"
<https://townhall.com/tipsheet/mattvespa/2019/07/22/good-news-weve-finished-50-miles-of-new-border-wall-n2550410>
- Breitbart "Exclusive: Completed Section of Trump's New Wall Helping Secure Border, Says Agents"
<https://www.breitbart.com/border/2019/07/23/exclusive-completed-section-of-trumps-new-wall-helping-secure-border-say-agents/>
- We Build the Wall is hosting a three day symposium on the topic of National and Border Security. Speakers include NBPC President Brandon Judd, Kris Kobach, Brian Kolfage, Steve Bannon, Tommy Fisher and more. Symposium at the Wall: Cartels, Trafficking and Asylum
<https://thewallsymposium.com/>

WARNING: This document is ~~LAW ENFORCEMENT SENSITIVE~~ and is designated ~~FOR OFFICIAL USE ONLY (FOUO)~~. It contains information that may be exempt from public release under the Freedom of Information Act (5 USC 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with Department of Homeland Security policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need to know" without prior approval.

From: (b)(6);(b)(7)(C)
Sent: Monday, July 29, 2019 10:38 AM
To: (b)(6);(b)(7)(C)
Cc: (b)(6);(b)(7)(C)
Subject: FW: Border Wall Weekly (22-26 July)
Attachments: Border Wall Construction Photos Week of July 26, 2019.pdf; USBP Border Wall Card S1 072619.pdf

Good morning All,

I (b)(6);(b)(7)(C) absence, I am sending out the Border Wall Weekly Activity Report for this week that was sent to DHS HQ and CBP leadership today. Specific to SDC is highlighted in yellow. In addition, attached are the Border Wall card and updated photos.

Please let me know if you have any questions or concerns.

Respectfully,

(b)(6);(b)(7)(C)

(b)(6);(b)(7)(C)
(A) Director of Logistics
U.S. Customs & Border Protection
San Diego Sector Border Patrol Headquarters
Mission Readiness Operations Division – Logistics
Cell (b)(6);(b)(7)(C)
Offic

(b)(6);(b)(7)(C)

>

Subject: Border Wall Weekly (22-26 July)

All,

Below is the Border Wall Weekly update that was sent yesterday to DHS HQ and CBP leadership.

Please note that RG (b) (7)(E) were NOT solicited by USACE yesterday and that is now anticipated for (b) (5)

Also, as you all are likely aware, the 284 stay has been lifted by the Supreme Court. Details

here: <https://apnews.com/5d893d388c254c7fa83a1570112ae90e>

Attached are the Border Wall card and updated photos.

Have a great weekend!

Thanks,

(b)(6);(b)(7)(C)

Executive Summary: To date, ~14 miles (18% and ~1.3 miles more than last week) of the FY18 new and replacement wall (~76-80 total miles) and ~39.5 miles (99%) of the FY17 replacement wall (~40 total miles) have been constructed.

FY 2017 Wall Program

- San Diego Primary Replacement Project (~14 miles):
 - ~13.1 miles (36 more panels than last week), have been constructed as of July 24. The last panels are expected to be installed in the next two weeks. The total project is estimated to be approximately 13.2 miles, however, final measurement will be done upon completion. (Photos attached)
- RGV Gates (35 gates):
 - Package 1 (b)(7)(E) gates i (b)(7)(E) County Construction is on-going a (b)(7)(E) gates. Construction completion is estimated for lat (b)(5). (Photos attached)
 - Packages 2 & 3 (b)(7)(E) gates i (b)(7)(E) County an (b)(7)(E) gates i (b)(7)(E) Award remains anticipated for July 31.
 - ROE-S signed to date: 30 of 43 (70%)
 - Surveys complete: 32 of 43 (74%)
 - Appraisals complete: 0 of 43 (0%)
 - Offers-to-Sell Delivered: 0 of 43 (0%)
 - Accepted Offers-to-Sell: 0 of 43 (0%)

FY 2018 Wall Program

- (b)(7)(E) Primary Replacement (b)(7)(E)
 - (b)(7)(E) more than last week), have been constructed as of July 24. Construction completion is estimated for (b)(5). (Photos attached)
 - (b)(7)(E) are under contract. The remainin (b)(7)(E) have yet to be awarded (b)(5)
- San Diego Secondary Replacement (~14 miles):
 - ~5.4 miles (0.2 miles more than last week), have been constructed as of July 24. Panel construction completion for is estimated for January 2020. (Photos attached)
- San Diego (b)(7)(E) Primary Replacement (b)(7)(E)
 - (b)(7)(E) more than last week), have been constructed as of July 24. Panel construction completion for is estimate (b)(5) (Photos attached)
- El Centro (b)(7)(E) Primary Replacement (b)(7)(E)
 - The USACE has been working through real estate challenges arising from poor land ownership records from previous barrier construction. DOJ is working with the USACE and CBP on obtaining the necessary private tracts of land. DOJ's involvement will allow for real estate clearance to continue, but the timeline is currently unknown pending the court issuing declarations of taking. The next panel installation (b)(7)(E) is anticipated to start i (b)(5).
- Rio Grande Valley Levee Wall (RG (b)(7)(E) / RGV (b)(7)(E)
 - RG (b)(7)(E) USAC (b)(5)
(b)(5) USACE has agreed on a new approach to clear real estate 2 miles at a time in an effort to keep the project moving. All Offers-to-Sell have been sent to landowners and are currently in negotiations.
 - ROE-S signed to date: 34 of 34 (100%)
 - Surveys complete: 34 of 34 (100%)

- Appraisals complete: 31 of 31 (100%) (only required for private tracts)
- Offers-to-Sell Delivered: 31 of 31 (100%) (only required for private tracts)
 - Some offers have been with land owners for over a month. Project designs are currently being developed and are not finalized. Many landowners have irrigation or drainage questions that CBP cannot answer with confidence as the design process is ongoing. Landowners are hesitant to sign without knowing the final plan for the property. CBP continues to engage landowners in an effort to incorporate any landowner concerns into the initial design phase to preclude court action, and move to offer acceptance in as many cases as possible.
- Accepted Offers-to-Sell: 7 of 31 (23%) (an increase of 1 from last week)
- RG (b) (7)(E) Limited construction continues on the enforcement zone patrol road. CBP met this week to review the levee seepage mitigation design. IBWC comments are due back July 31. Once the final design is approved by all stakeholders, and real estate is cleared, levee wall construction will commence.
 - ROE-S signed to date: 19 of 19 (100%)
 - Surveys complete: 19 of 19 (100%)
 - Appraisals complete: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)
 - Offers-to-Sell Delivered: 11 of 16 (69%) (only required for private tracts; an increase of 5 from last week)
 - Accepted Offers-to-Sell: 0 of 16 (0%)
- Rio Grande Valley Border Wall System (RGV (b) (7)(E) i (b) (7)(E) County):
 - This project comprises the areas that require additional consultation with (b) (7)(E) County elected officials (as required by the FY19 appropriation language). USBP has received all proposed alignments. The proposals are currently undergoing hydraulic analysis and modeling which is now anticipated to be completed in late (b) (5), which will then be reviewed by RGV Sector to identify any operational gaps. USBP and USACE will then discuss the findings of the analysis with the cities in an effort to seek a consensus on alignments while meeting operational requirements and treaty obligations. These meetings are anticipated to occur with the cities in September. It is anticipated that this may continue past September 30, 2019, which was the deadline established in the FY19 appropriation language.
 - ROE-S signed to date: 136 of 155 (88%)
 - Surveys complete: 20 of 155 (13%)
 - Appraisals complete: 0 of 152 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 152 (0%) (only required for private tracts)
 - Accepted Offers-to-Sell: 0 of 152 (0%)

FY 2019 Wall Program

- Rio Grande Valley Levee Wall (RGV (b) (7)(E))
 - The contract award remains anticipate (b) (5). Construction start is anticipated for (b) (5), assuming availability of real estate.
 - ROE-S signed to date: 81 of 95 (85%)

- Surveys complete: 88 of 95 (92%)
- Appraisals complete: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)
- Offers-to-Sell Delivered: 6 of 85 (7%) (only required for private tracts; an increase of 5 from last week)
- Accepted Offers-to-Sell: 0 of 85 (0%)
- Rio Grande Valley Border Wall System (RG (b) (7)(E))
 - The Contractor is currently developing the construction schedule and design. Construction start is anticipated for (b) (5).
 - USBP continues to work with the USACE on barrier coating. USBP will apprise leadership of the potential impacts of the costs in advance of its execution.
 - This project is U.S. Fish and Wildlife property and is currently real estate cleared. Four private tracts will require easements for access during construction. The USACE is currently working to obtain access.
- Rio Grande Valley Border Wall System (Remainin (b) (7)(E))
 - The RFP packages for the FY19 projects RG (b) (7)(E) and RG (b) (7)(E) are anticipated to advertise (b) (5) and RG (b) (7)(E) is on track for (b) (5). USACE has changed the acquisition strategy from the pre-qualified sources list (#3) to the Western MATOC.
 - Real estate numbers have been updated for FY19, however as the alignments are finalized, these are subject to change.
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - This award remains on hold with GAO Protest submitted by four companies. USACE has submitted the corrective action plan which the GAO appears to have accepted which should resolve the protest within 30-60 days.
 - ROE-S signed to date: 23 of 23 (100%)
 - Surveys complete: 0 of 23 (0%)
 - Appraisals complete: 0 of 21 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 21 (0%) (only required for private tracts)
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - ROE-S signed to date: 170 of 177 (96%) (an increase of 1 from last week)
 - ROE-S DTs filed: 4 (pending)
 - Surveys complete: 0 of 177 (0%)
 - Appraisals complete: 0 of 174 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 174 (0%) (only required for private tracts)
 - RG (b) (7)(E) Border Wall System (b) (7)(E)
 - ROE-S signed to date: 75 of 89 (84%) (an increase of 1 from last week)
 - Surveys complete: 0 of 89 (0%)
 - Appraisals complete: 0 of 74 (0%) (only required for private tracts)

- Offers-to-Sell Delivered: 0 of 74 (0%) (only required for private tracts)
- RG (b) (7)(E) Border Wall System (b) (7)(E)
 - ROE-S signed to date: 113 of 145 (78%) (an increase of 8 from last week)
 - ROE-S DTs filed: 3 (pending)
 - Surveys complete: 16 of 145 (11%)
 - Appraisals complete: 0 of 145 (0%) (only required for private tracts)
 - Offers-to-Sell Delivered: 0 of 145 (0%) (only required for private tracts)
- As approved in late FY18, USBP will be constructing model enforcement zone at the Border Patrol Academy in Artesia, New Mexico to execute effective deployment, test and evaluation activities. Construction will include approximately 300 feet of primary and 300 feet of secondary border barrier with various toppings at various heights.
 - Construction is estimated to start in earl (b) (5) and complete by the end o (b) (5)

Treasury Forfeiture Funds (TFF)

- CBP continues to plan to be flexible in its execution of the TFF, including planning for the possible execution o (b) (7)(E)
 - USBP is currently scoping the projects i (b) (7)(E) and awaiting the hydrology and hydraulic analysis which is anticipated to be completed in lat (b) (5)
 - All Treasury Forfeiture Funds have been allocated to the Border Wall program as of July 25 in the amount of \$601M.

Acquisition

- The Eastern MATOC (\$5B in capacity) award remains on hold with a GAO Protest submitted by four companies. USACE has submitted the corrective action pla (b) (5)

FY 2020 Wall Program

- No update this week.

***We Build the Wall* Coordination**

- USBP is developing a checklist to evaluate both past and future border wall construction for donation acceptance. It is estimated that this checklist will be completed in mid-August for CBP and DHS leadership approval. USBP will then follow back up with the *We Build the Wall* organization and present the checklist at an in person meeting in late August.

DoD Coordination Update

- **284 Counter-Narcotics Funding (approximatel (b) (7)(E)**
 - All of the DoD-assisted projects are now subject to a permanent injunction issued by the Federal District Court for the Northern District of California on June 28, 2019. The District Court's injunction bars the Government from taking any action to construct border barrier using the funds DoD had identified for the projects in the Yuma, El Paso, El Centro, and Tucson Sectors. The Government has appealed the District Court's decision that DoD's transfer of funds was impermissible. The Government is also seeking a stay of the injunction pending its appeal of the District Court's decision.

- The Supreme Court is anticipated to make a decision by the end of this week on the requested stay.
- The border wall projects included in DHS's request for assistance remain high priority areas for the USBP in order to obtain operational control of the border. Therefore, while the Government will not be undertaking any construction activity for these projects using DoD funds in light of the injunction referenced above, CBP will continue its environmental planning efforts to include the completion of environmental surveys to identify and consider potential impacts to the proposed border wall project areas in the event these projects proceed under future funding. The environmental planning efforts for these projects are funded by CBP appropriations.
- **2808 Military Construction Funding:** USBP is awaiting SECDEF's decision on the use of 10 U.S.C. § 2808 funds. SECDEF confirmed by U.S. Senate on July 23.

Media

- Fox News "Trump has not built a single mile of new border fence, agency confirms"
<https://www.foxnews.com/politics/trump-has-not-built-a-single-mile-of-new-border-fence-agency-confirms>
- Townhall "Good News: We've Finished 50 Miles of New Border Wall"
<https://townhall.com/tipsheet/mattvespa/2019/07/22/good-news-weve-finished-50-miles-of-new-border-wall-n2550410>
- Breitbart "Exclusive: Completed Section of Trump's New Wall Helping Secure Border, Says Agents"
<https://www.breitbart.com/border/2019/07/23/exclusive-completed-section-of-trumps-new-wall-helping-secure-border-say-agents/>
- We Build the Wall is hosting a three day symposium on the topic of National and Border Security. Speakers include NBPC President Brandon Judd, Kris Kobach, Brian Kolfage, Steve Bannon, Tommy Fisher and more. Symposium at the Wall: Cartels, Trafficking and Asylum
<https://thewallsymposium.com/>

WARNING: This document is ~~LAW ENFORCEMENT SENSITIVE~~ and is designated ~~FOR OFFICIAL USE ONLY (FOUO)~~. It contains information that may be exempt from public release under the Freedom of Information Act (5 USC 552). This document is to be controlled, handled, transmitted, distributed, and disposed of in accordance with Department of Homeland Security policy relating to FOUO information, and is not to be released to the public or personnel who do not have a valid "need to know" without prior approval.

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)




Construction of FY17 RGV Gates (Package 1) Projects as of July 26, 2019

FOR OFFICIAL USE ONLY

(b) (7)(E)


(b) (7)(E)

(b) (7)(E)

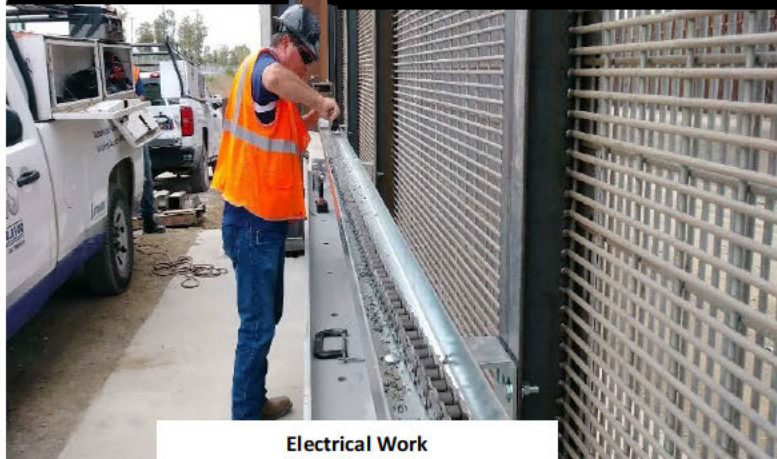

Electrical Work

(b) (7)(E)

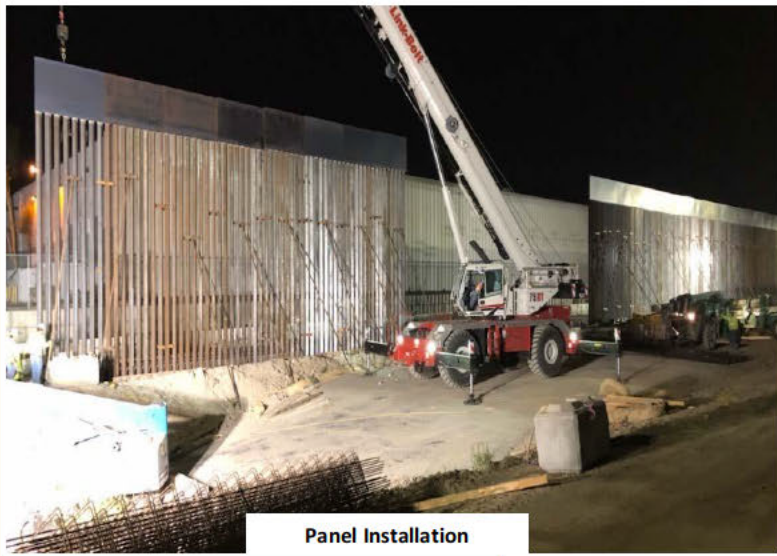

Panel Installation

Construction of FY18 San Diego SECONDARY Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

(b) (7)(E)

(b) (7)(E)

(b) (7)(E)



Legacy Barrier Demolition


Construction of (b) (7)(E) Primary Replacement Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

(b) (7)(E)

07.16.2019 09:31

Installed Panels

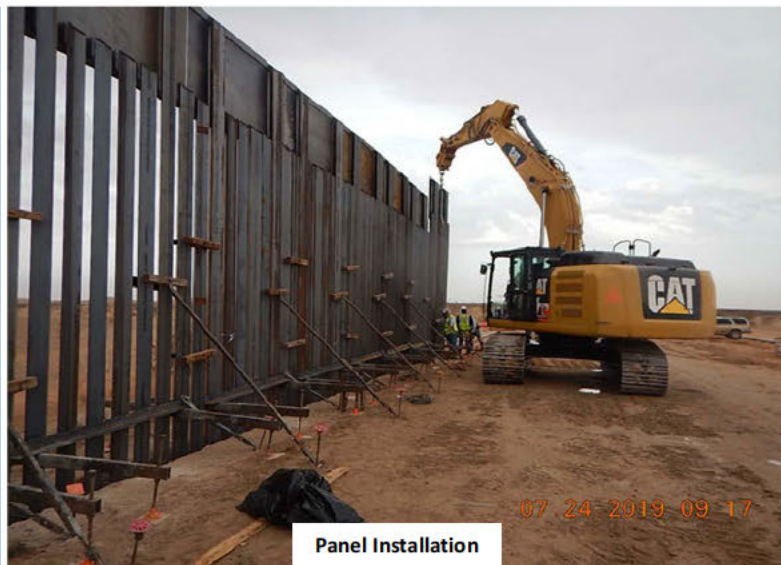

07.24.2019 09:17

Panel Installation

(b) (7)(E)

07.24.2019

Panel Installation





07.24.2019

Panel Installation

Construction of (b) (7)(E) Primary Replacement Border Wall Project as of July 26, 2019

FOR OFFICIAL USE ONLY

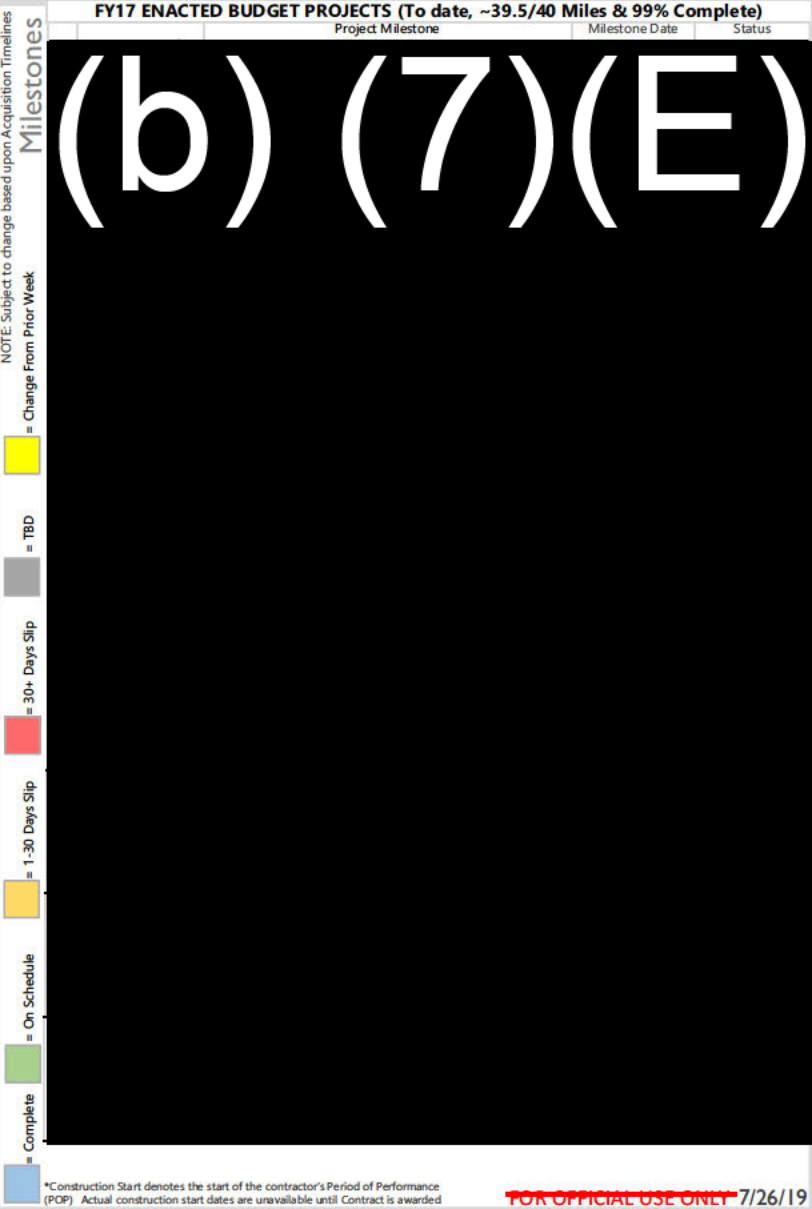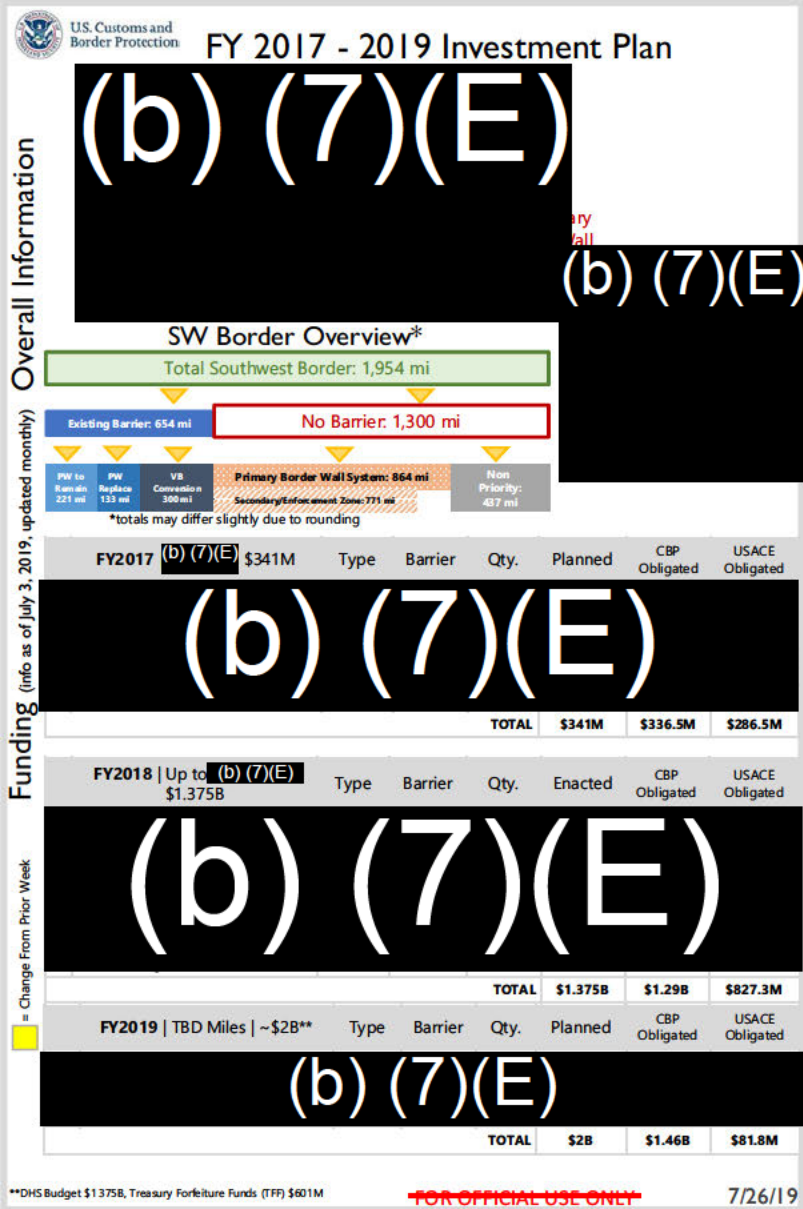

NOTE: Subject to change based upon Acquisition Timelines

Milestones

= TBD

= 30+ Days Slip

= 1-30 Days Slip

= On Schedule

= Complete

FY18 ENACTED BUDGET PROJECTS – Continued

(b) (7)(E)

1/19/2018 – (b) (7)(E) ARB Approved (b) (7)(E) of levee wall in (b) (7)(E) County, Texas and (b) (7)(E) of bollard wall in (b) (7)(E) County, Texas
9/6/2018 – (b) (7)(E) ARB Approved (b) (7)(E) of existing secondary wall in San Diego Sector, along the international border adjacent to (b) (7)(E) Mexico and (b) (7)(E) of new secondary wall extending to the (b) (7)(E) that is without secondary wall

FY19 ENACTED BUDGET PROJECTS

(b) (7)(E)

4/30/2019 – (b) (7)(E) Pending ARB Approval – (b) (7)(E) of Border Wall System in (b) (7)(E) Texas

*Construction Start denotes the start of the contractor's Period of Performance (POP)
Actual construction start dates are unavailable until Contract is awarded

FOR OFFICIAL USE ONLY 7/26/19

FY19 DoD SECTION 284 PROJECTS

(b) (7)(E)

NOTE: Subject to change based upon Acquisition Timelines

= Change From Prior Week

= TBD

= 30+ Days Slip

= 1-30 Days Slip

= On Schedule

= Complete

Real Estate

Project	Miles/# of Land Tracts**	Initial Land Ownership Determination	Appraisal/Valuation Complete	Real Estate Possession
---------	--------------------------	--------------------------------------	------------------------------	------------------------

FY18

(b) (7)(E)

**Construction Start denotes the start of the contractor's Period of Performance (POP)
Actual construction start dates are unavailable until Contract is awarded
*** of tracts may change as we proceed through the Real Estate Acquisition Process

FOR OFFICIAL USE ONLY 7/26/19
