To: Deschambault, Lynda[Deschambault.Lynda@epa.gov]; Greg

Reller[gr@burlesonconsulting.com]; Cory Koger[Cory.S.Koger@usace.army.mil]; Chang, Kay

SPK[Kay.Chang@usace.army.mil]

From: Brown, Anthony R (RM)

Sent: Mon 5/1/2017 4:34:58 PM

Subject: RE: UPCS Construction Progress Schedule

ATT00001.txt

OK thanks for the reminder

From: Deschambault, Lynda [mailto:Deschambault.Lynda@epa.gov]

Sent: Monday, May 01, 2017 9:26 AM

To: Greg Reller; Cory Koger; Chang, Kay SPK; Brown, Anthony R (RM)

Subject: FW: UPCS Construction Progress Schedule

Importance: High

Thanks Tony! Please keep EPA contractors cc'd on communications.

From: Brown, Anthony R (RM) [mailto:anthony.brown@bp.com]

Sent: Tuesday, April 25, 2017 7:58 PM

**To:** Stetler, Chris@waterboards.ca.gov (Chris.Stetler@waterboards.ca.gov)

<<u>Chris.Stetler@waterboards.ca.gov</u>>; <u>scott.bohman@copperenv.com</u>; James Padgett

(<u>JPadgett@usaenviro.com</u>)<<u>JPadgett@usaenviro.com</u>>; 'Tony Six' <<u>TSix@usaenviro.com</u>>;

'Gary Morgan' (GMorgan@usaenviro.com) < GMorgan@usaenviro.com>; Johnson, Mike

 $(COPPER\ ENVIRONMENTAL\ CONSULTING) < \underline{Mike.Johnson@copperenv.com} >;\ And y \\$ 

Slavik < andy.slavik@copperenv.com >

Cc: Doug Carey < douglas.carey@waterboards.ca.gov >; Ferguson, Scott@Waterboards

(scott.ferguson@waterboards.ca.gov) < scott.ferguson@waterboards.ca.gov>; Witt,

Darin@waterboards (<u>Darin.Witt@waterboards.ca.gov</u>) < <u>Darin.Witt@waterboards.ca.gov</u>>;

Zentner, Taylor@Waterboards (taylor.zentner@waterboards.ca.gov)

<taylor.zentner@waterboards.ca.gov>; Deschambault, Lynda <Deschambault.Lynda@epa.gov>;

McCarthy, Dave T (Copper Environmental Consulting) < <u>dave.mccarthy@copperenv.com</u>>;

Olson, Eric (COPPER ENVIRONMENTAL CONSULTING) <eric.olson@copperenv.com>;

matt.esquibel@copperenv.com; philthompson705@gmail.com; Andrew Bachman

(ABachman@usaenviro.com) < ABachman@usaenviro.com>; Grice, Steve (CONTRACTOR)

< <u>SGrice@usaenviro.com</u>>; David Hoffman < <u>DHoffman@broadbentinc.com</u>>; Souza, Michelle

(msouza@broadbentinc.com) <msouza@broadbentinc.com>; Lombardi, Marc

<marc.lombardi@amecfw.com>; Andrews, Andy (andy.andrews@amecfw.com)

<andy.andrews@amecfw.com>; abby.cazier@copperenv.com; Herrscher, Russell (UNKNOWN

BUSINESS PARTNER) < rherrscher@usaenviro.com>

Subject: UPCS Construction Progress Schedule

## Importance: High

Hi Chris, 30 staff members on site today. The USA crew is finishing up safety training/orientation and will be starting up again on the remaining UPCS construction items from now through early June (weather permitting). Attached is the latest UPCS schedule (subject to access, weather, etc.). See the attached report on over winter UPCS engineering/inspection activities – from yesterday. Also, Darin sent a note out regarding status of the spring HDS commissioning – which has begun - Darin (and others) are certainly welcome!! Copper point of contact for UPCS is now Scott Bohman (Bill Matheson is off on another job this year). Copies of the remaining UPCS submittals to follow from Mike at Copper. AMECFW to provide draft ICT test schedule as ICT shake down and commissioning approach in the next 45 days or so. Also attached below are photographs showing road maintenance. Hope this update helps you and your engineering staff. Call my cell 24/7 should you have questions.

Mike and Andy, request Copper please prepare a removal action "LAS Spring Commissioning (HDS and Aspen) Schedule Summary" for distribution to Lynda and Chris. Gary is not working on Leviathan this year and the subject schedule will help Lynda and Chris plan activities/staff site visits.

More updates to come... Hope this helps... Tony...

Anthony R Brown

Operations Project Manager - Mining

Atlantic Richfield Company

Remediation Management

4 Centerpointe Drive, Suite 200

La Palma, California USA 90623

MS Lync: 657-529-4537

Cell: 951-265-4277

----- Forwarded message -----

From: Andy Slavik < Andy.slavik@copperenv.com>


Date: Tue, Apr 25, 2017 at 6:00 PM


Subject: California Access Road Work Pictures - 4/25/17

To: philthompson705@gmail.com

Phil,

Some pics from today's roadwork. California access road is incredibly saturated and we are running into a lot of downed trees as well making progress difficult. We are close to the Haypress Flats turnoff as of this afternoon.

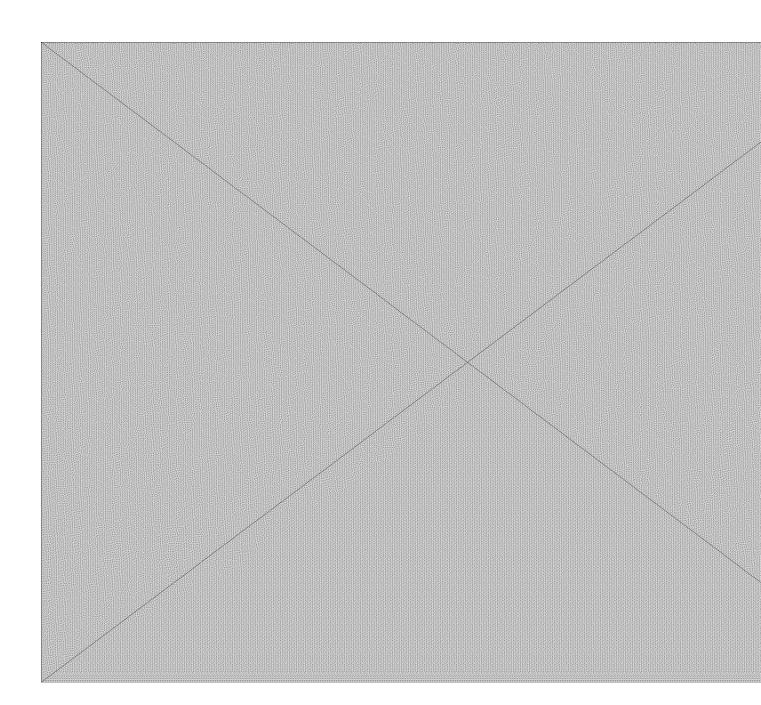

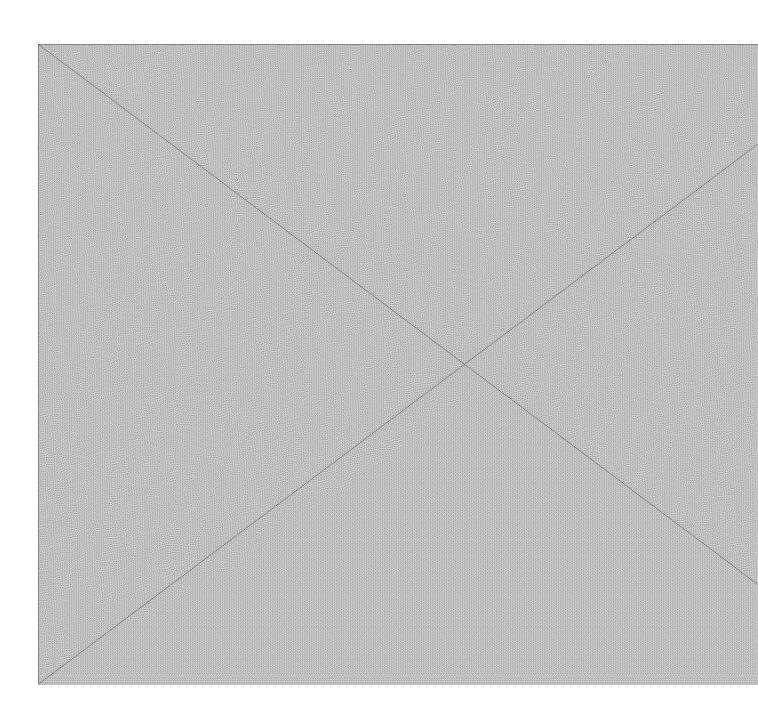



Andy

Andy Slavik

Copper Environmental Consulting

406 East Park Avenue, Suite 2

Anaconda, MT 59711

Phone (406) 563-2700

Mobile (775) 684-9698

Fax (406) 563-2701

Email: Andy.Slavik@copperenv.com

www.copperenv.com
