



## Weekly Construction Report

March 23, 2018

Job Name: EPA

Job Number: 17-1163

Address: 1595 Wynkoop Denver CO,

Project Manager: Chad Bartlett

On-Site Superintendent: Richard Abeyta

---

### Weekly Overview:

**Arens Electric-** They are installing new lights. They demoed the lights from the library and started installing them. They are pulling in wire for the lights.

**Acoustical finishers-** They are working on the drywall finishing at all locations on both the 3<sup>rd</sup> and 4<sup>th</sup> floors.

**Acoustical ceiling-** They are installing the new grid and patching at all locations.

**Custom Air-** They are installing new duct at all locations.

**All Pro Sprinkler-** They started relocation the sprinkler heads.

**AC Floors-** They are installing and patching the raised floor.

**A Splash of Paint-** They started painting walls this week.

**Linx-** They did some work at the patch panel.

Inspections Received:

Important Dates:

Weather & Site Conditions:

Services Connected/Disconnected:

Pictures:

## Weekly Construction Report


March 23, 2018



I installed the carbon filter at the building return air.

## Weekly Construction Report


March 23, 2018

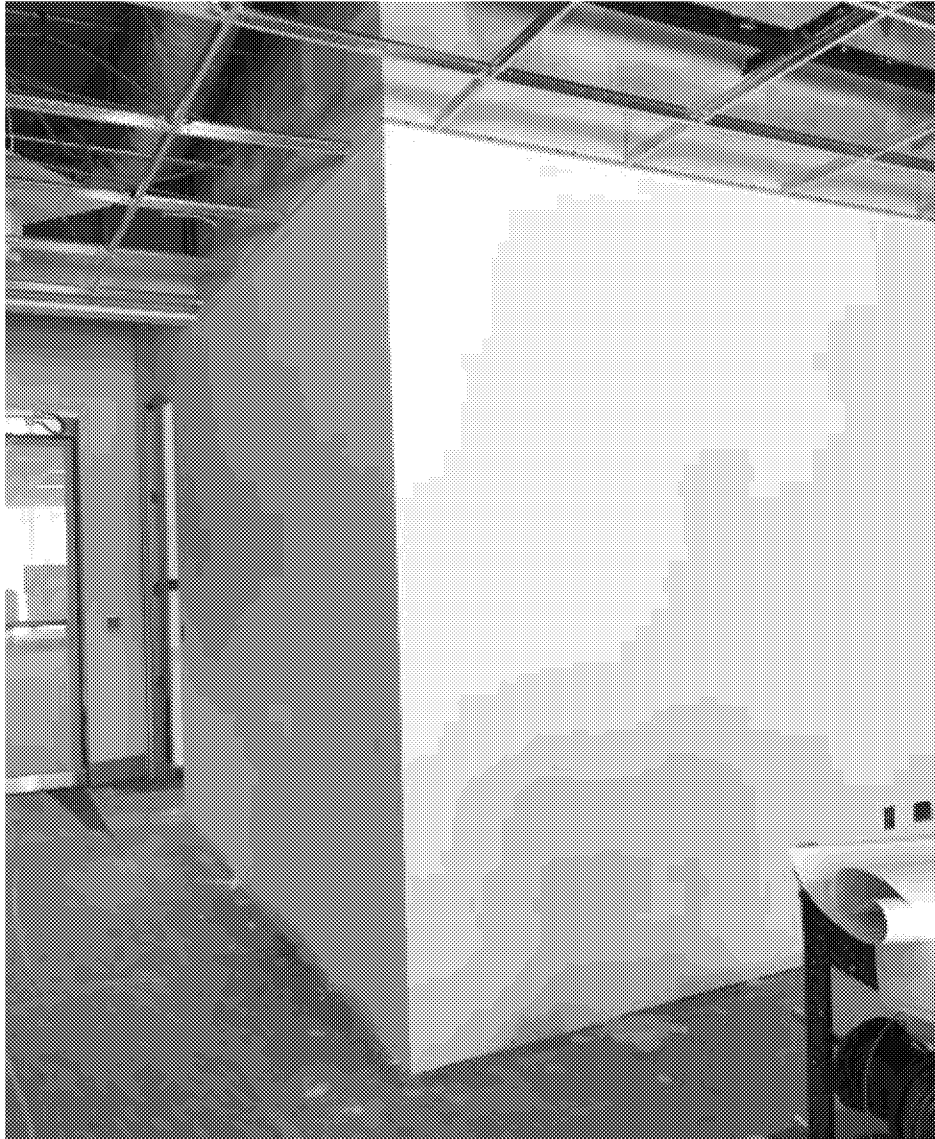

We started installing the new grid just outside the library.

## Weekly Construction Report

March 23, 2018

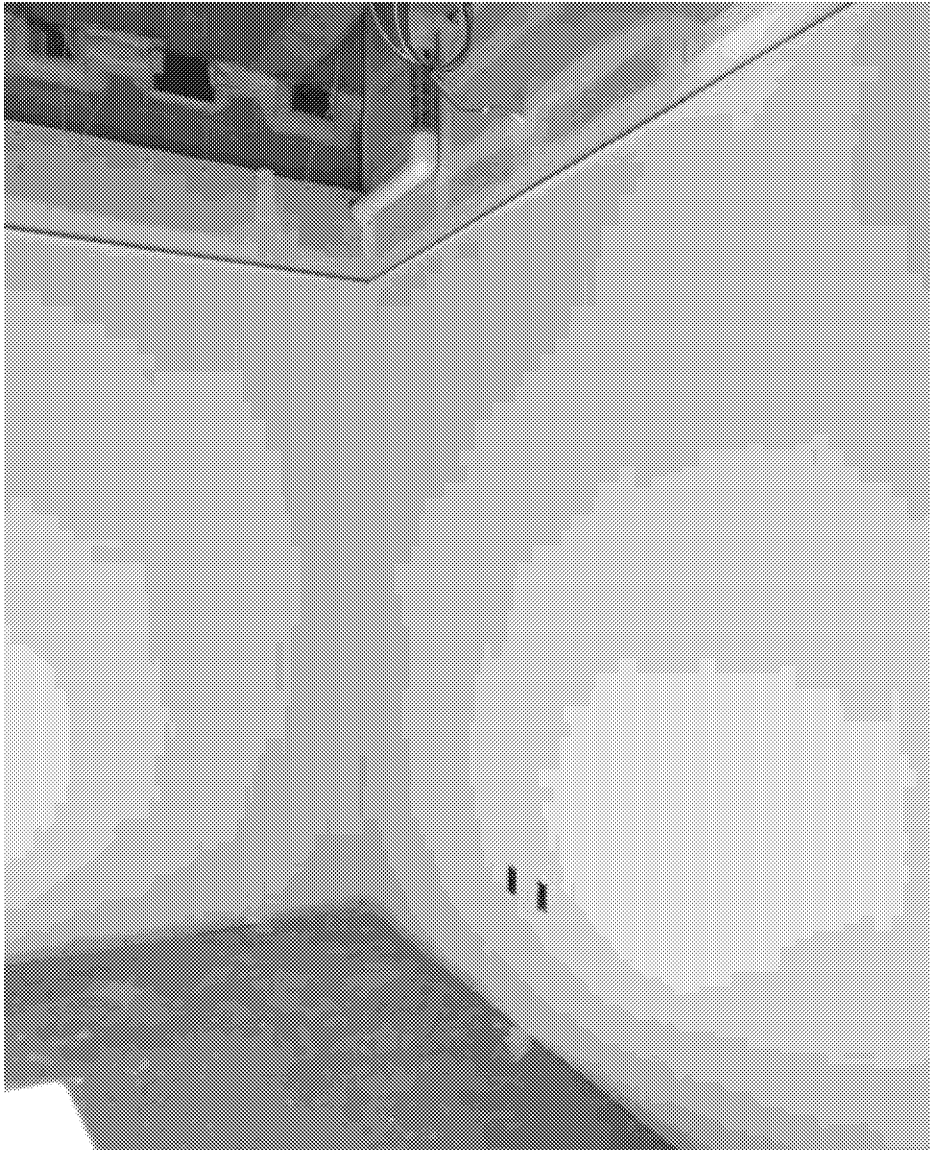

This is the new ceiling grid being installed in office 3102.

## Weekly Construction Report

March 23, 2018



This is the new lights and grid just outside the library.

## Weekly Construction Report

March 23, 2018



This is more of the new ceiling grid.

## Weekly Construction Report

March 23, 2018



These are the new linear diffusers at the outside windows.



## Weekly Construction Report

March 23, 2018



This is the pipe cutter and threading machine for the sprinklers.



## Weekly Construction Report

March 23, 2018



This is the new grid and light at office 3125.

## Weekly Construction Report

March 23, 2018



This is the new raised floor outside Mechanical room 316.

## Weekly Construction Report

March 23, 2018



More of the raised floor.

## Weekly Construction Report


March 23, 2018



This is the corridor outside office 3102 with new grid and lights.

## Weekly Construction Report

March 23, 2018

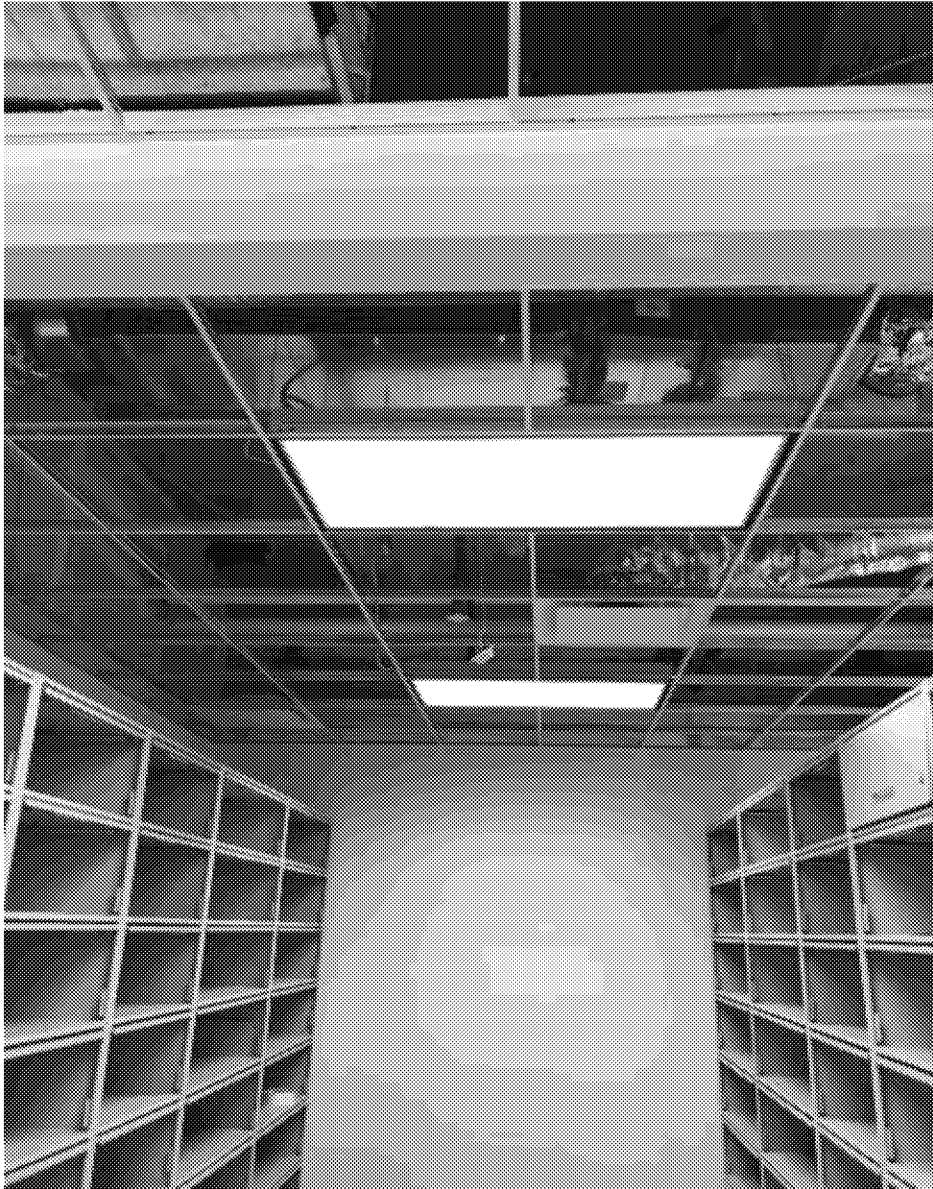

This is the new grid and lights above the high density shelving.

## Weekly Construction Report

March 23, 2018



This is the new grid and lights at work area 3315.
