APPLICATION FOR PAYMENT

Project: NASA Measurement Systems Lab
Contract For: General Services Admin. PDN: EN-GS-03-P-17-DX-

C-0005

Remit To: W.M. Jordan Company Inc. 11010 Jefferson Ave Newport News VA 23601

General Services Admin. PDN: EN-GS-03-

Via Architect: AECOM Application No.: 16123-48 Period To: 01/31/21

Customer Contract #:

Contract Date: 11/29/16 Customer No.: 202144 Job No.: 16123

	OWNER
	ARCHITECT
	CONTRACTOR

Distribution to:

100 S Independence Mall West Philadelphia PA 19108

P-17-DX-C-0005


CONTRACTOR'S APPLICATION FOR PAYMENT


Application is made for Payment, as shown below, with the Contract. Schedule of Values is attached.		
1. ORIGINAL CONTRACT SUM	\$	95,598,160.00
2. NET CHANGE BY CHANGE ORDERS	\$	6,561,148.78
3. CONTRACT SUM TO DATE (line 1 + 2)	\$	102,159,308.78
 TOTAL COMPLETED AND STORED TO DATE (Column G of Schedule of Values) RETAINAGE: 	\$	102,021,845.19
 a. 0.70443594 % of Completed Work (Column D + E of Schedule of Values) 	·	18,678.54
b. % of Stored Material (Column F of Schedule of Values)	\$	0.00
Total Retainage (Line 5a + 5b or Total of Column I of S	shodulo of Valuas	718,678.54
6. TOTAL EARNED LESS RETAINAGE (Line 4 less Line 5 Total)	-	101,303,166.65
 LESS PREVIOUS CERTIFICATES FOR PAYM (Line 6 from prior Application) 	ENT\$	100,925,246.63
8. CURRENT PAYMENT DUE	\$	377,920.02
9, BALANCE TO FINISH, INCLUDING RETAINAG (Line 3 less Line 6)	åE\$	856,142.13
CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous		
months by Owner	8,248,934.78	-1,687,786.00
Total approved this Month	0.00	0.00
TOTALS	8,248,934.78	-1,687,786.00
NET CHANGES by Change Order	6.561.148.78	


Contract For:


The undersigned Contractor certifies that to the best of the Contractor's knowledge, information and belief, the Work covered by this Application for Payment has been completed in accordance with the Contract Documents, that all amounts have been paid by the Contractor for Work for which previous received from the Owner, County/City of: ARCHITECT'S CERTIFICATE FOR PAYMENT In accordance with the Contract Documents, based on on-site observation and the data comprising this application, the Architect certifies to the Owner that to the best of the Architect's knowledge, Information and Delief, REG. #717995 the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled payment of the AMOUNT CERTIFIED. AMOUNT CERTIFIED.....\$ (Attach explanation if the amount certified differs from the amount applied for in Line 8. Initial all figures on this Application and on the Schedule of Values that are changes to conform to the amount certified.) ARCHITECT: Date: This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to the Contractor named herein. Issuance, payment and acceptance of payment are


without prejudice to any rights of the Owner or Contractor under this Contract

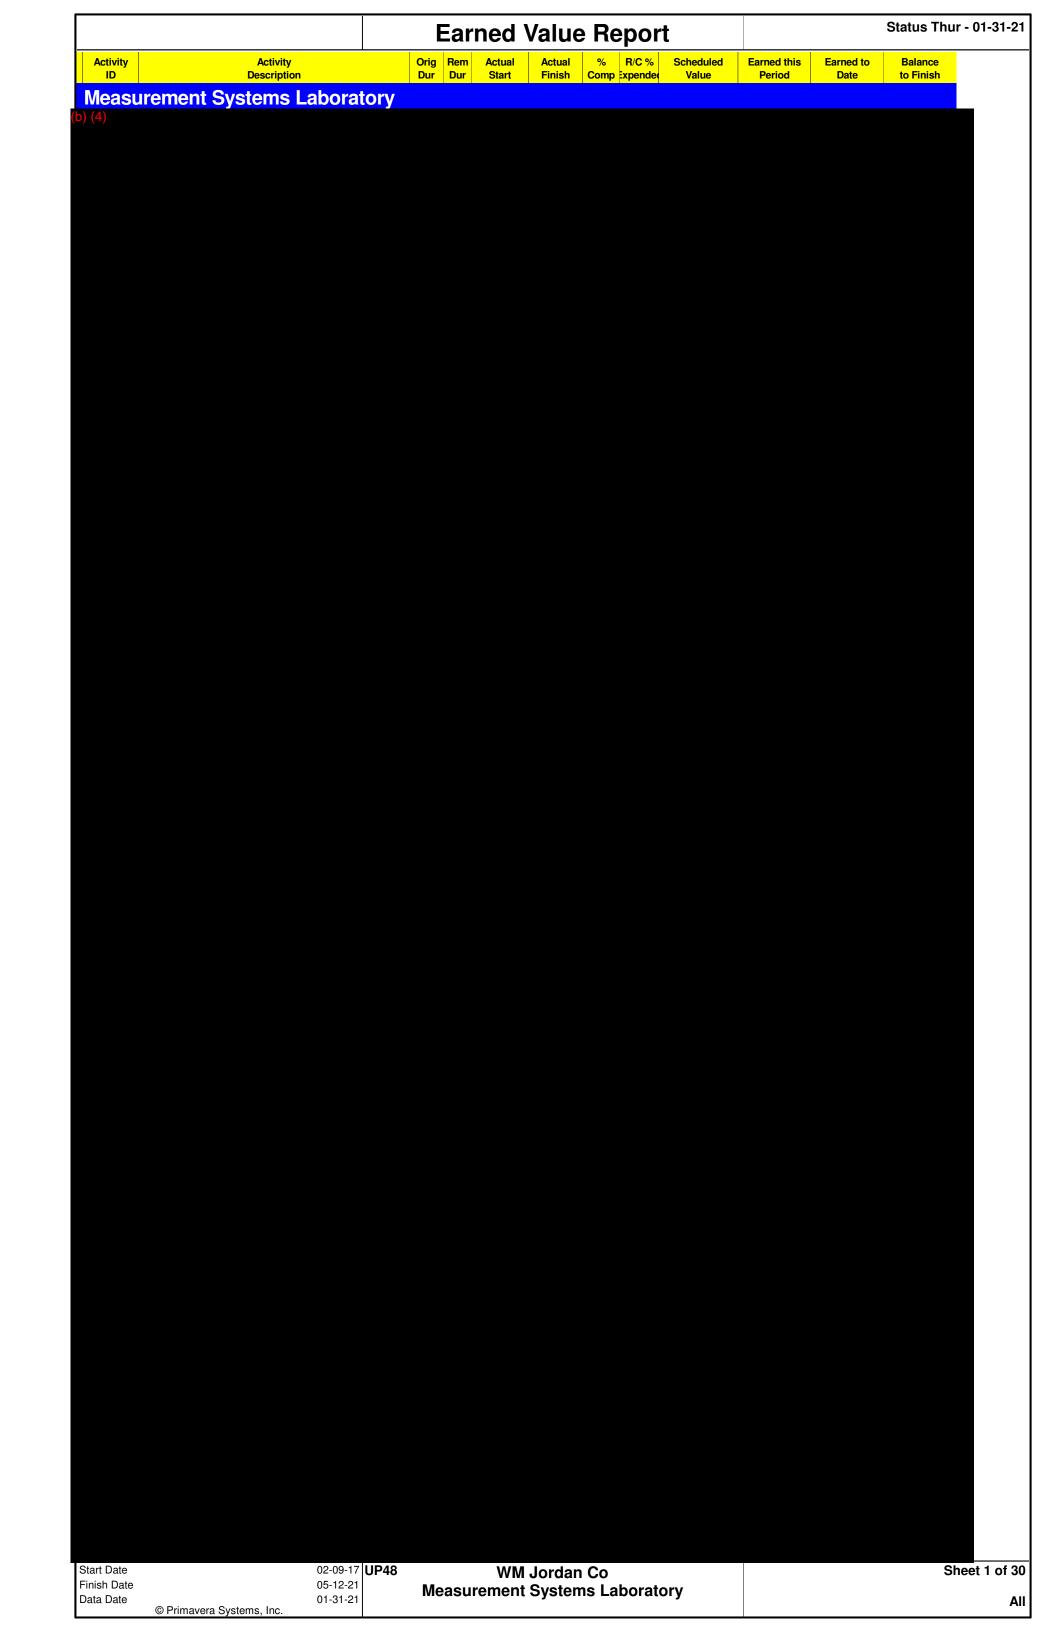


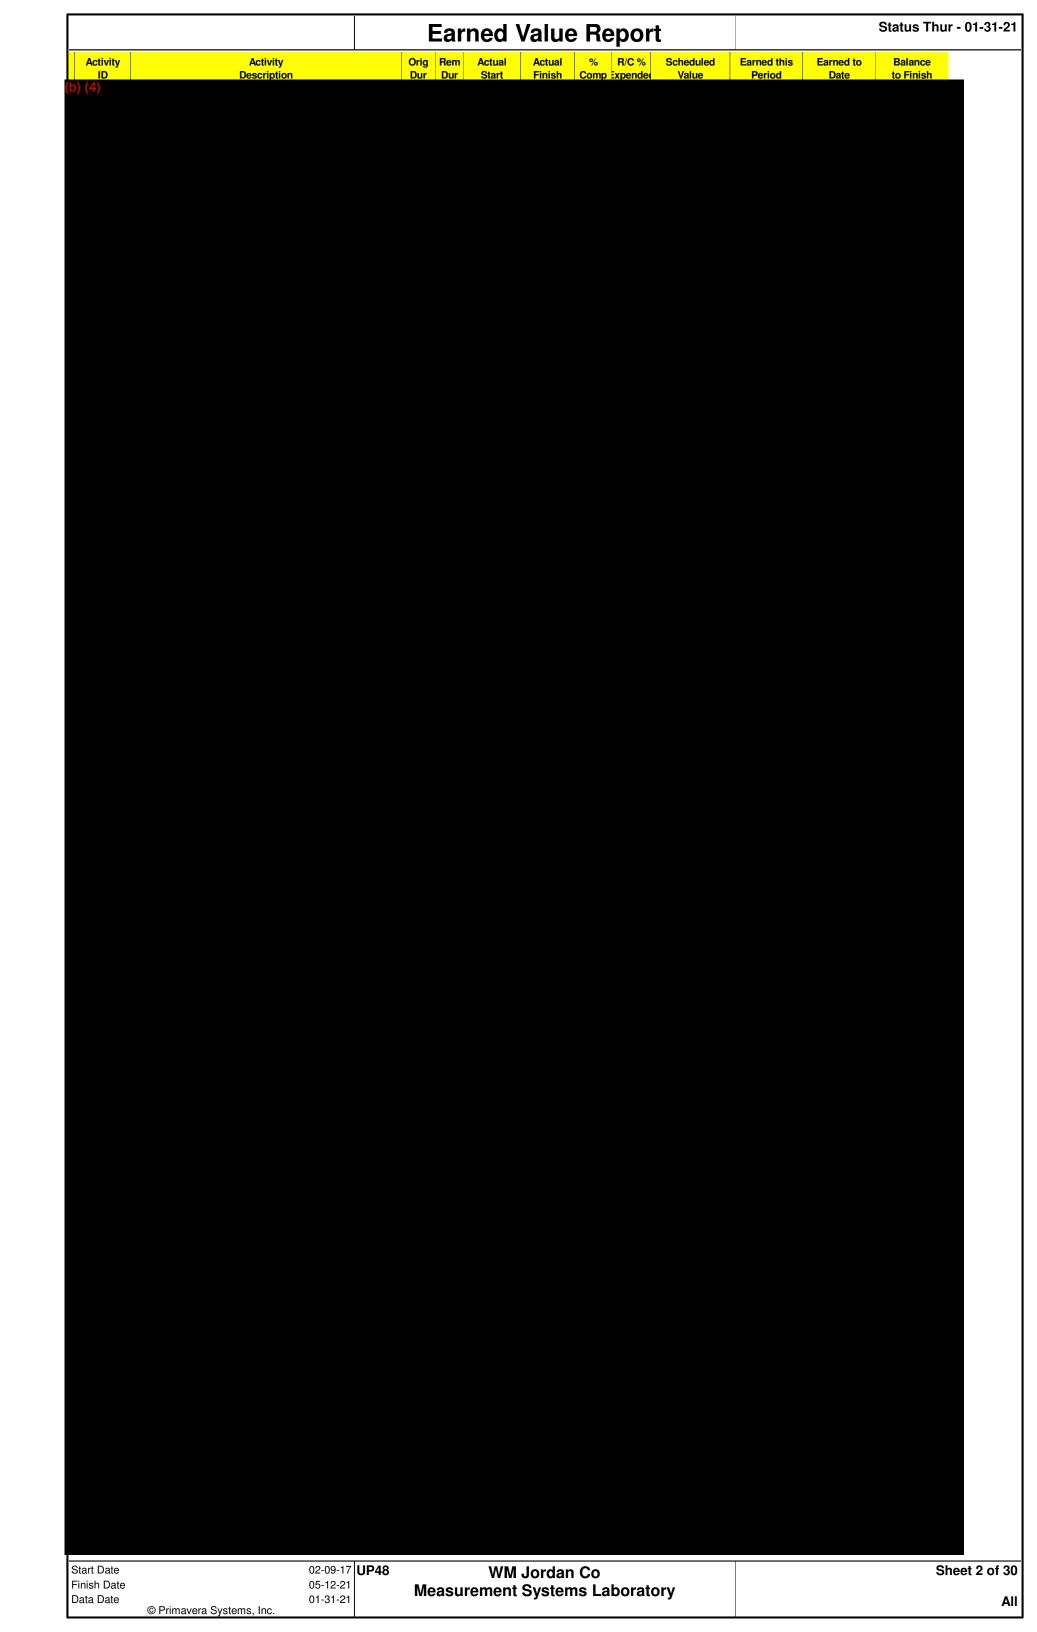


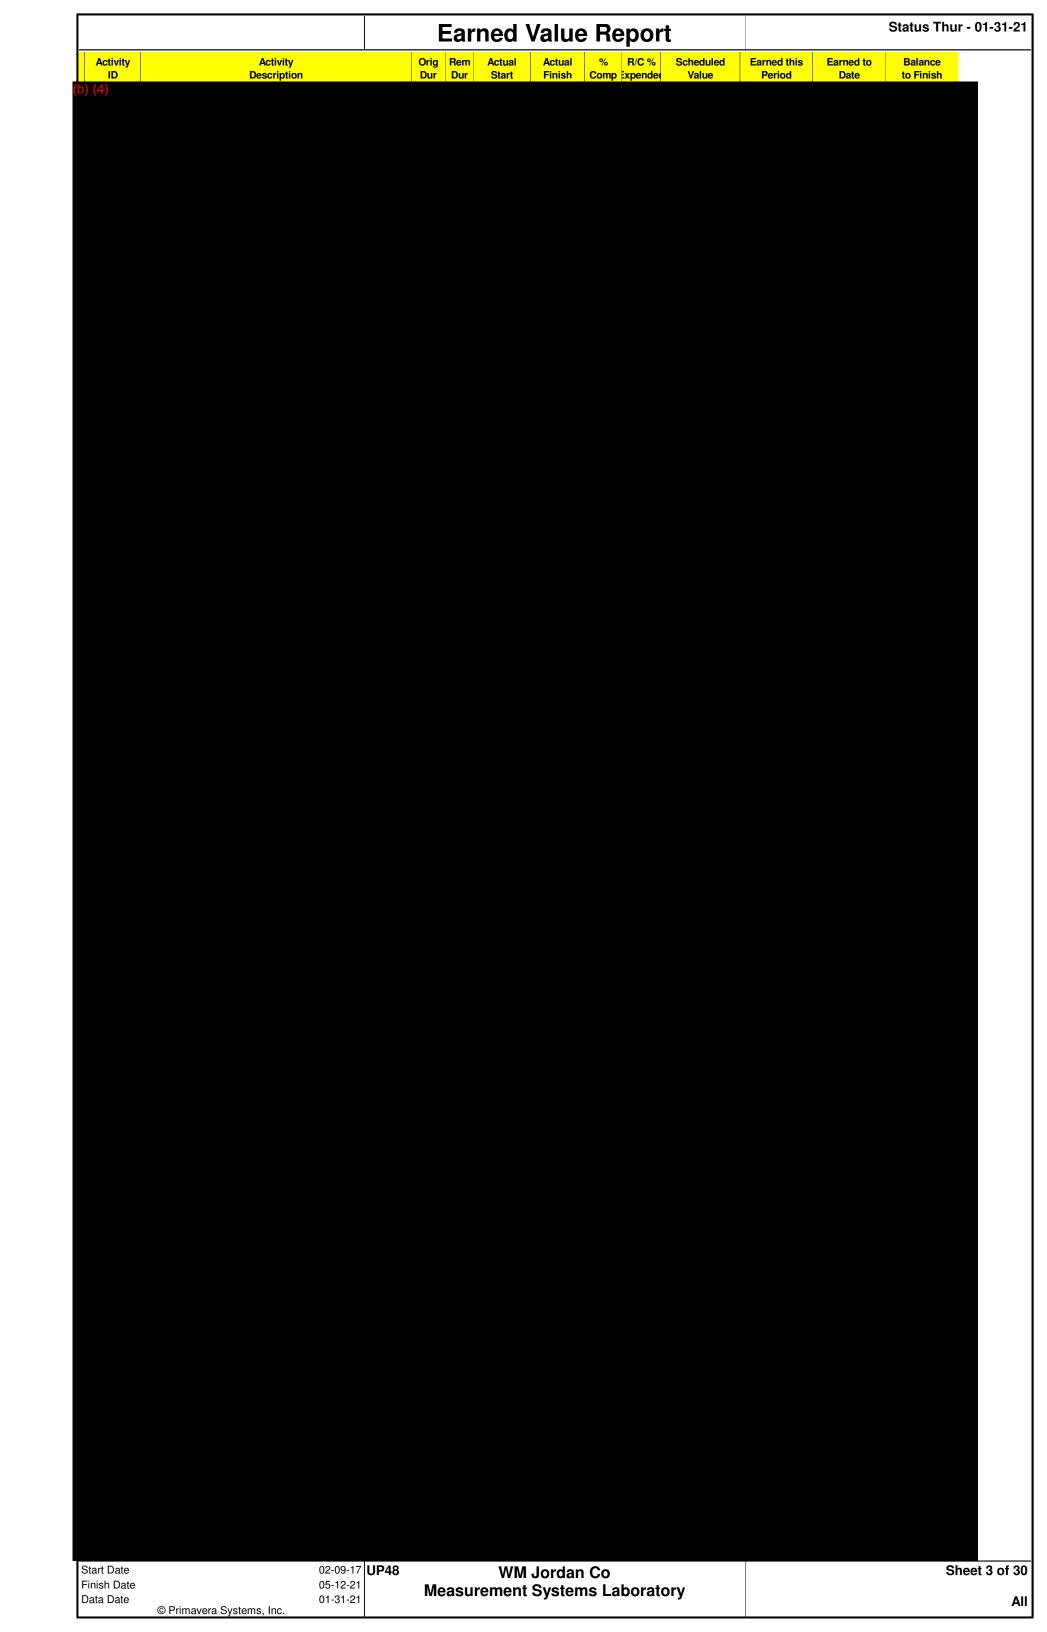


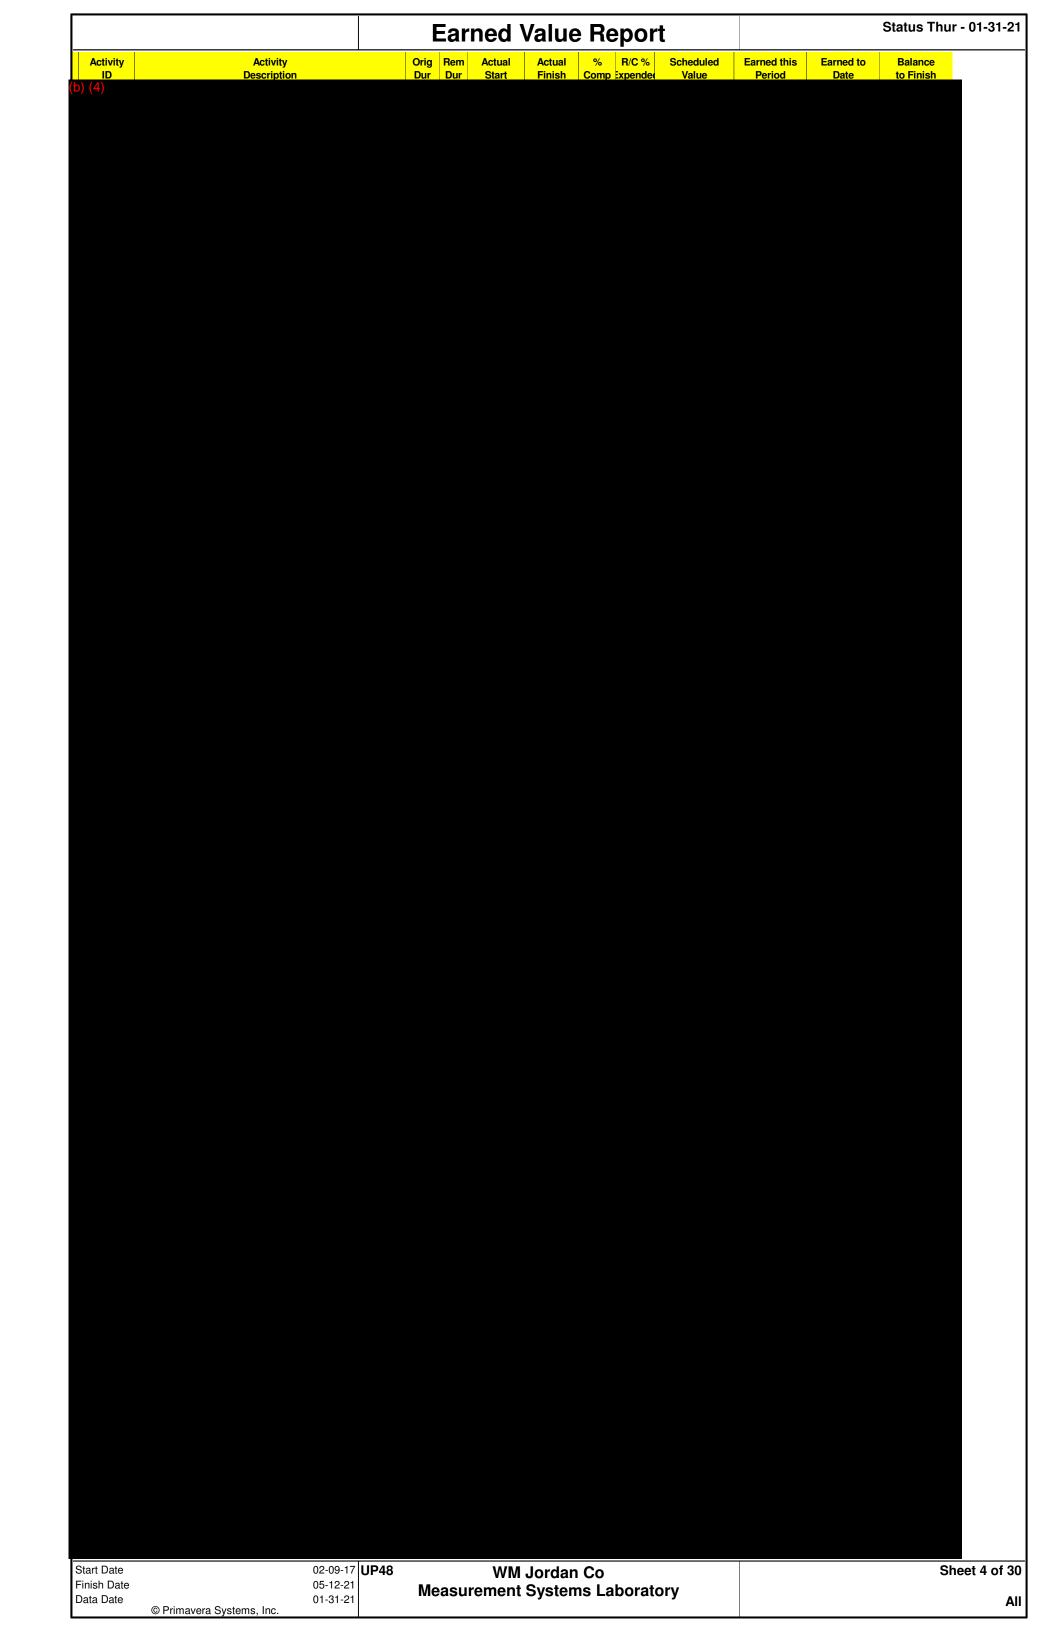


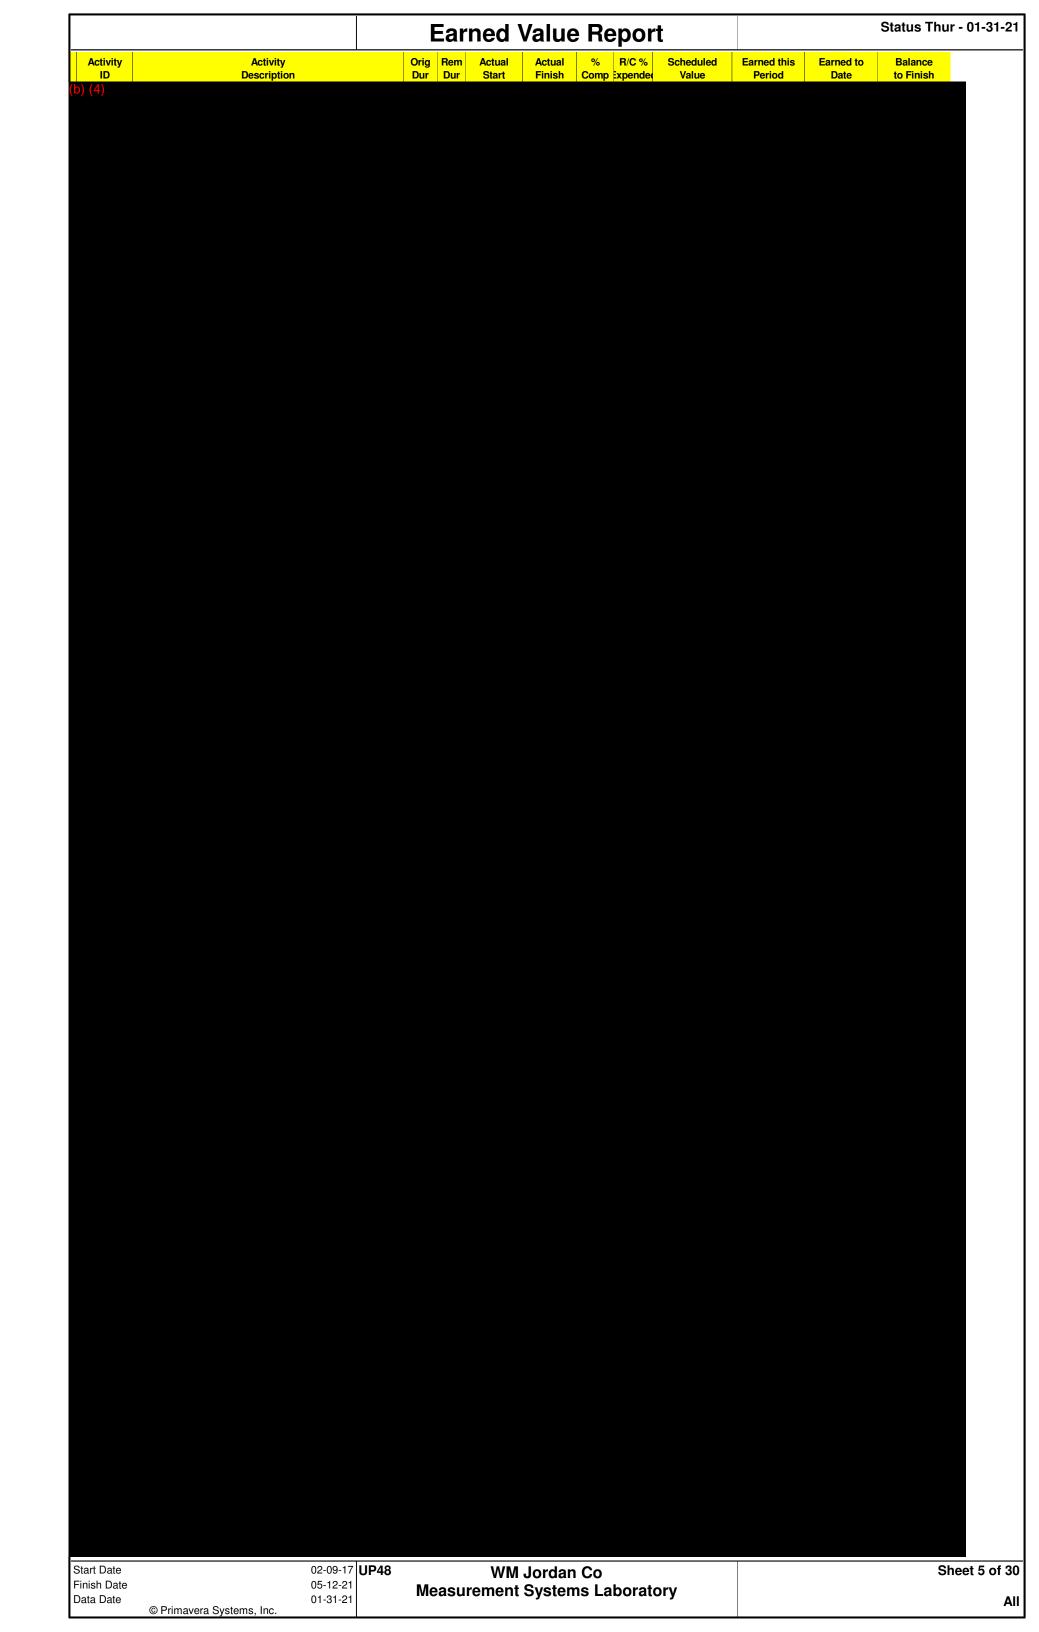


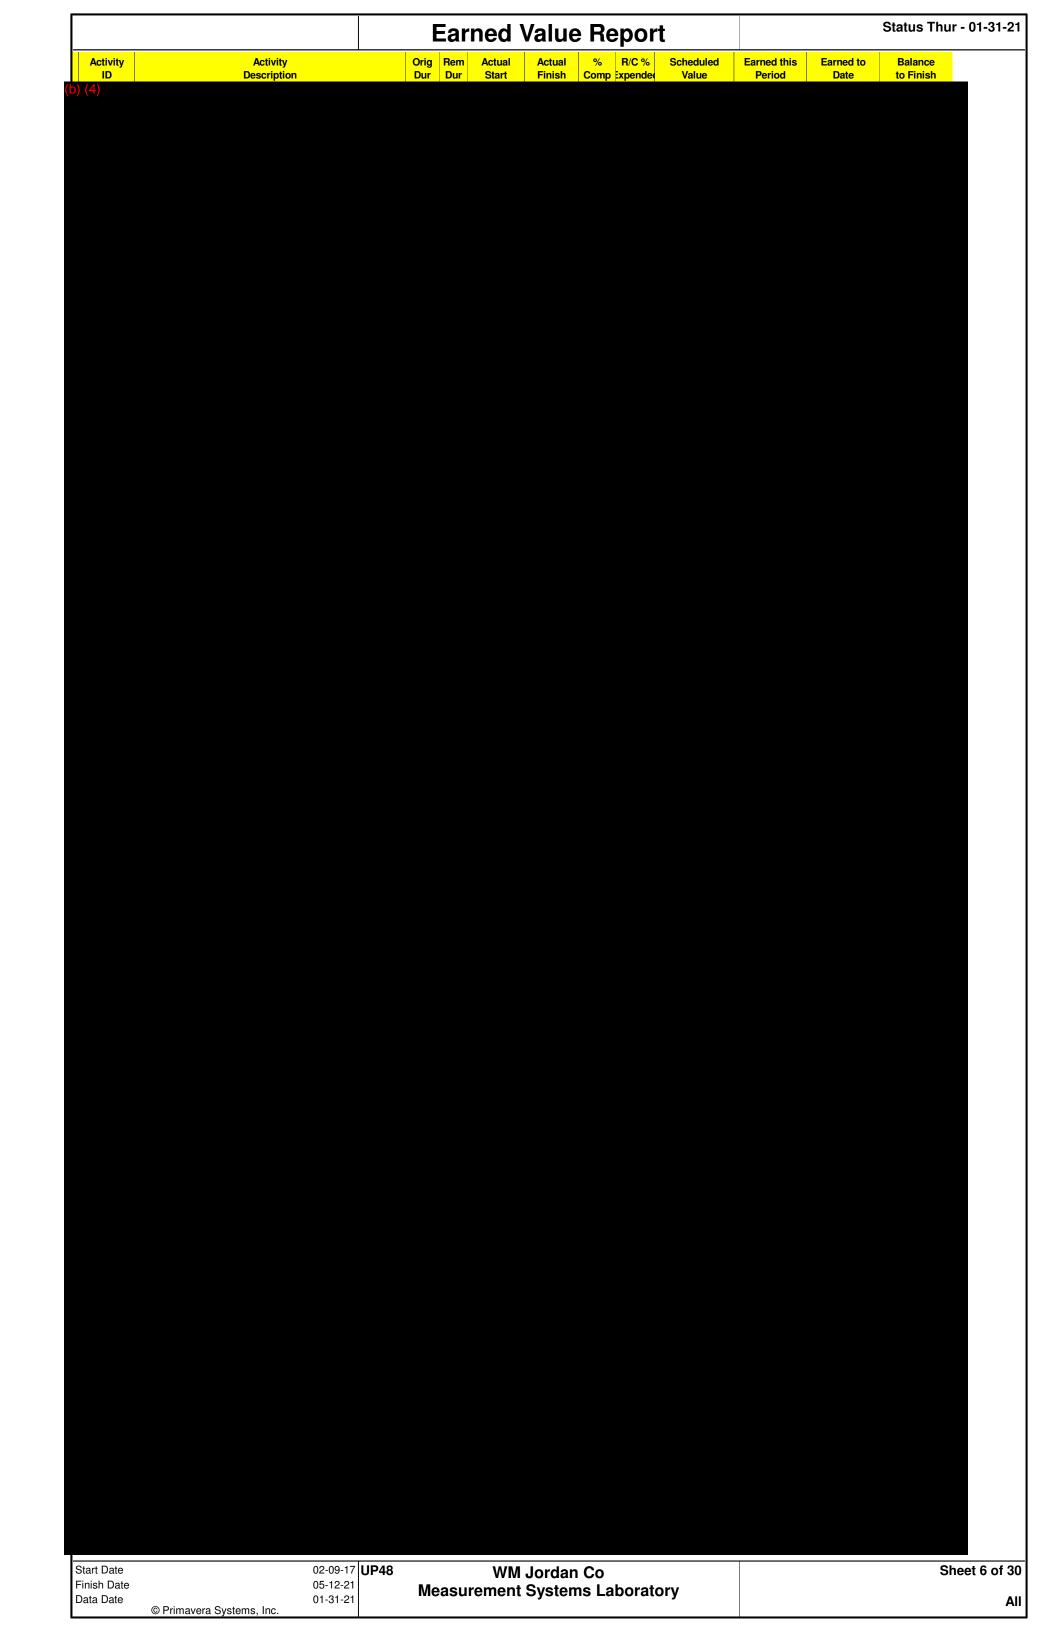


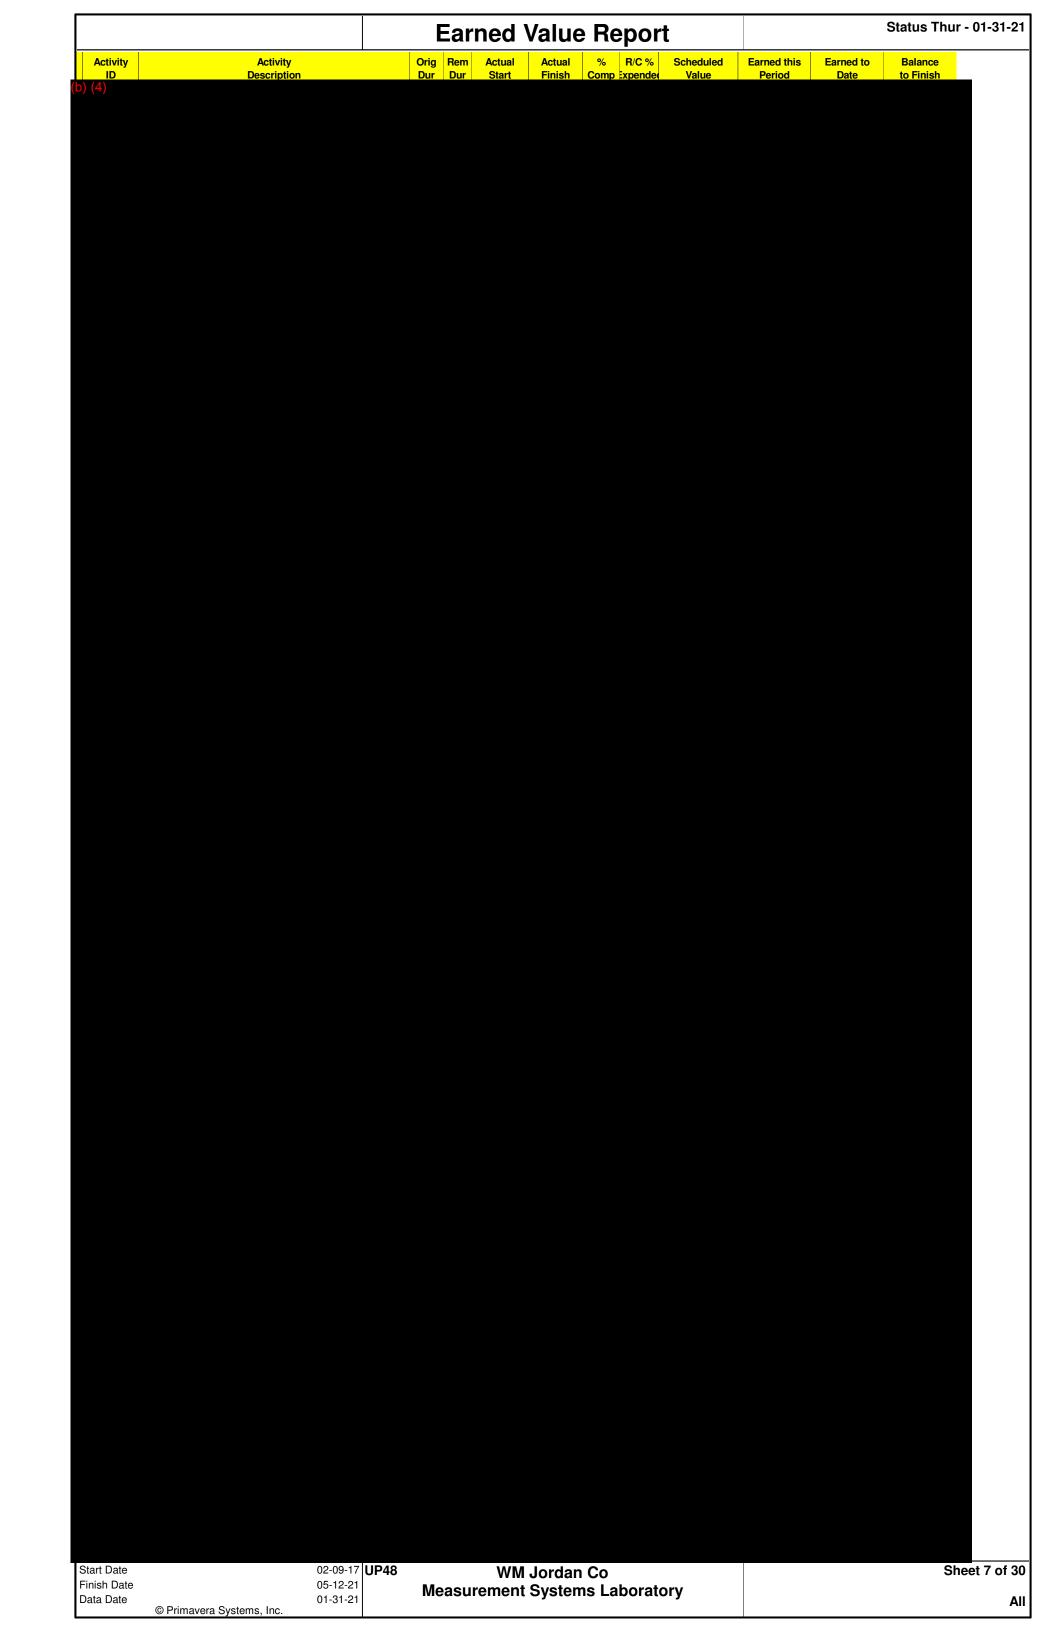


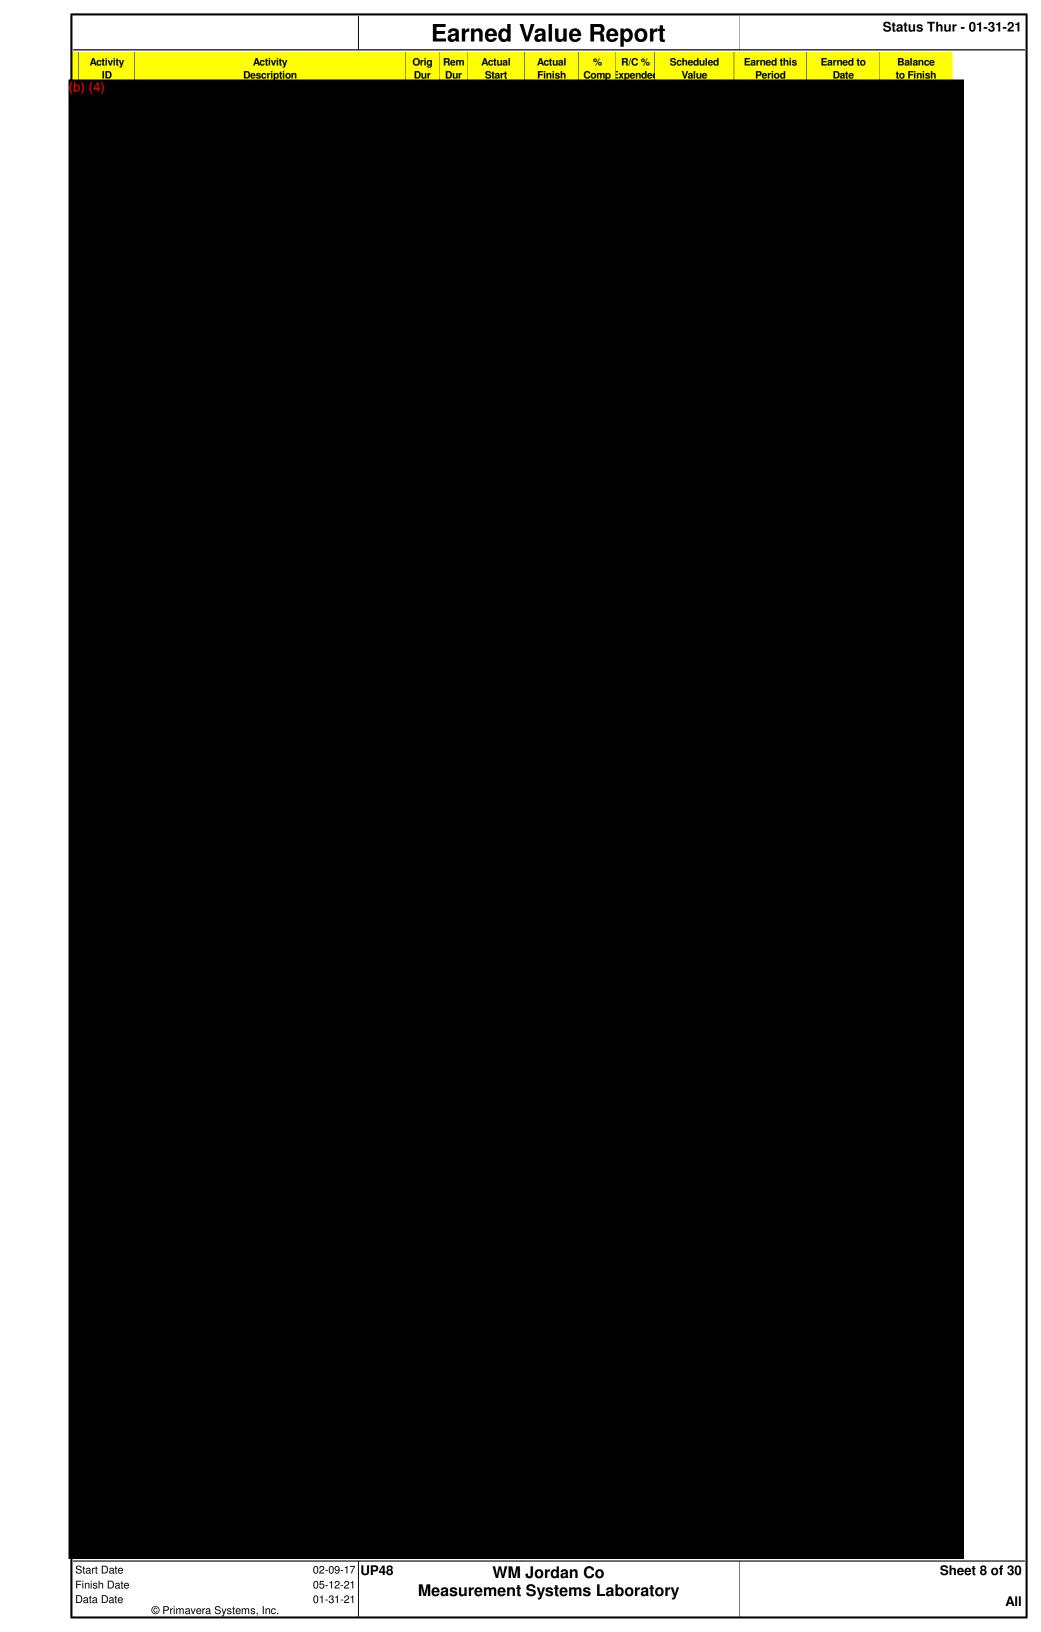





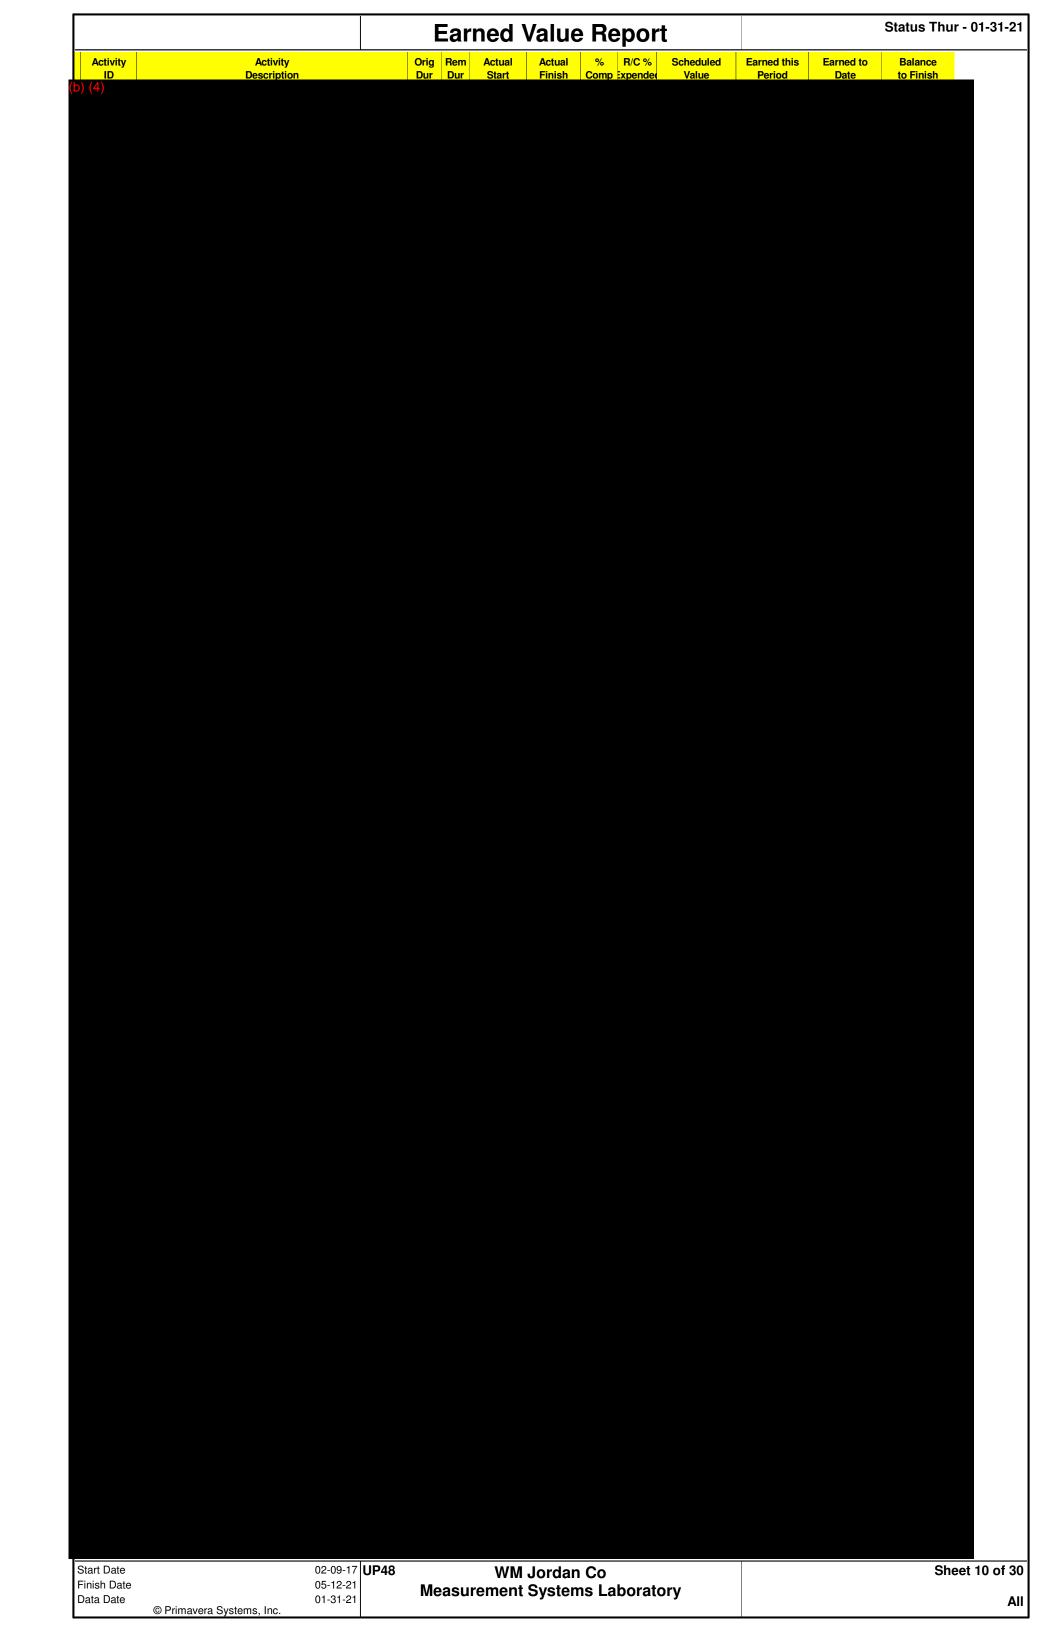


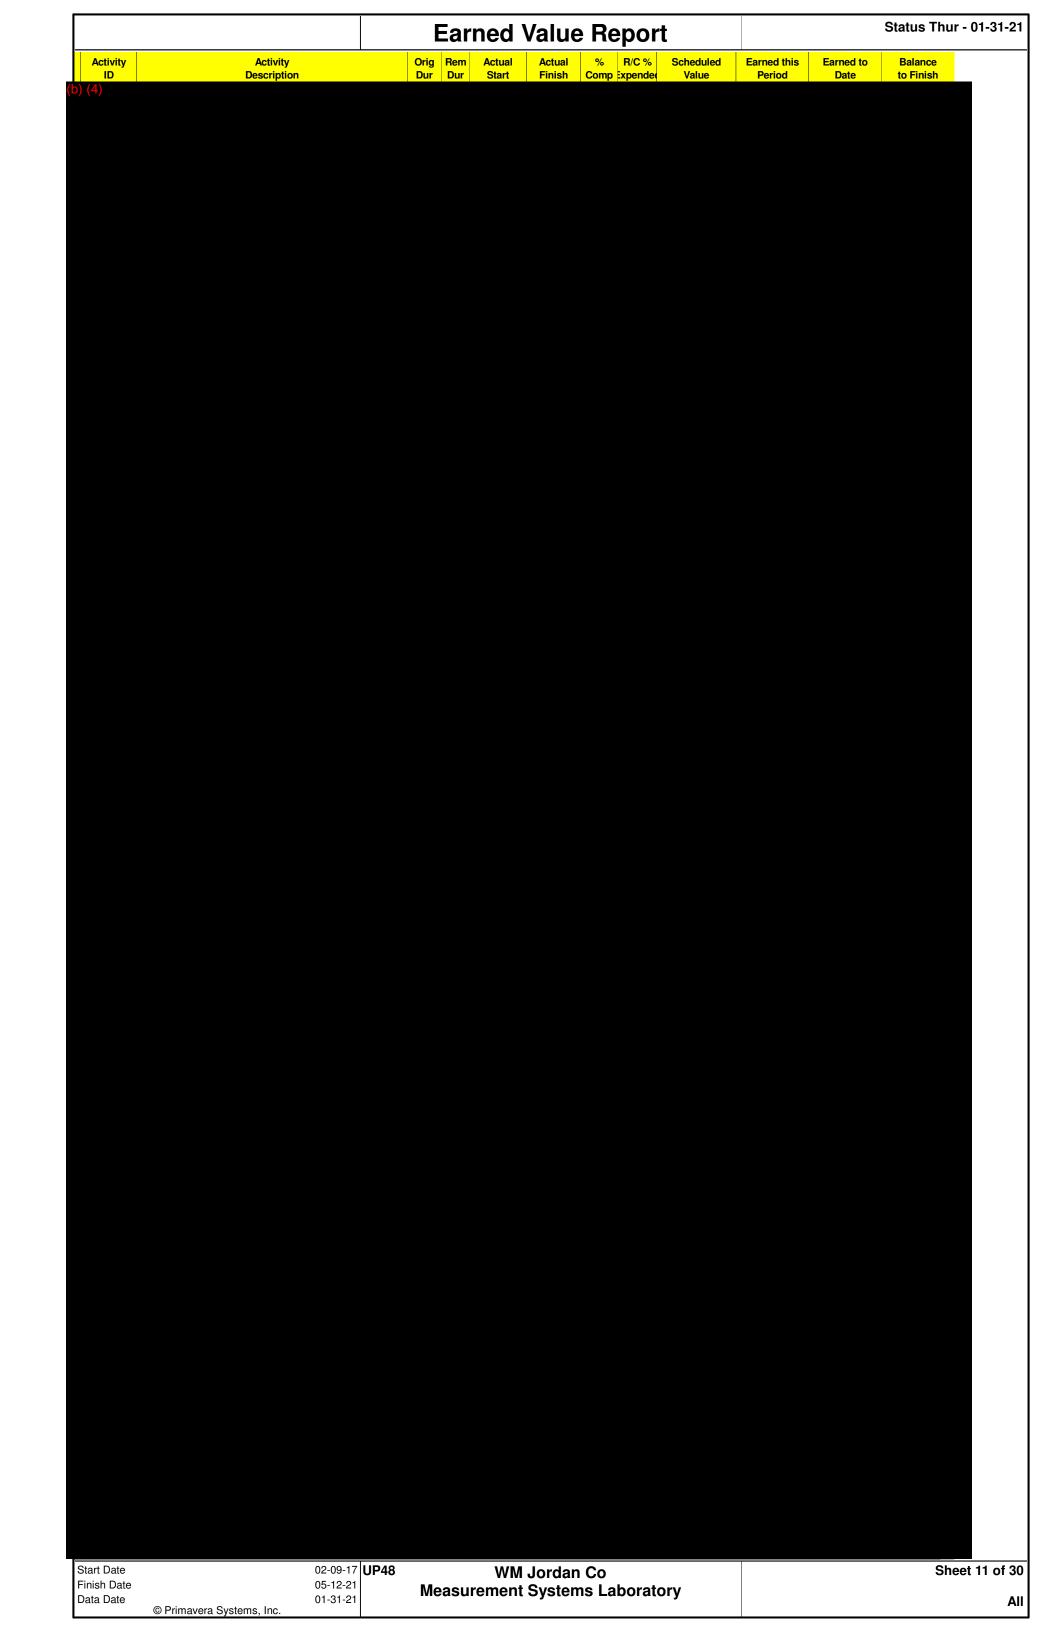





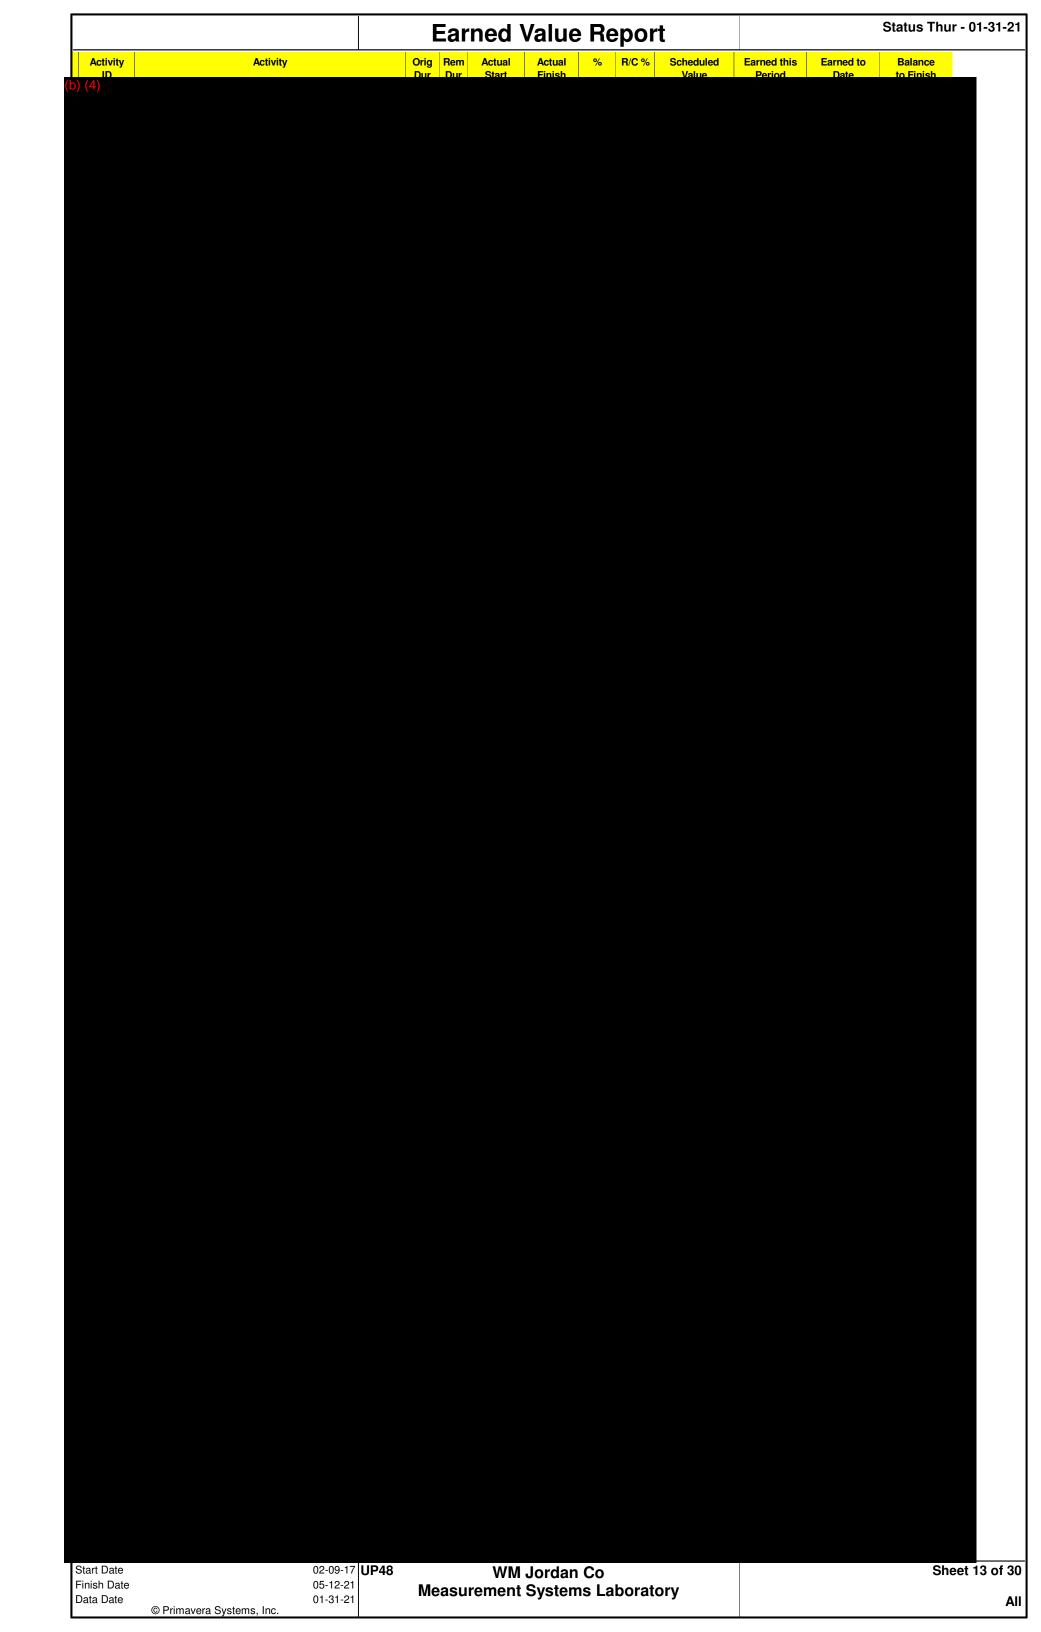


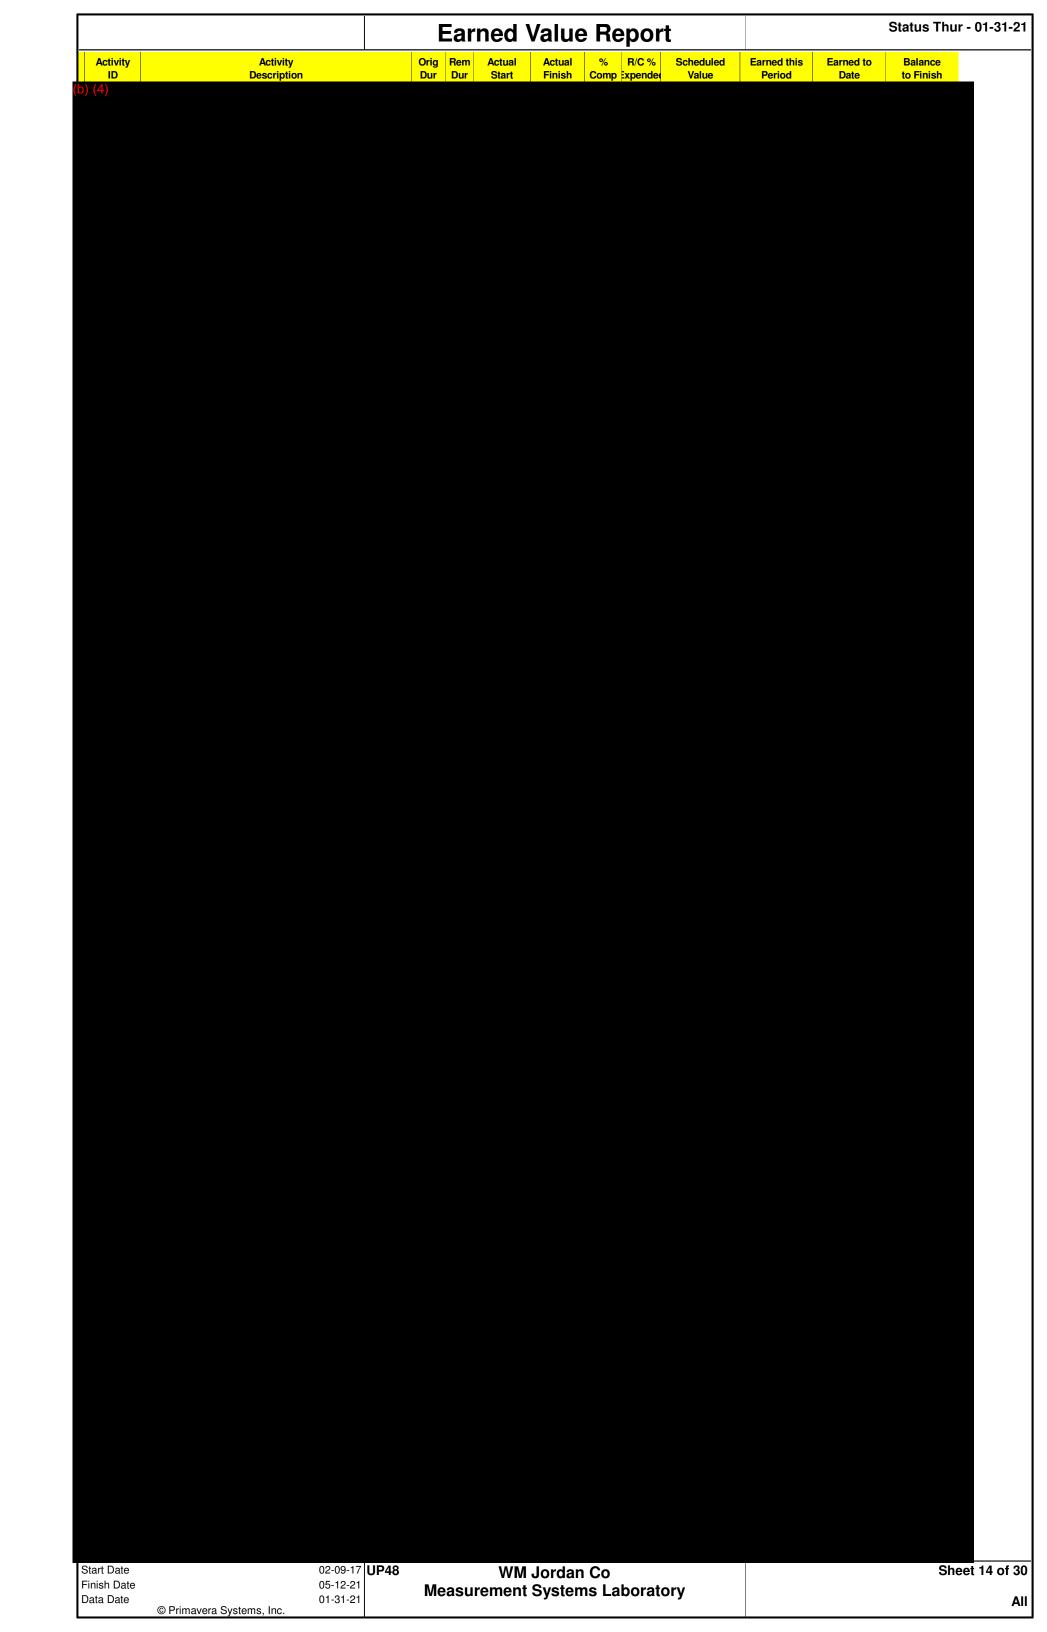


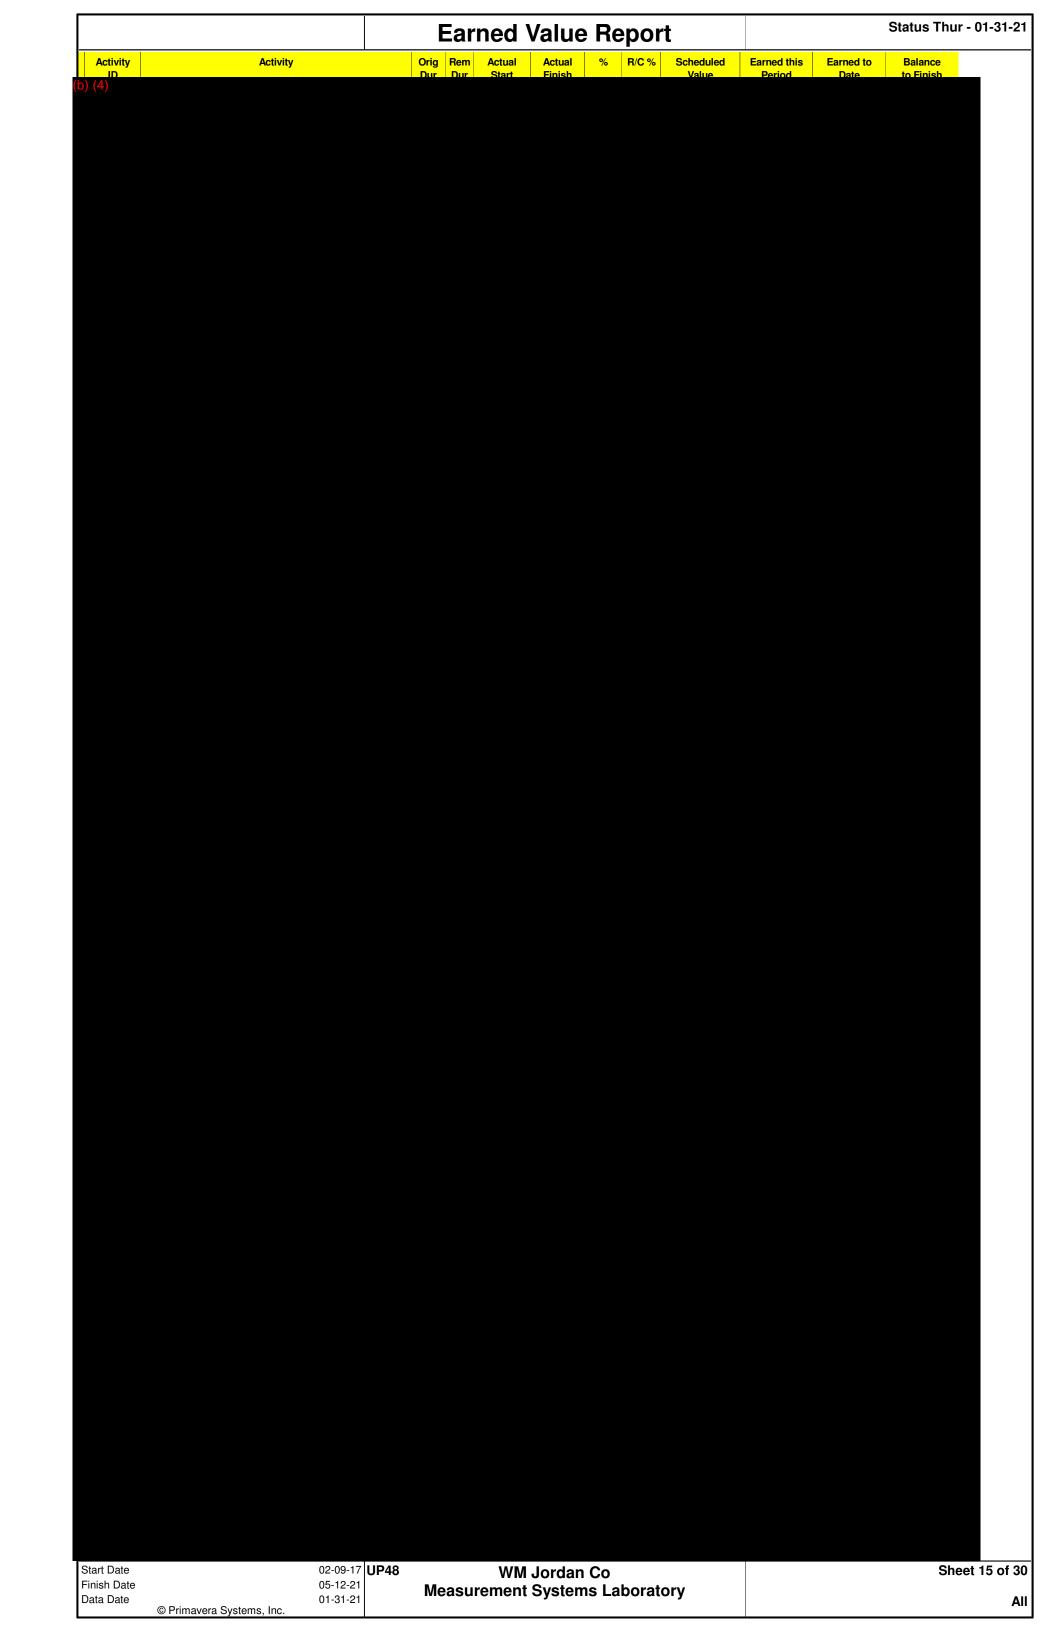


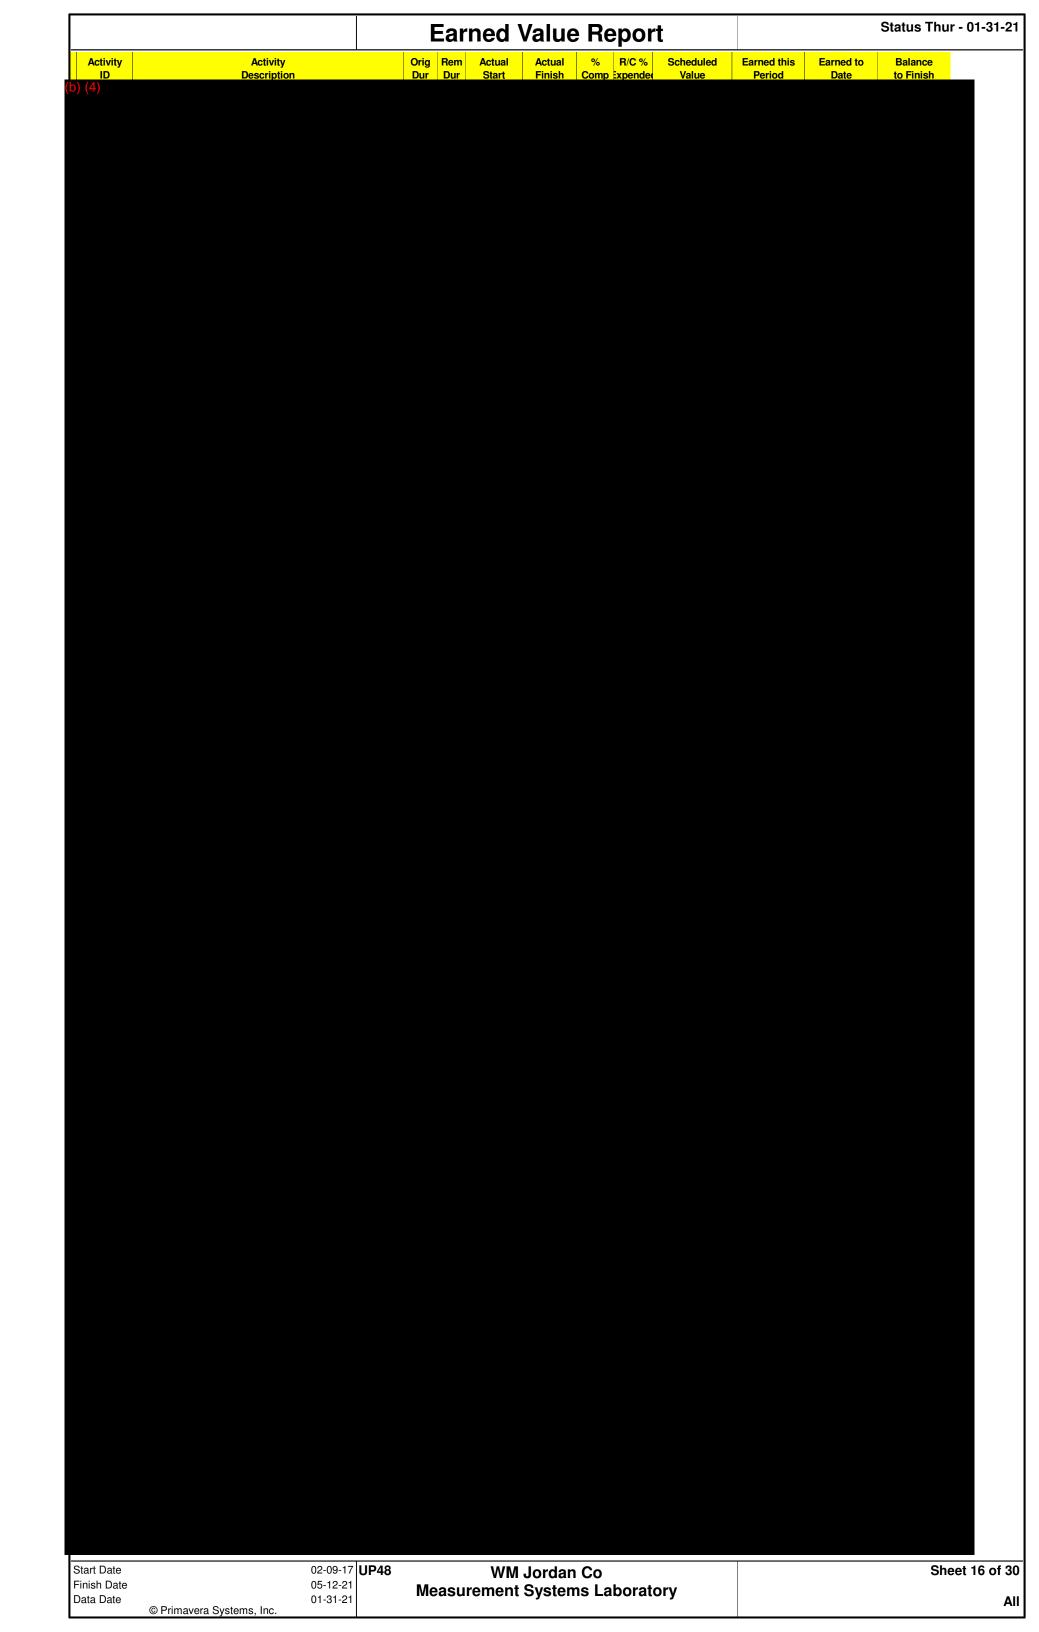





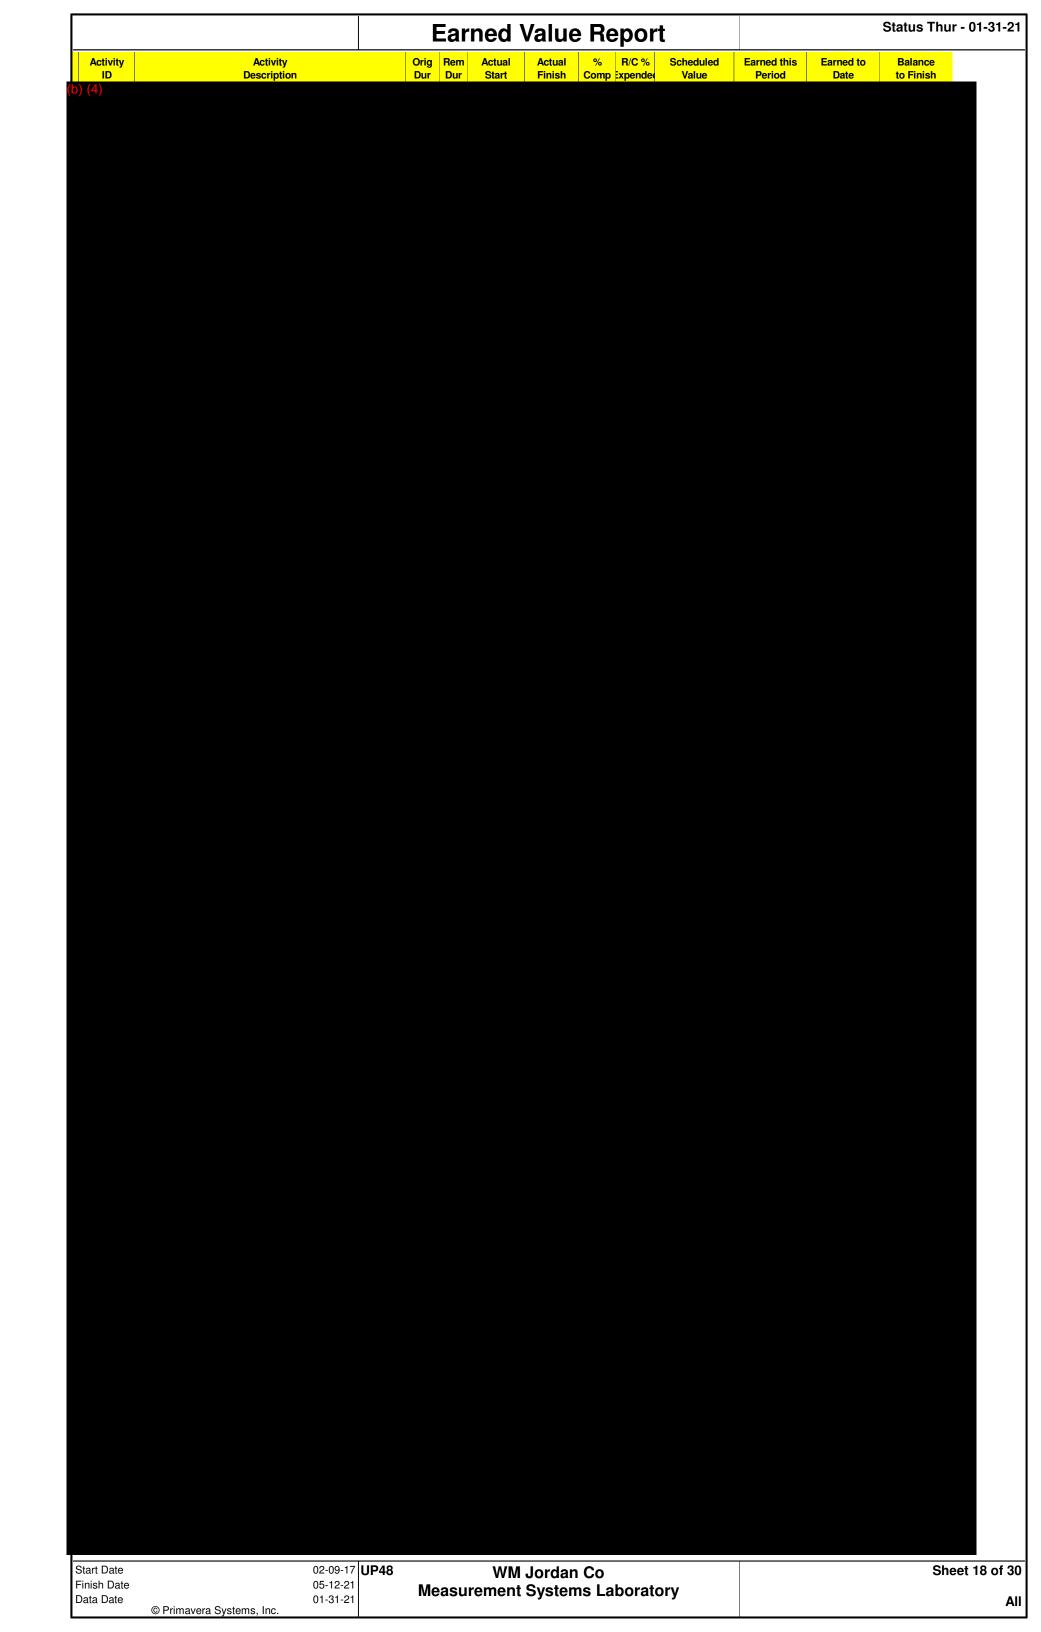


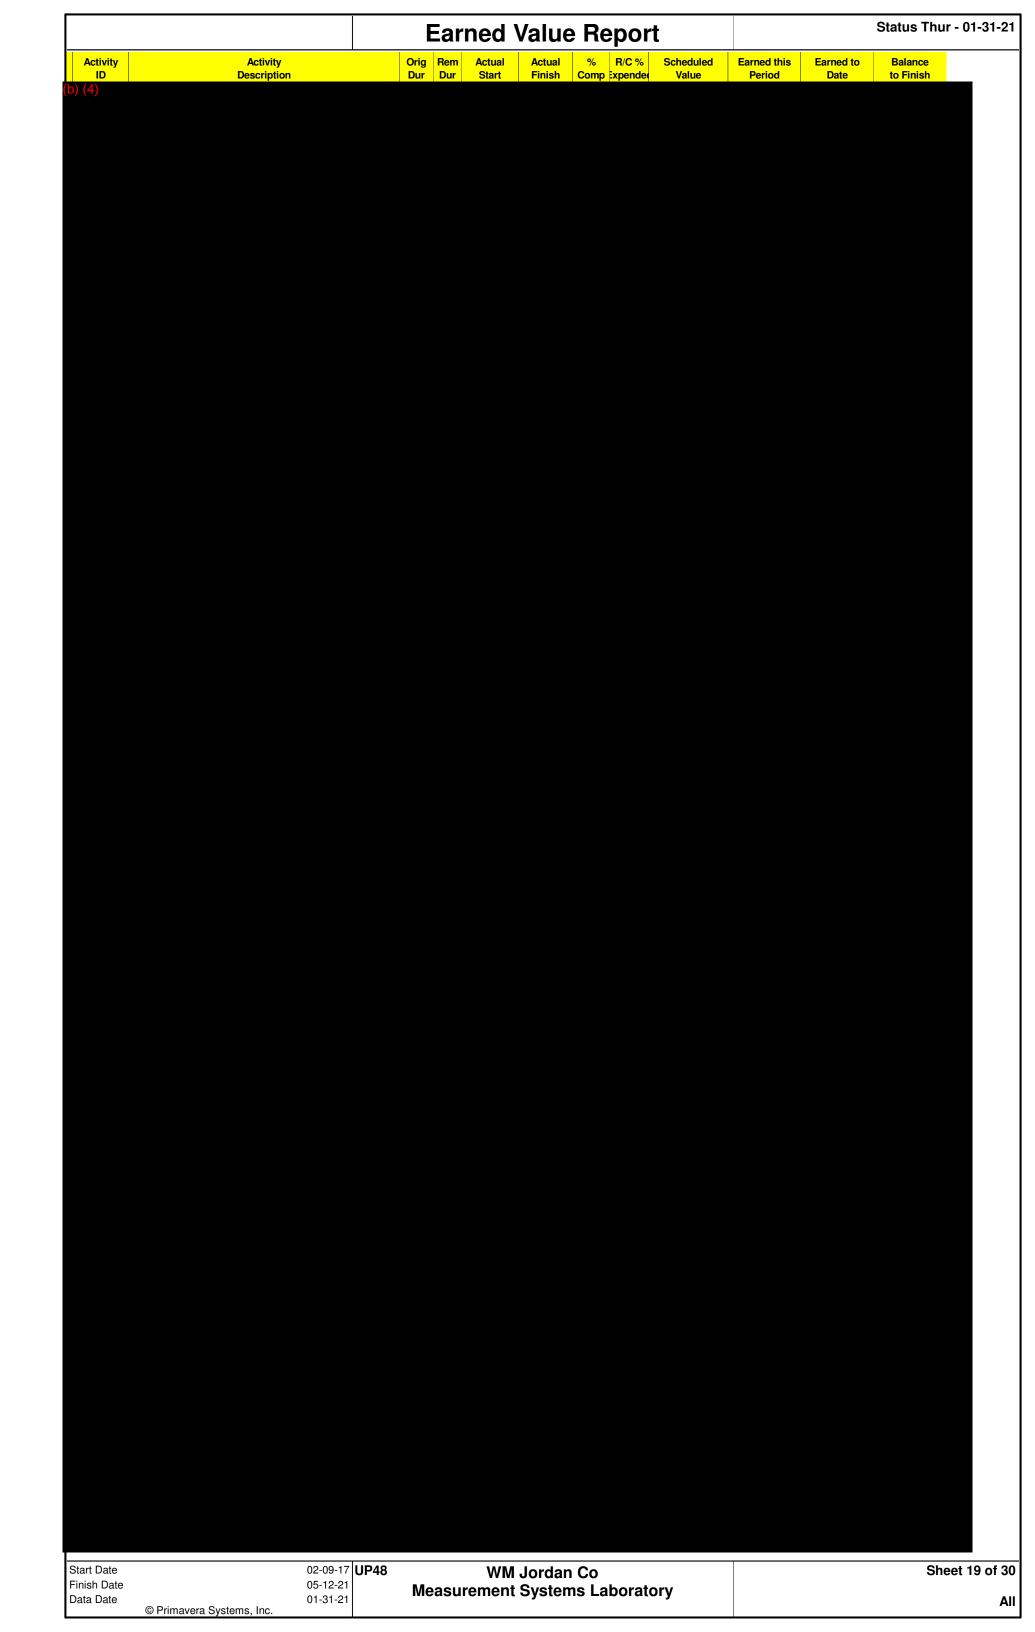


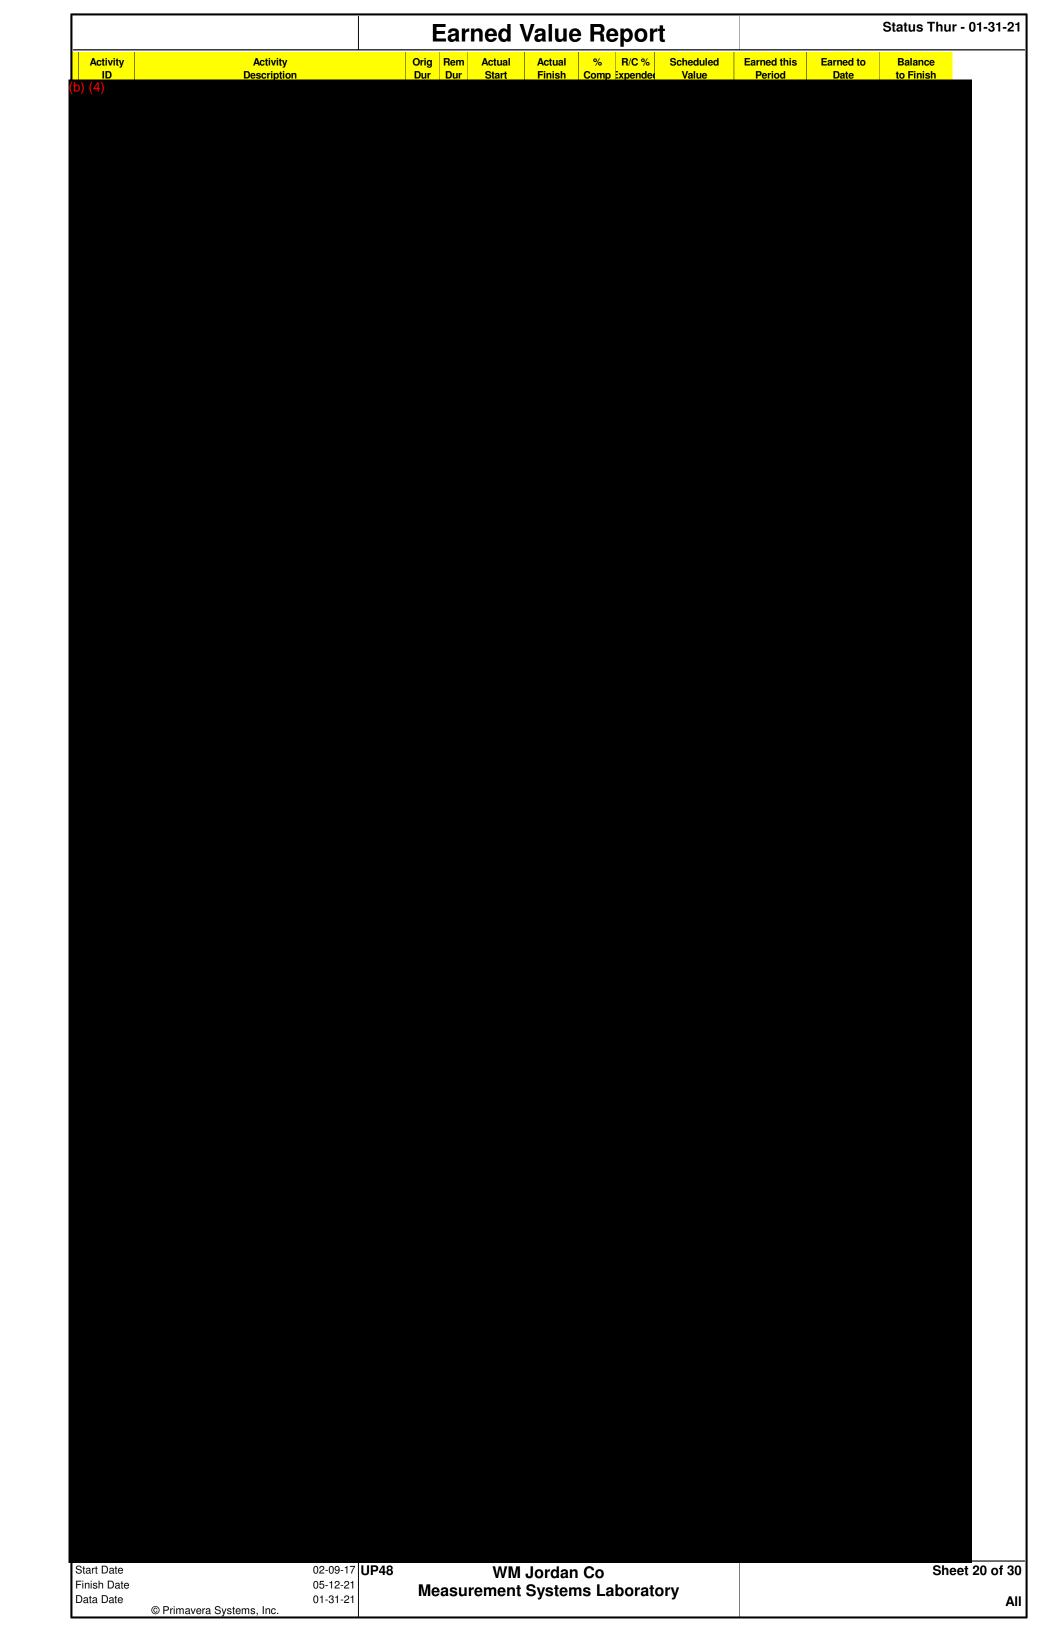


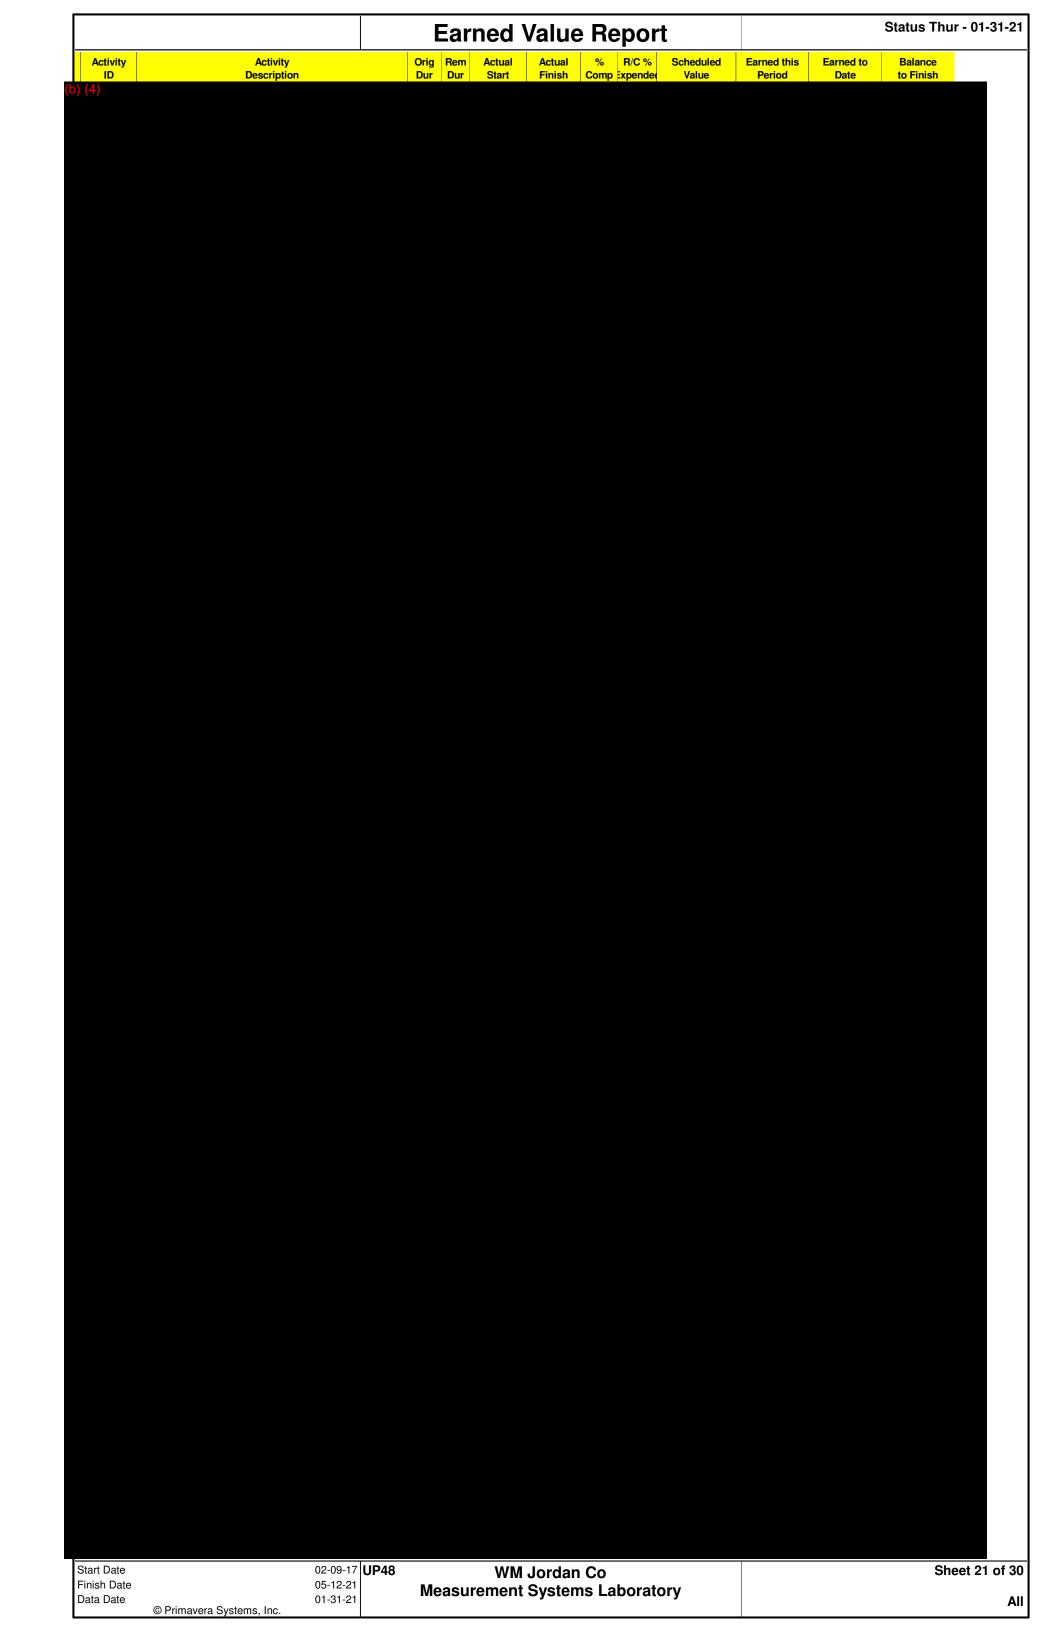


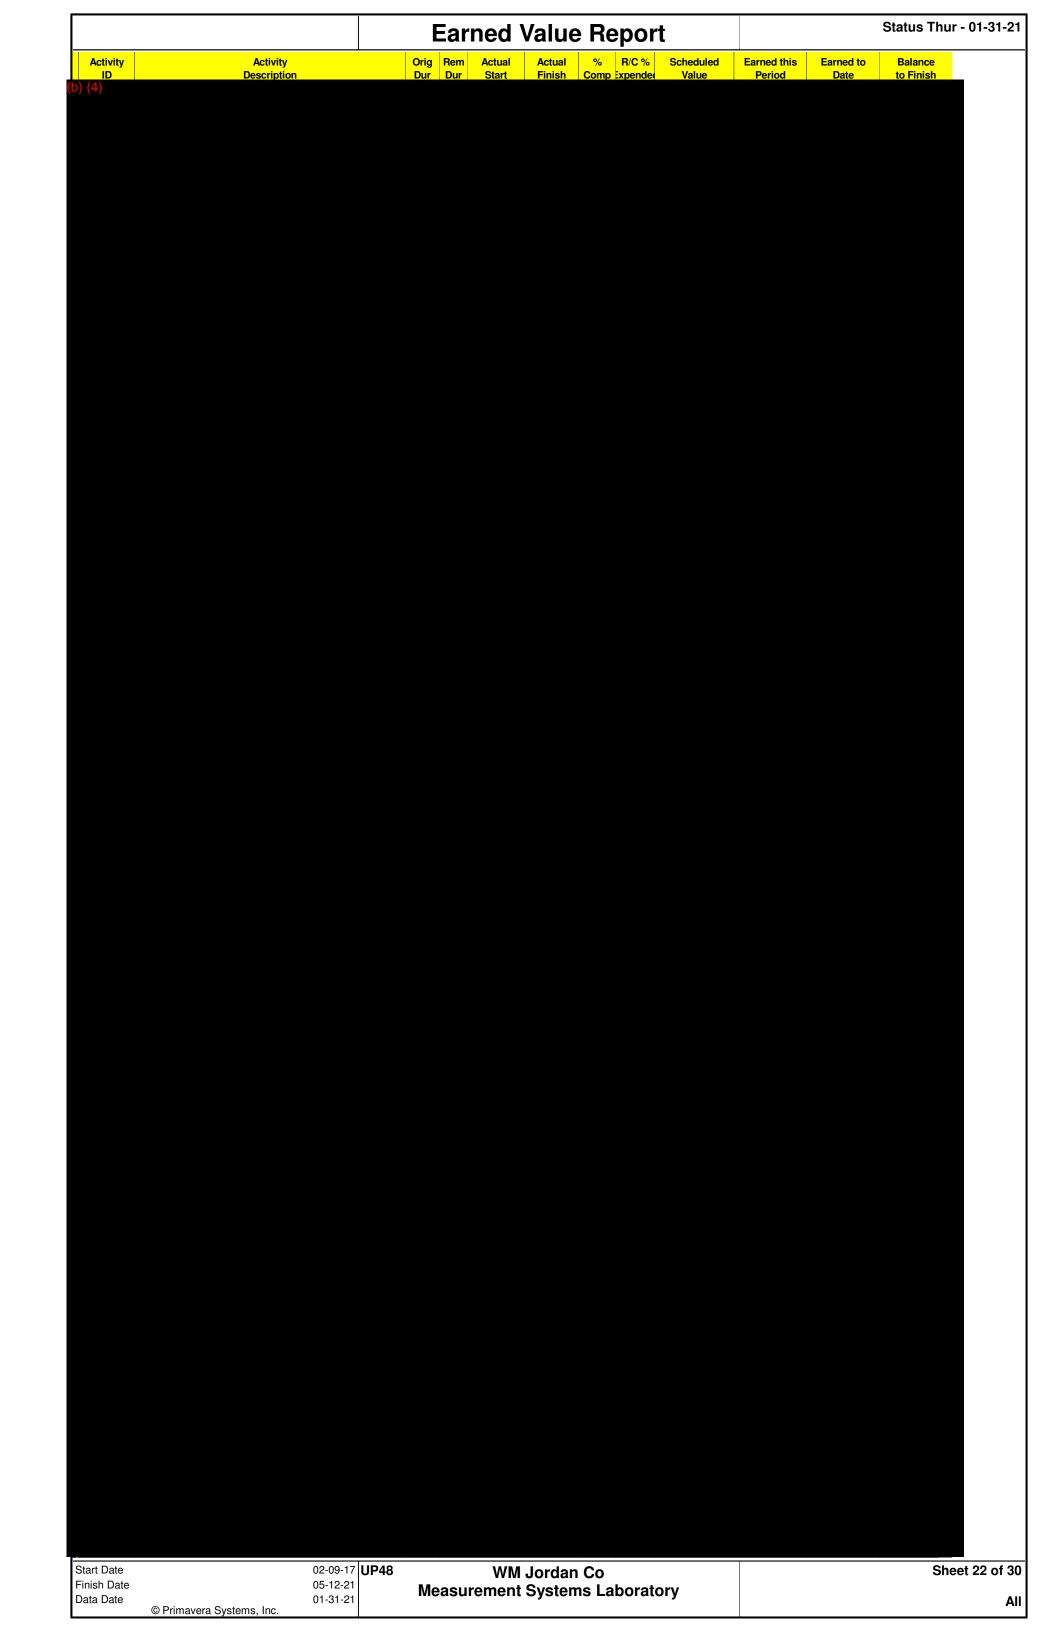


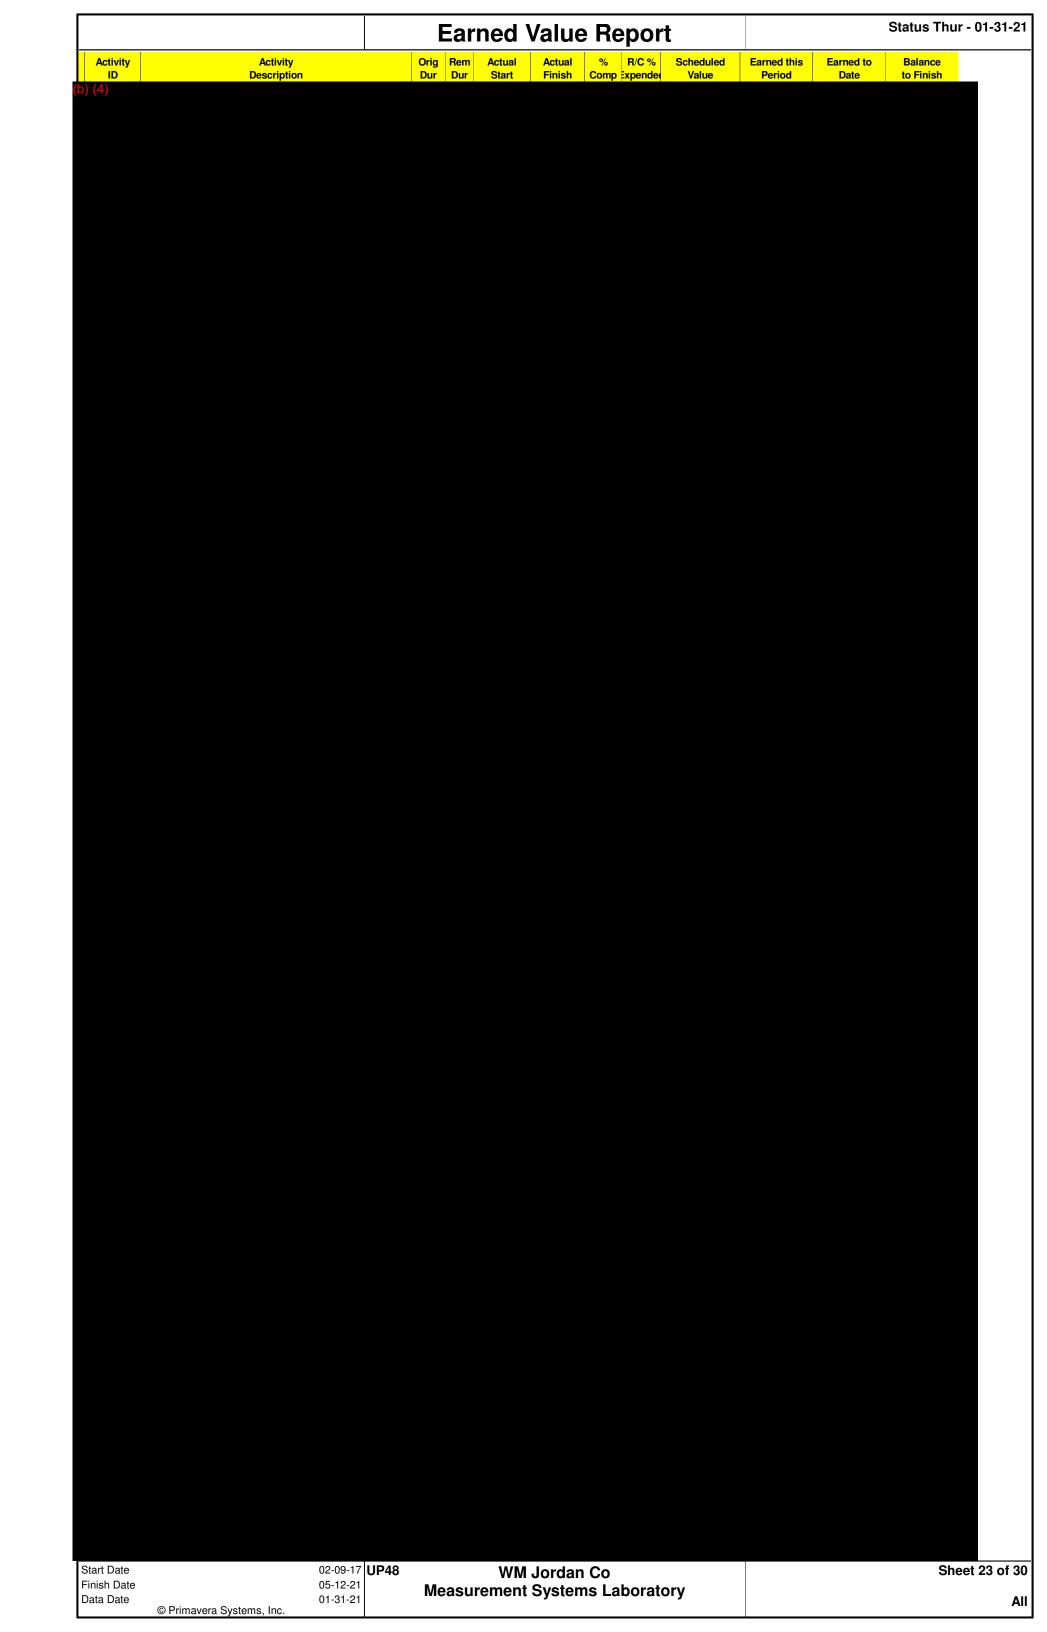





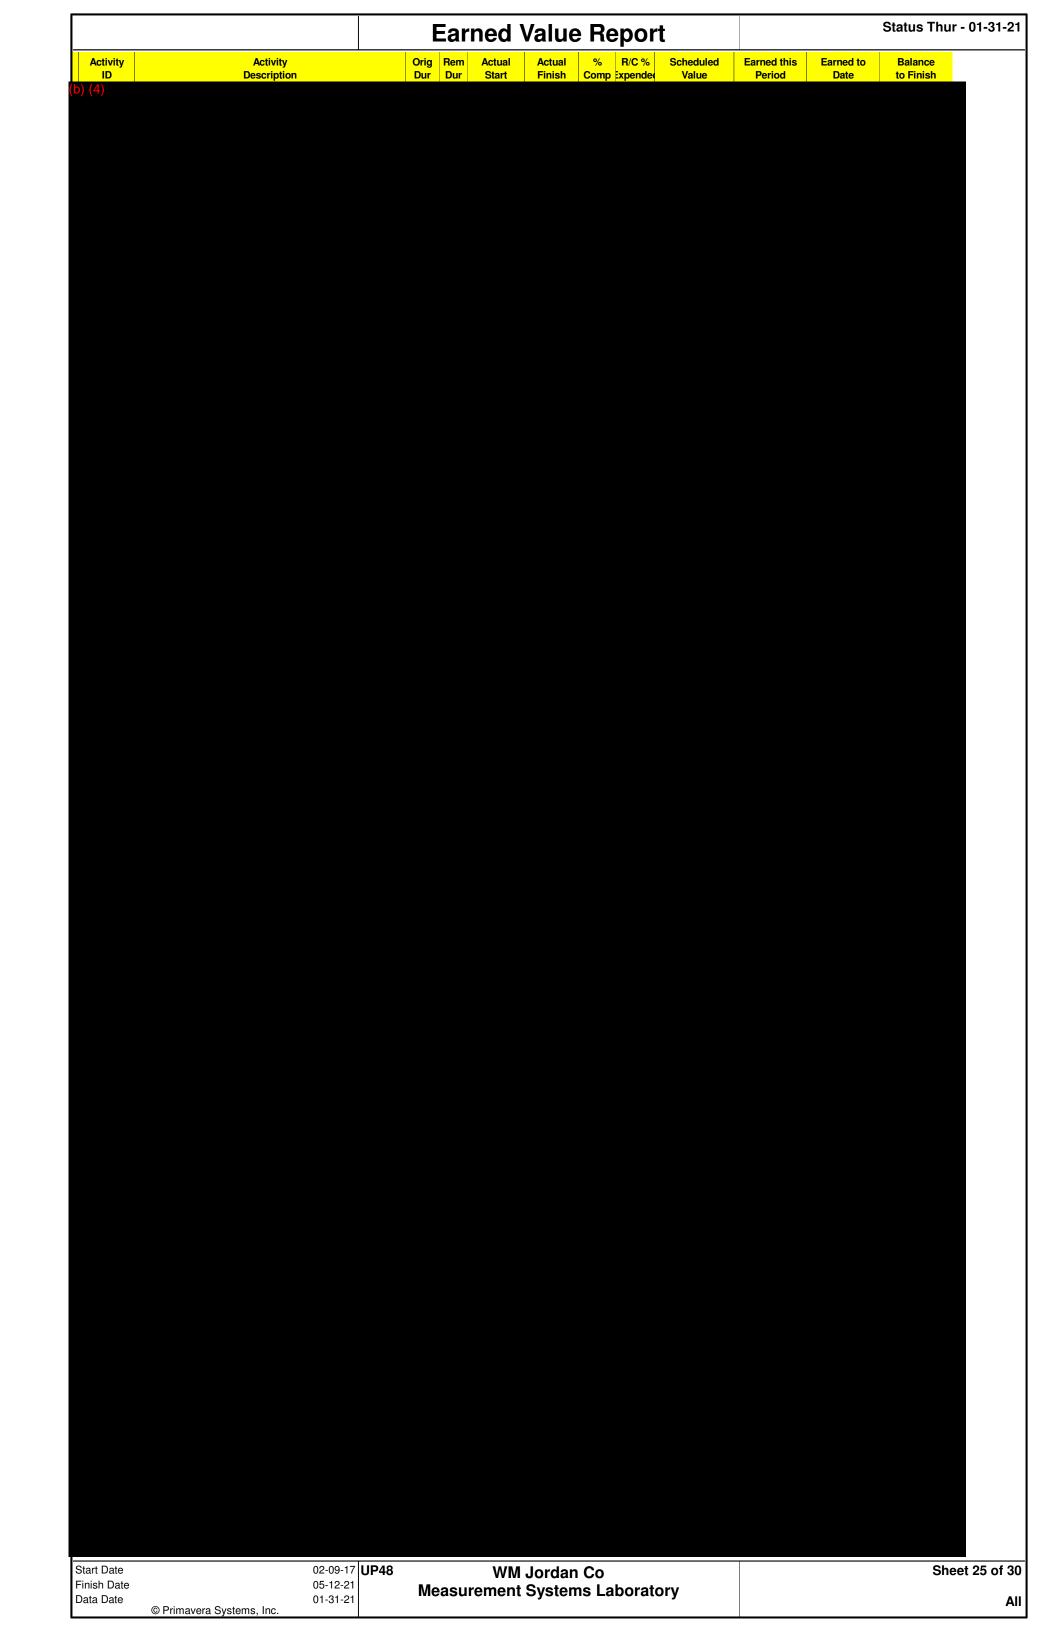

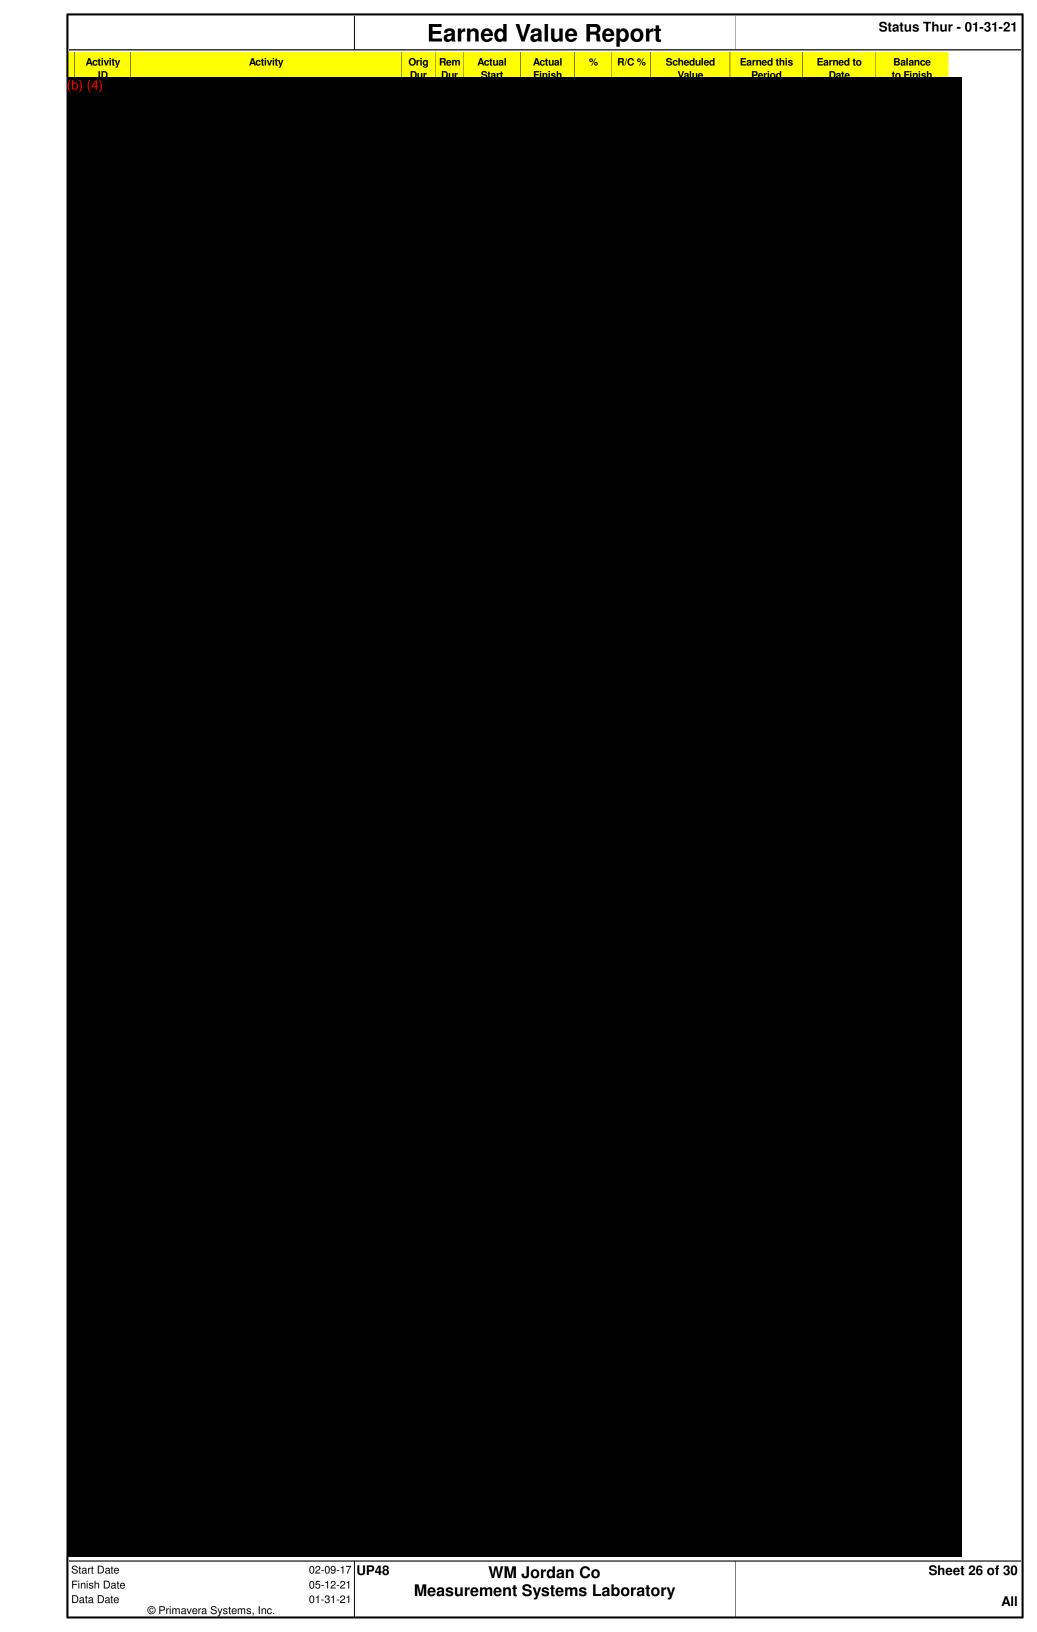

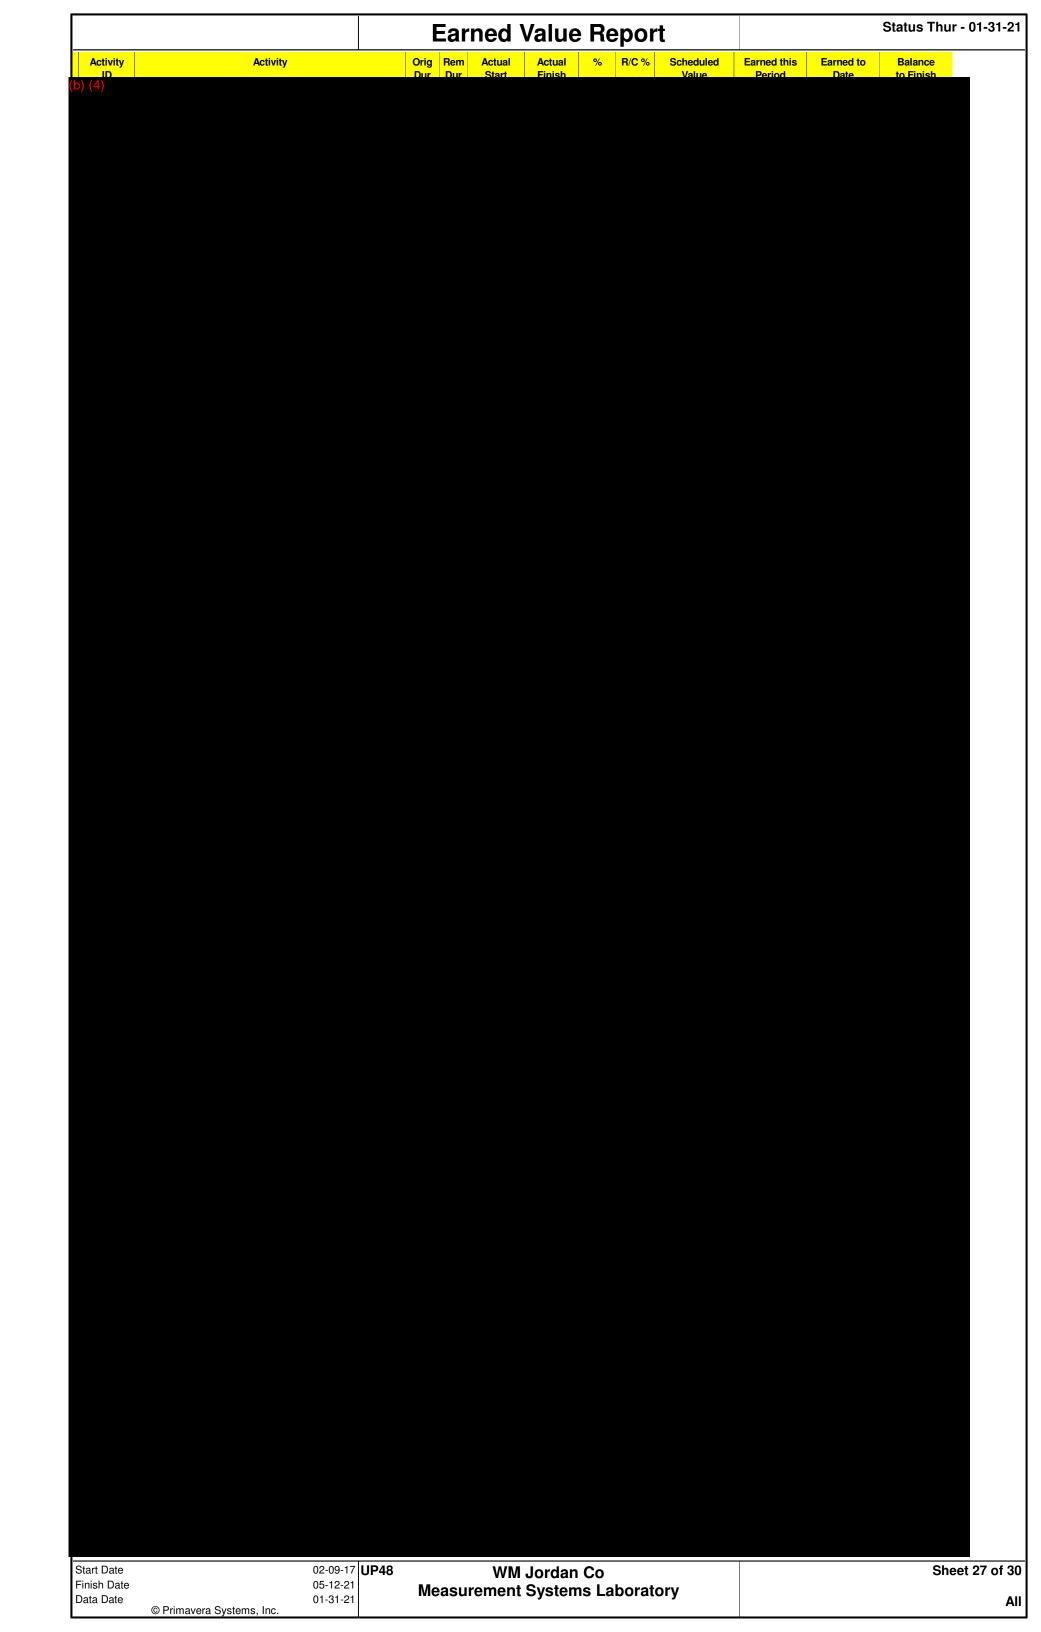

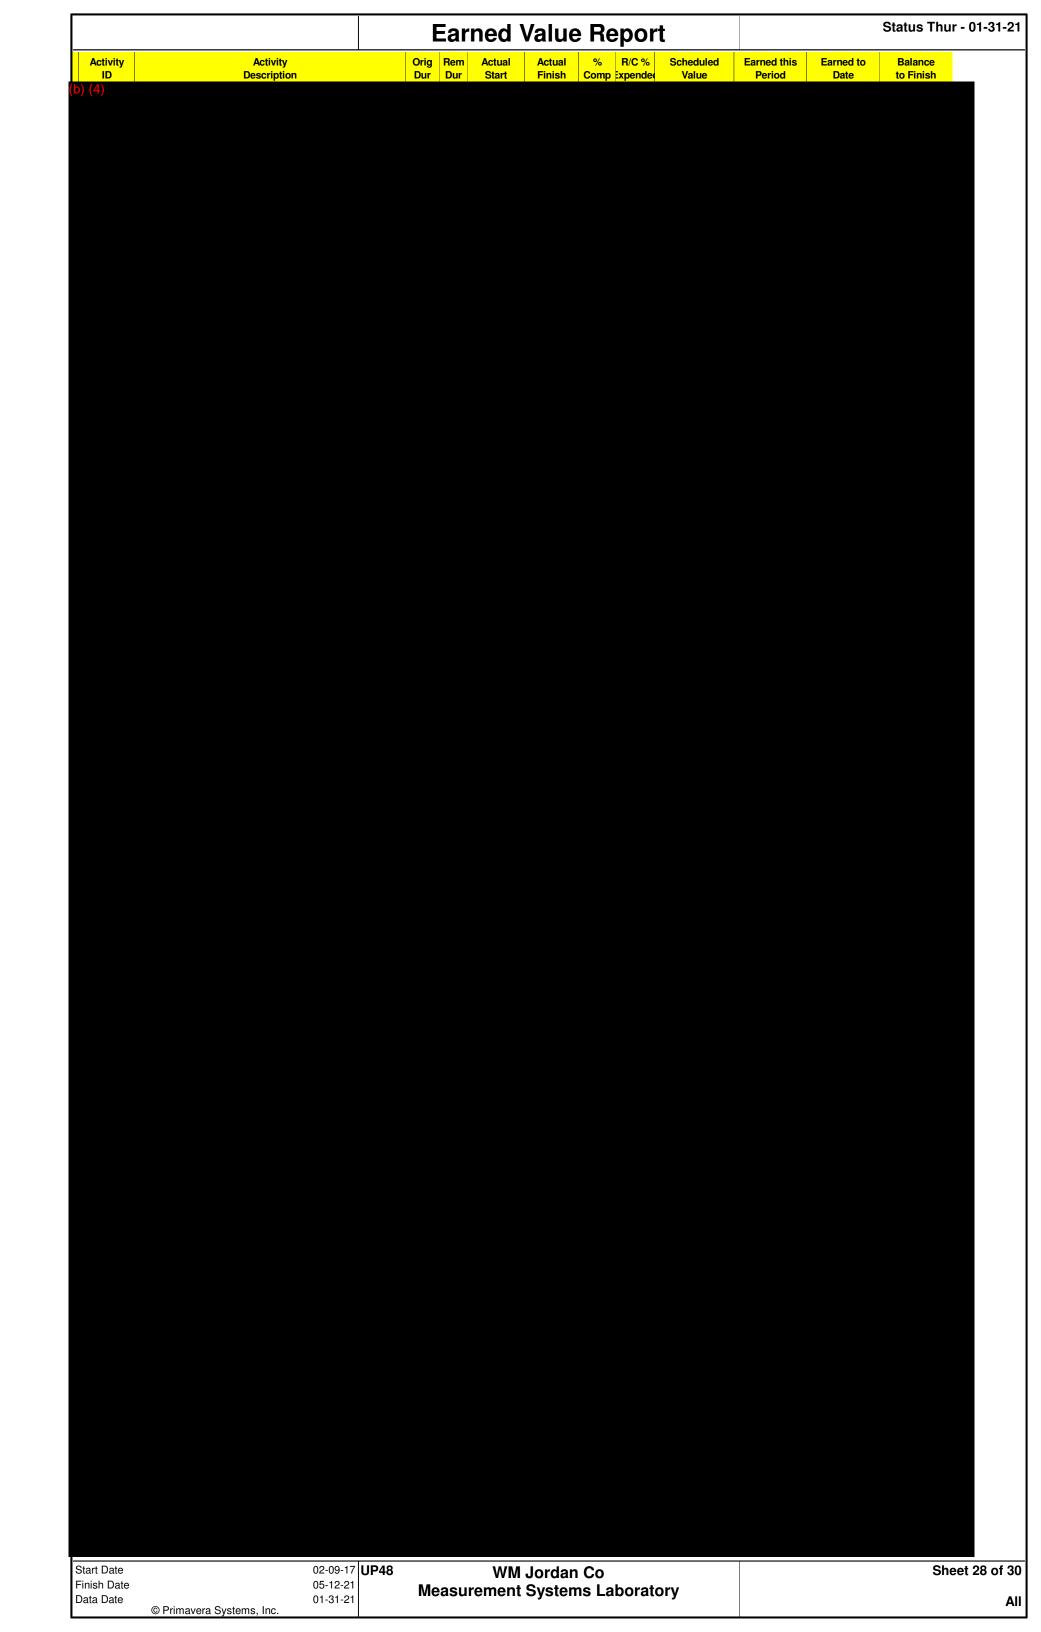



		Earned	Status Thur - 01-31-21		
Activity ID	Activity Description	Orig Rem Actual Dur Dur Start	Actual % R/C % Sched Finish Comp Expende Value	duled Earned this lue Period	Earned to Balance Date to Finish
<i>ڪ</i> ر (.)					
Start Date	02-09-17	UP48 WA	// Jordan Co		Sheet 30 of 30
Finish Date Data Date	05-12-21 01-31-21 imavera Systems, Inc.		t Systems Laboratory		Al
