APPLICATION FOR PAYMENT

Distribution to:

Project: NASA Measurement Systems Lab

Contract For: General Services Admin, PDN: FNLGS-03-P-17 DV

Via Archite Application No Period T

Customer Contract

Contract Date: 11/29/16 Customer No.: 202144 Job No.: 16123

-1,657,186.00

-1,657,186.00

0.00

or: General Services Admin. PDN: EN-	GS-03-P-17-DX-
C-0005	OWNER
ct: AECOM	ARCHITECT
o.: 16123-43	CONTRACTOR
o: 08/31/20	CONTRACTOR
#:	
11/20/16	

To: General Services Admin. PDN: EN-GS-03-

11010 Jefferson Ave

Newport News VA 23601

P-17-DX-C-0005

months by Owner

TOTALS

Total approved this Month

NET CHANGES by Change Order

Remit To: W.M. Jordan Company Inc.

100 S Independence Mall West

Philadelphia PA 19108

CONTRACTOR'S APPLICATION FOR PAYMENT

Application is made for Payment, as shown below, in connection with the Contract. Schedule of Values is attached. 1. ORIGINAL CONTRACT SUM\$ 95,598,160.00 2. NET CHANGE BY CHANGE ORDERS\$ 6.509,048.78 3. CONTRACT SUM TO DATE (line 1 + 2)\$ 102,107,208.78 4. TOTAL COMPLETED AND STORED TO DATE\$ 101,365,976.70 (Column G of Schedule of Values) 5. RETAINAGE: a. 0.64898862 % of Completed Work 657,853.65 (Column D + E of Schedule of Values) % of Stored Material 0.00 (Column F of Schedule of Values) Total Retainage 657.853.65\$ (Line 5a + 5b or Total of Column I of Schedule of Values) 6. TOTAL EARNED LESS RETAINAGE\$ 100,708,123.05 (Line 4 less Line 5 Total) 7. LESS PREVIOUS CERTIFICATES FOR PAYMENT\$ 100,244,381.12 (Line 6 from prior Application) 8. CURRENT PAYMENT DUE\$ 463,741.93 9. BALANCE TO FINISH, INCLUDING RETAINAGE\$ 1,399,085.73 (Line 3 less Line 6) **CHANGE ORDER SUMMARY ADDITIONS DEDUCTIONS** Total changes approved in previous

8,166,234.78

8,166,234.78


6,509,048.78


0.00


Contract For:


The undersigned	Contractor cert	ifies that to the	hact of the	Contractor's
THE UNDERSONED	COMMACION GEN	mes mai to me	Desi Oi lie	Compacions


J) (6)	Application for
	ct Documents, that
	hich previous
	from the Owner,
	75 101411111
	28 TORCE
State of: V	County/City of:
Notary Public (b) (6)	UBL
My Commission expires.	17/1
ARCHITECT'S CERTIFICATE FO	R PAYMENT Comments, based on on-site observations EXPLORATION Cation, the Architect certifies to the cation, the Architect certifies and the cation and the cation.
In accordance with the Contract D	acuments based on an site observations EXP
and the data comprising this applic	cation, the Architect cortifies to the
Owner that to the best of the Archi	tect's knowledge information and policy
the Work has progressed as indica	tect's knowledge, information and reliev ONWEA
	uments, and the Contractor is entitled to
payment of the AMOUNT CERTIF	
AMOUNT CERTIFIED	
	certified differs from the amount applied
	is Application and on the Schedule
of Values that are changes to conf	orm to the amount certified.)
ARCHITECT:	
By:	Date:
	The AMOUNT CERTIFIED is payable only to
	ance, payment and acceptance of payment are
without prejudice to any rights of th	ne Owner or Contractor under this Contract

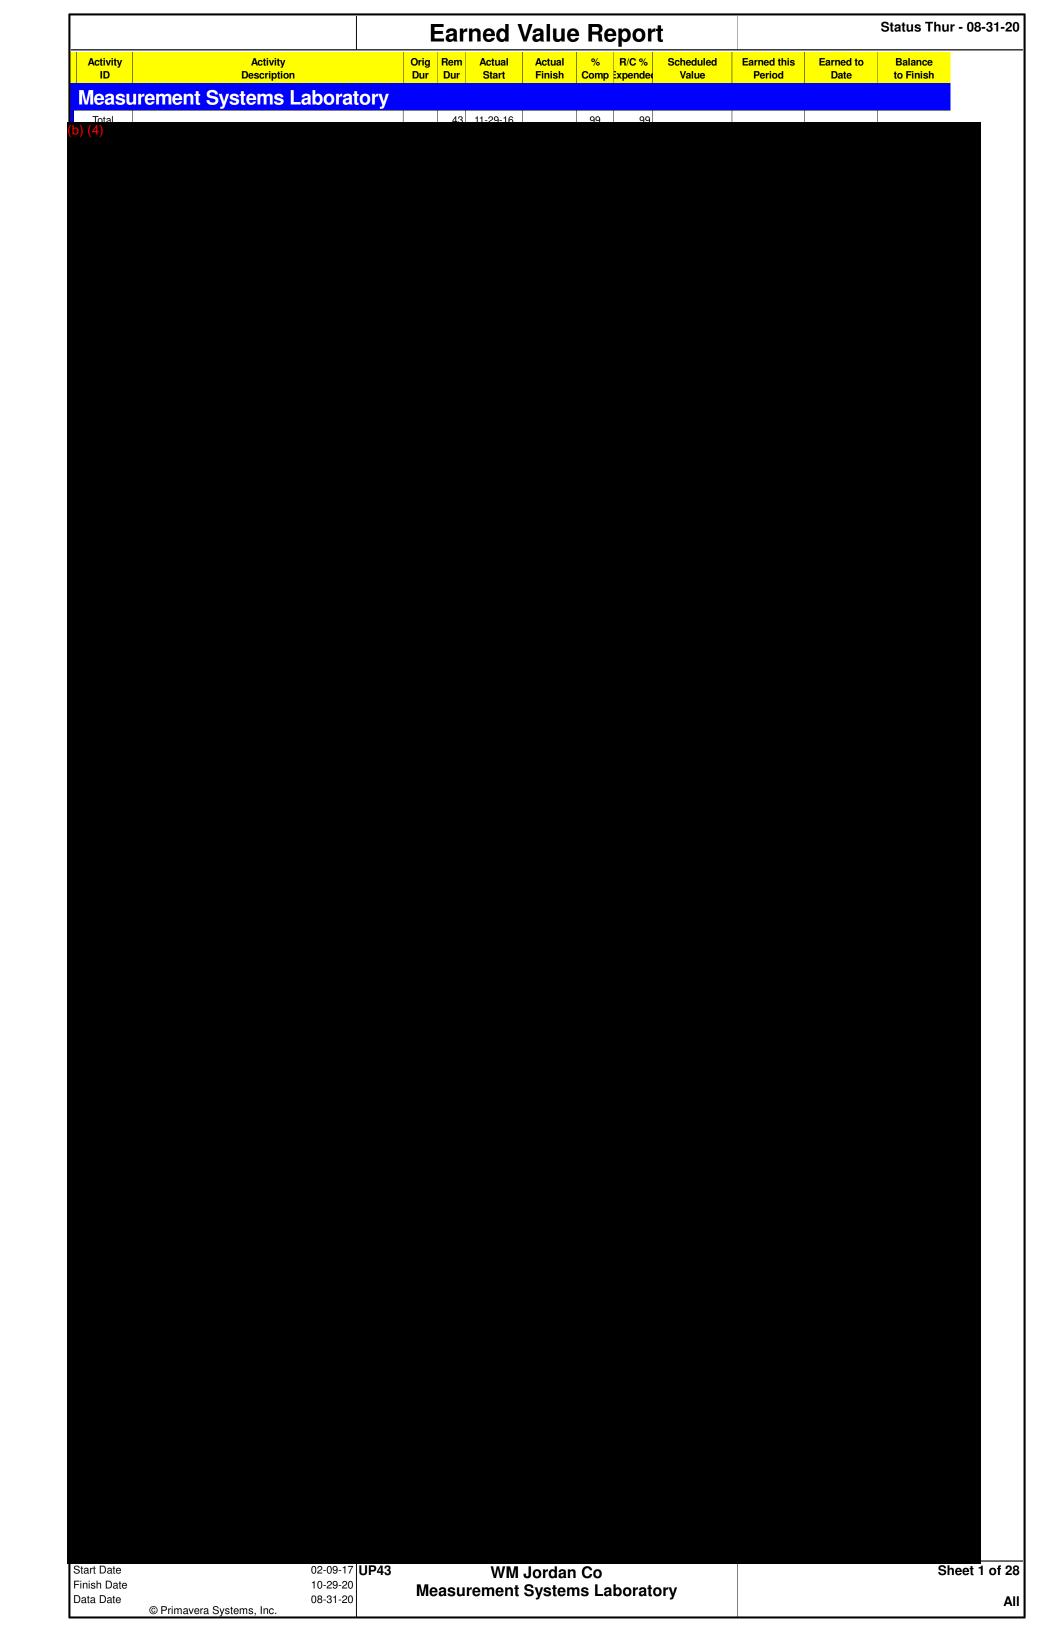


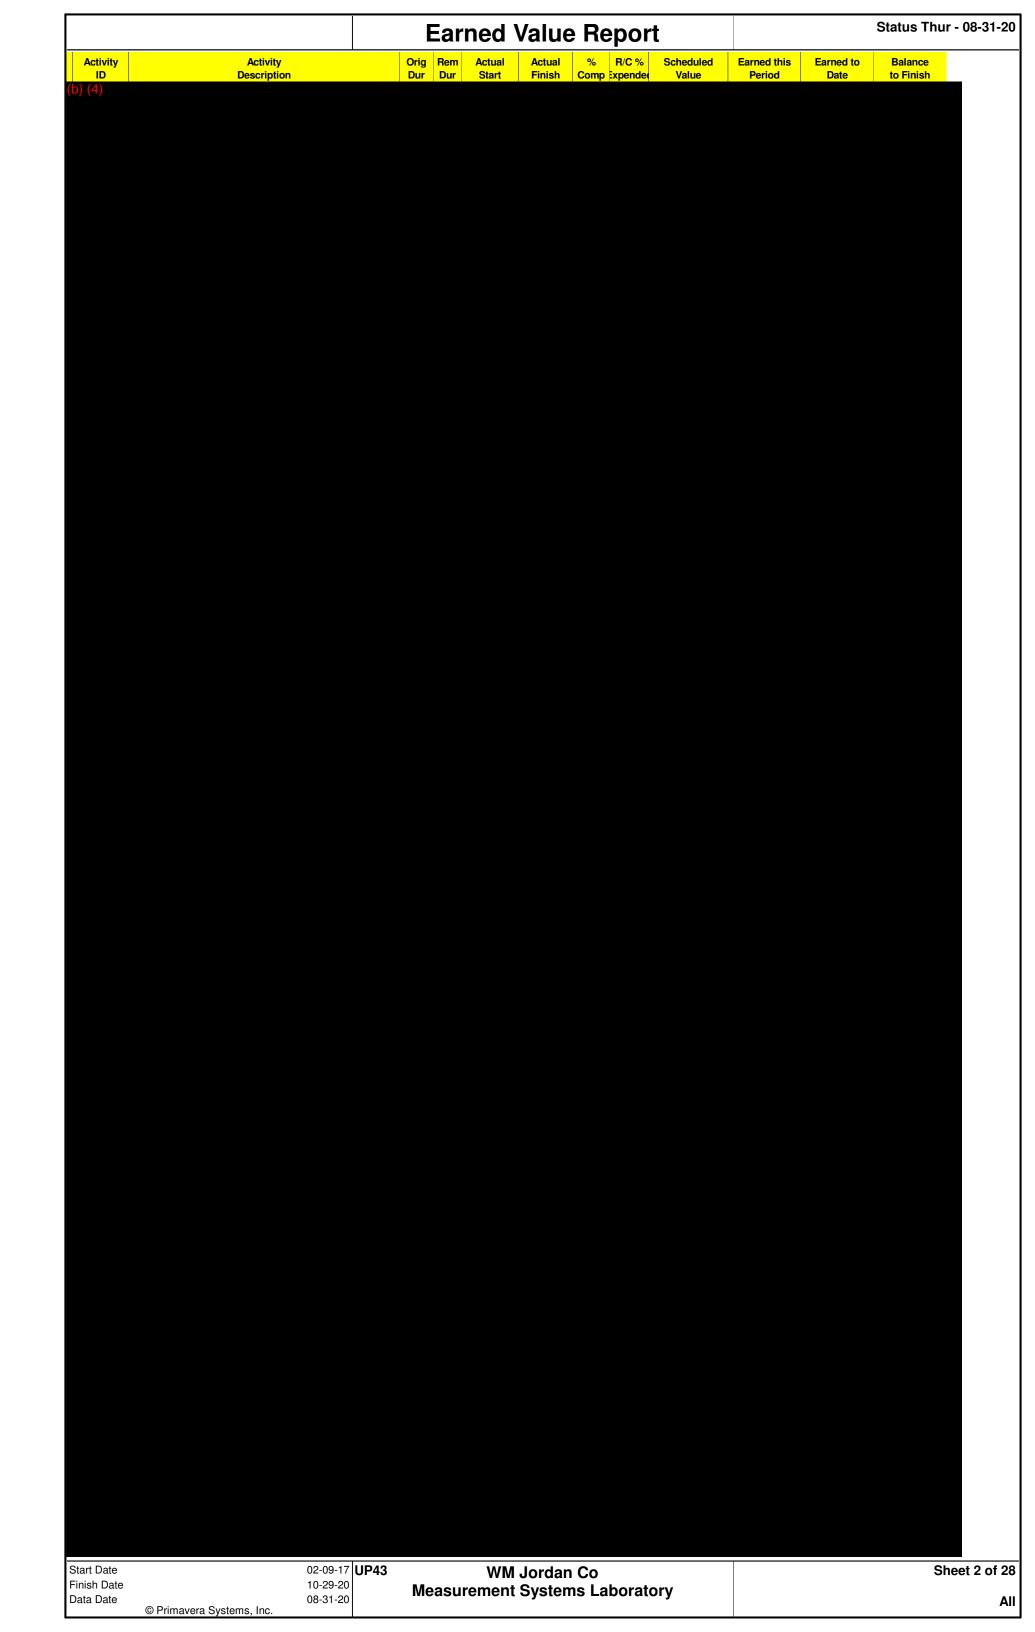





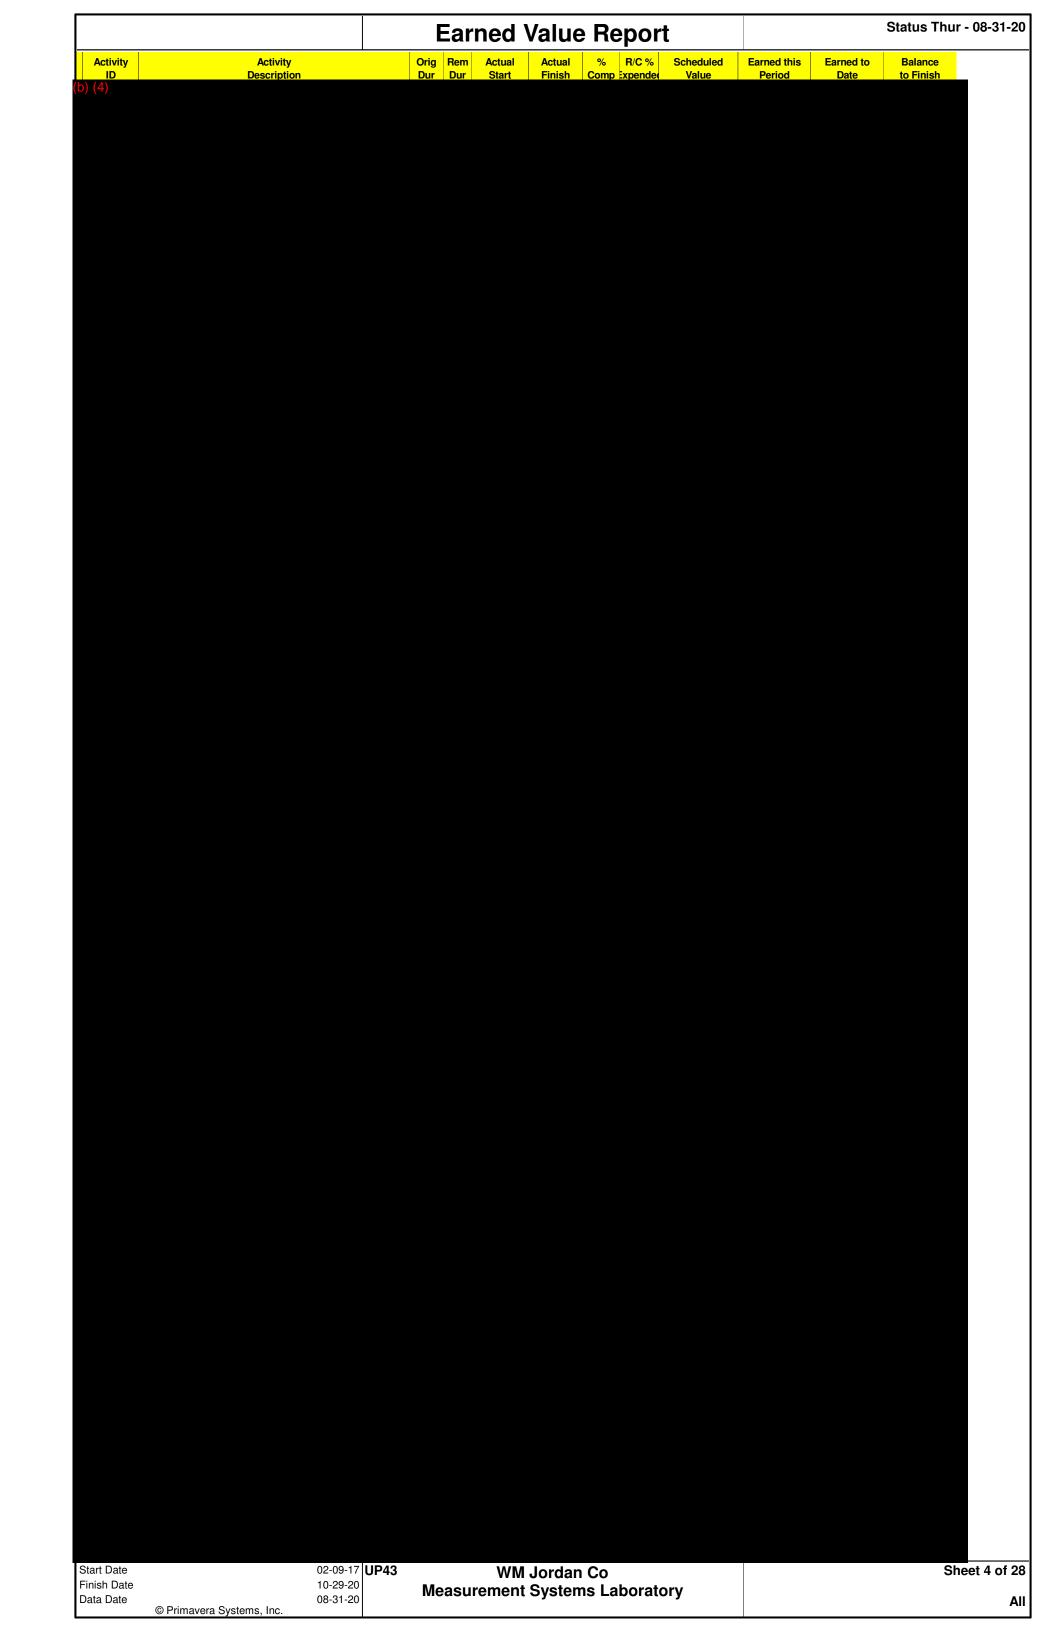


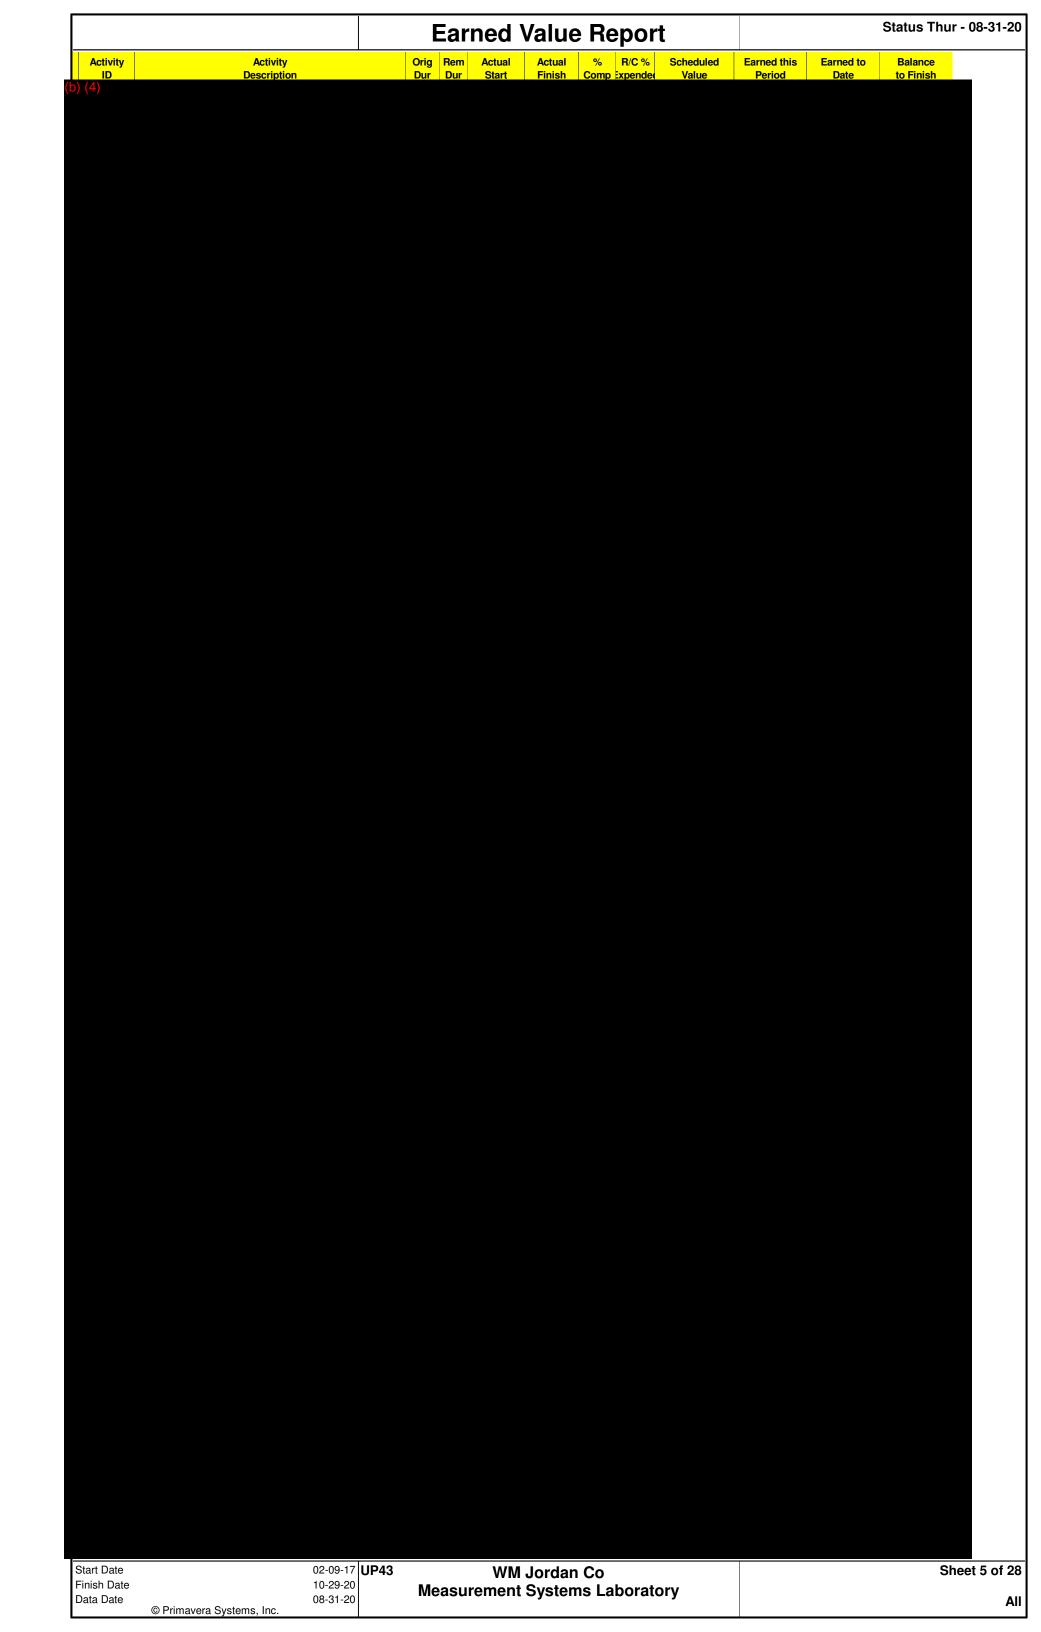


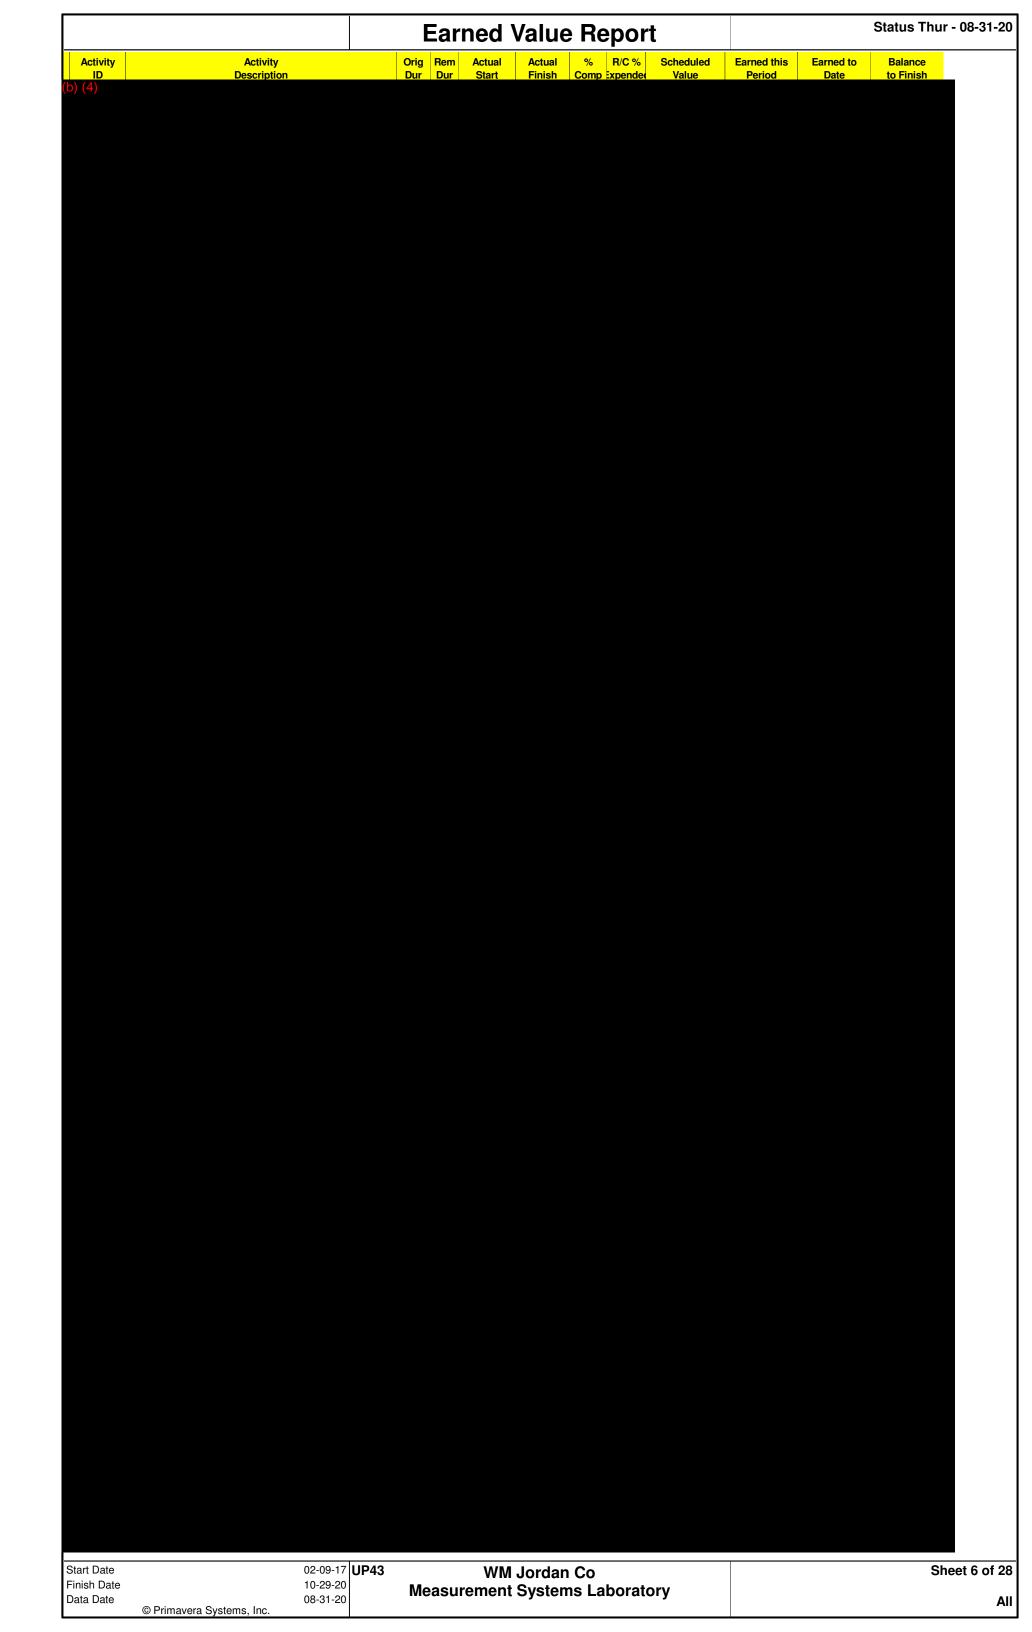


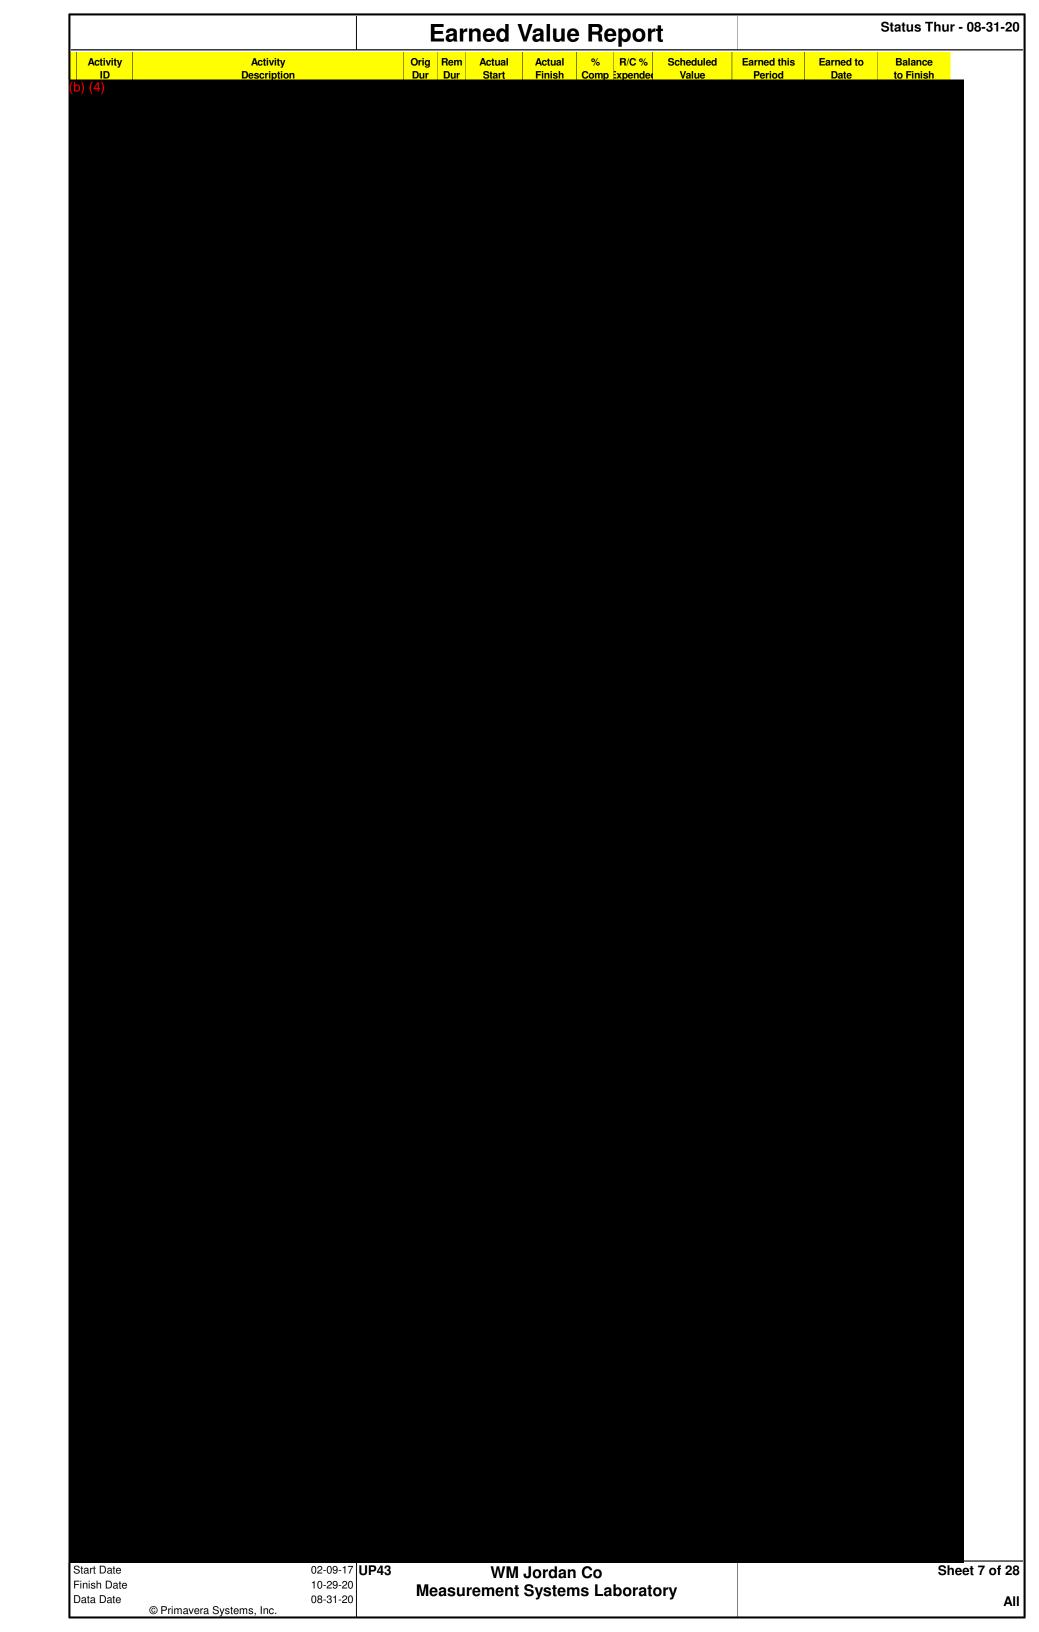


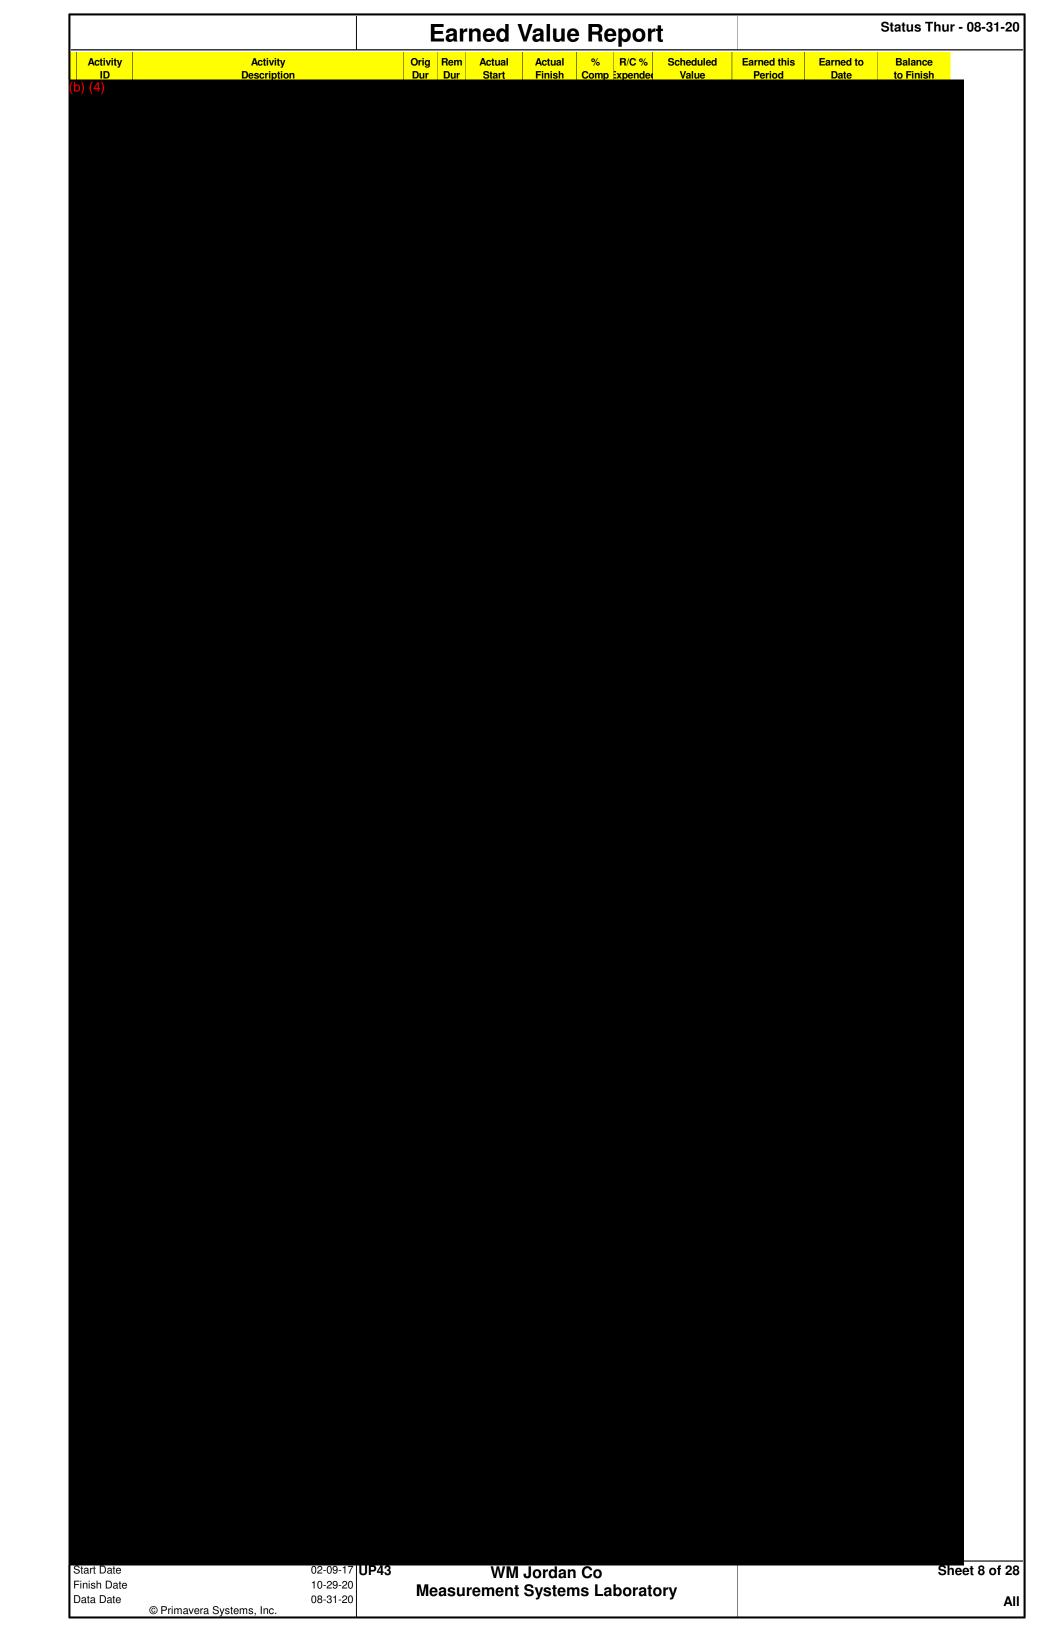


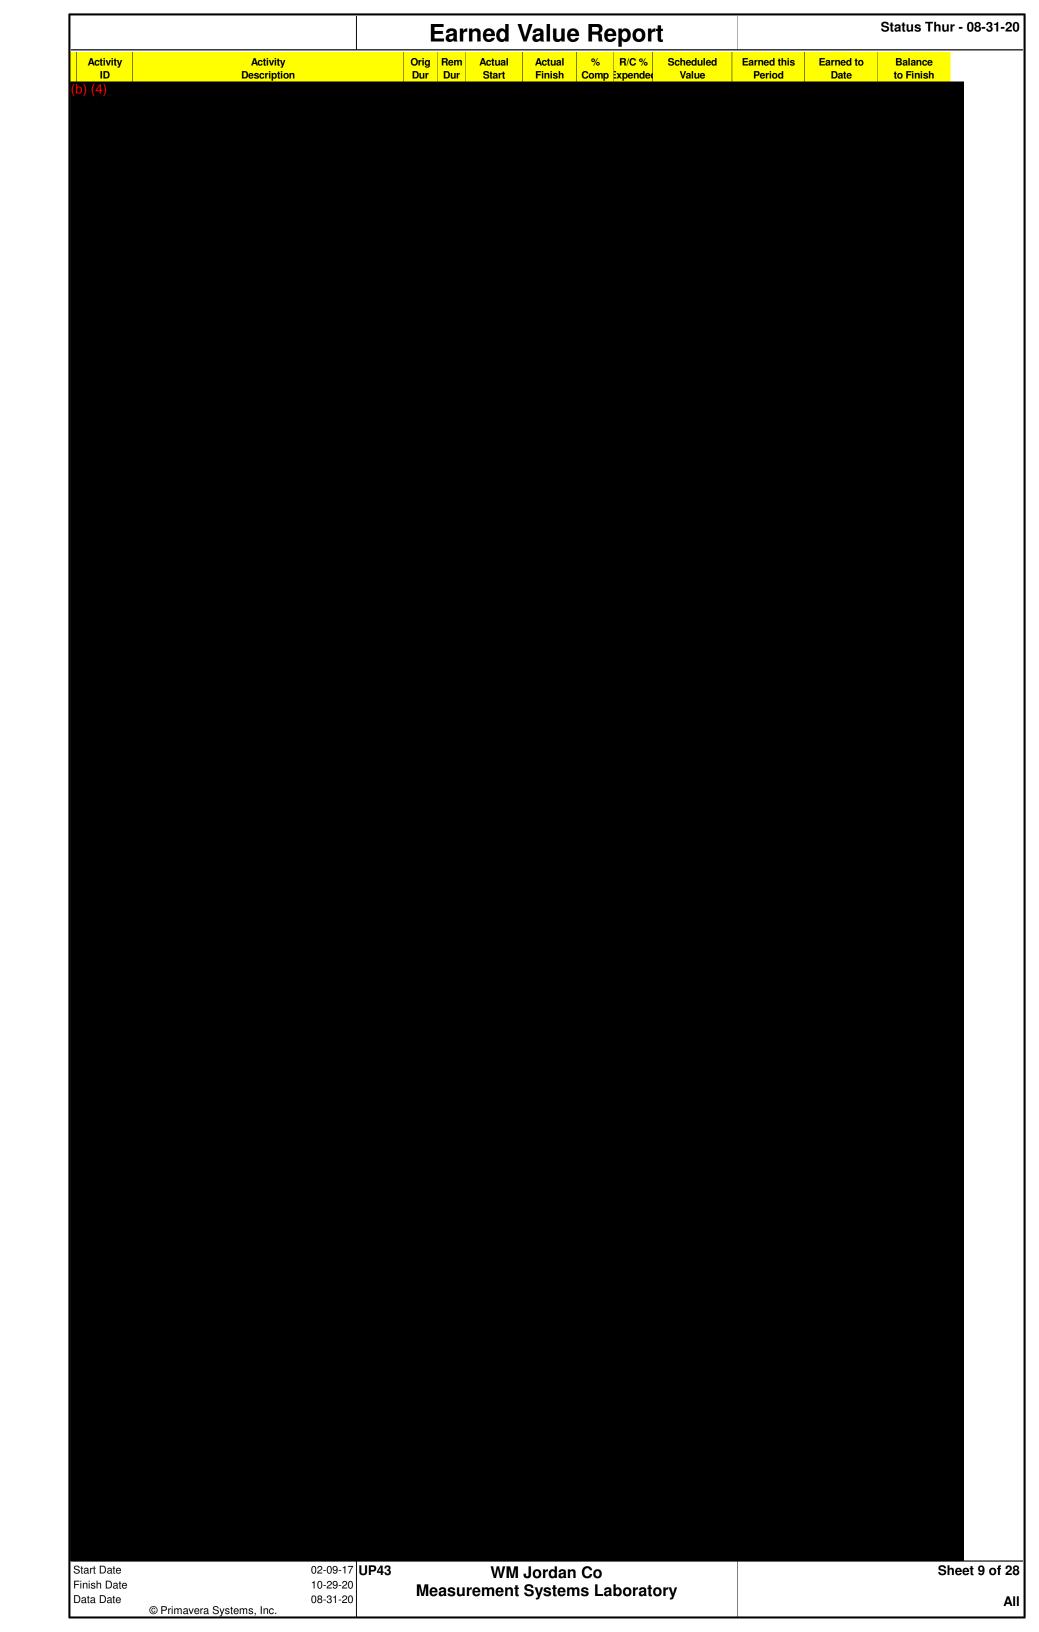


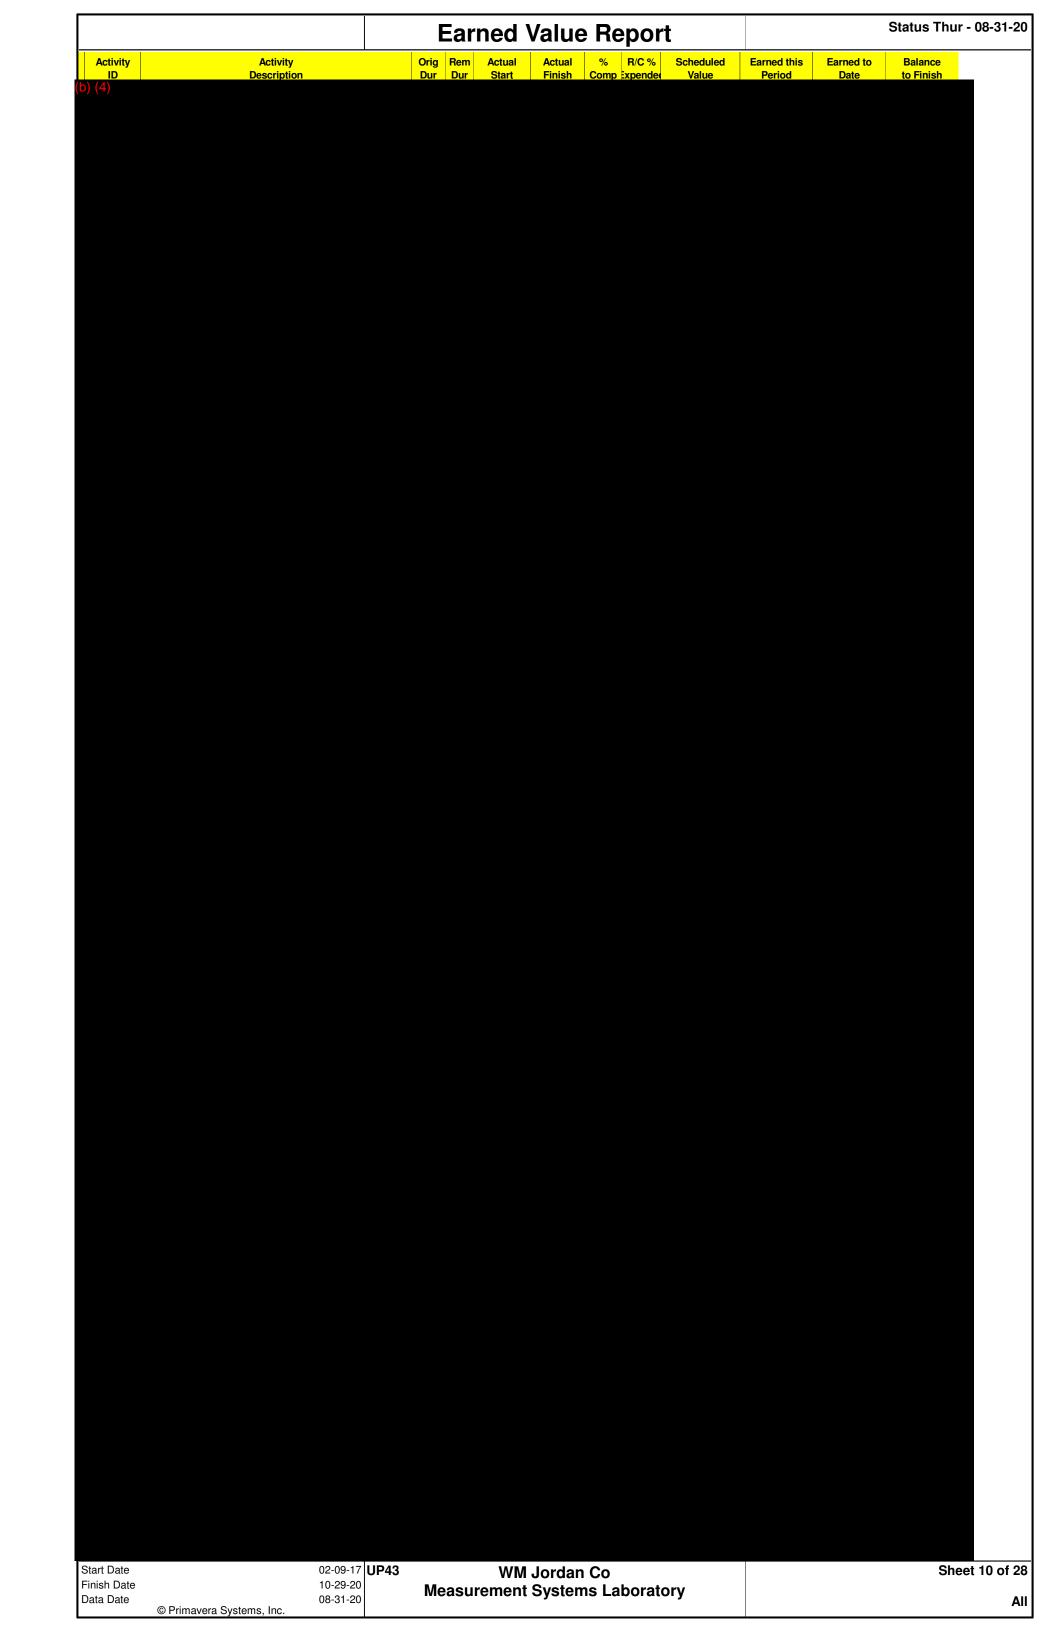


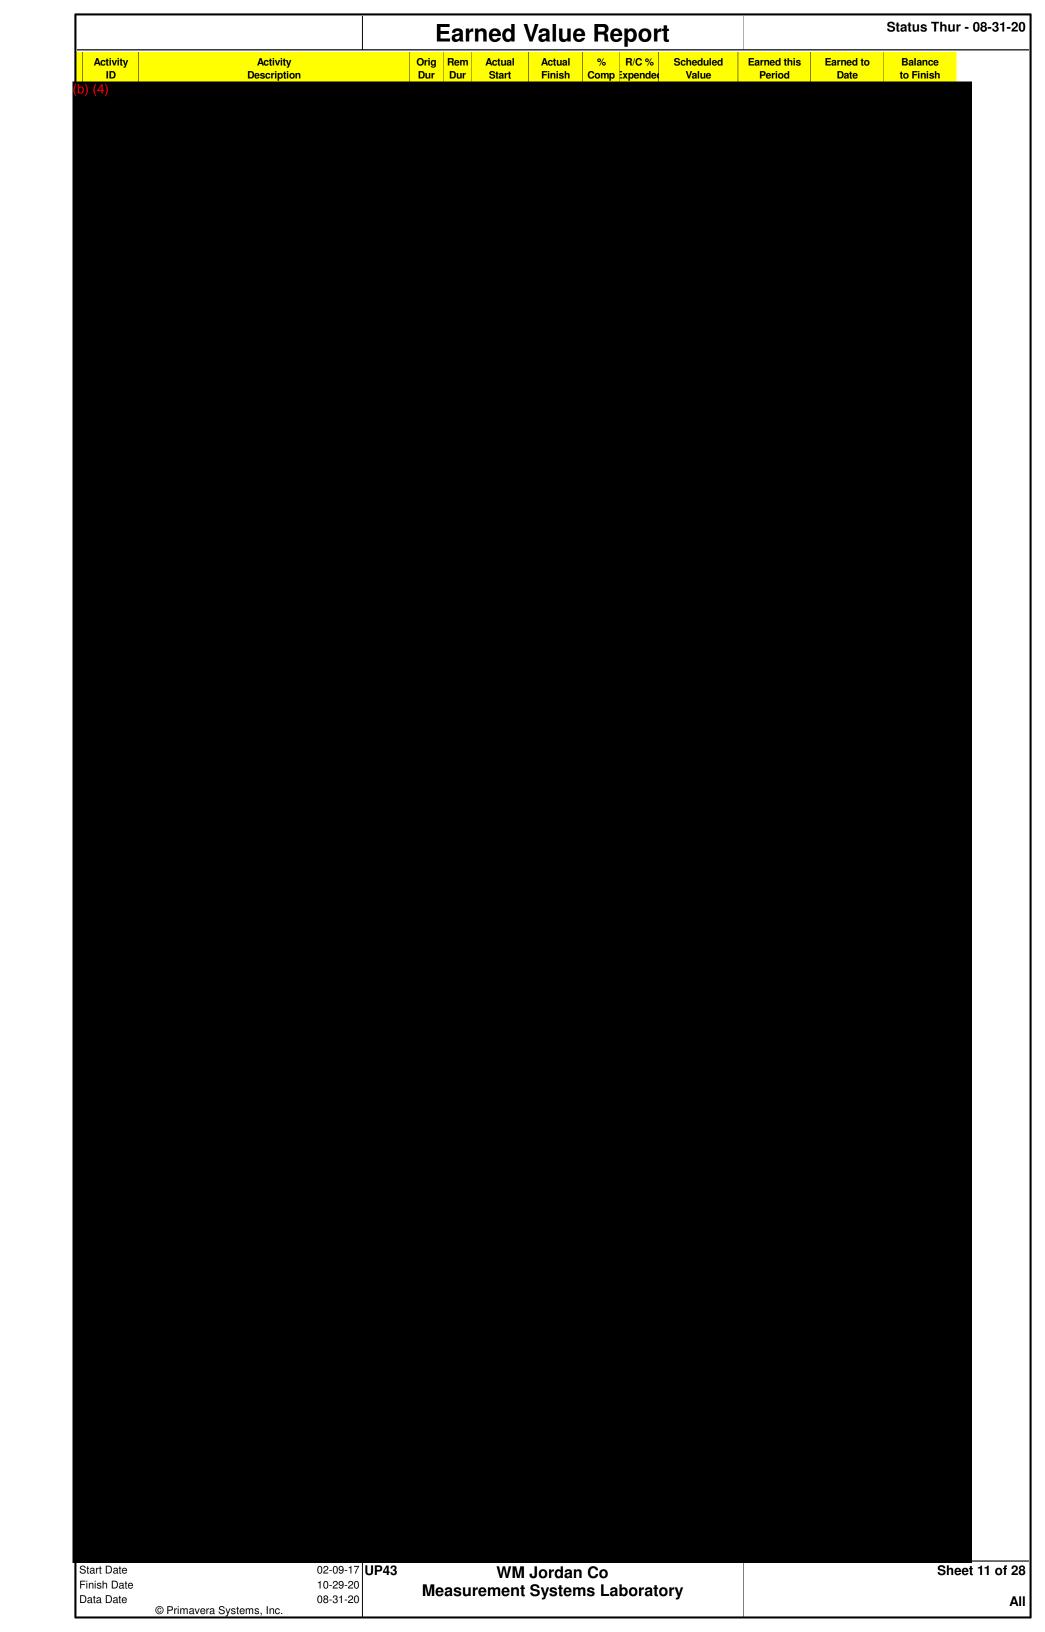


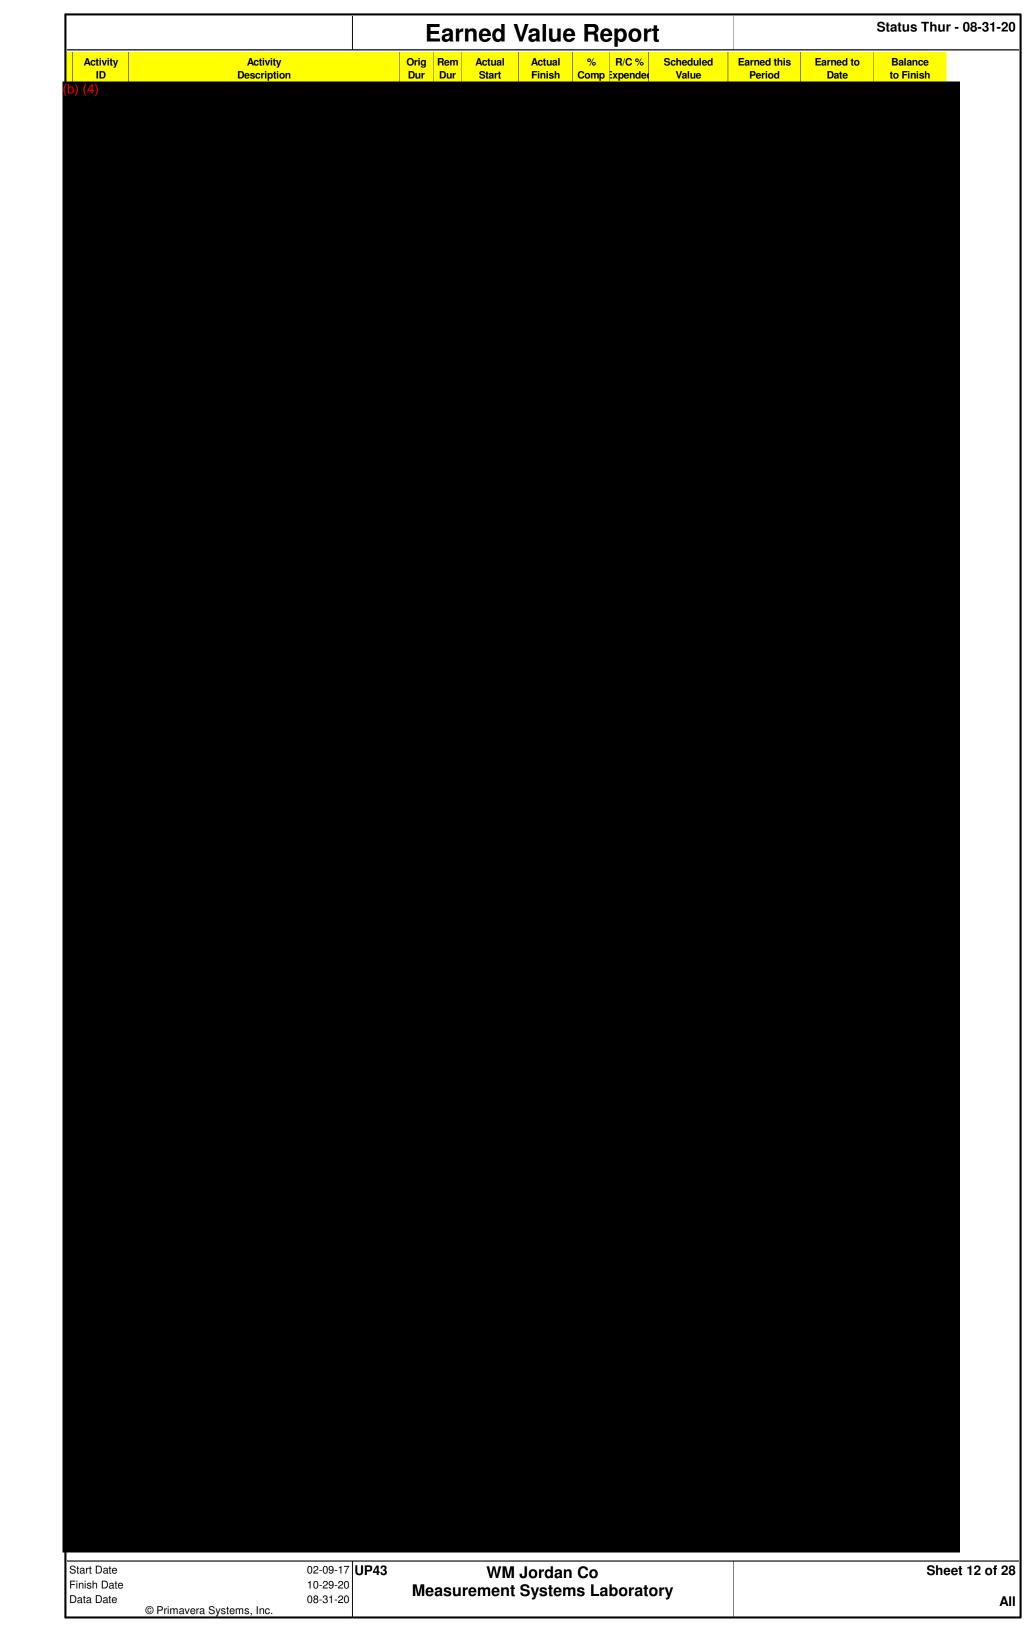





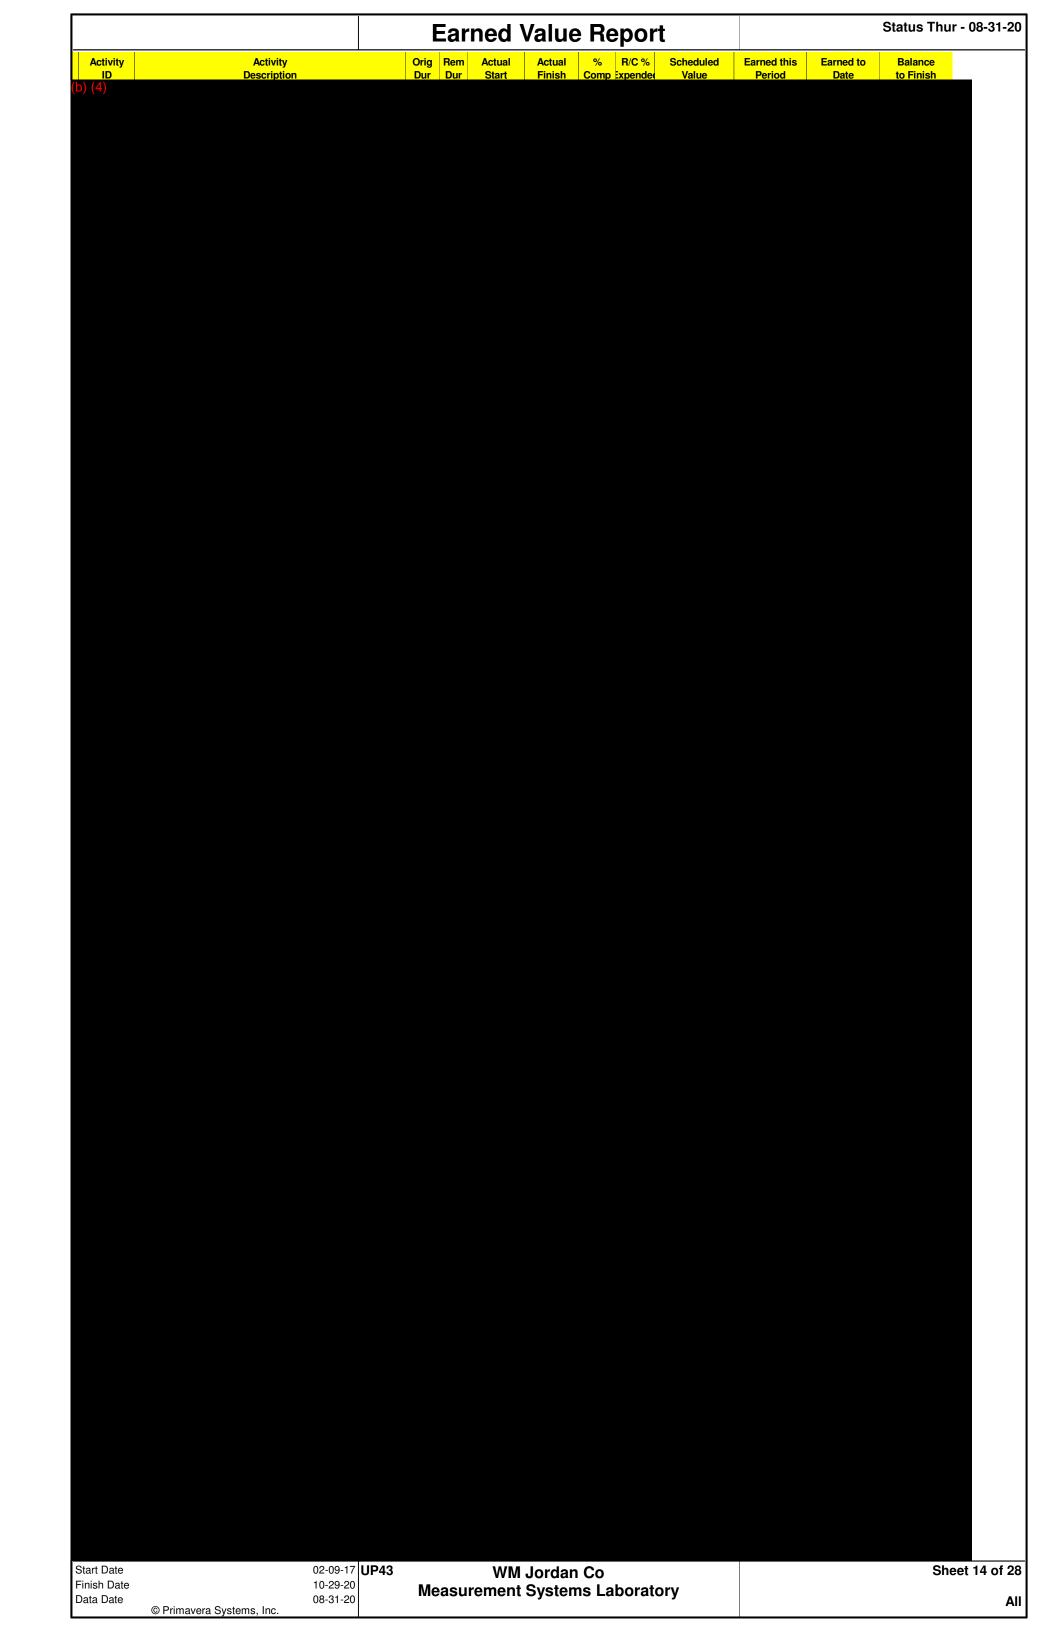


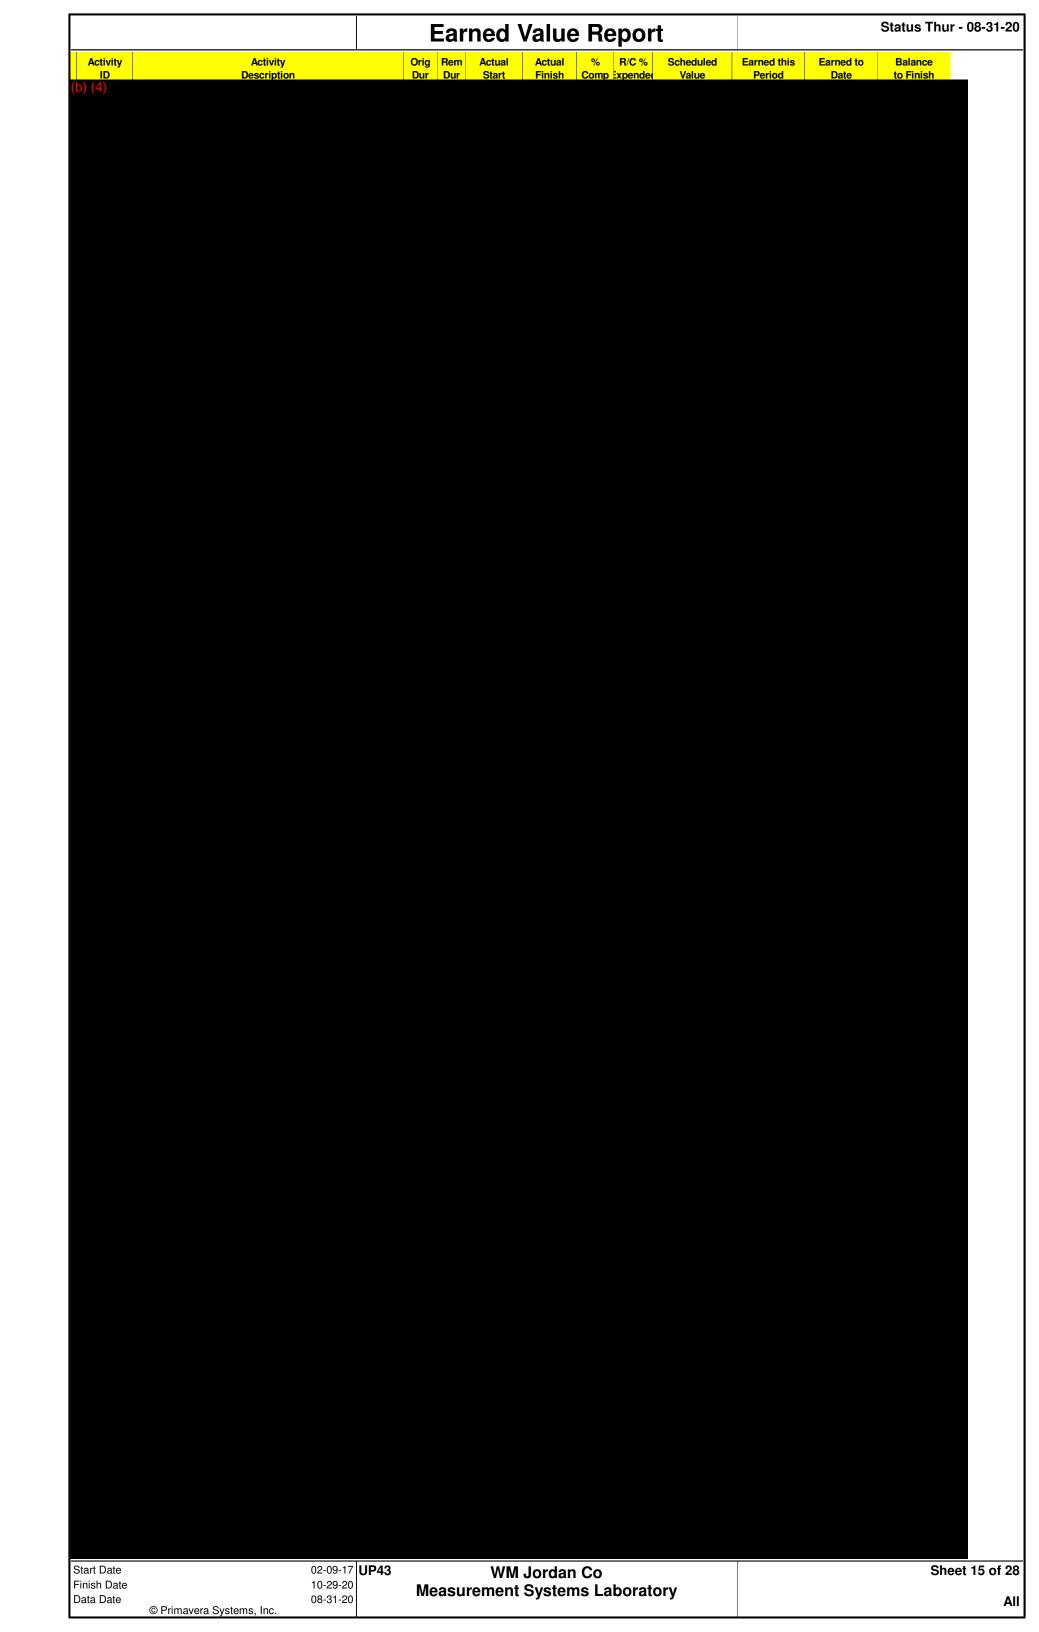


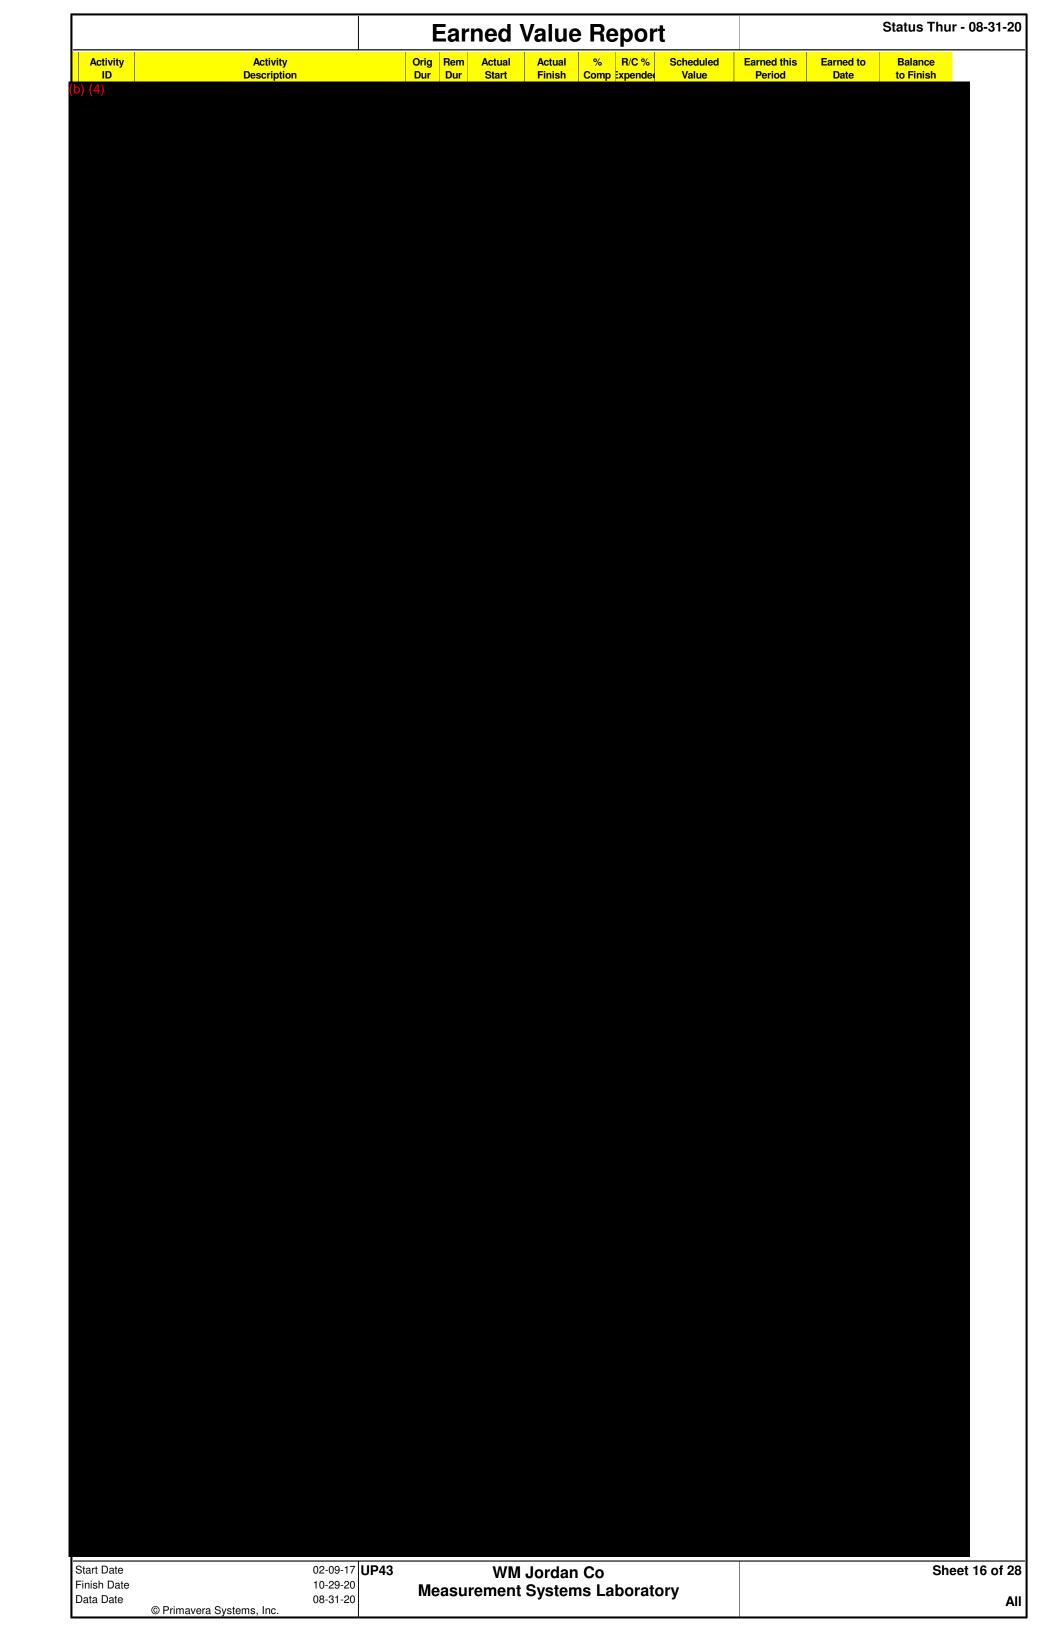


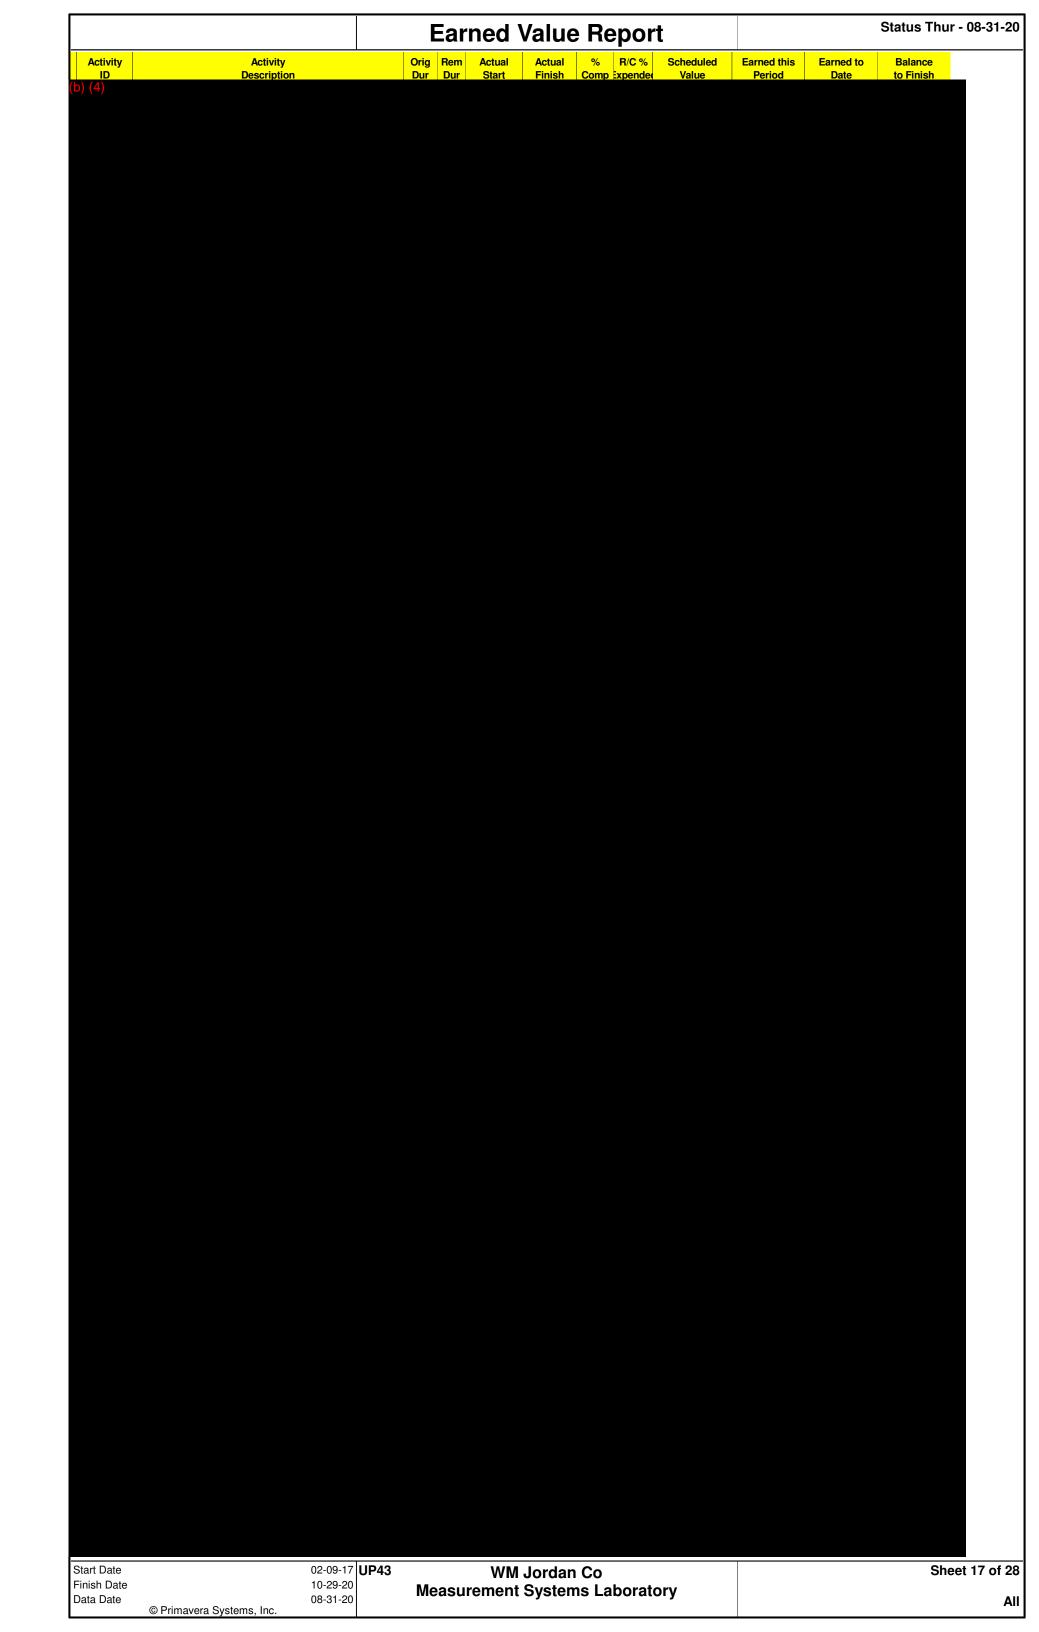



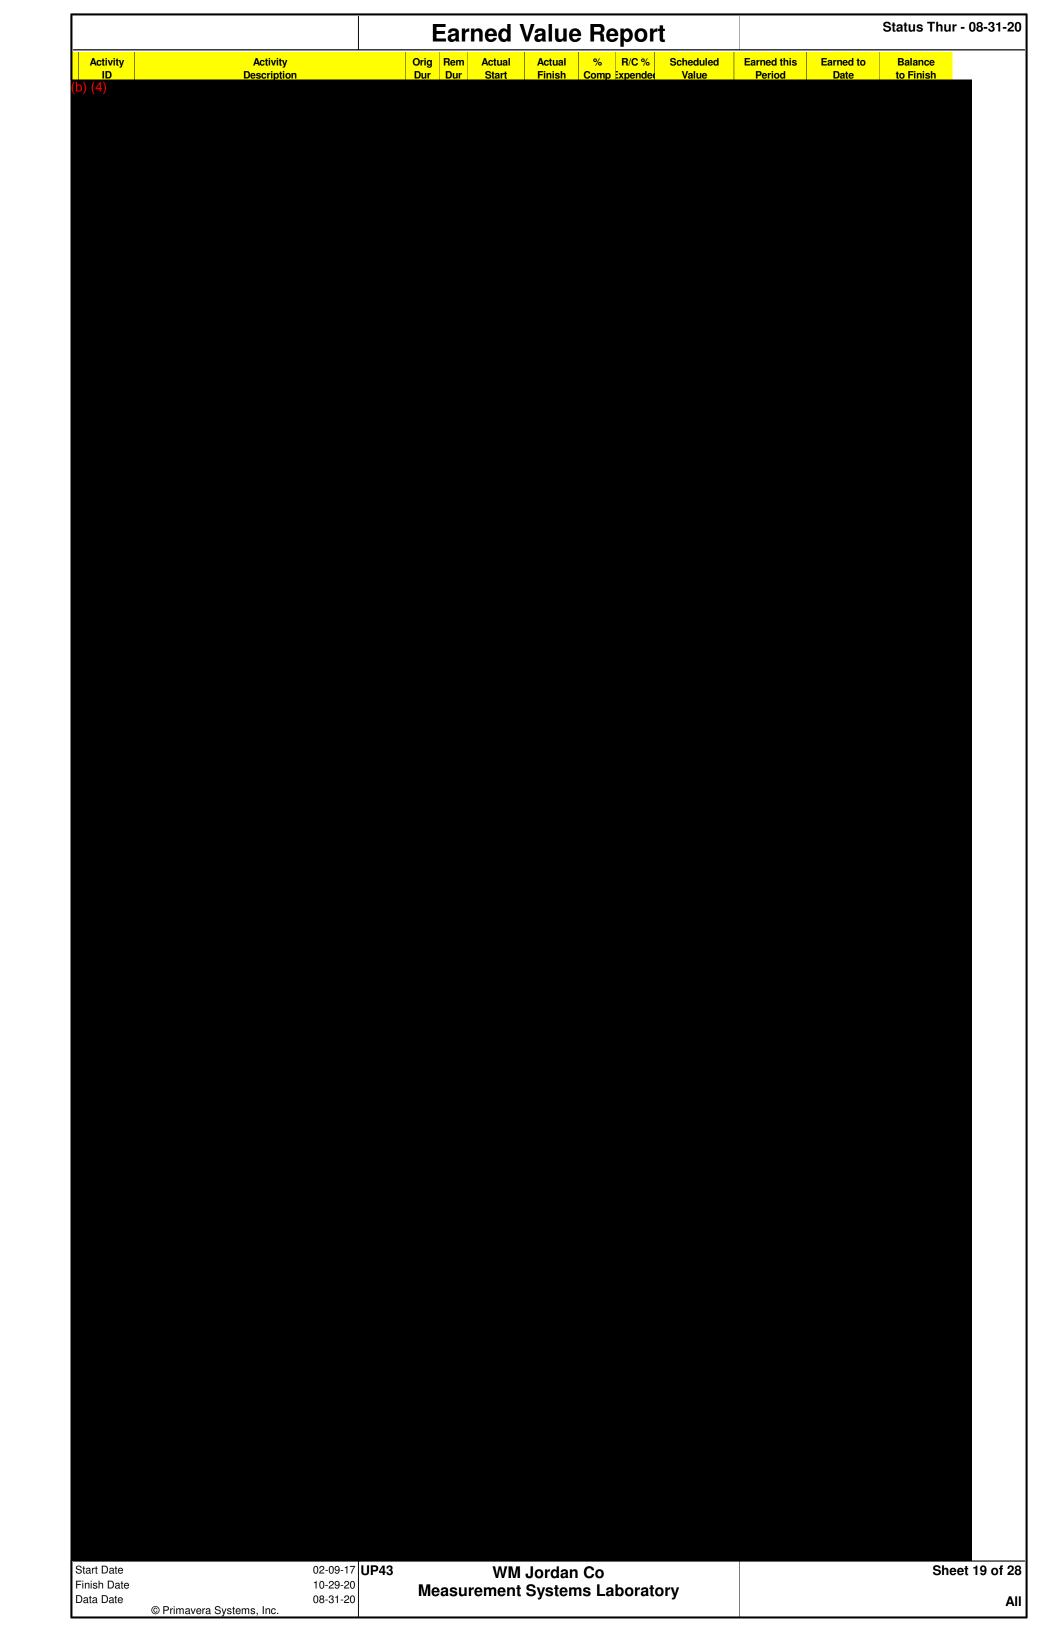





		Earned Value Report	Status Thur - 08-31-20
(b) (4)			
Start Date Finish Date	02-09-17 UP43 10-29-20	WM Jordan Co Measurement Systems Laboratory	Sheet 22 of 28
Data Date © Primavera Systems, Inc.	08-31-20		All

