APPLICATION FOR PAYMENT

Project: NASA Measurement Systems Lab

Contract For: General Services Admin. PDN: EN-GS-03-P-17-DX-

C-0005

Remit To: W.M. Jordan Company Inc. 11010 Jefferson Ave Newport News VA 23601 Via Architect: AECOM Application No.: 16123-49 Period To: 02/28/21

Customer Contract #:

Contract Date: 11/29/16 Customer No.: 202144 Job No.: 16123

	OWNER
	ARCHITECT
	CONTRACTOR

Distribution to:

To: General Services Admin. PDN: EN-GS-03-

P-17-DX-C-0005

100 S Independence Mall West


Philadelphia PA 19108


C	0	Ν	Į	R	Α	C.	F۱	0	R	'S	Α	PΙ	ᇺ	IC,	AΊ	IK)I	V	F	ЭF	t	7,	۱Y	M	E	Л.	T
---	---	---	---	---	---	----	----	---	---	----	---	----	---	-----	----	----	----	---	---	----	---	----	----	---	---	----	---


Application is made for Payment, as shown below, with the Contract. Schedule of Values is attached.		
1. ORIGINAL CONTRACT SUM	\$	95,598,160.00
2. NET CHANGE BY CHANGE ORDERS	\$	6,561,148.78
3. CONTRACT SUM TO DATE (line 1 + 2)	\$	102,159,308.78
4. TOTAL COMPLETED AND STORED TO DATE (Column G of Schedule of Values) 5. RETAINAGE:	\$	102,058,098.03
a. 0.70418571 % of Completed Work (Column D + E of Schedule of Values)	•	18,678.54
b. % of Stored Material (Column F of Schedule of Values)	\$	0.00
Total Retainage	\$	718,678.54
(Line 5a + 5b or Total of Column I of S	chedule of Values)	
6. TOTAL EARNED LESS RETAINAGE	\$	101,339,419.49
(Line 4 less Line 5 Total) 7. LESS PREVIOUS CERTIFICATES FOR PAYM (Line 6 from prior Application)	·	101,303,166.65
8. CURRENT PAYMENT DUE	\$	36,252.84
 BALANCE TO FINISH, INCLUDING RETAINAG (Line 3 less Line 6) 	£\$	819,889.29
CHANGE ORDER SUMMARY	ADDITIONS	DEDUCTIONS
Total changes approved in previous		
months by Owner	8,248,934.78	-1,687,786.00
Total approved this Month	0.00	0.00
TOTALS	8,248,934.78	-1,687,786.00
NET CHANGES by Change Order	6 561 148 78	


Contract For:


In accordance with the Contract Documents, based on on-site observations REC and the data comprising this application, the Architect certifies to the MY Owner that to the best of the Architect's knowledge, information and belief	AND G. CE
the Work has progressed as indicated, the quality of the Work is in accordance with the Contract Documents, and the Contractor is entitled to payment of the AMOUNT CERTIFIED.	4・ケ
payment of the AMOUNT CERTIFIED.	11
AMOUNT CERTIFIED\$	•
(Attach explanation if the amount certified differs from the amount applied	
for in Line 8. Initial all figures on this Application and on the Schedule	
of Values that are changes to conform to the amount certified.)	
ARCHITECT:	
By: Date:	
This Certificate is not negotiable. The AMOUNT CERTIFIED is payable only to	
the Contractor named herein. Issuance, payment and acceptance of payment are	
without prejudice to any rights of the Owner or Contractor under this Contract	

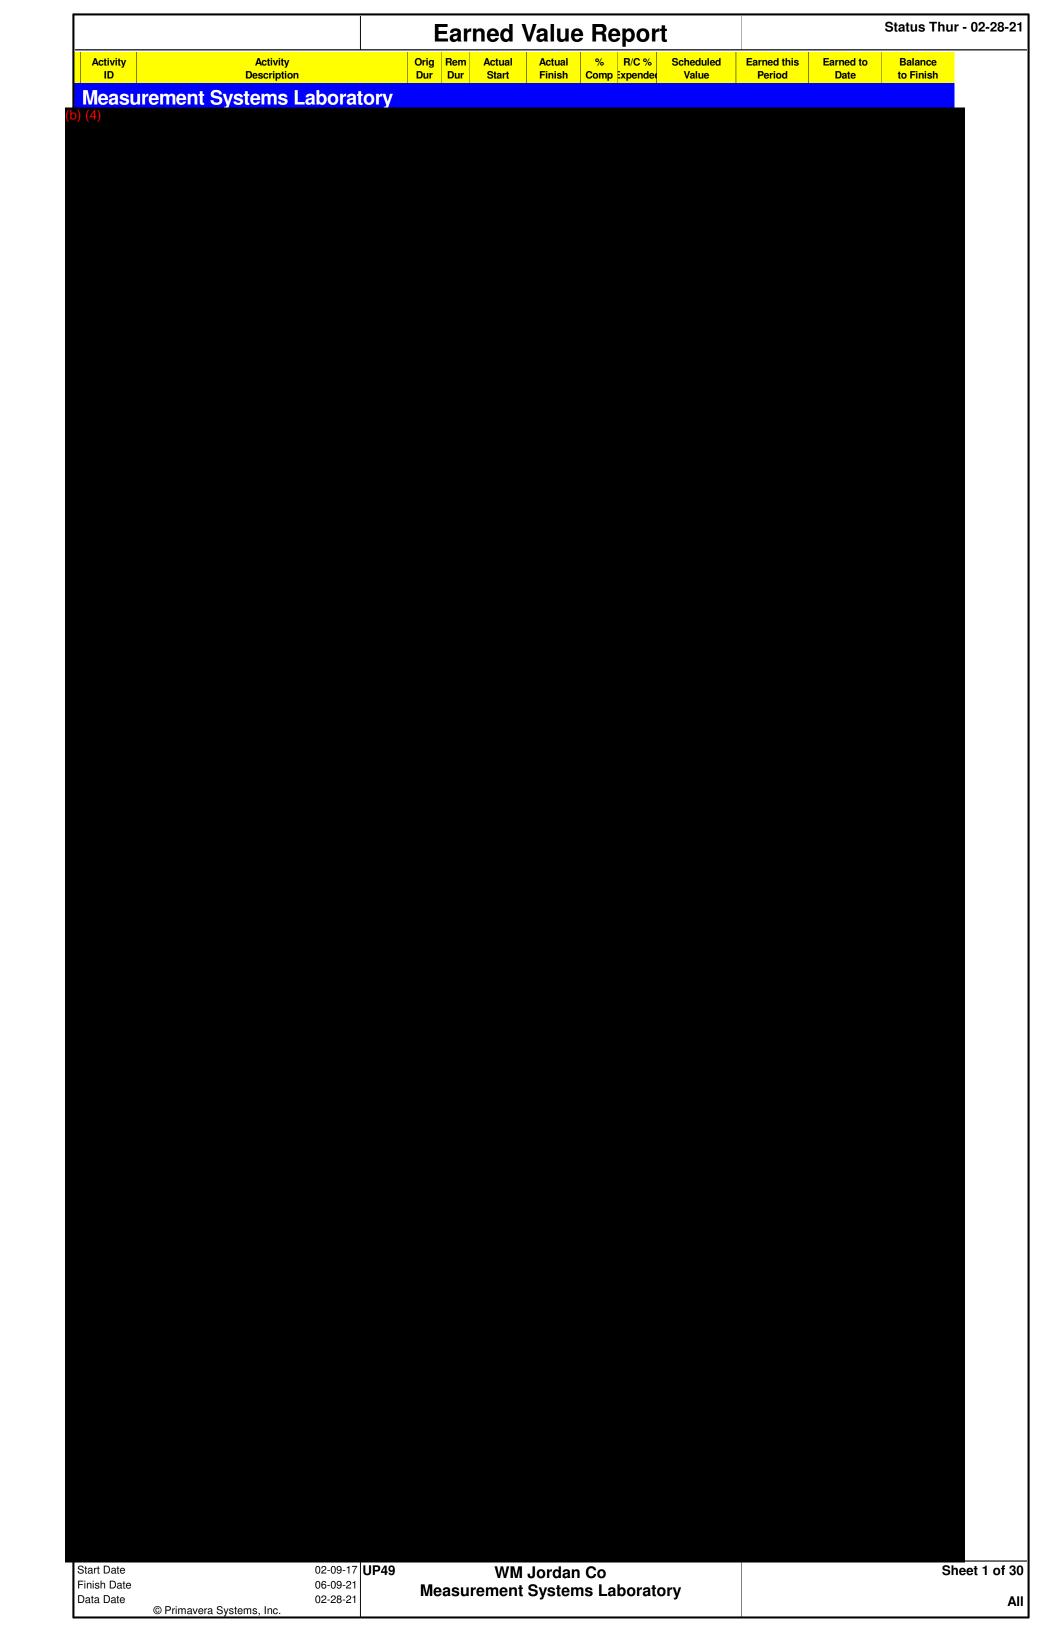


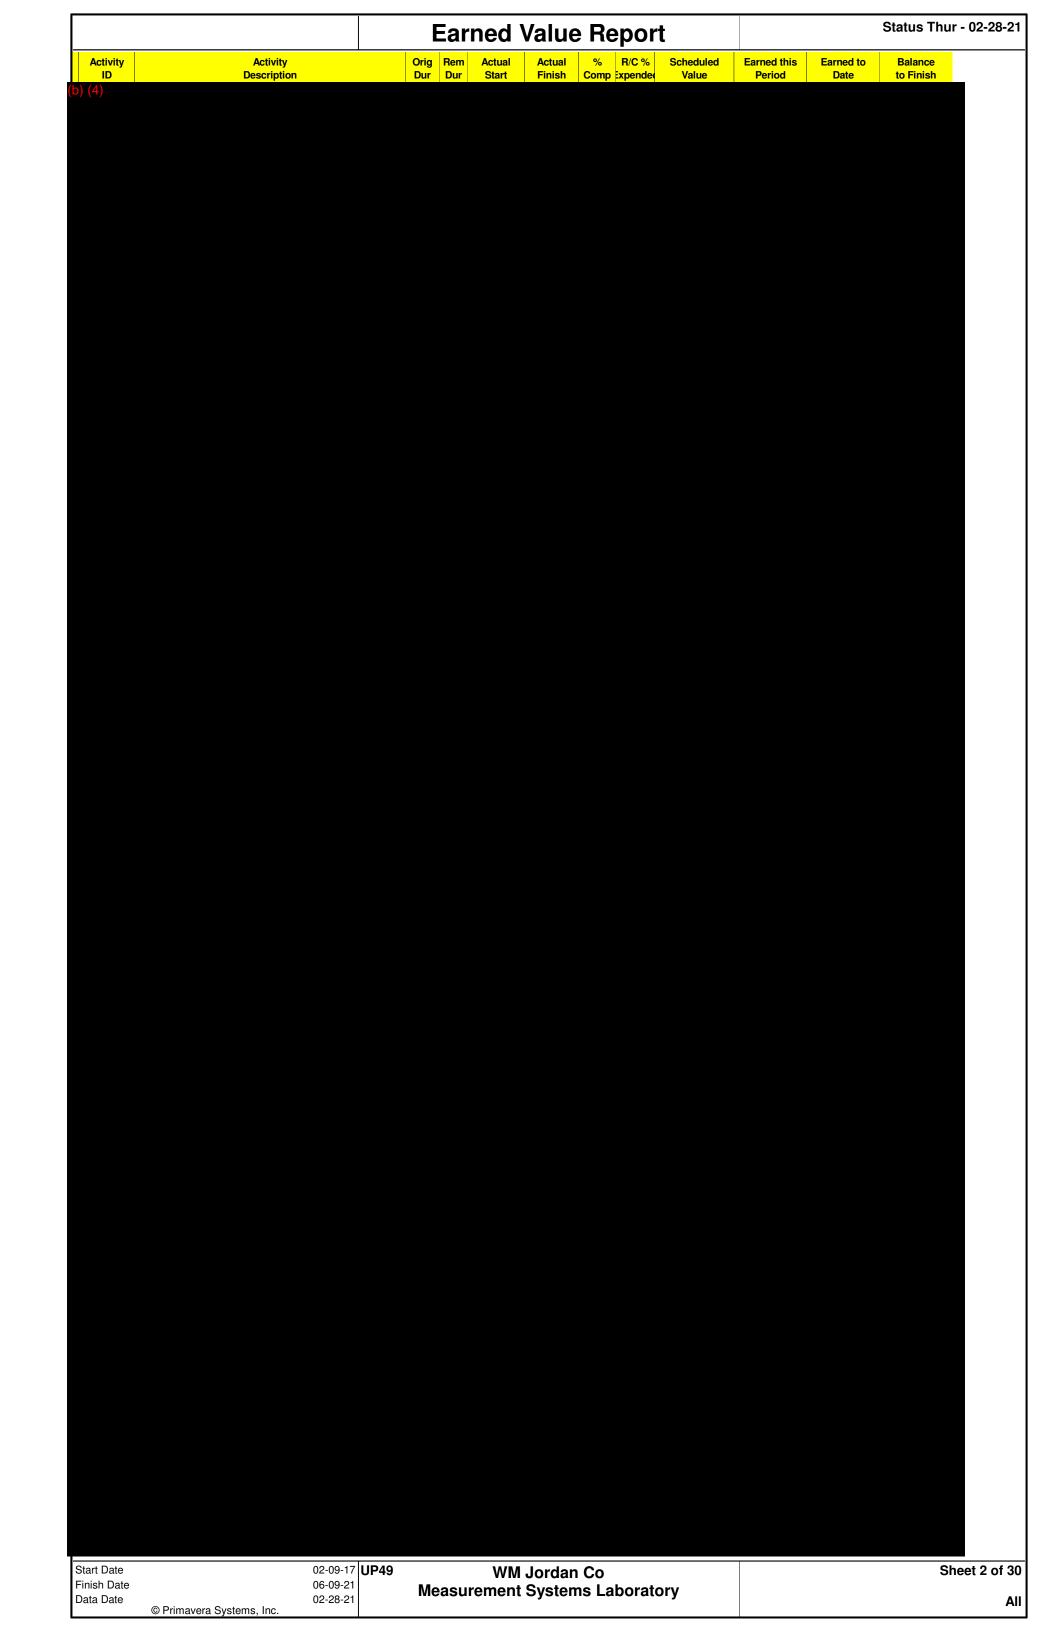





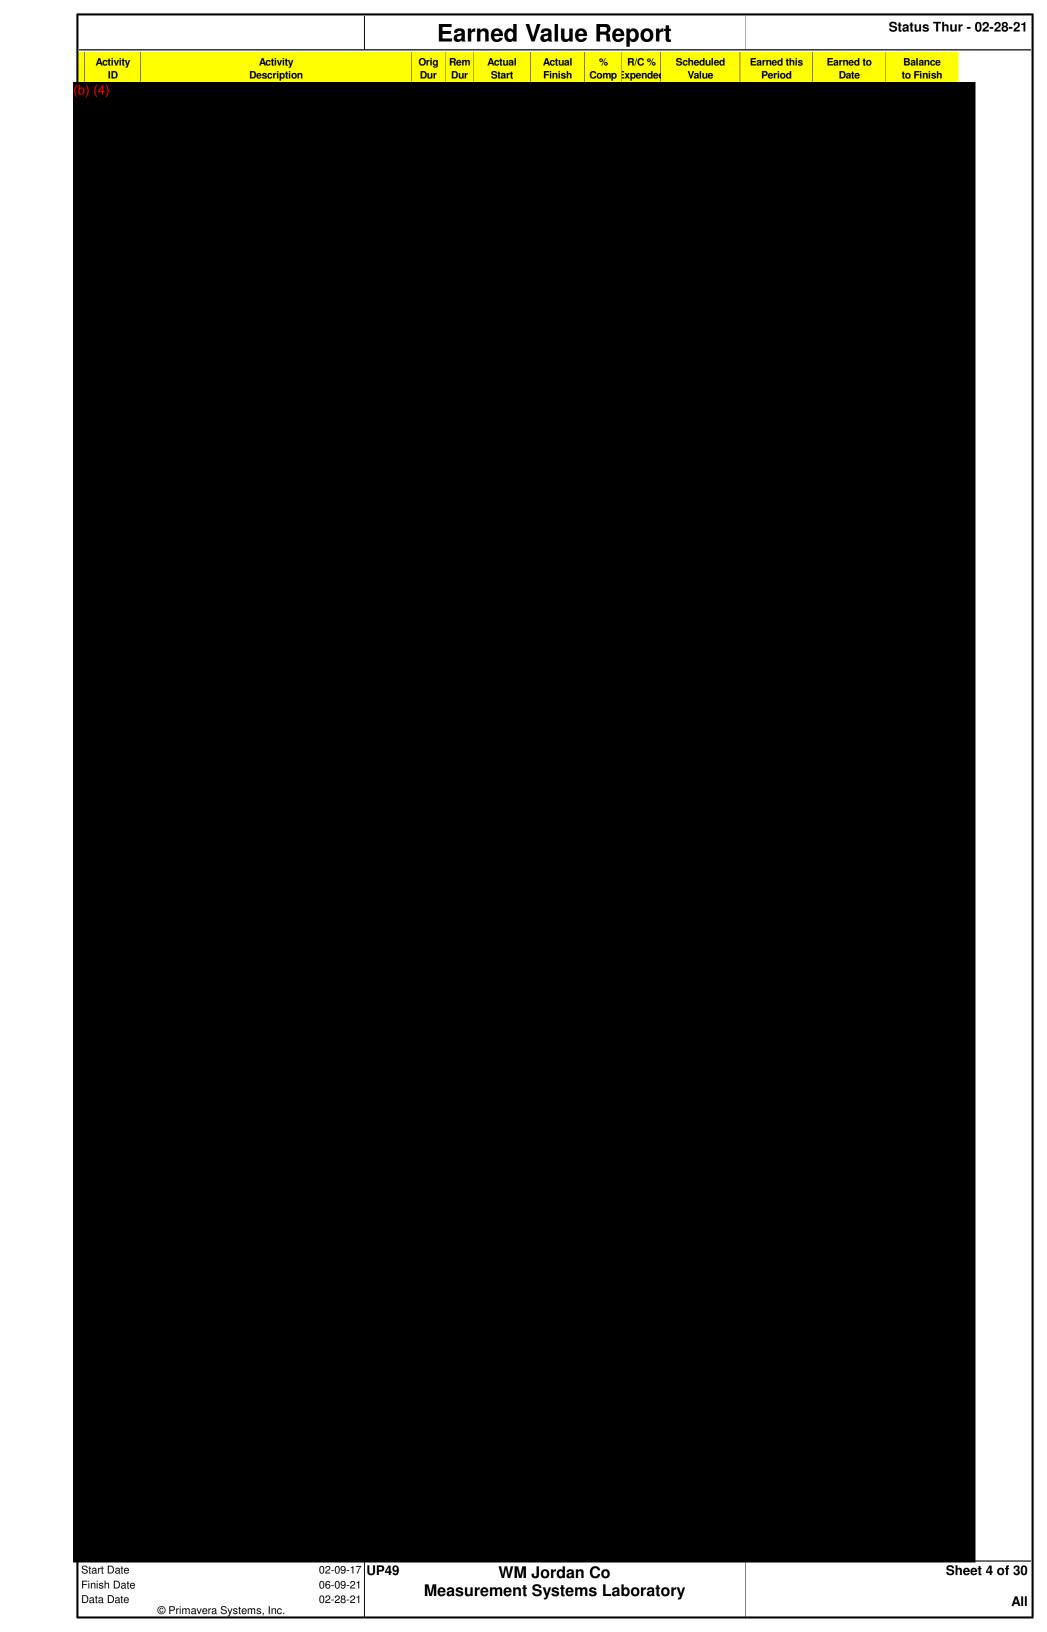


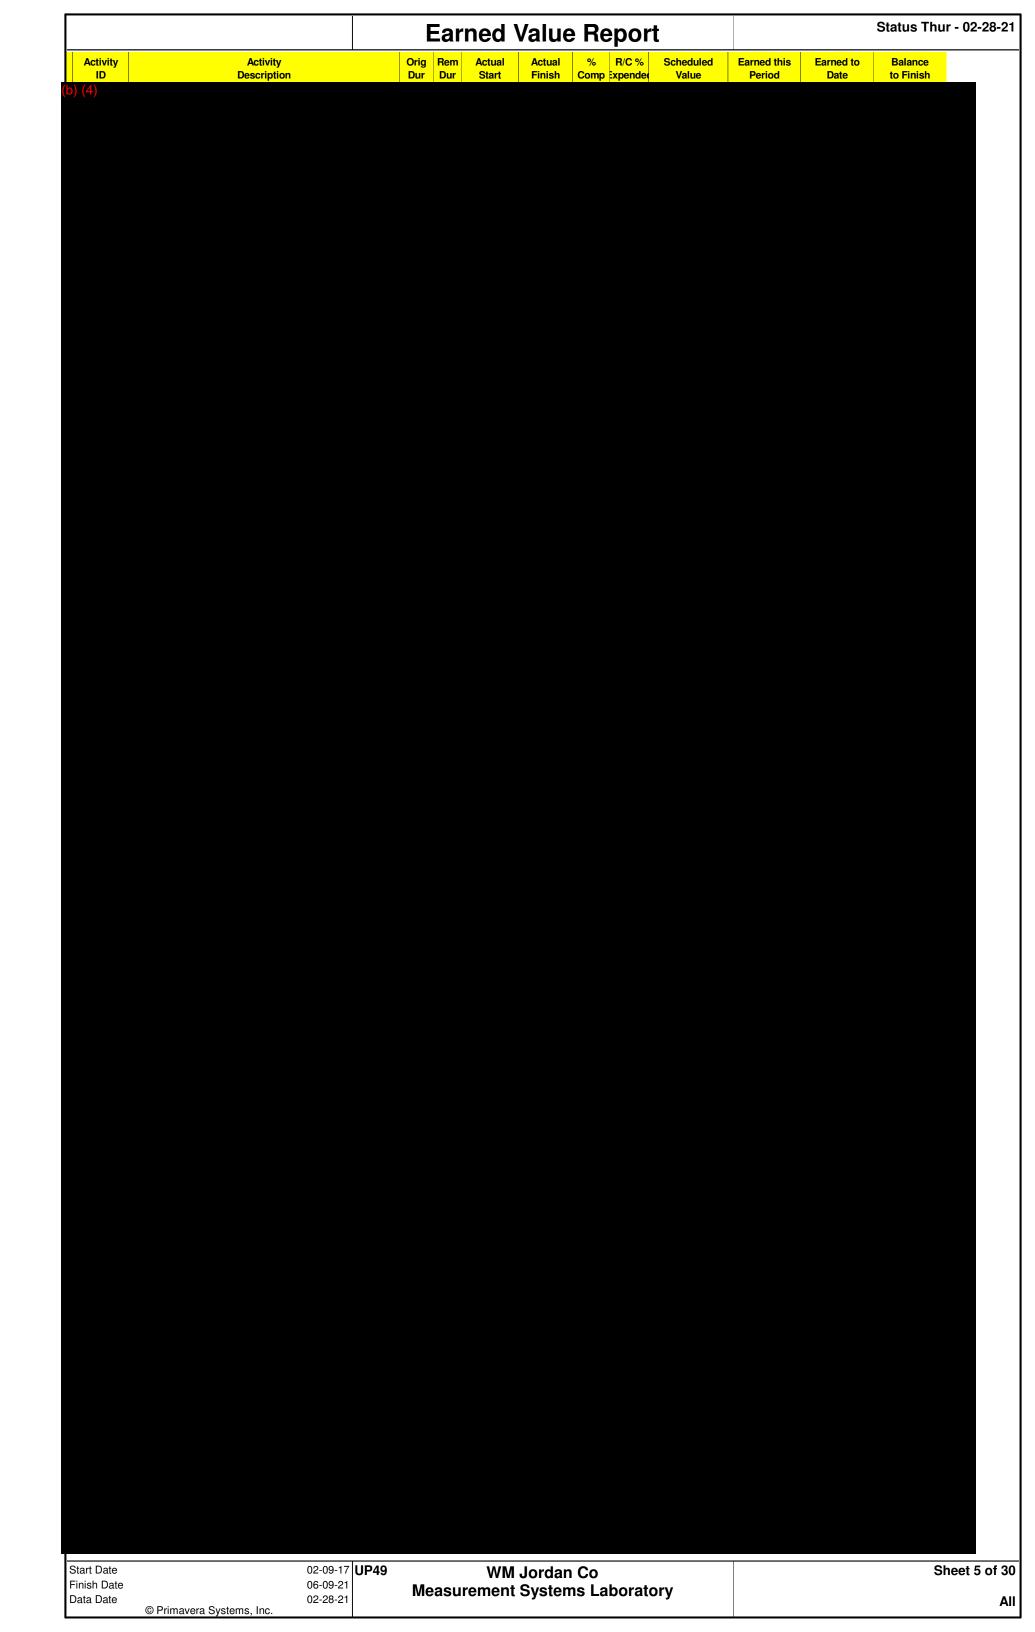


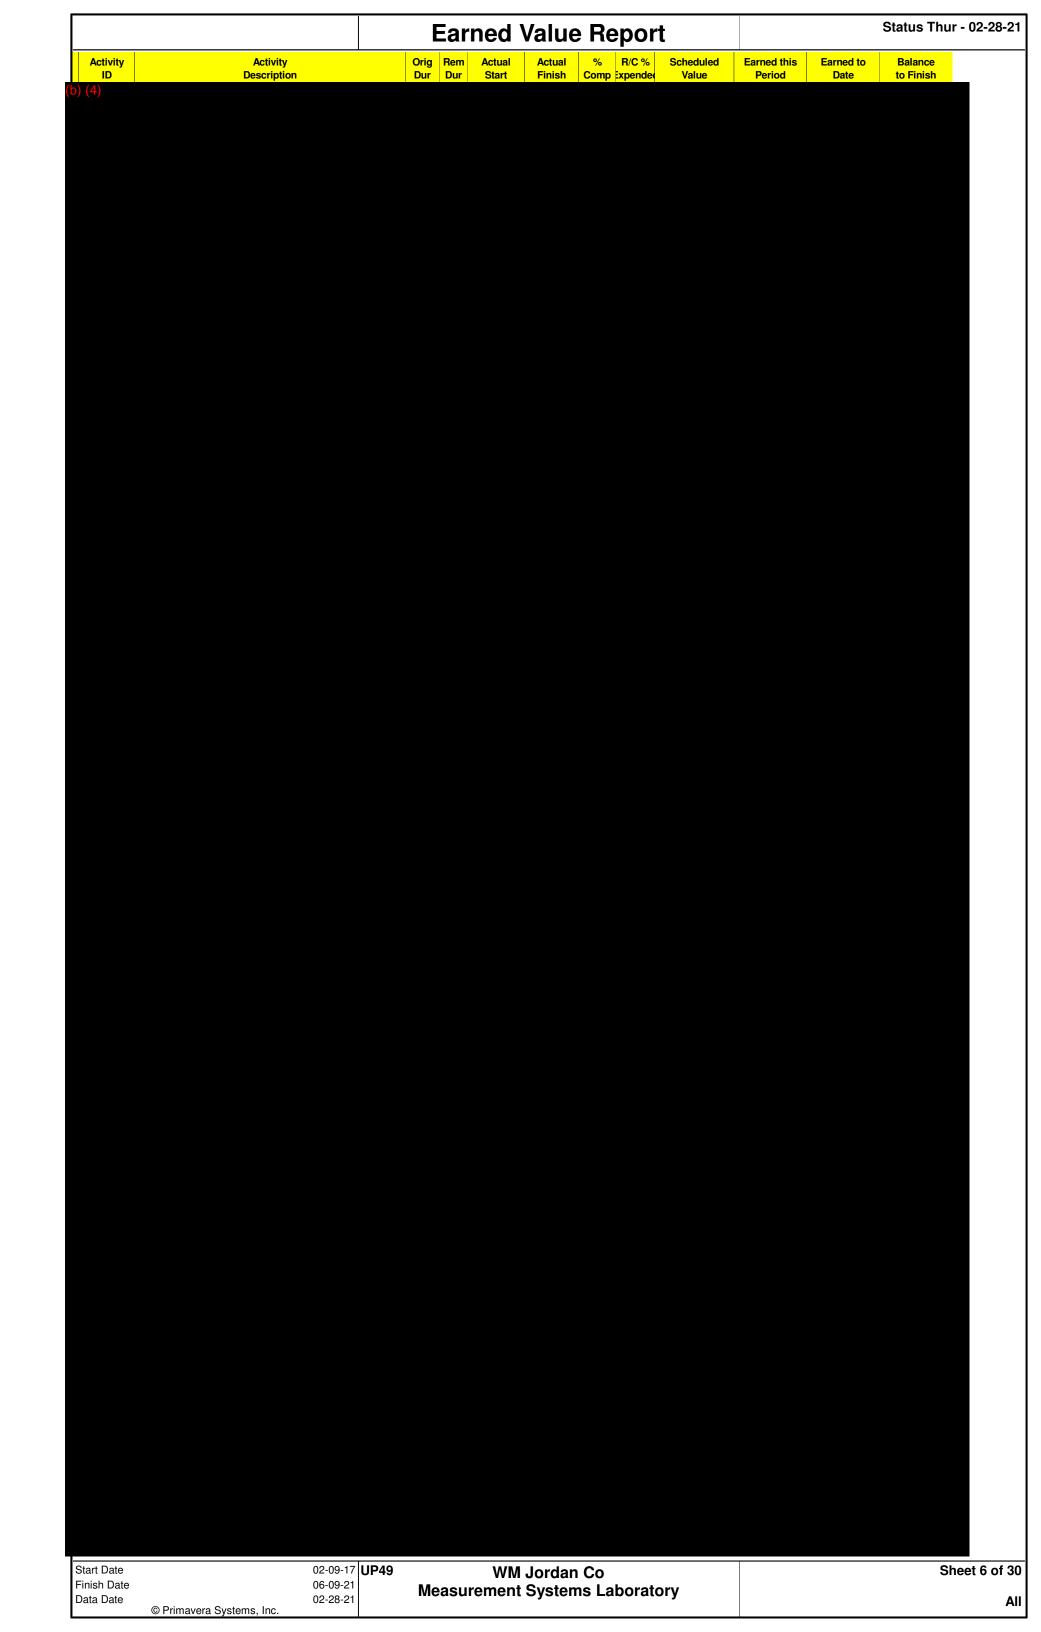


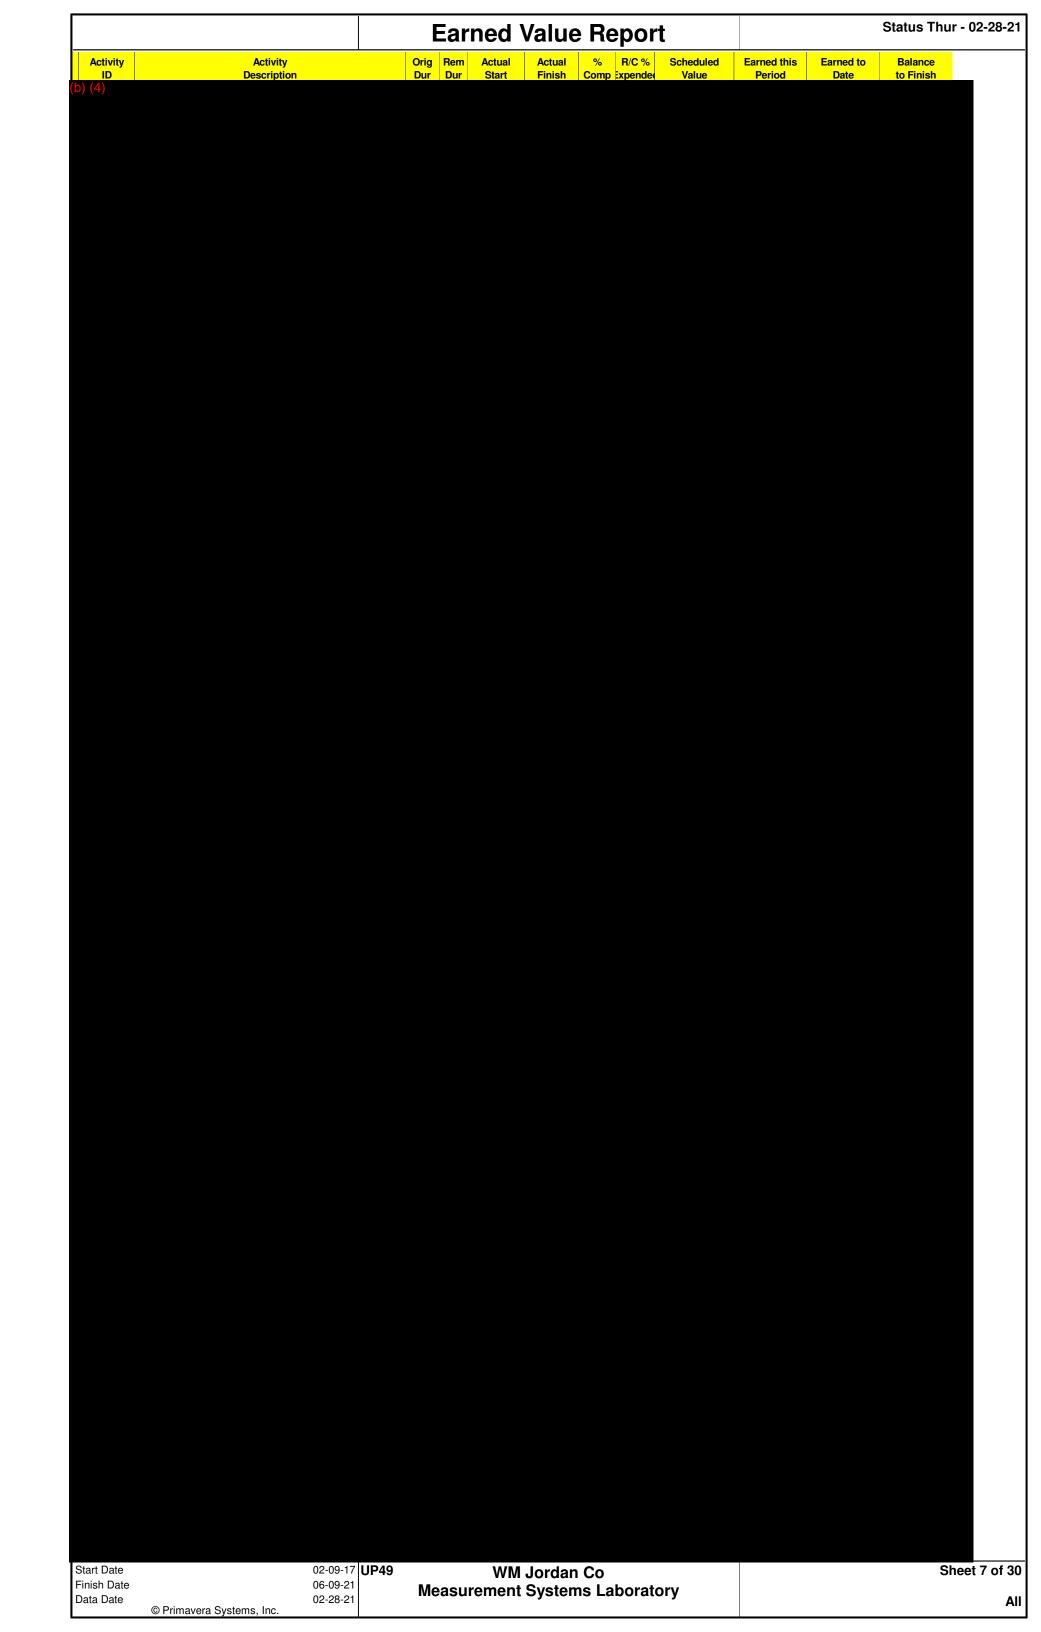


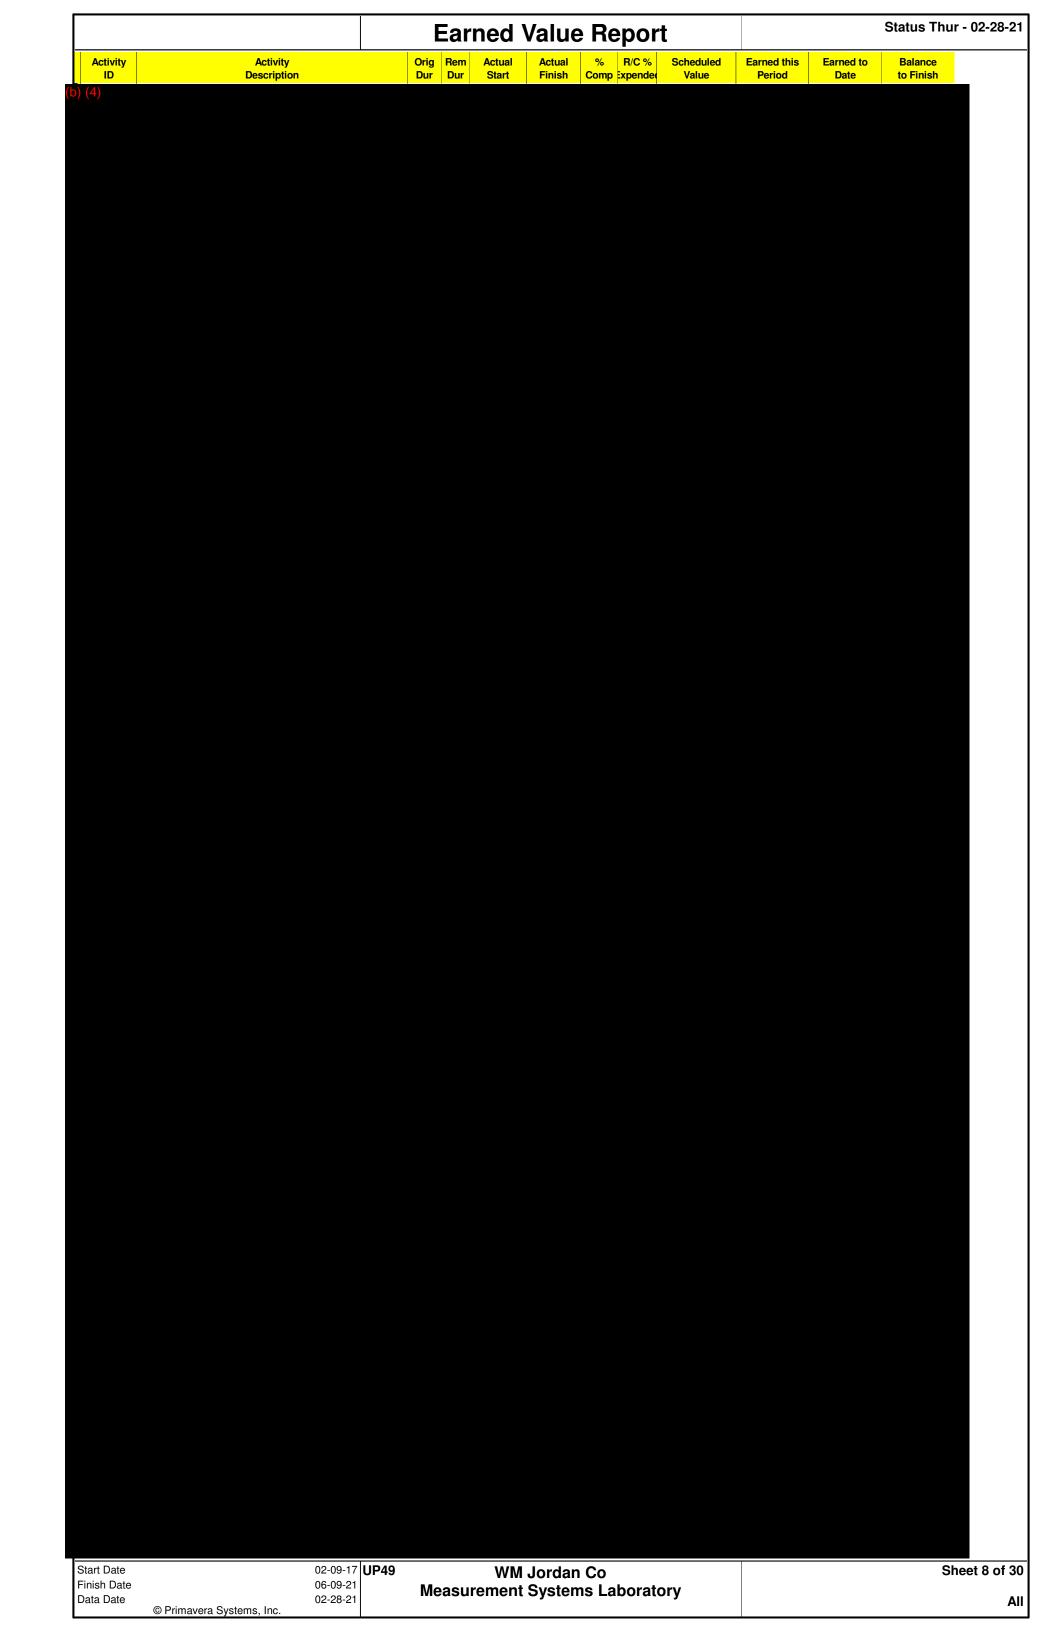


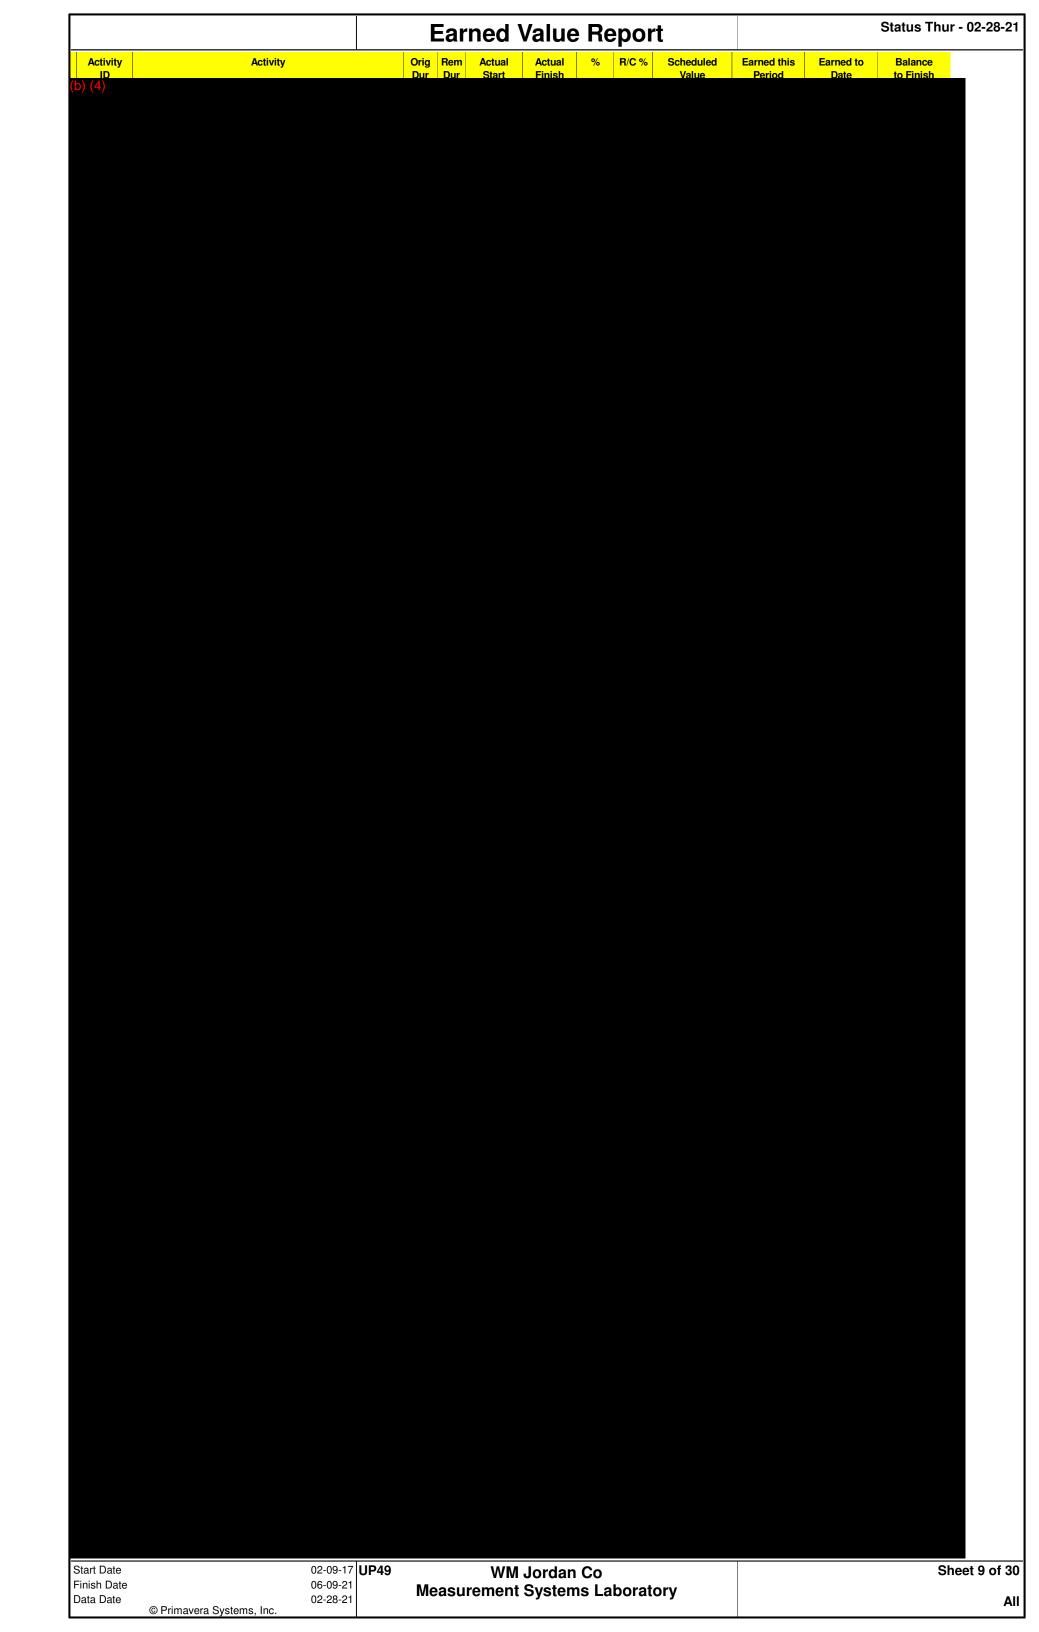





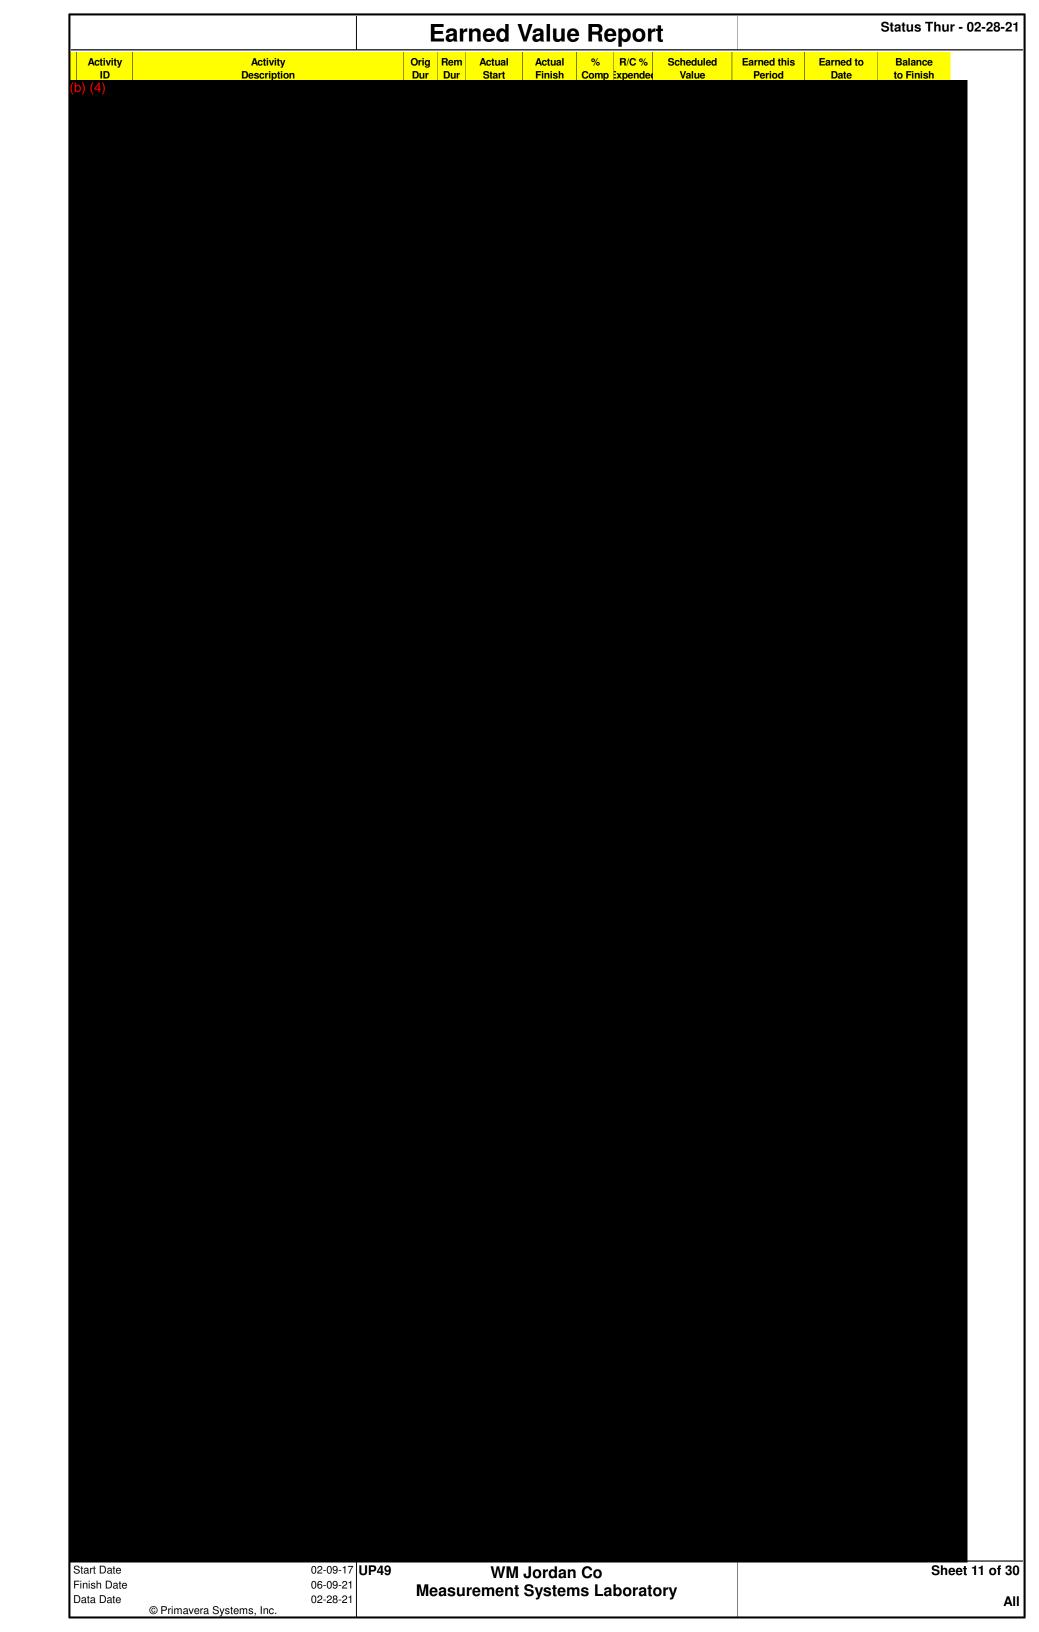





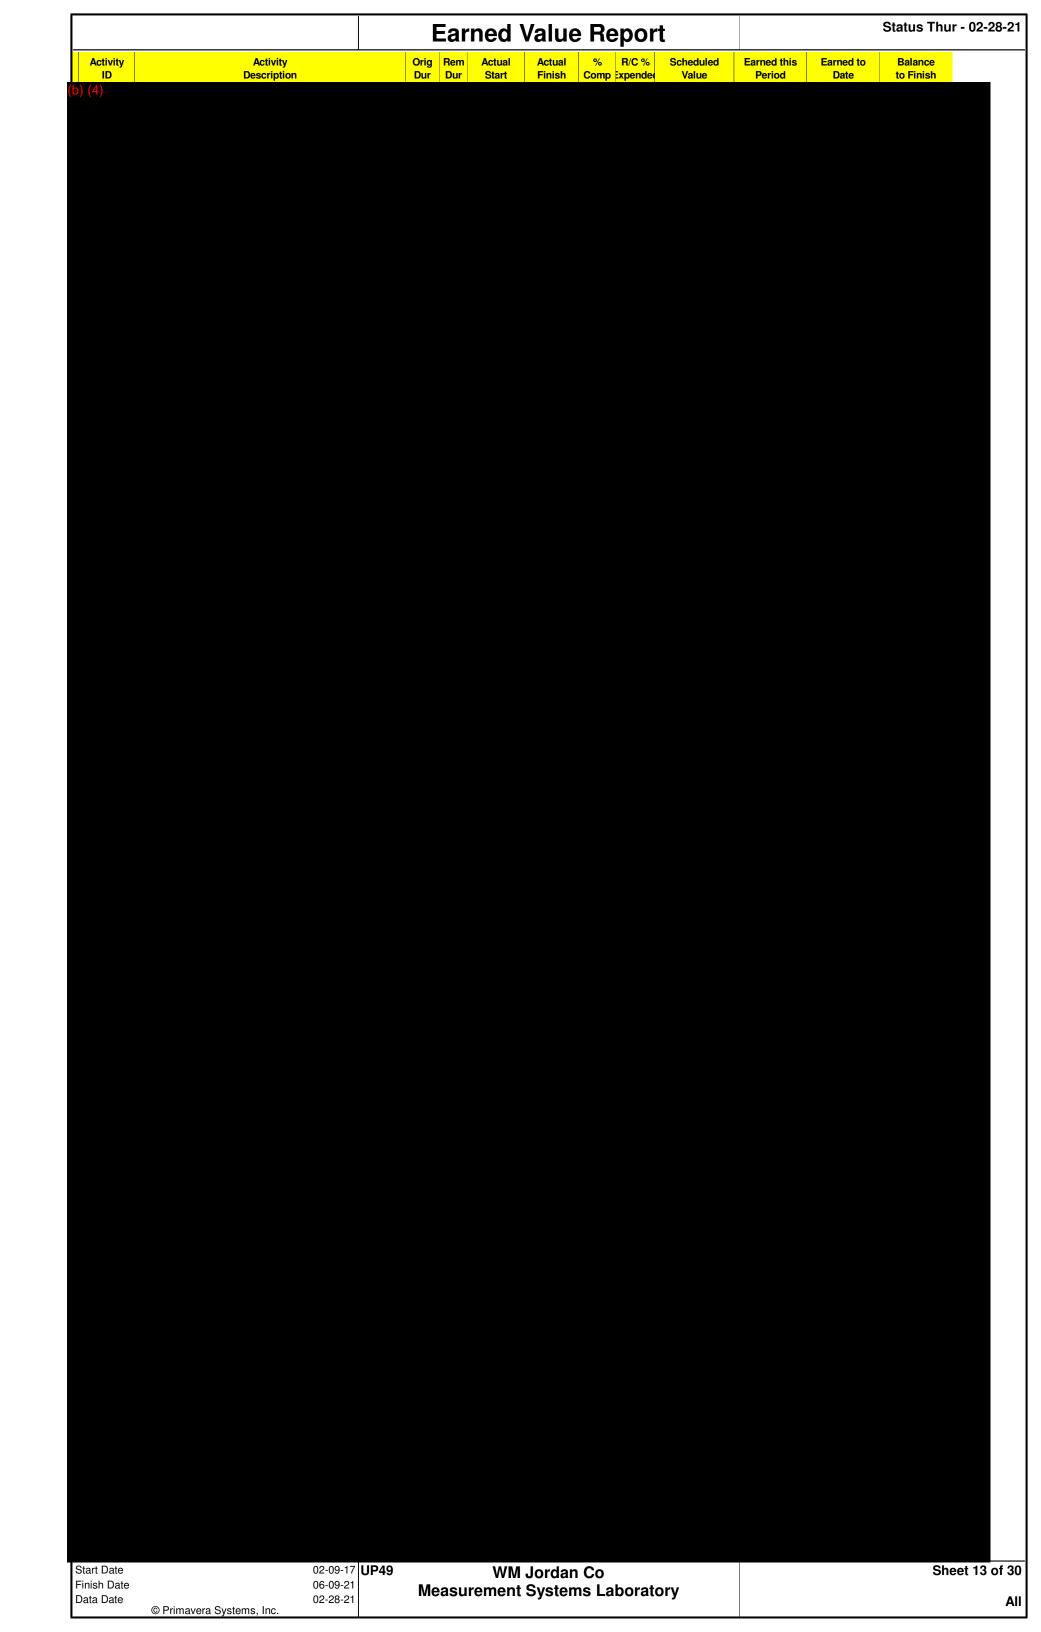


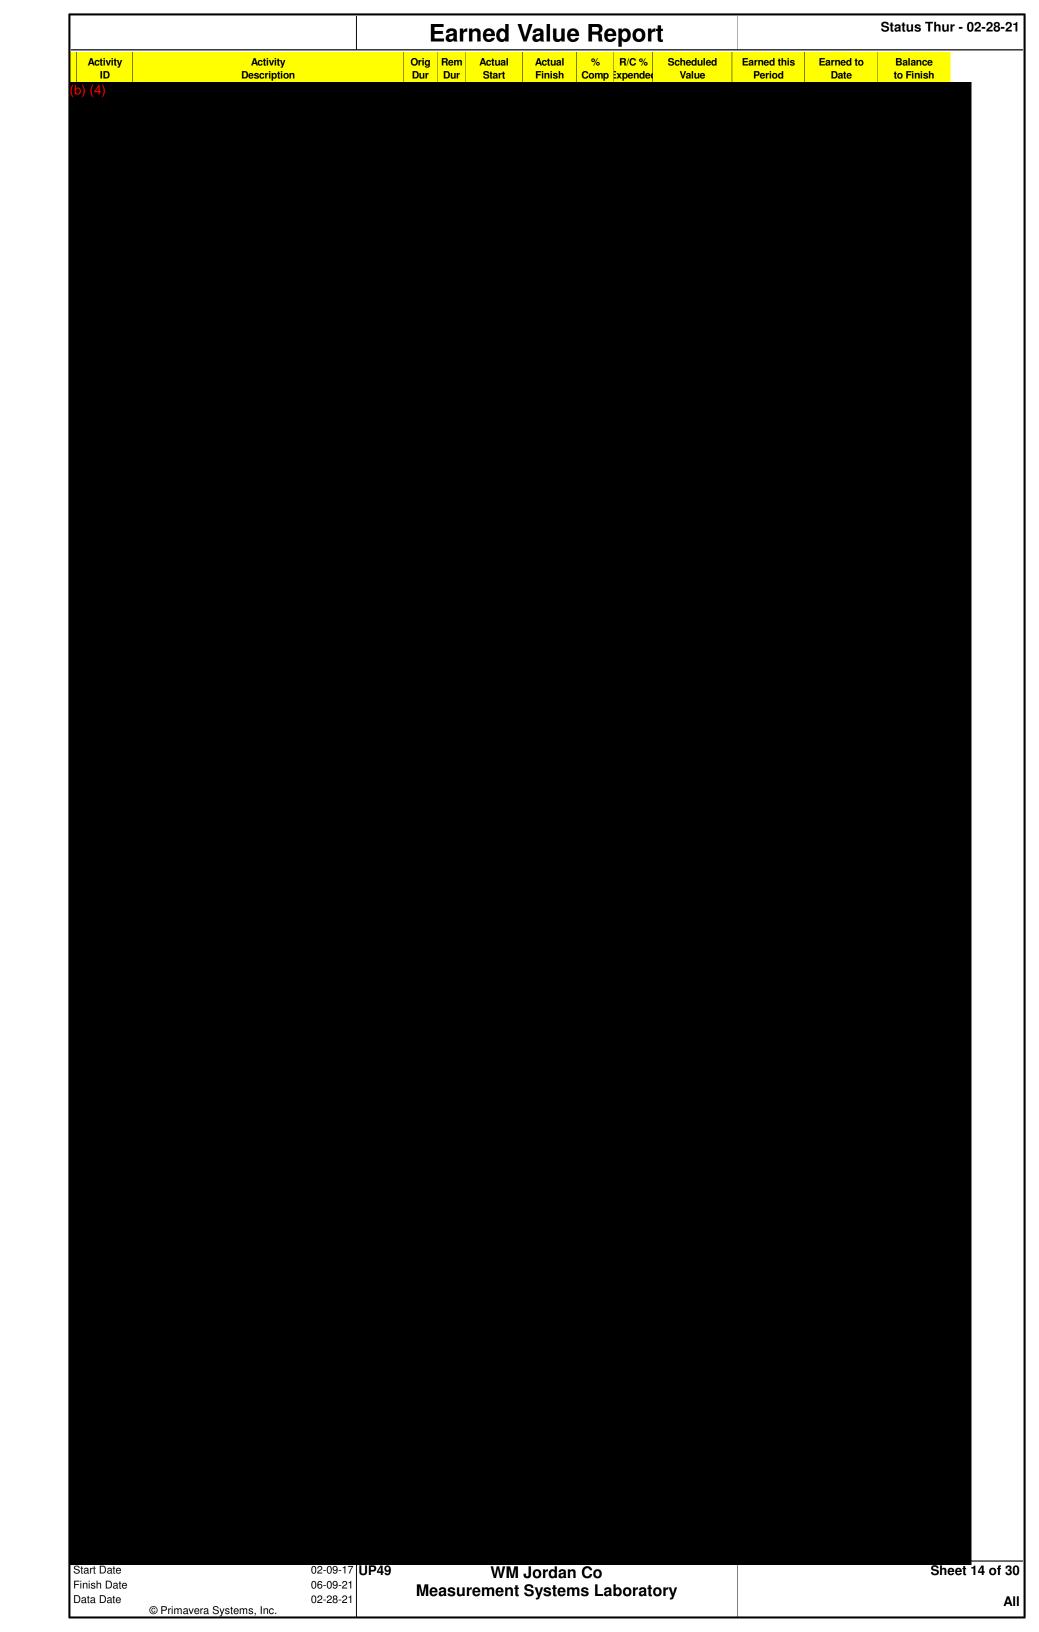





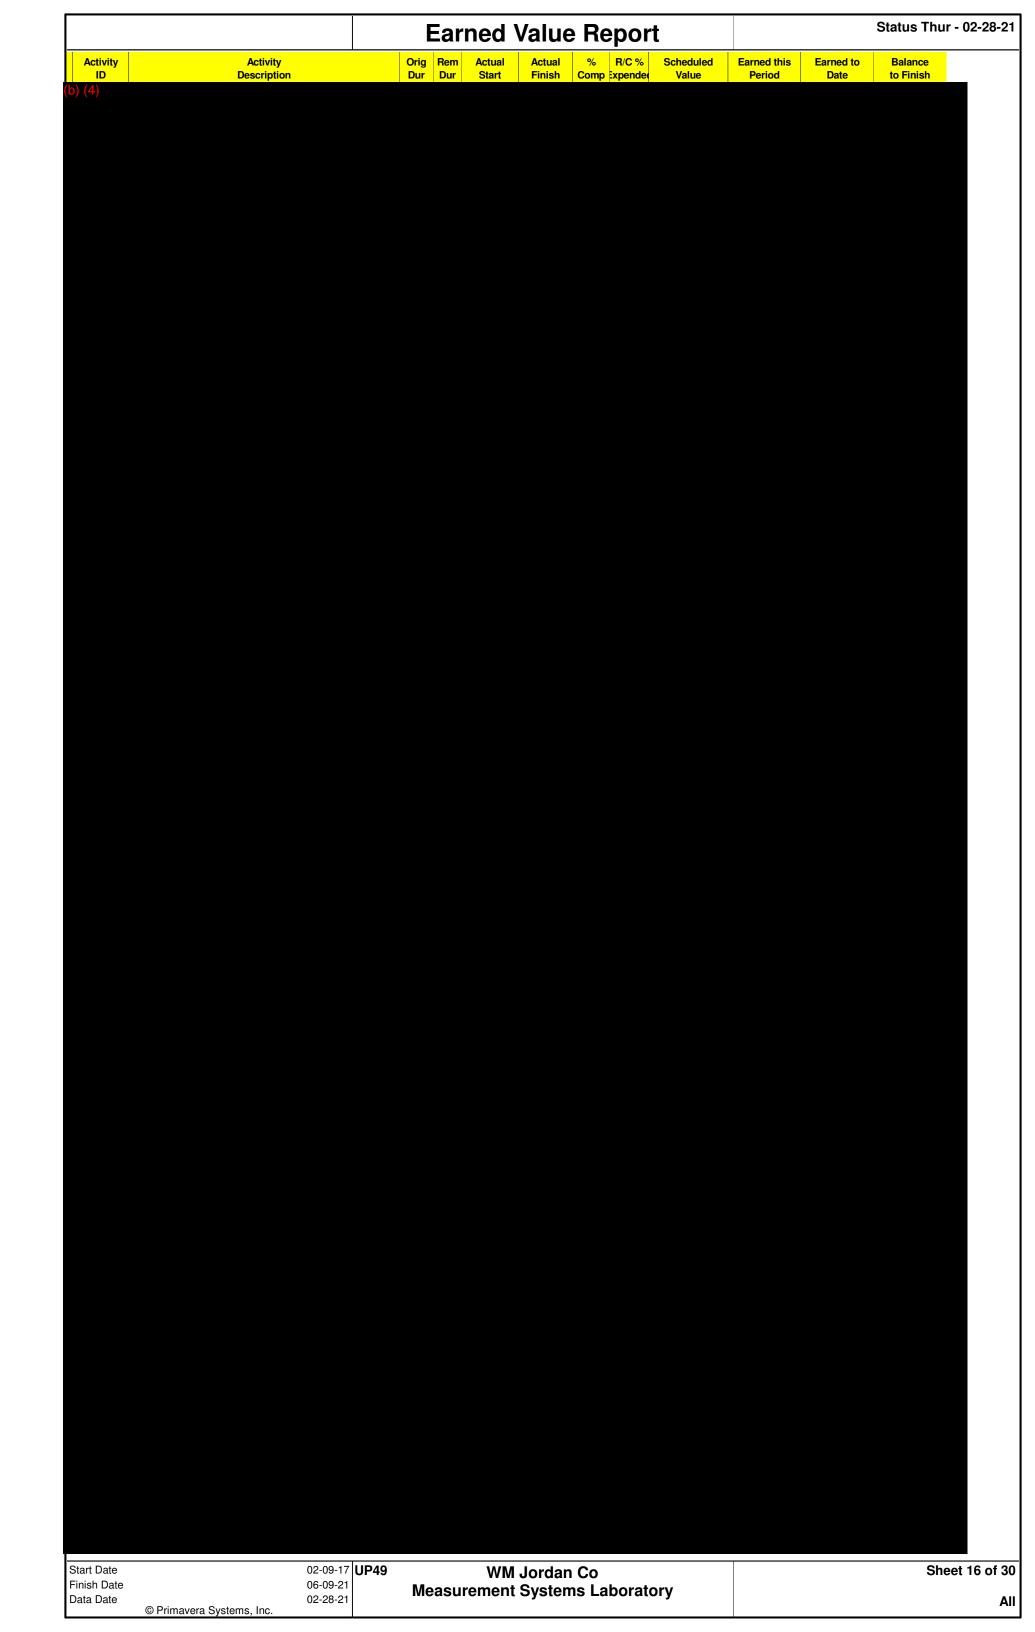


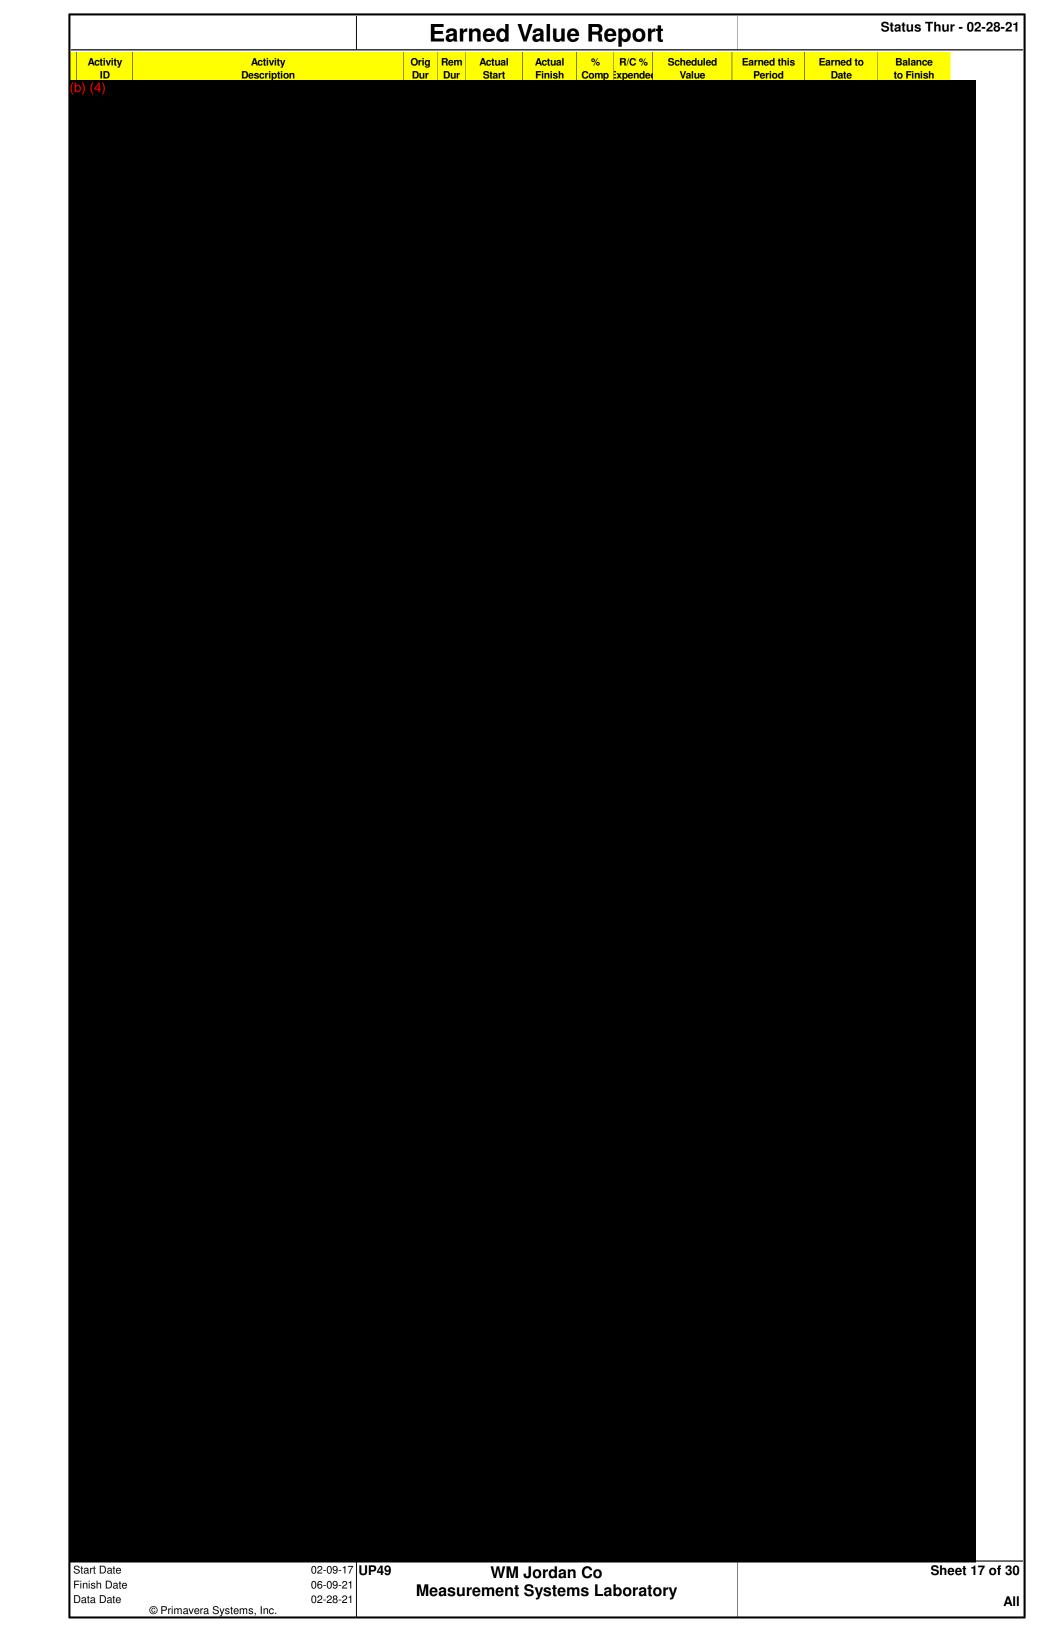


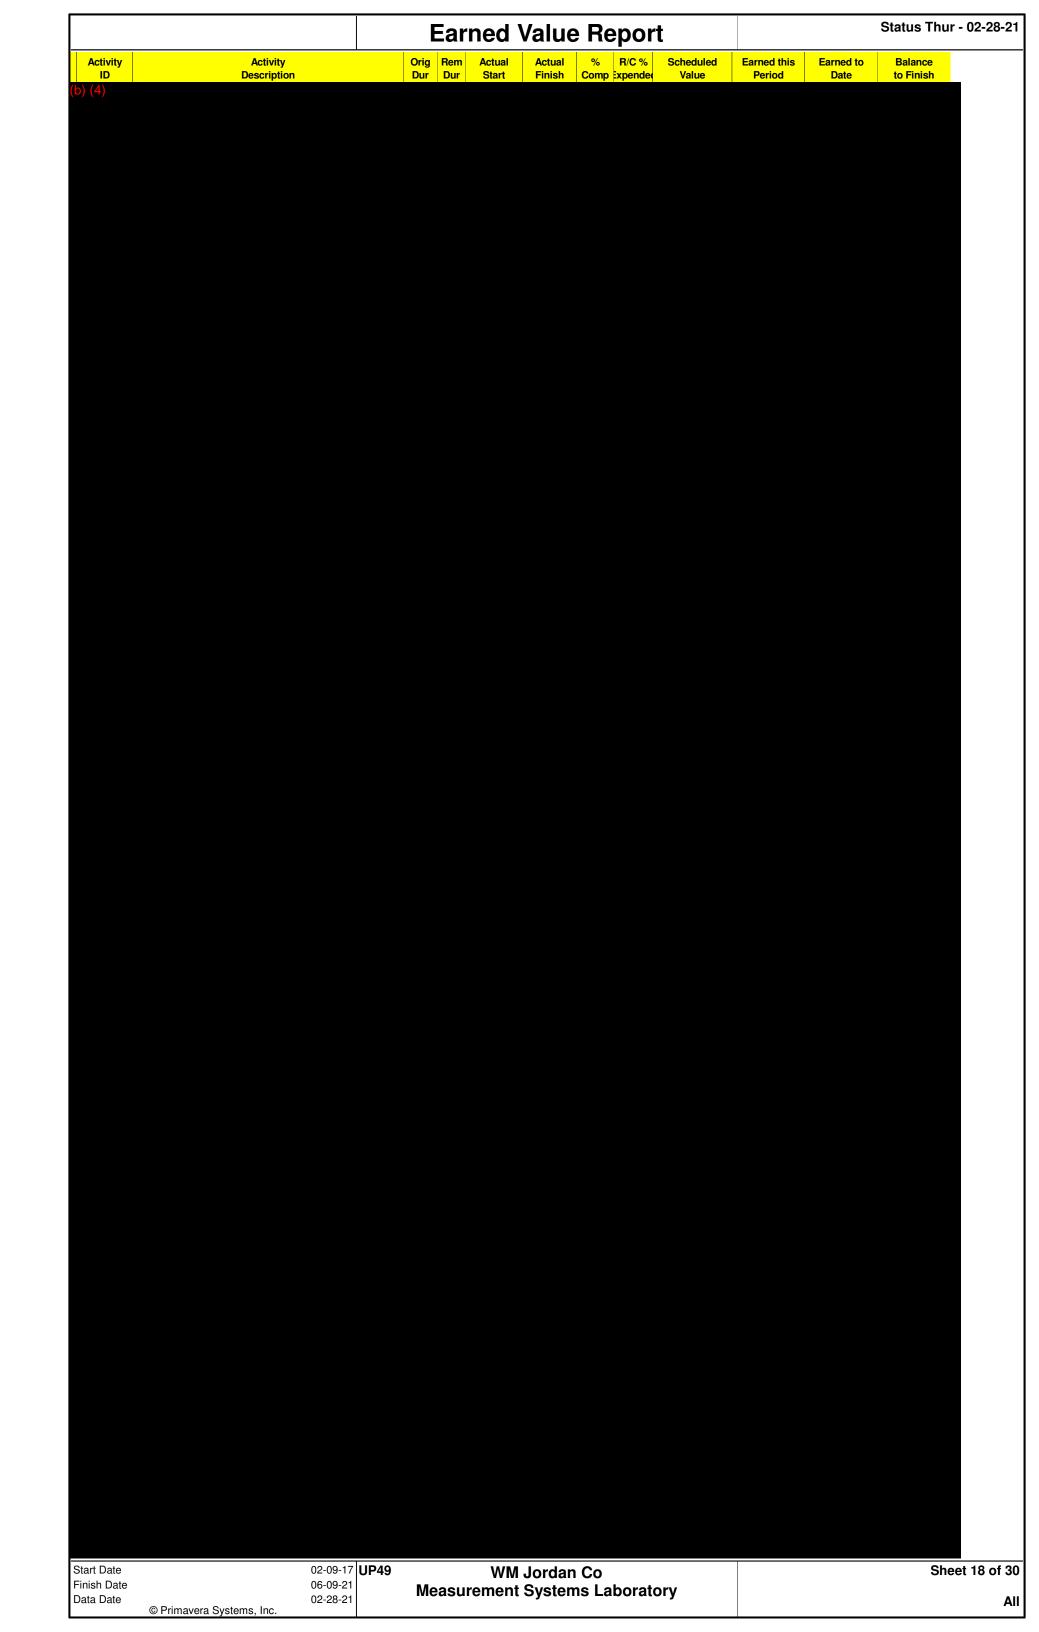


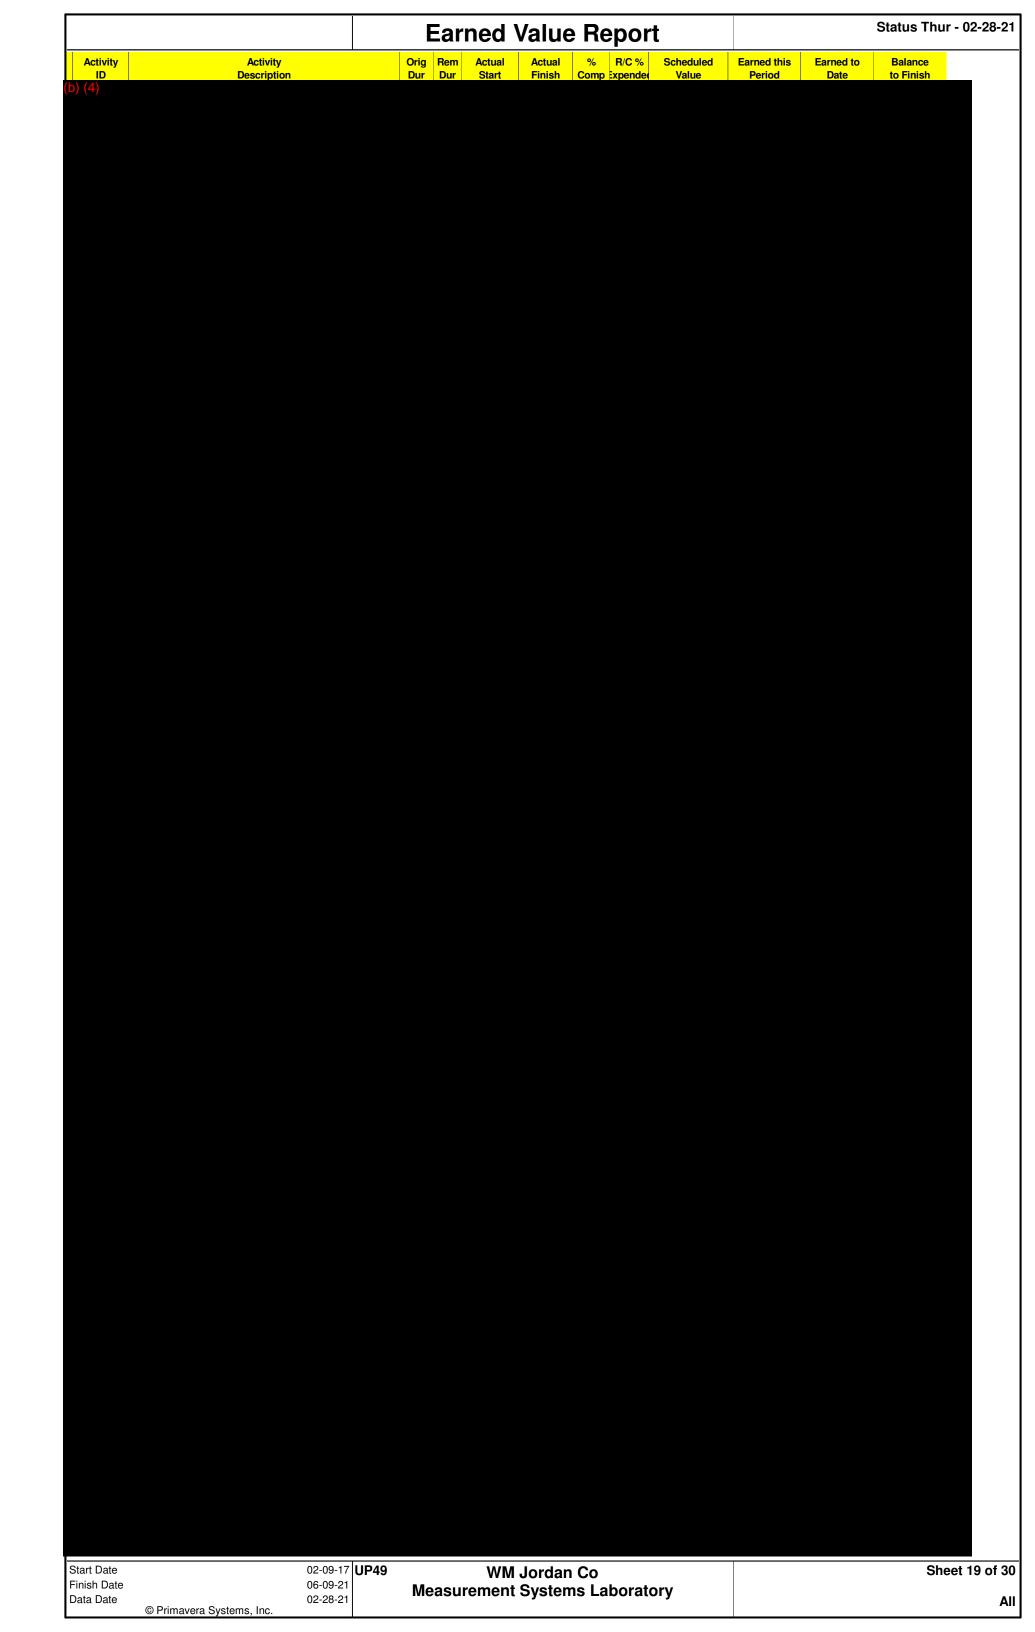


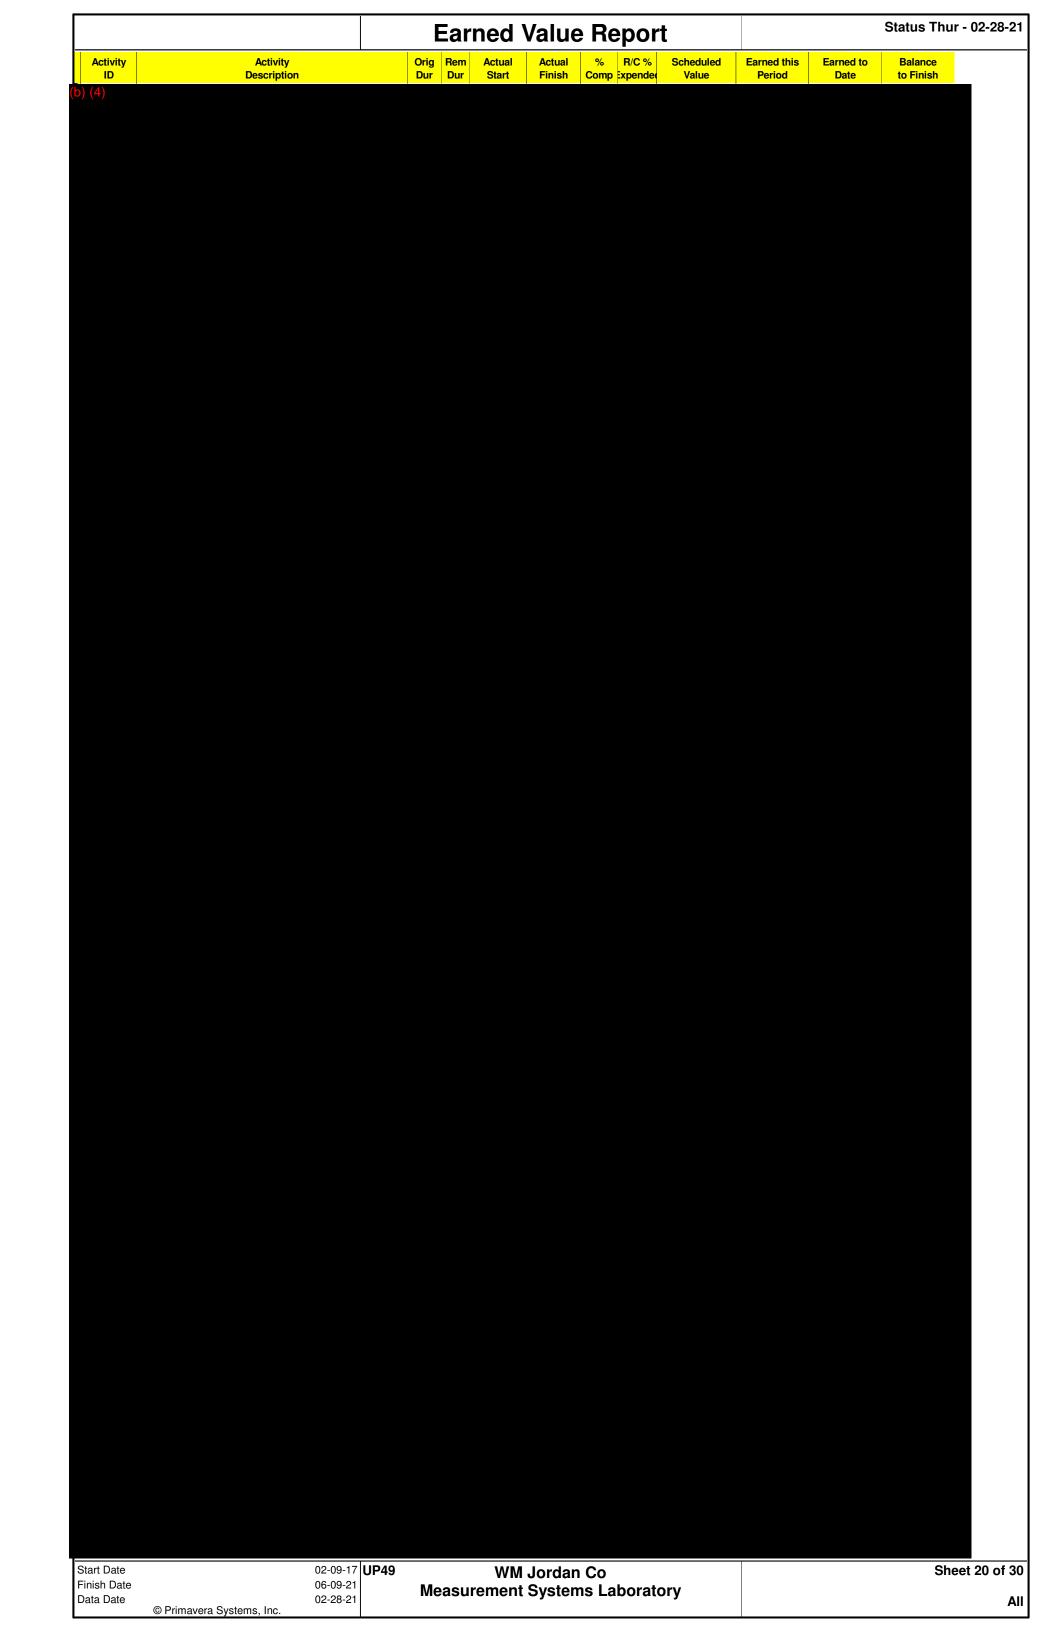


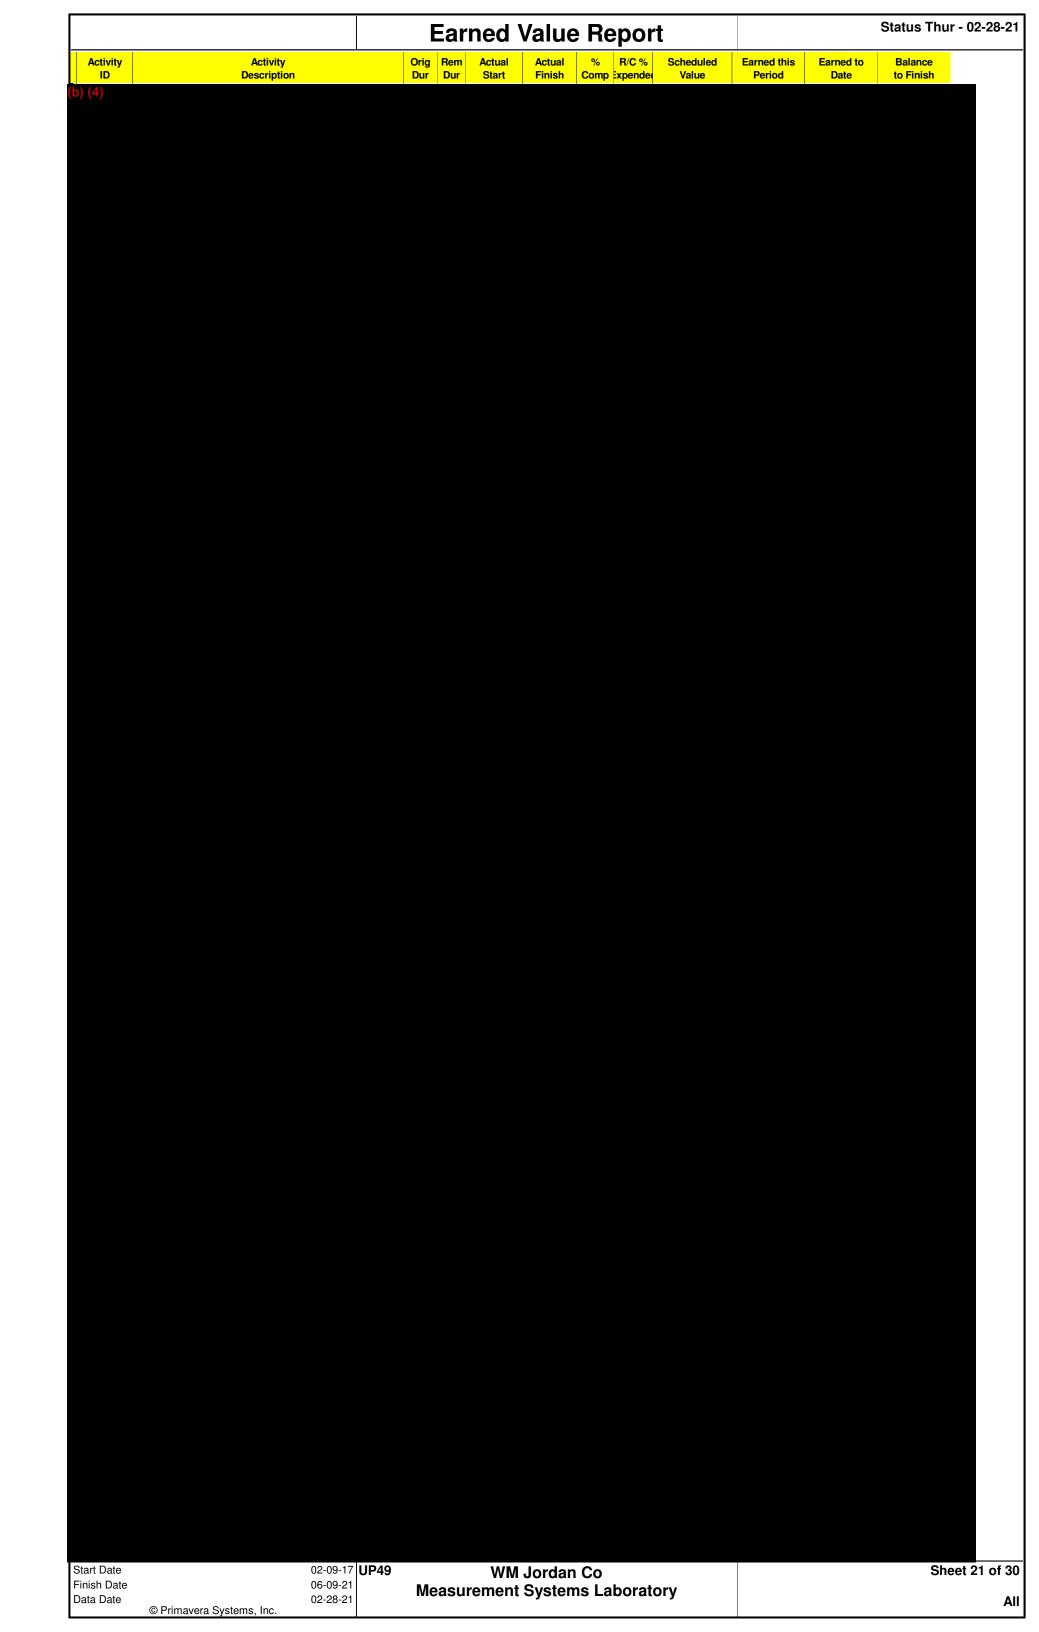





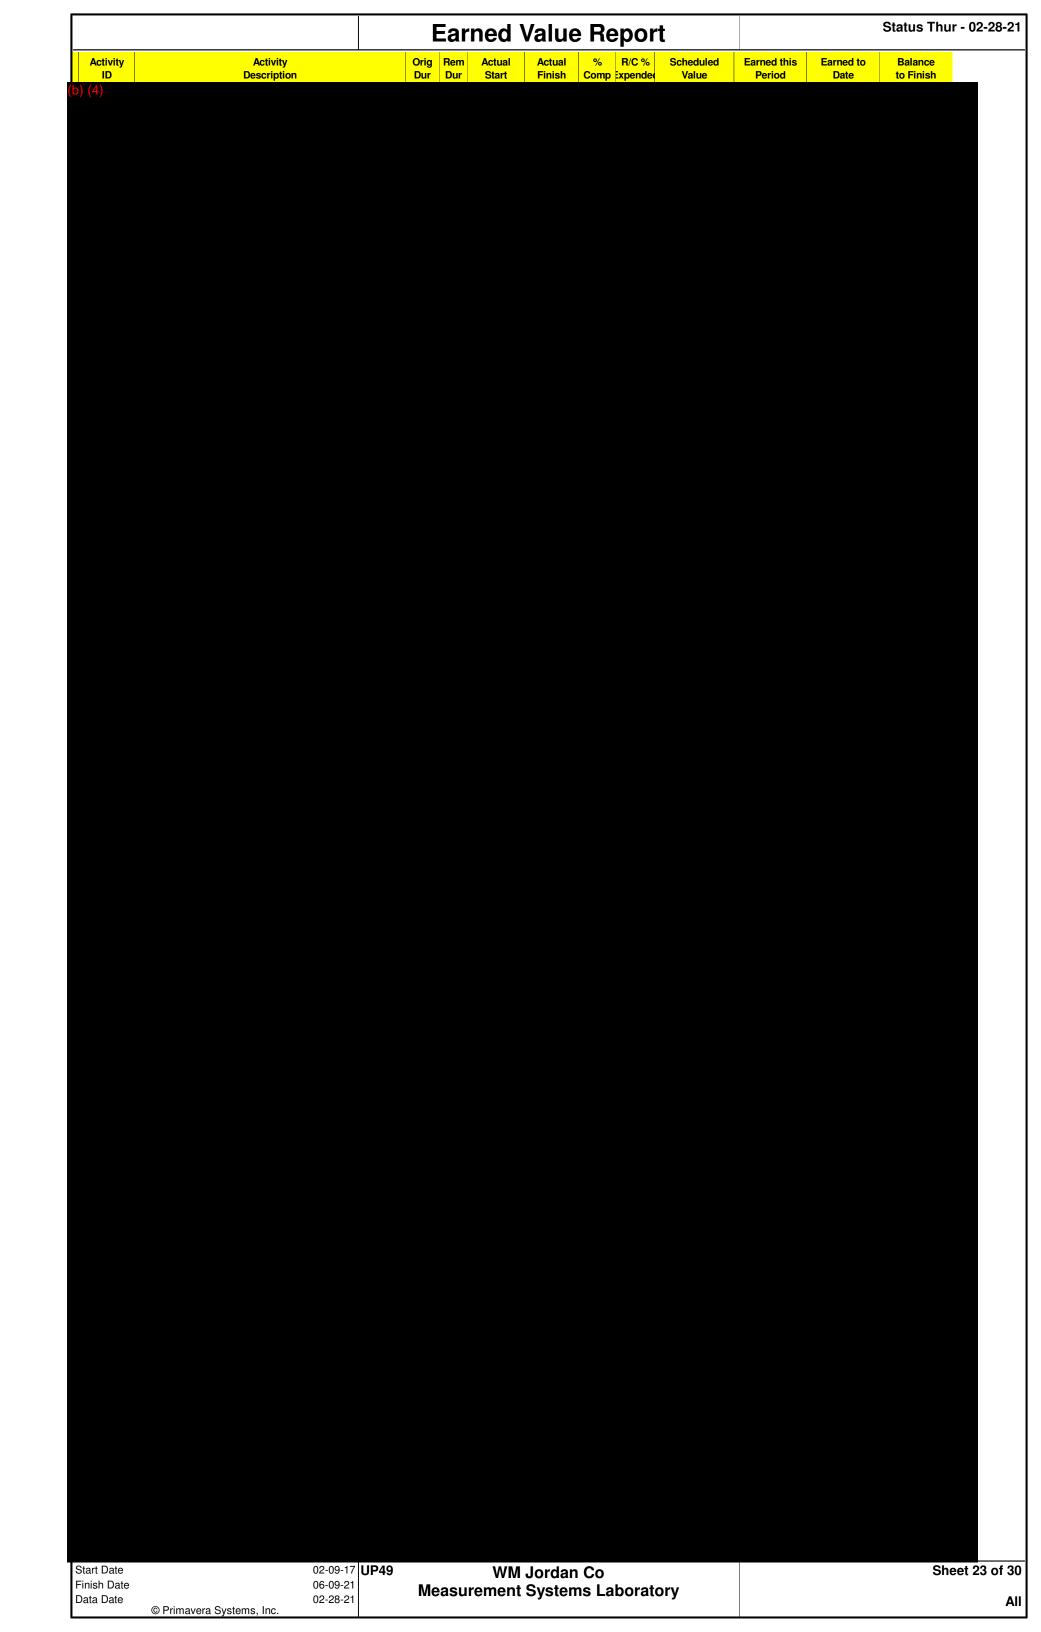


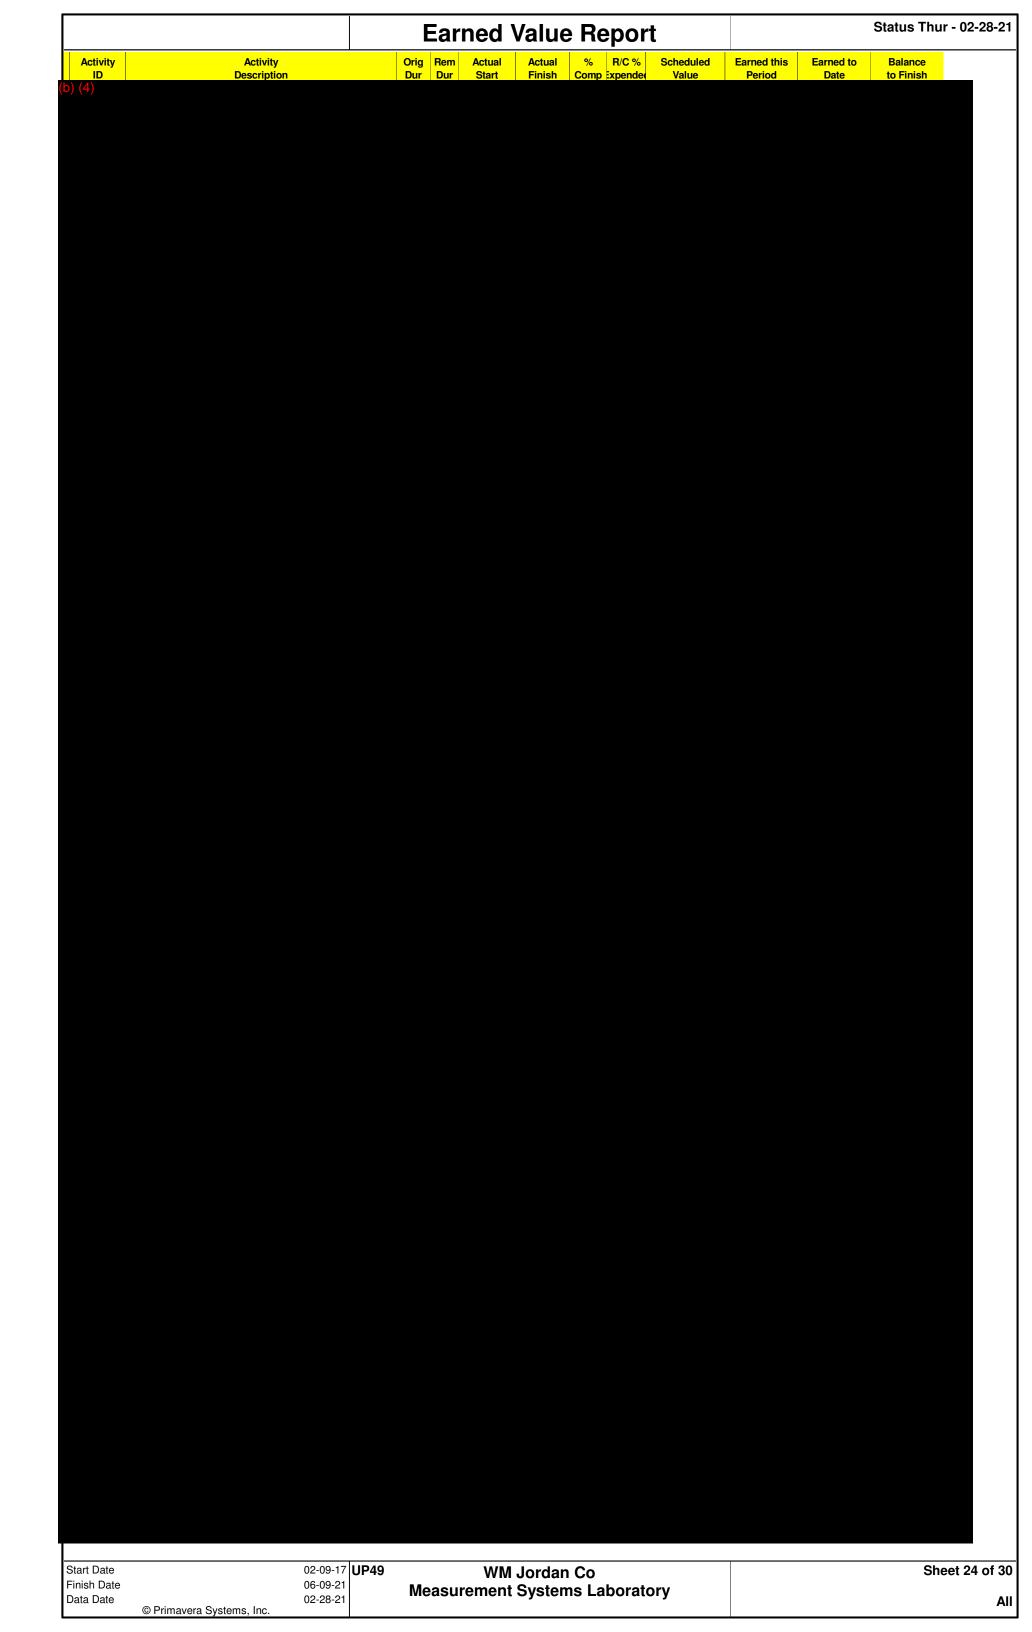


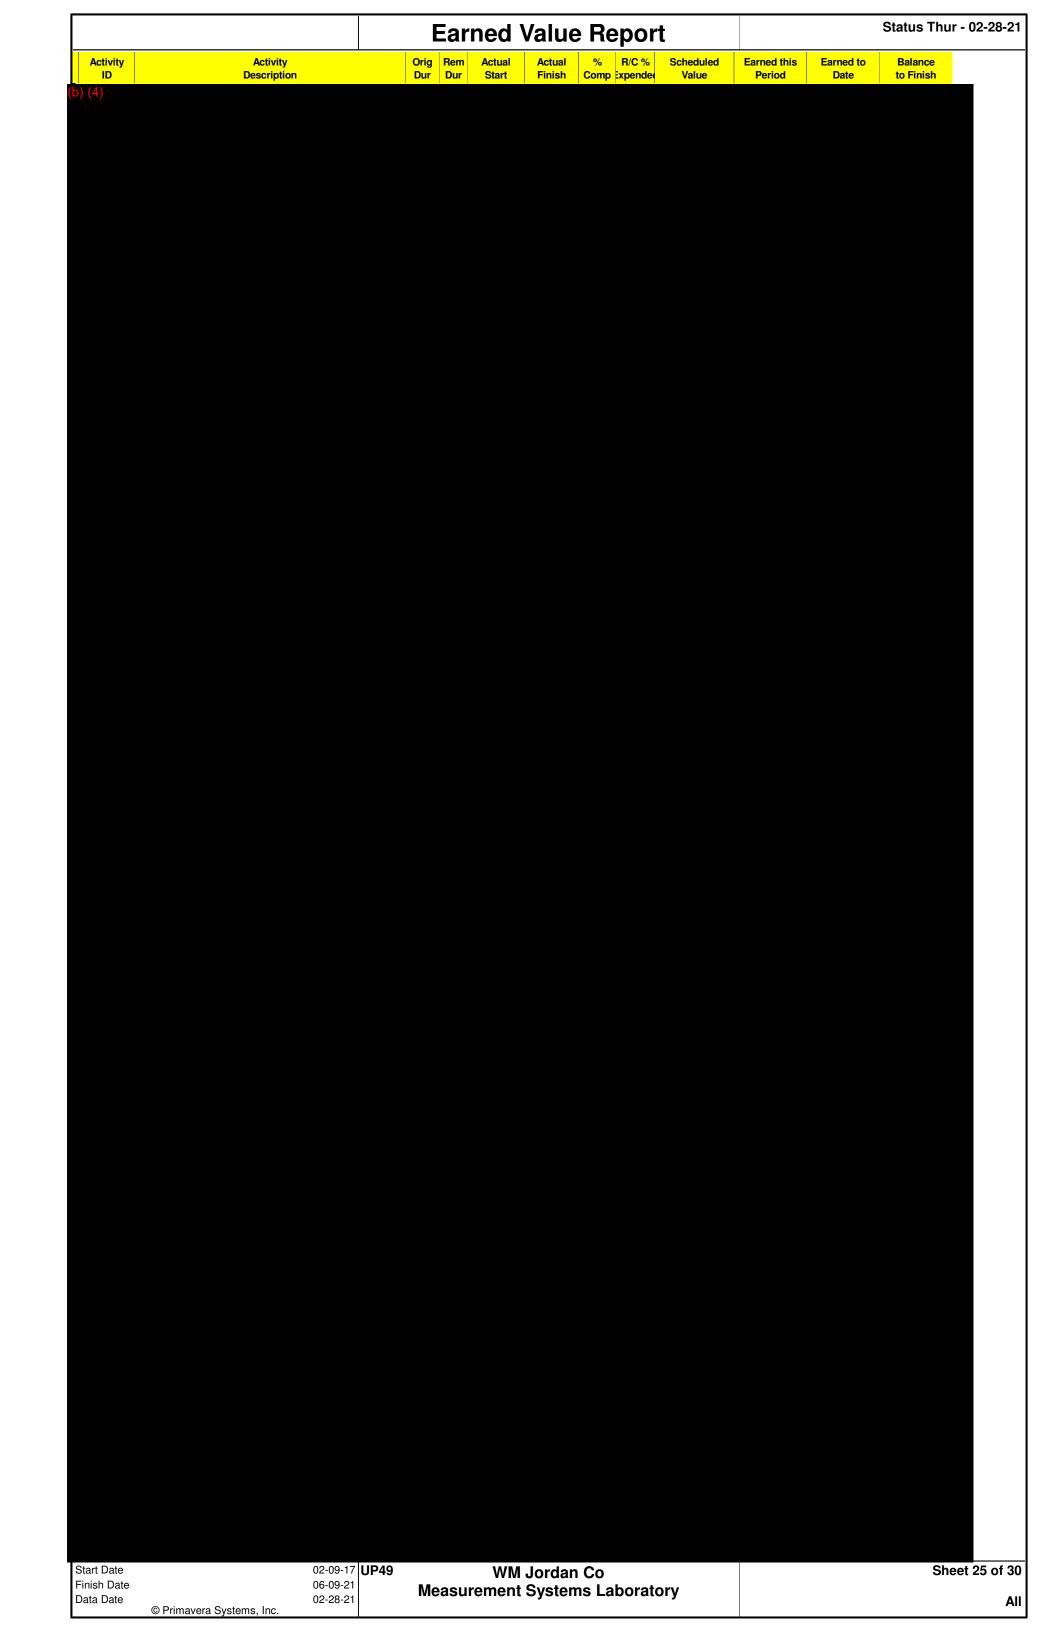

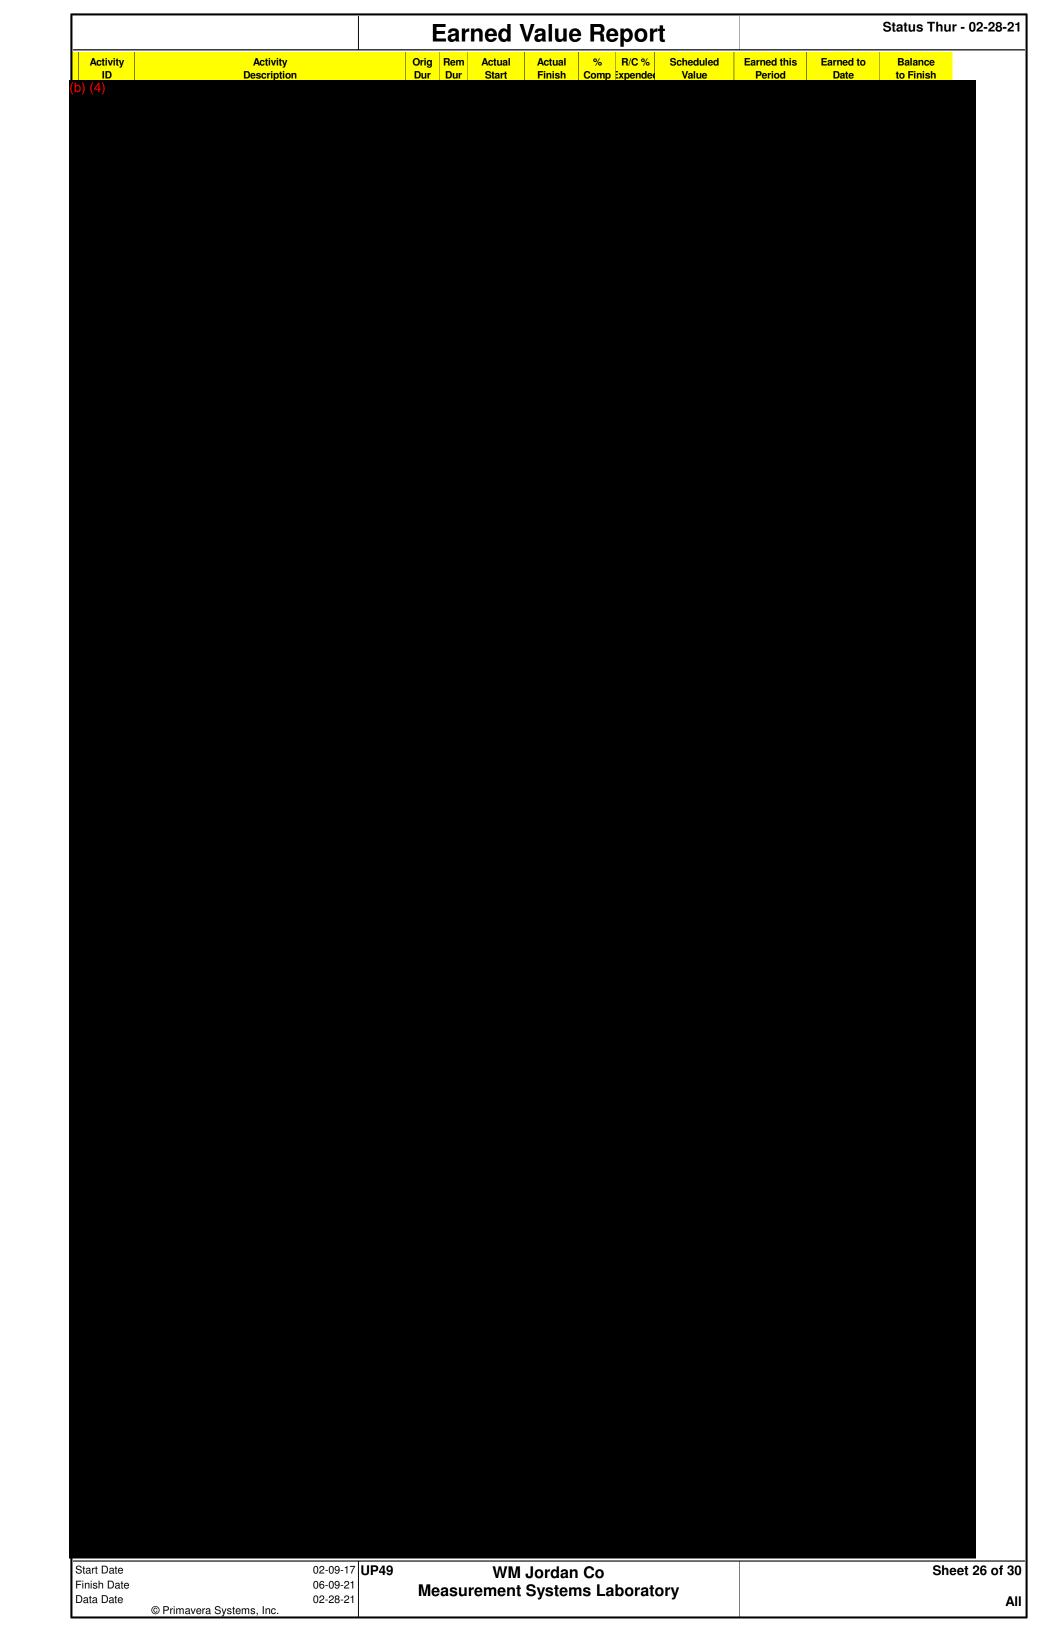

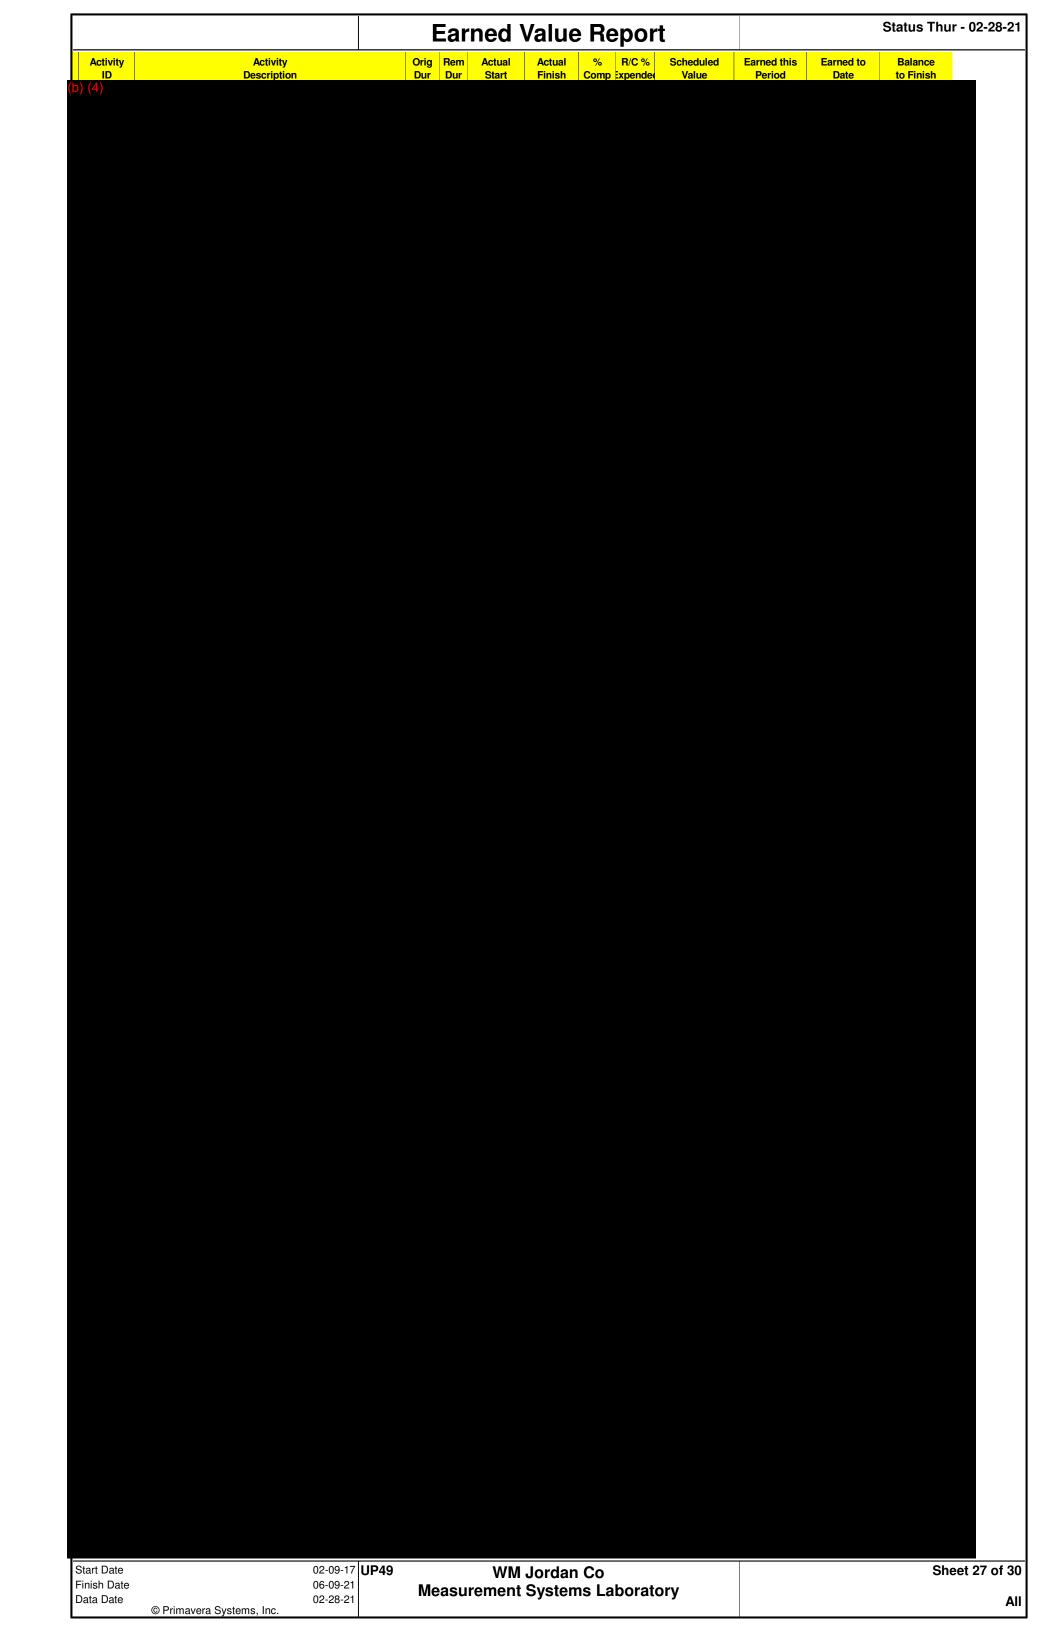

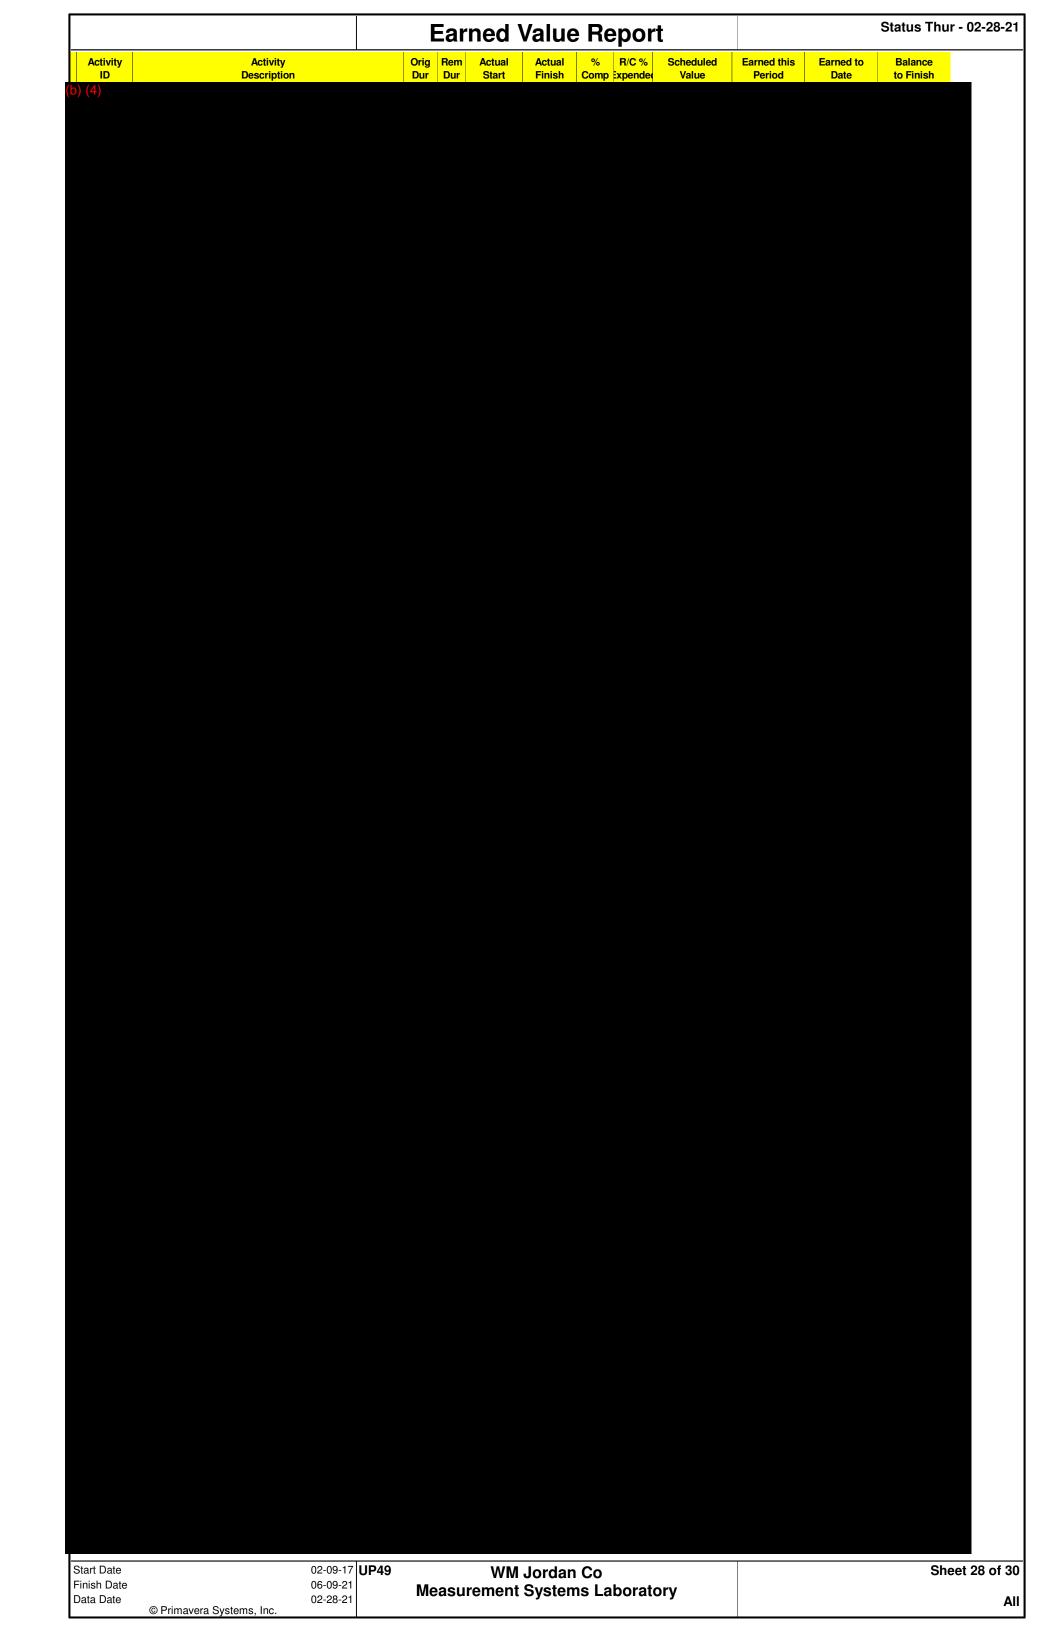

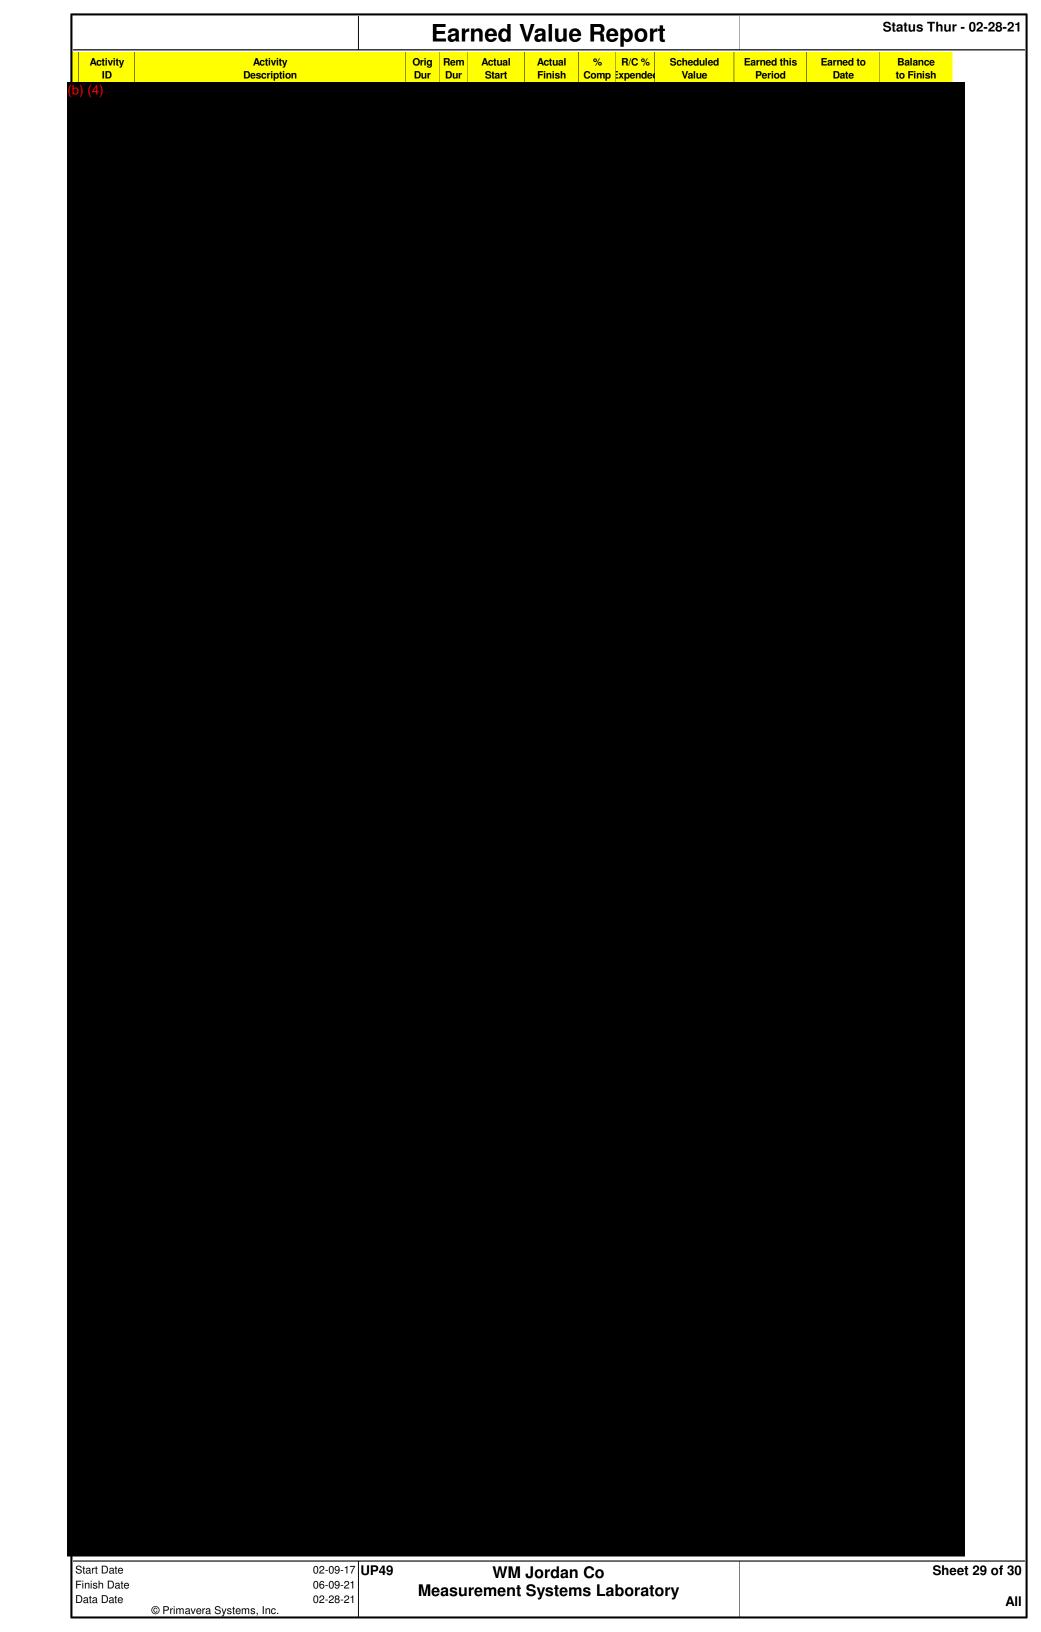

		Earn	ed Value	Report	t			Status Thu	r - 02-28-21
Activity ID b) (4)	Activity Description	Orig Rem Dur Dur	Actual Actual Start Finish	% R/C % Expended	Scheduled Value	Earned this Period	Earned to Date	Balance to Finish	
5) (4)									
Start Date	02-09-17	IIP49	WM Jordan	<u> </u>				Cha	et 30 of 30
