




## Parametrix, Inc. Daily Inspection Report

Report # Page 1 of 2


| Project:   | Sesko Nuisance A | batement  | Owner: _(     | City/Sesko       | Job No.:           | 235-1896-054 |
|--|------------------|-----------|---------------|------------------|--------------------|--------------|
| Date:  | 12/17/01 Da      | /: Monday | _ Contractor: | BRC              | Cont. Rep/.Title   | );           |
| W <b>e</b> ather   | A.M.:40 °        | P.M       | °F            | Site Conditions: | (Good)(Fair)(Poor) | Good         |
| Location and Type of Work: Arsenal Way Property  |                  |           |               |                  |                    |              |
| Number and Classification of Contractors, Men, and Equipment (Include condition of equipment):   |                  |           |               |                  |                    |              |
| Excavator, John Deer JD 590D and Excavator Cat 322B  |                  |           |               |                  |                    |              |
| Truck, Double Axle with drag on box, Freightliner S-20, puling a 27' Flat Bed Trailer  |                  |           |               |                  |                    |              |
| Pickup Truck with 12' trailer  |                  |           |               |                  |                    |              |
| 4 Men (Ron, Mark and 2 truck drivers)  |                  |           |               |                  |                    |              |
| Work in Progress (Include report of operations, materials received and condition, work start/stop time, and any unusual conditions):   |                  |           |               |                  |                    |              |
| BRC arrived at 0800. Truck and excavator arrived at 0830. BRC was on the site and determining procedure for the day. At about 0845 they began loading heavy crane components (crane arms)  |                  |           |               |                  |                    |              |
| Sesko was moving equipment off site. Drove large dozer off site. Three wreckers arrived. One hauled off a utility truck bed. Others standing by at 0930.   |                  |           |               |                  |                    |              |
| Sesko stated that he understood BRC was to begin at 1000.  |                  |           |               |                  |                    |              |
| Al Duke, Janet Lunceford on site at 0815. Bremerton police officer arrived at 0900. No problems encountered. Took photos of equipment staging and condition of parking lot road. Weather was clear and sunny, but cold. There had been heavy rain the previous weekend. Little standing water. |                  |           |               |                  |                    |              |
| Left site at 0945.   |                  |           |               |                  |                    |              |
| Returned to site at 2:00pm. The truck and trailer were just leaving. One small cat was loaded on trailer.  |                  |           |               |                  |                    |              |
| Work Completed:  |                  |           |               |                  |                    |              |
| Load of misc steel scrap and small catepillar dozer removed. Several pumps, one small trailer frame and other misc material  |                  |           |               |                  |                    |              |
| removed.   |                  |           |               |                  |                    |              |
|  |                  |           |               |                  |                    |              |
| Discrepancies Noted (Nonconformance Report #):   |                  |           |               |                  |                    |              |
| None   |                  |           |               |                  |                    |              |
|  |                  |           |               |                  |                    |              |
| Discussions with Contractor (Include orders given and received):   |                  |           |               |                  |                    |              |
| Concerned about safety due to people on site.  |                  |           |               |                  |                    |              |
|  |                  |           |               |                  |                    |              |
| Ann Course for Dissure Orders on Dates on Dates  |                  |           |               |                  |                    |              |
| Any Cause for Dispute, Change Orders, or Delays, and Reasons:  None  |                  |           |               |                  |                    |              |
| None   |                  |           |               |                  |                    |              |
| Extra Work in Progress—Description (Include Extra Work Report form):   |                  |           |               |                  |                    |              |
| None   |                  |           |               |                  |                    |              |
| Items for Office Action:   |                  |           |               |                  |                    |              |
| Visitors:  |                  |           |               |                  |                    |              |
|  |                  |           |               | Signature 1      | <b></b>            |              |

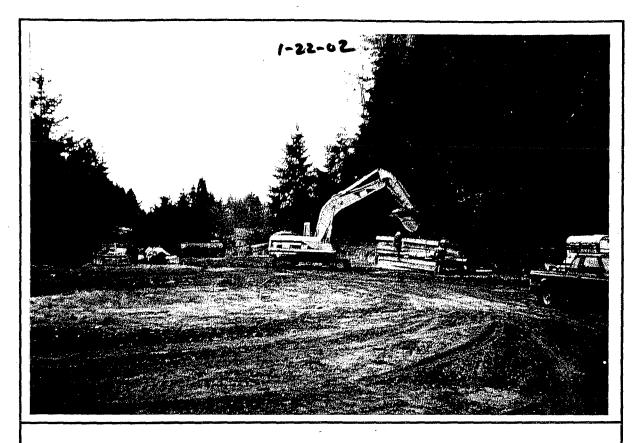


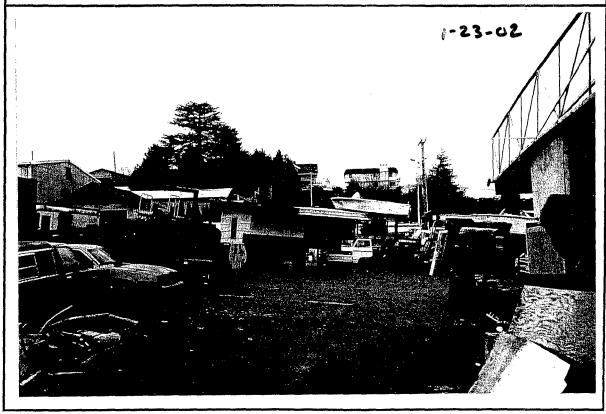


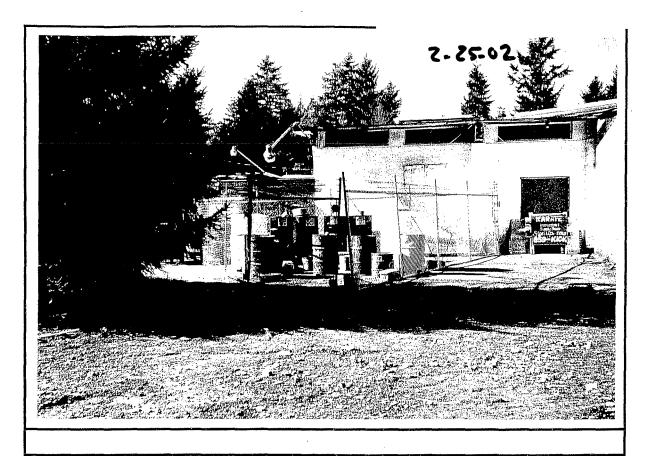



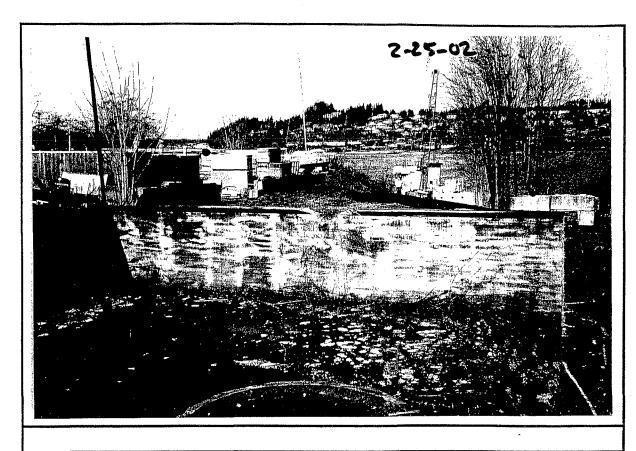

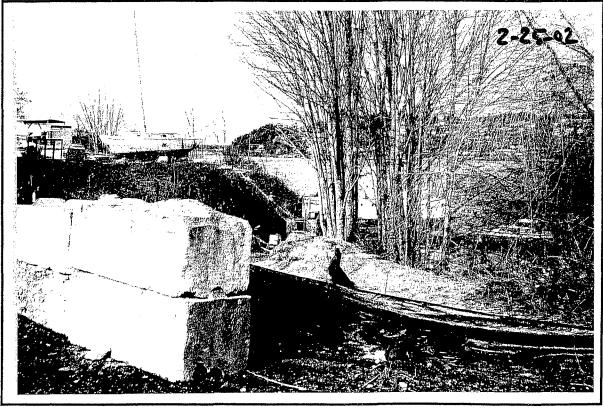

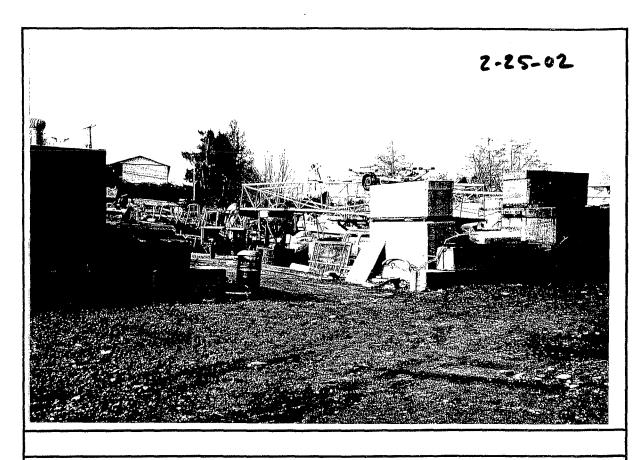



Jask Jour Mg 7-21-93 agreed to disallow dual use of Lesk property -Andial back doesn't allow Jublic assembly. To for Natach às as an auditori
