




402966

## Plainwell No. 2 Dam Area

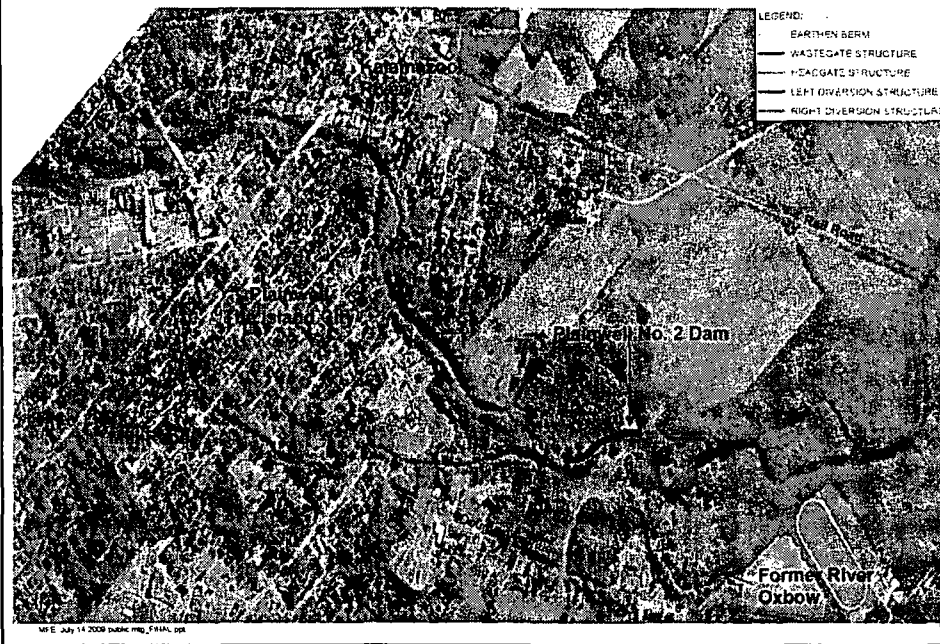

## Plainwell No. 2 Dam Project Goals

- 1.9 miles of linear bank removal
- 8.9 acres - total area removed
- 14,200 cubic yards targeted for removal
  - 12,000 cubic yards of soil removed from banks and floodplain
  - 2,200 cubic yards from oxbow/river area

## Plainwell No. 2 Dam Schedule

- **Two construction seasons to complete**


2009 Aug. – December  
2010 May - October



## Plainwell No. 2 Dam Project Activities

- Access to River
- Construct staging areas and roadways
- Excavation, Verification and Restoration
- Habitat Restoration and monitoring – 3 yrs
- Bank Monitoring – 3 yrs
- Vegetation Monitoring – 3 yrs
- Exotic/Invasive Species Control

## Current Progress

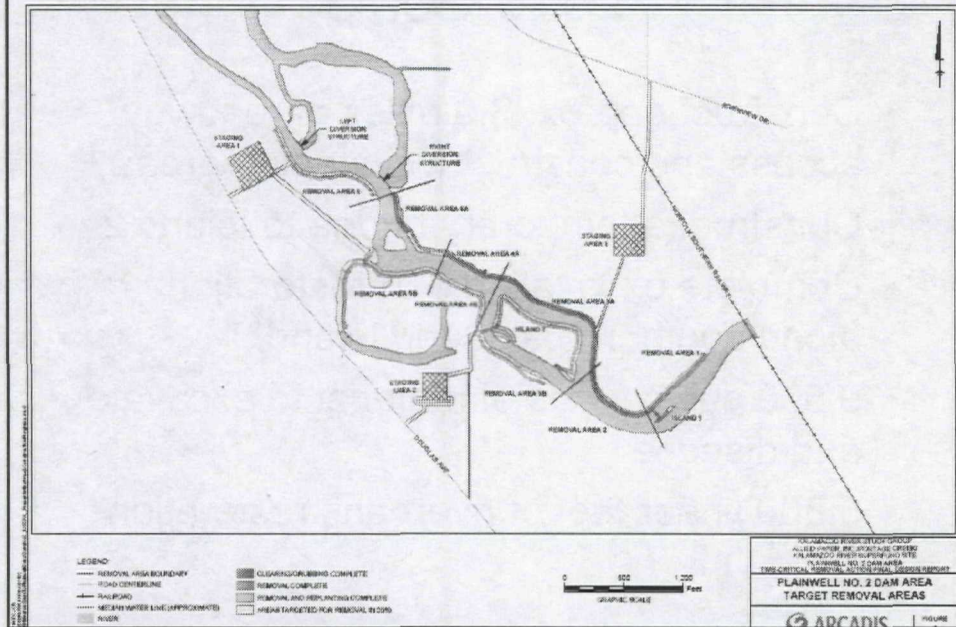

## 2009 Accomplishments


- Completed excavation and restoration along northern bank
- 4,725 cubic yards of material excavated and disposed
- 4,900 linear feet of riverbank restoration



## 2010 Goals



- Construct approx. 2.0 miles of roadway access and construct two staging areas
- Construct a temporary bridge to Island 2
- Complete excavation and restoration along southern bank and Island 2
- 9,500 cubic yards of material to excavate and dispose
- 5,800 linear feet of riverbank restoration







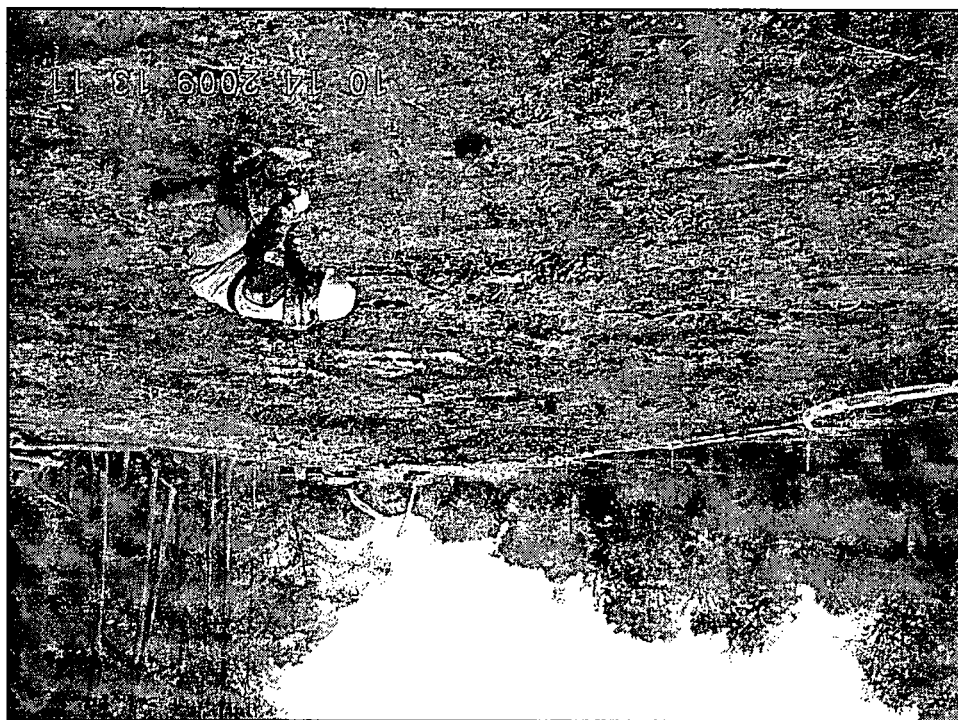

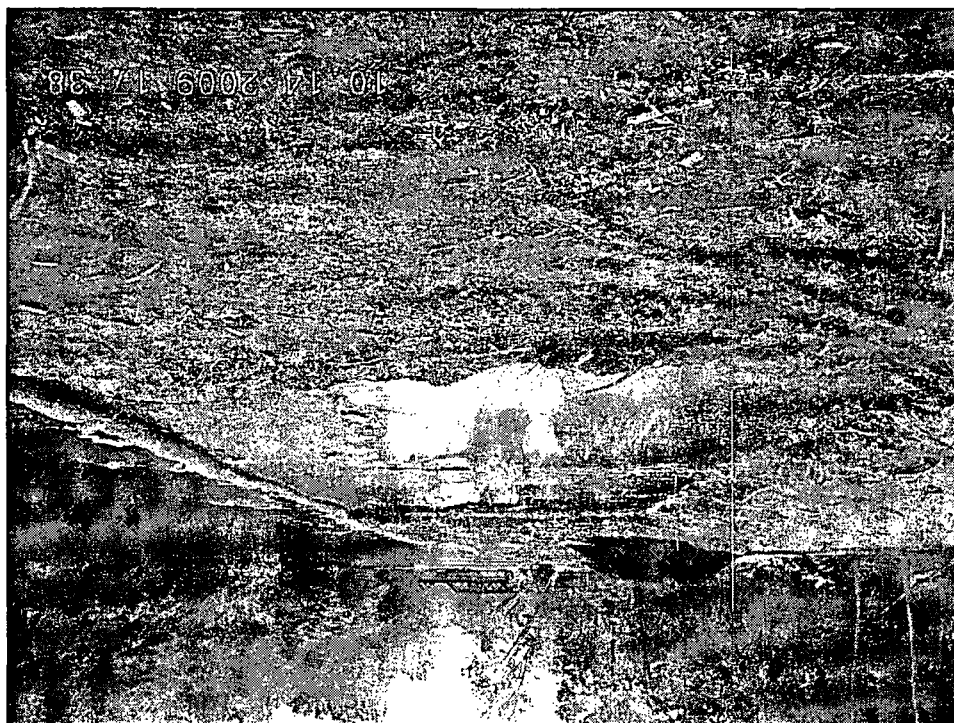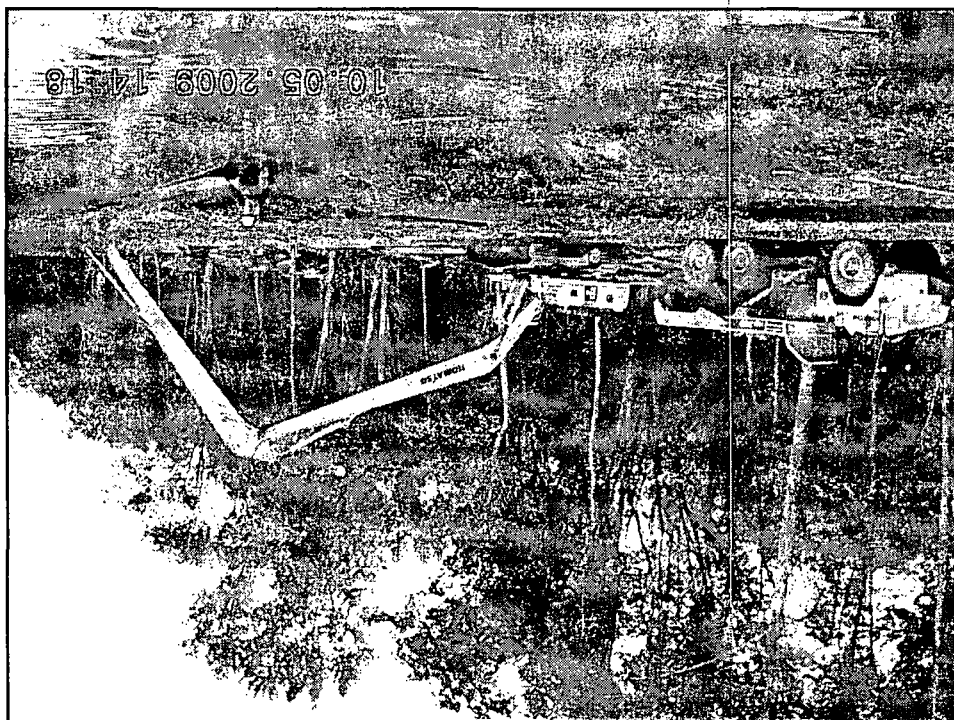

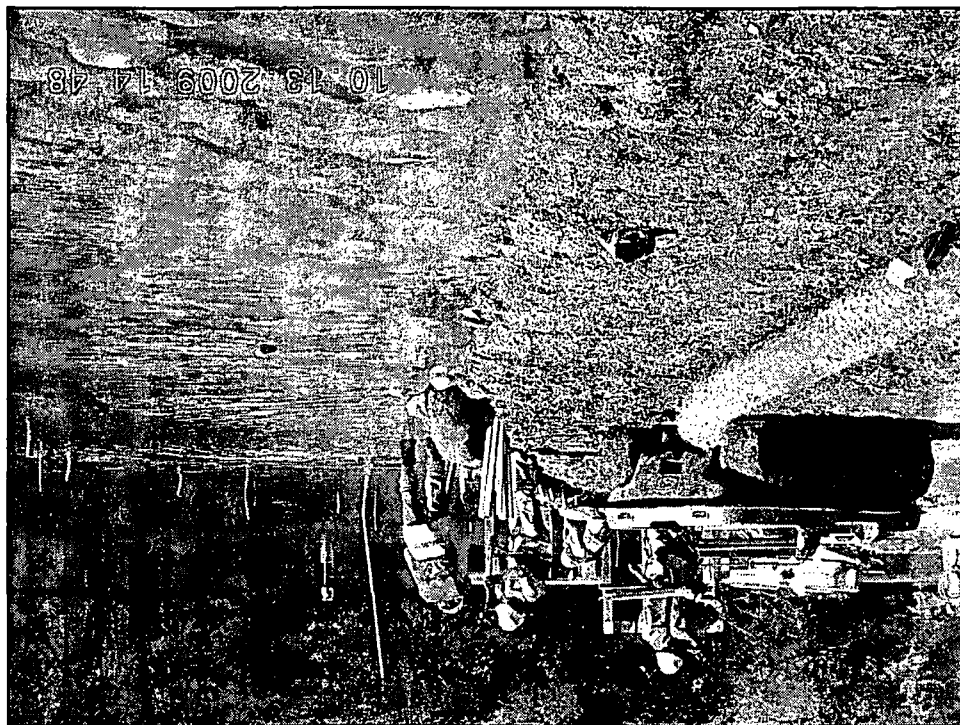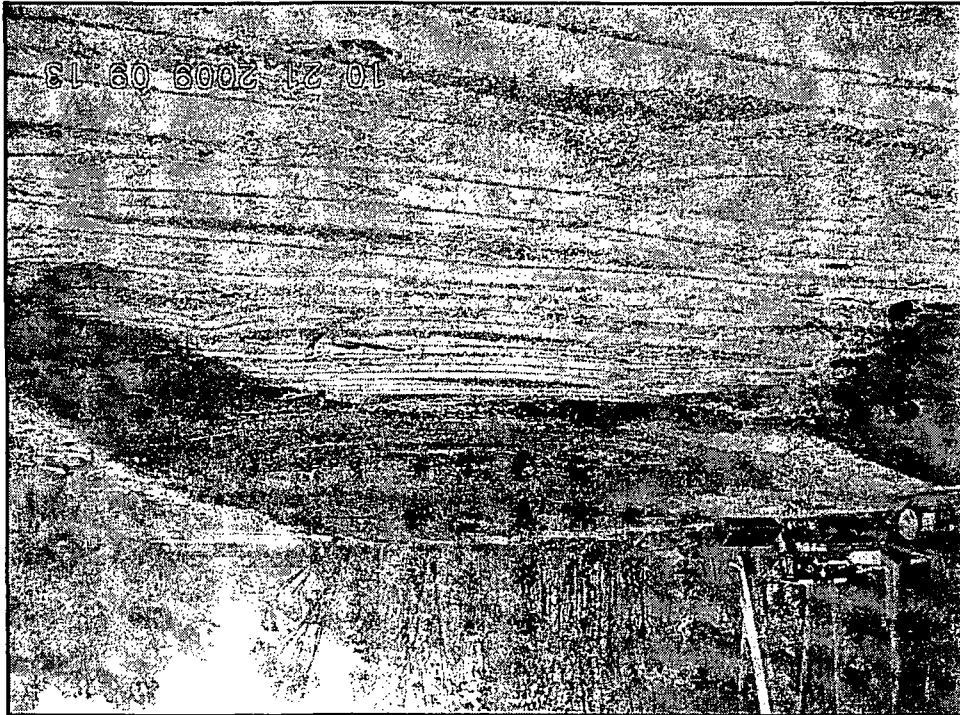

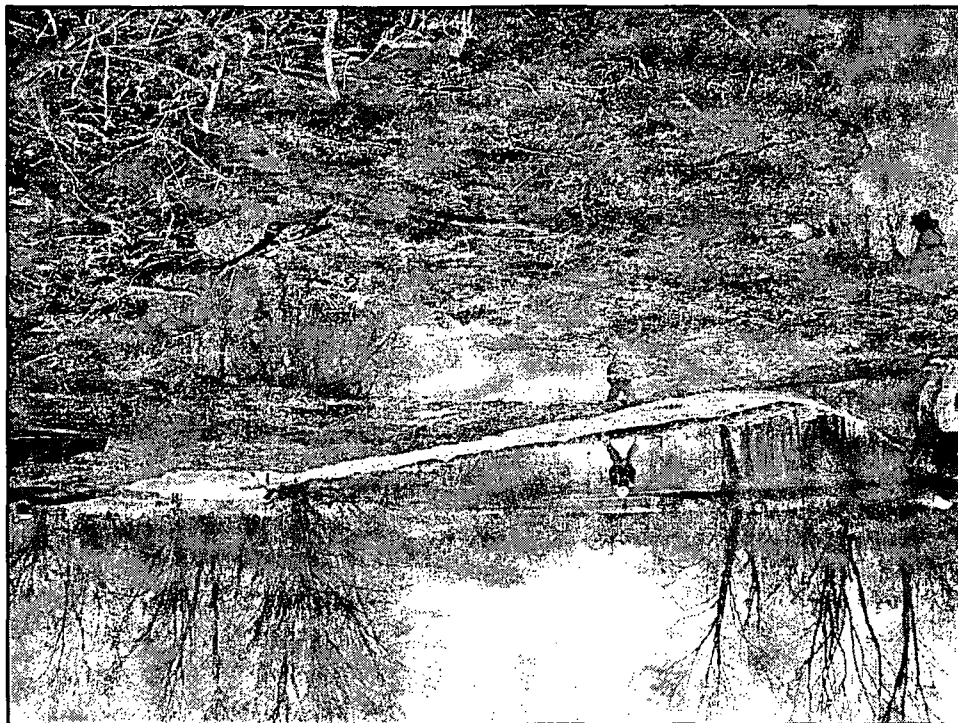



**Questions?**

**Contact Information**

**Sam Borries**  
**(312) 353-8360**  
**[borries.samuel@epa.gov](mailto:borries.samuel@epa.gov)**
