

U.S. ENVIRONMENTAL PROTECTION AGENCY
 POLLUTION/SITUATION REPORT
 Portage Creek Area - Removal Polrep



US EPA RECORDS CENTER REGION 5



435741

UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
 Region V

Subject: POLREP #21
 Progress
 Portage Creek Area
 059B05
 Kalamazoo, MI
 Latitude: 42.2839750 Longitude: -85.5791570

To: Sam Borries, U.S. EPA
 Jason El-Zein, U.S. EPA
 John Maritote, U.S. EPA
 Mike Ribordy, U.S. EPA
 Mark Mills, Michigan DNR
 Daria Devantier, MDEQ
 Paul Bucholtz, MDEQ
 Bruce Merchant, Kalamazoo City
 Debbie Jung, Kalamazoo City
 Lisa Williams, U.S. FWS
 Todd Goeks, NOAA
 Valencia Darby, Department of Interior
 Mark Johnson, ATSDR

From: Craig Thomas, On-Scene Coordinator

Date: 10/31/2012

Reporting Period: 10/13/2012 - 10/31/2012

1. Introduction

1.1 Background

Site Number:	059B05	Contract Number:	EP-S5-09-05
D.O. Number:	0087	Action Memo Date:	7/5/2011
Response Authority:	CERCLA	Response Type:	Time-Critical
Response Lead:	EPA	Incident Category:	Removal Action
NPL Status:	NPL	Operable Unit:	05
Mobilization Date:	9/26/2011	Start Date:	8/30/2011
Demob Date:		Completion Date:	
CERCLIS ID:	MID006007306	RCRIS ID:	NA
ERNS No.:		State Notification:	Yes
FPN#:		Reimbursable Account #:	

1.1.1 Incident Category

Fund-lead removal action

1.1.2 Site Description

See POLREP #1

1.1.2.1 Location

See POLREP #1

1.1.2.2 Description of Threat

See POLREP #1

1.1.3 Preliminary Removal Assessment/Removal Site Inspection Results

See POLREP #1

2. Current Activities**2.1 Operations Section****2.1.1 Narrative**

Seasonal demobilization operations were conducted during this reporting period. In addition, site preparations began in both SA5A and SA3A in anticipation of removal activities next construction season.

2.1.2 Response Actions to Date

From October 15 to October 31, EPA, START and ERRS contractors conducted the following activities:

Site Activities - Axtell Creek, SA5D & SA5C

- Demobilized pumps, de-watering system, engineering & environmental controls and equipment from SA5C;
- Removed curb cuts and replaced damaged sections of sidewalks;
- Conducted post-construction site structural feature assessment; and
- Began site restoration activities in accordance with the site Restoration Plan.

Site Activities - SA5A

- Conducted pre-construction sampling and pre-removal contaminated sediment confirmation sampling in each grid;
- Staged bypass pump discharge pipes on east bank for the winter to save time and re-mobilization costs; and
- Removed trees, brush and fencing from creek banks in preparation for removal operations next year.

Site Activities - SA3A

- Conducted pre-removal contaminated sediment confirmation sampling;
- Constructed an aggregate access road and staging area for equipment and load-out pad; and
- Removed trees and brush from creek banks in preparation for removal operations next year.

Site Activities - Staging Pad

- Solidified and loaded out 1205.32 tons of non-TSCA (< 50ppm PCBs) contaminated sediments for disposal at C&C Landfill in Marshall, Michigan;
- Treated 42,344 gallons of potentially contaminated contact water in EPA's mobile wastewater treatment plant, with a total of 695,715 gallons treated to date;
- Shut down EPA's mobile waste water treatment plant for the season and demobilized support trailer; and
- Pumped out and transport 10,000 gallons of potentially contaminated contact water from the staging pad sump for treatment off site.

Project Management Activities

- Continued weekly progress meetings with City of Kalamazoo;
- Conducted data validation for additional post-removal confirmation sediment samples collected from SA5C&D;
- Continued discussions with property owners in SA5A, SA3A, SA1C and SA1B regarding site access, preparation and restoration; and
- Completed implementation of seasonal site shut-down / demobilization plan;

2.1.3 Enforcement Activities, Identity of Potentially Responsible Parties (PRPs)

See POLREP #1

2.1.4 Progress Metrics

Waste Stream	Medium	Quantity	Manifest #	Treatment	Disposal
Non-TSCA contaminated sediments	solidified sediment	1205.32 tons	NTSCA-190 to NTSCA-213	disposal	C&C Landfill, Marshall MI
Construction & Demolition	solid waste	13.94 tons	23922	disposal	C&C Landfill, Marshall, MI
Scrap Steel	scrap metal	460 lbs	n/a	recycling	Shupan Recycling
Shipping Pallets	wood	100	n/a	recycling	Holland Pallet
Tires	tires	38	n/a	recycling	Tire Reclaimers

2.2 Planning Section

A summary of removal activities that will take place from October 31 through the end of the year include:

Site Activities - Staging Pad

- Continue to pump out and transport potentially contaminated contact water from the staging pad sump for treatment off site on an as-needed basis.

Site Activities - Axtell Creek, SA5D & SA5C

- Complete restoration activities according to site Restoration Plan.

Project Management Activities

- Conduct data validation for pre-removal confirmation core sampling conducted in SA5A & SA3A as well as post-construction sampling in SA5D;
 - Review Post-Removal Structure Feature Assessment report for Axtell Creek, SA5D & SA5C;
 - Obtain access agreements for properties in SA5A, SA3A, SA1C and SA1B; and
 - Plan for removal operations in SA5A, SA3A, SA1C and SA1B during the next construction season.

2.2.1 Anticipated Activities

See POLREP #2

2.2.1.1 Planned Response Activities

See above

2.2.1.2 Next Steps

See above

2.2.2 Issues

None

2.3 Logistics Section

The current resources present on site during this reporting period include:

- Office trailers
- Portable restrooms and hand-washing stations (demobilized)
- Portable generators (demobilized)
- Submersible pumps (demobilized)
- Equipment storage container
- ERRS work crews and subcontractor work crews
- START sampling contractor (demobilized)
- Heavy equipment (demobilized)
- Water truck (demobilized)

- Street sweeper (demobilized)
- Mixing boxes
- Frac (water) tank (demobilized)
- Pressure wash trailer (demobilized)
- Bypass pumps and piping (demobilized)
- Sheet piling and steel bridge personnel support structures (demobilized)
- Mobile wastewater treatment plant
- Temporary steel bridge (demobilized)
- Monitoring Equipment (demobilized)

The only equipment that will remain on site during the seasonal de-mobilization will be the office trailers, equipment storage container and EPA's mobile wastewater treatment plant.

2.4 Finance Section

2.4.1 Narrative

See table

Estimated Costs *

	Budgeted	Total To Date	Remaining	% Remaining
Extramural Costs				
ERRS - Cleanup Contractor	\$7,889,265.00	\$5,872,000.00	\$2,017,265.00	25.57%
TAT/START	\$400,000.00	\$275,000.00	\$125,000.00	31.25%
Intramural Costs				
Total Site Costs	\$8,289,265.00	\$6,147,000.00	\$2,142,265.00	25.84%

* The above accounting of expenditures is an estimate based on figures known to the OSC at the time this report was written. The OSC does not necessarily receive specific figures on final payments made to any contractor(s). Other financial data which the OSC must rely upon may not be entirely up-to-date. The cost accounting provided in this report does not necessarily represent an exact monetary figure which the government may include in any claim for cost recovery.

2.5 Other Command Staff

2.5.1 Safety Officer

Craig Thomas and Paul Ruesch serve as safety officer(s). The HASP is reviewed and signed by all site personnel. All new personnel, including sub-contractors, are provided a site orientation and safety briefing. Safety meetings are held each morning with all site workers.

2.6 Liaison Officer

Craig Thomas and Paul Ruesch serve as liaison(s) with local officials and interested parties.

2.7 Information Officer

See Section 2.6

2.7.1 Public Information Officer

See Section 2.6

2.7.2 Community Involvement Coordinator

Don DeBlasio - U.S. EPA

3. Participating Entities

3.1 Unified Command

N/A

3.2 Cooperating Agencies

U.S. Environmental Protection Agency
 Michigan Department of Environmental Quality
 Michigan Department of Agriculture and Rural Development
 Michigan Department of Natural Resources
 U.S. Fish and Wildlife Service
 City of Kalamazoo:
 Department of Public Services
 Parks and Recreation Department
 Economic Development Department
 Community Planning & Development
 Public Safety Department
 Fire Department
 Police Department
 ReDevelopment Department
 Bronson Methodist Hospital
 Kalamazoo Nature Center

4. Personnel On Site

U.S. EPA - 2
 ERRS contractor (Environmental Quality Management, Inc) - 13
 START contractor (Dynamac/Weston) - 1
 CMC Contracting (sheet pile removal subcontractor) - 5
 Rain for Rent (groundwater extraction subcontractor) - 2
 Katerberg Verhage (restoration subcontractor) - 3
 Farm & Garden/Viskers (fencing contractor) - 2
 Total Tree Service - 7
 Baker Corporation Pump Division - 3

TOTAL PERSONNEL = 38

5. Definition of Terms

C&D - Construction and Demolition (waste)
 ERRS - Emergency and Rapid Response Services
 FOSC - Federal On Scene Coordinator
 U.S. FWS - United States Fish and Wildlife Service
 HASP - Health and Safety Plan
 HDPE - High density polyethylene (plastic)
 mg/kg - milligrams per kilogram
 mg/m3 - milligrams per cubic meter
 MDARD - Michigan Department of Agriculture and Rural Development
 MDEQ - Michigan Department of Environmental Quality
 NA - Not Applicable
 NOAA - National Oceanic and Atmospheric Administration
 NPL - National Priorities List
 NRDA - Natural Resource Damage Assessment
 ntu - nephelometric turbidity units
 PCB - polychlorinated biphenyl
 ppm - parts per million
 PRPs - Potentially Responsible Parties
 RTK GPS - Real Time Kinematic Global Positioning System
 SA - Slope Area
 START - Superfund Technical Assessment and Response Team
 U.S. EPA - United States Environmental Protection Agency

6. Additional sources of information

6.1 Internet location of additional information/report

See the project website at <http://www.epaosc.org/portagecreekarea>.

6.2 Reporting Schedule

The next POLREP will be generated as needed.


7. Situational Reference Materials

See the project website at <http://www.epaosc.org/portagecreekarea>.


Additional information on the overall Kalamazoo River Project can be found at <http://www.epa.gov/Region5/cleanup/kalproject/index.htm>.

10/29/2012 17:54



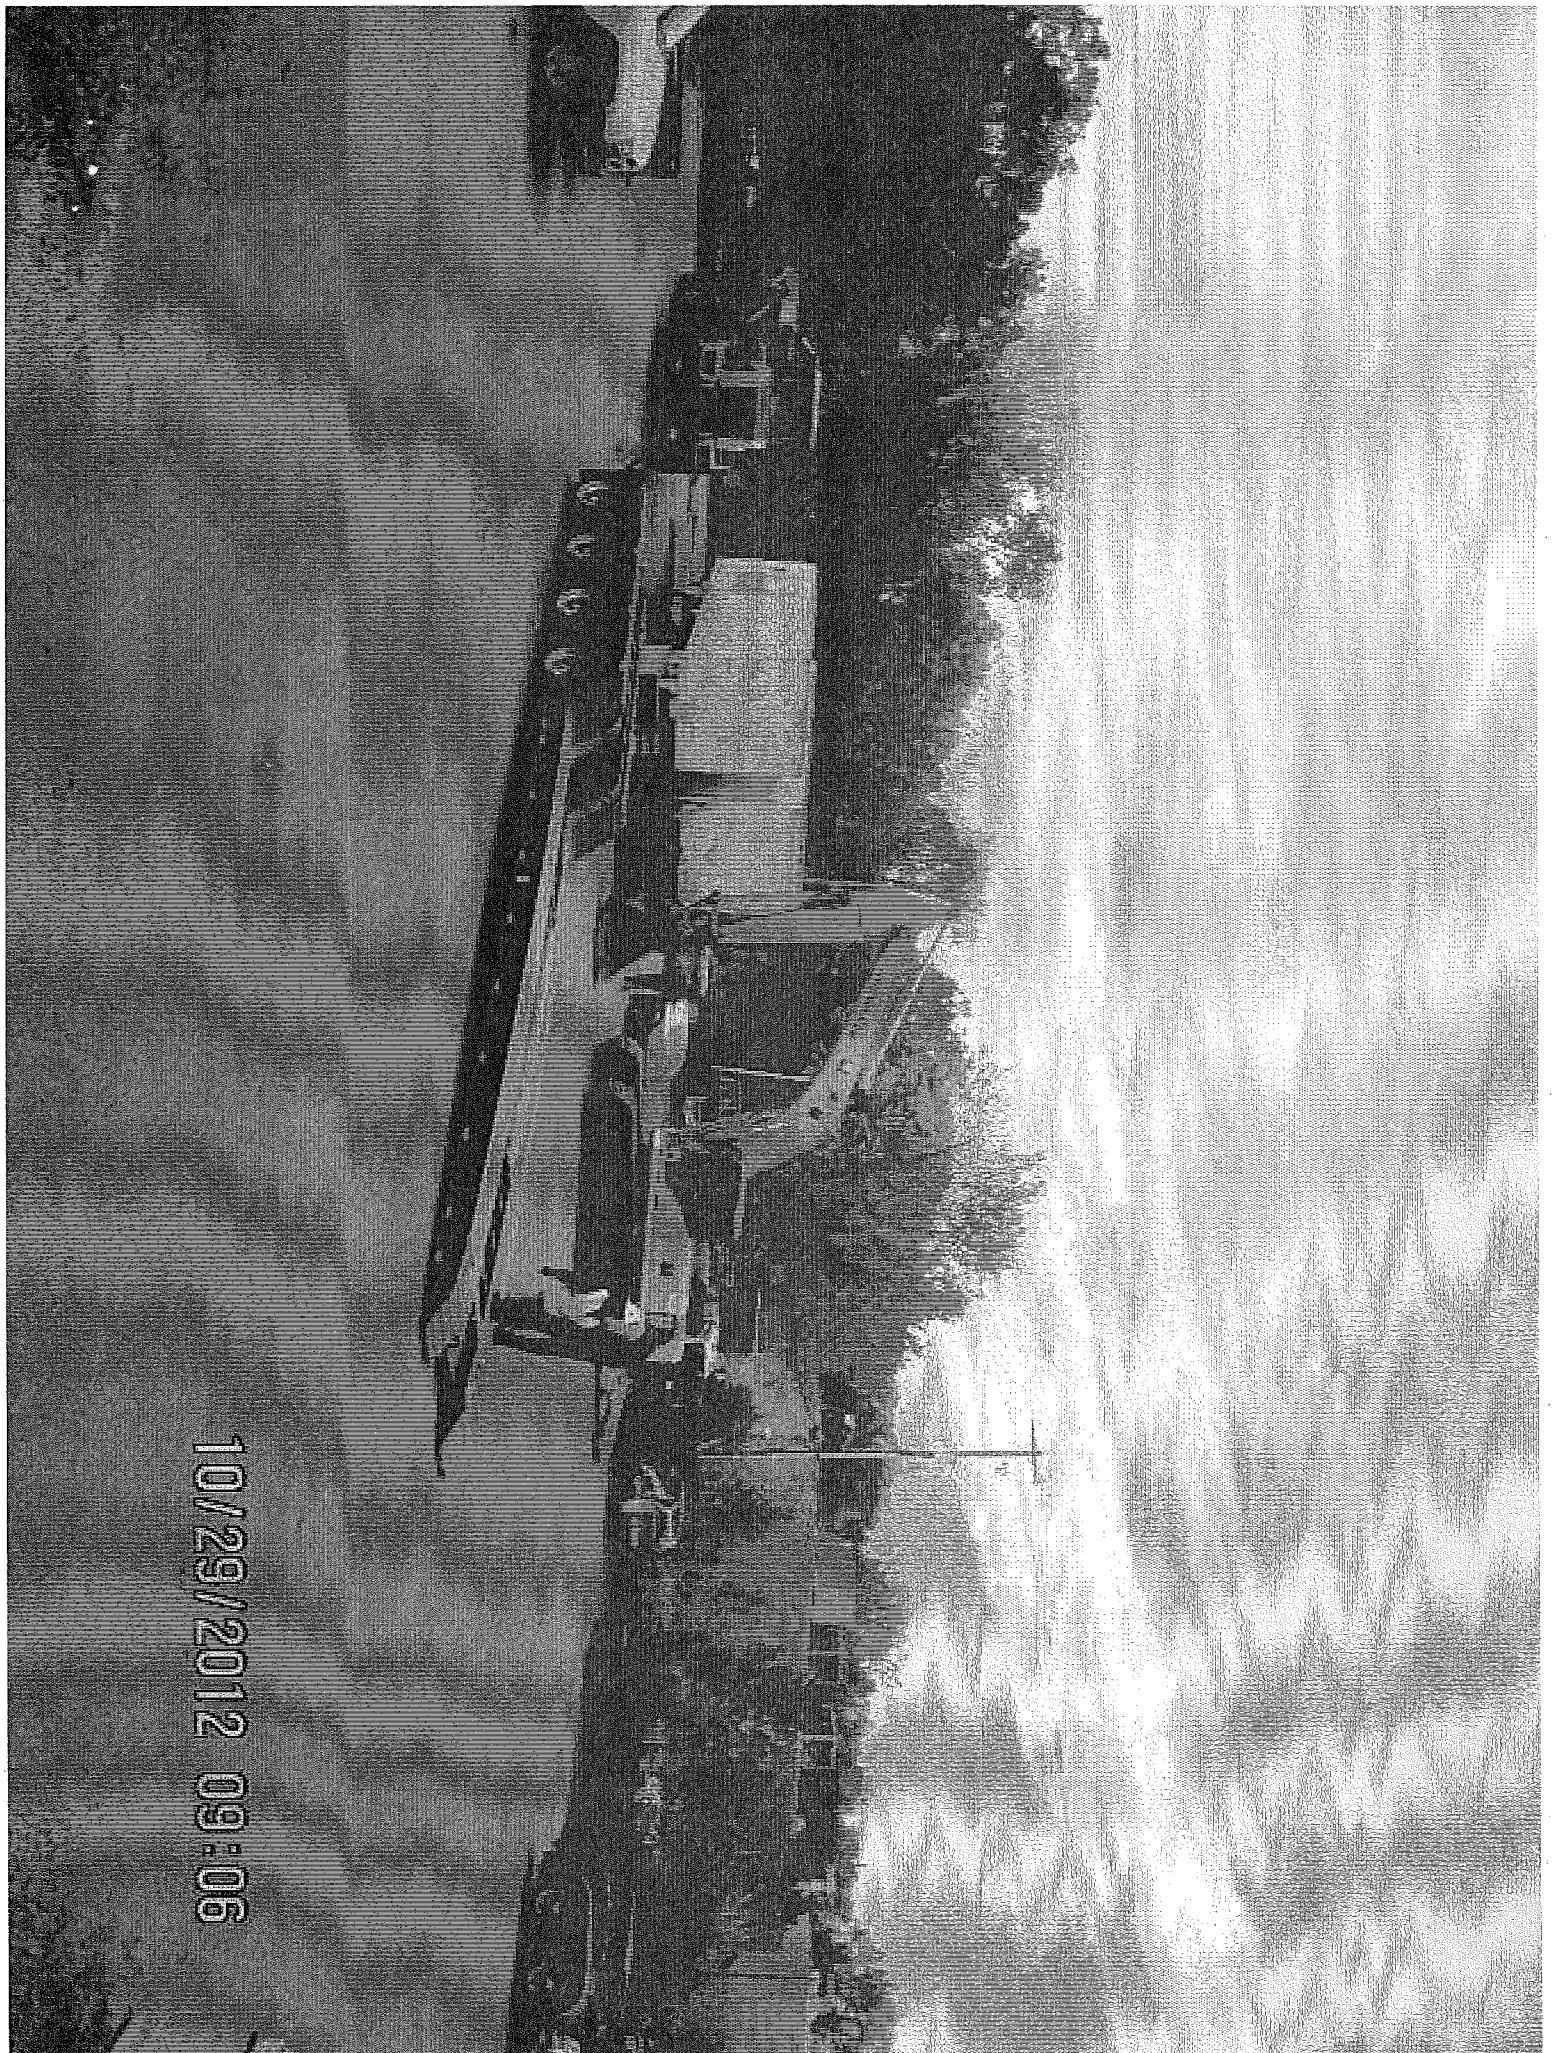

10/29/2012 09:06

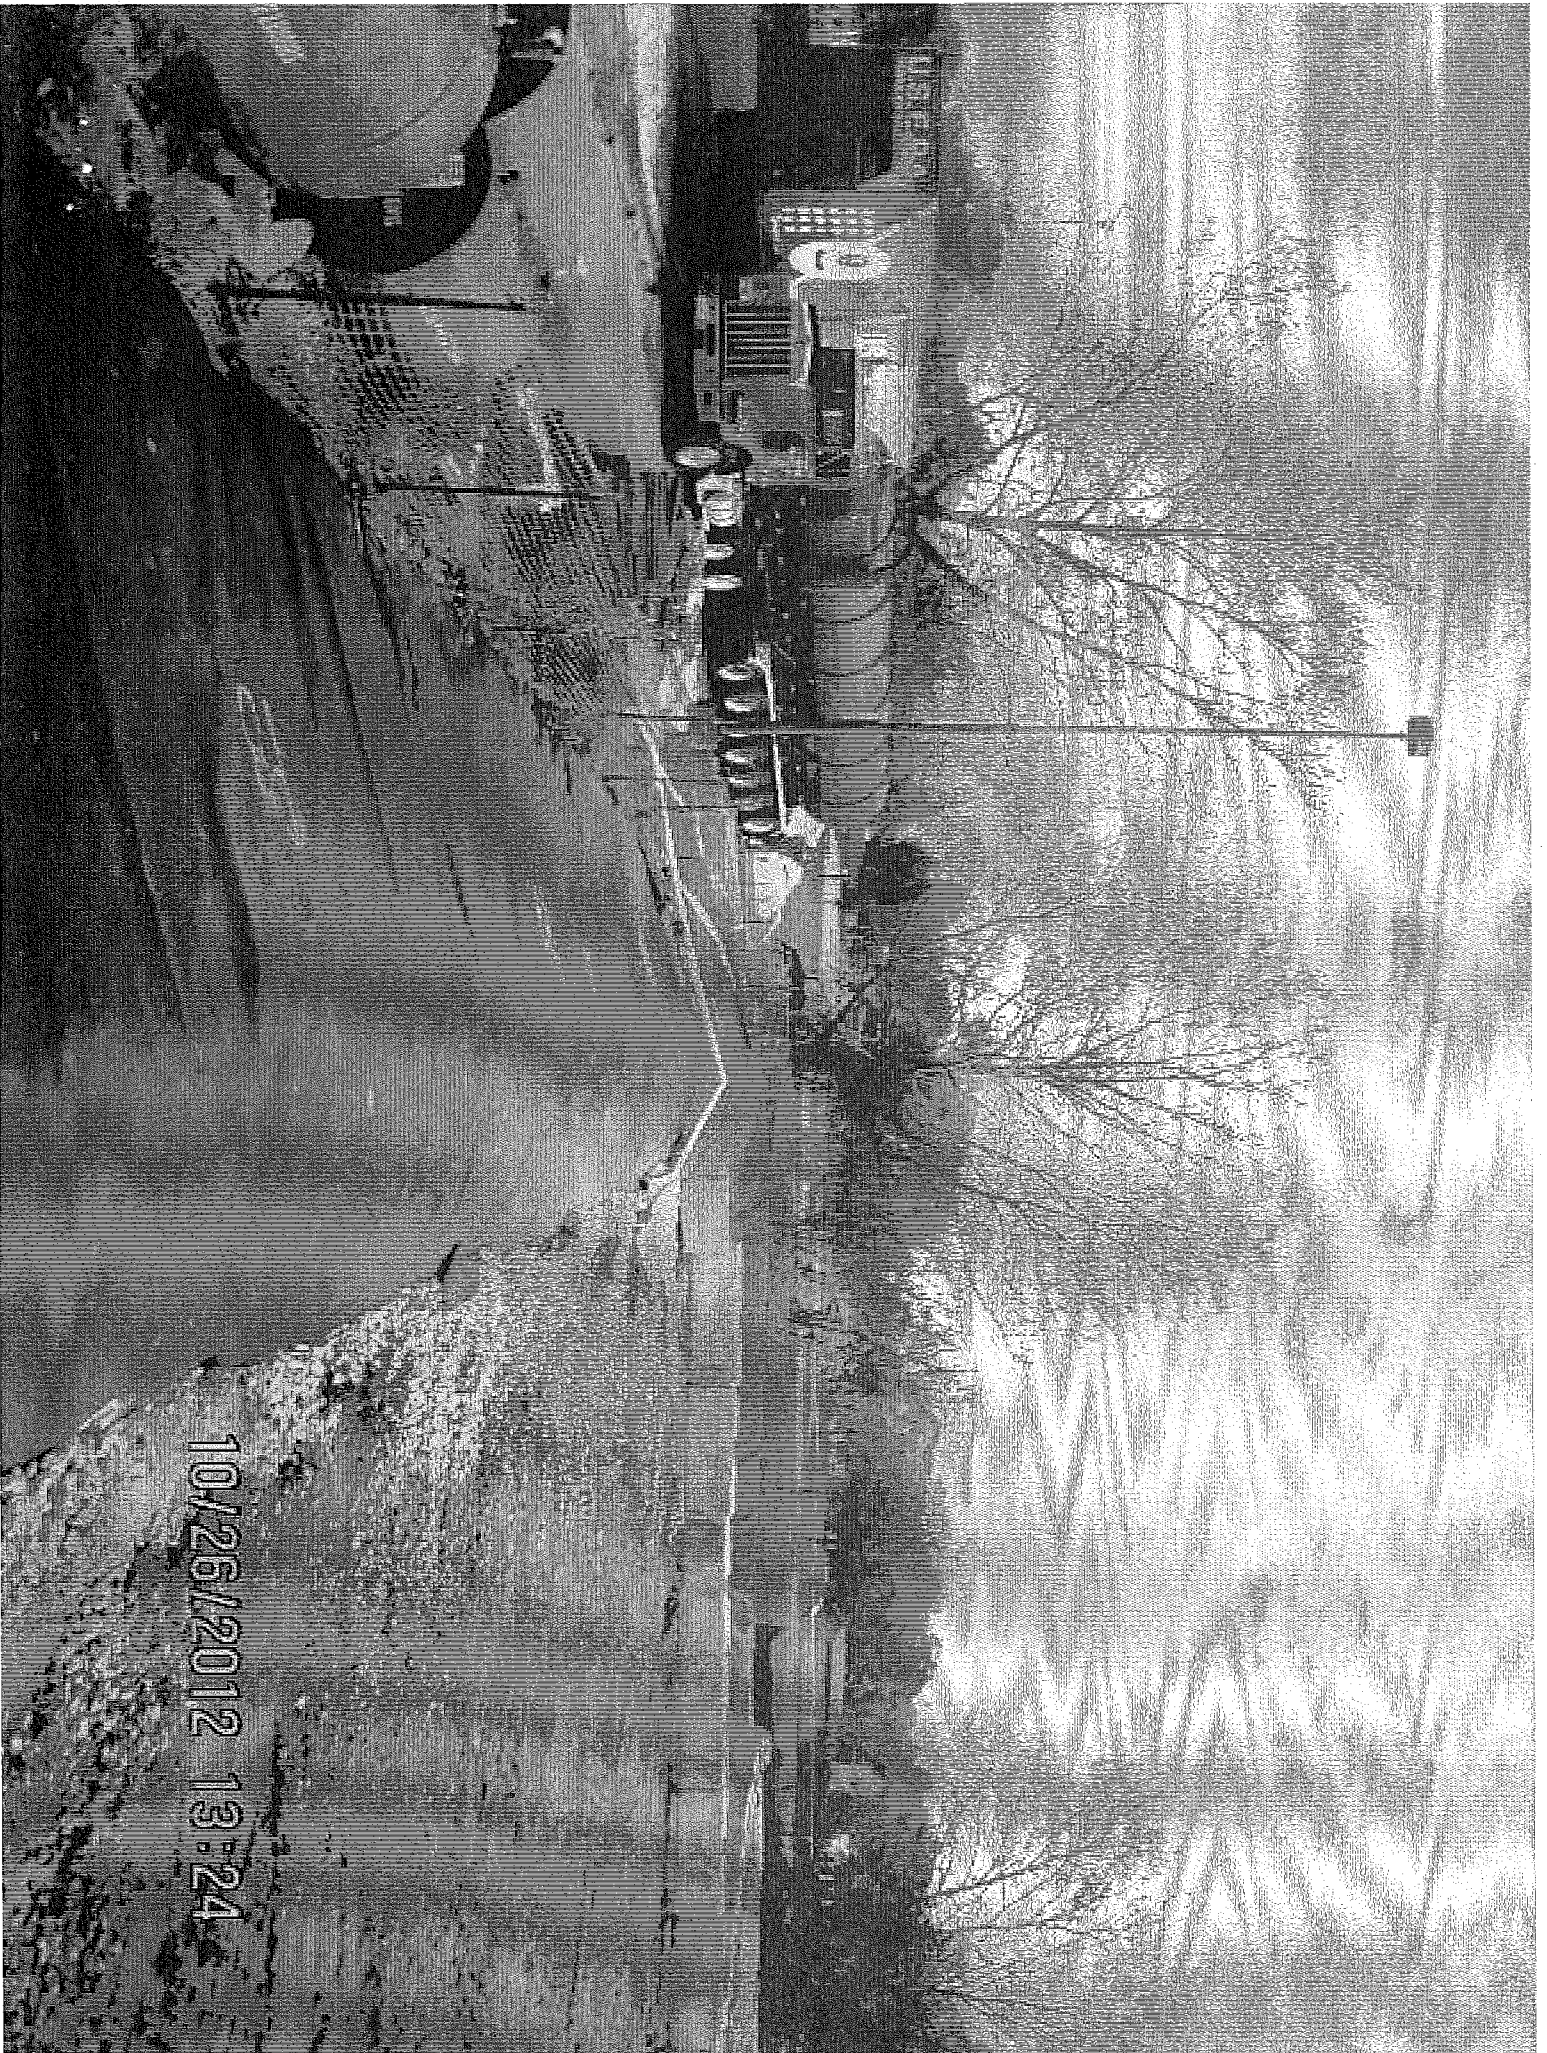

10/26/2012 13:24
