

Plainwell No. 2 Dam Area Time-Critical Removal Action

Weekly Construction Update

Progress Report #27—July 26, 2010

Work Completed: July 15 – July 21, 2010

- Began the removal of resuspension controls in Removal Area 3B.
- Completed the excavation of targeted top-of-bank and floodplain soils from Removal Area 4B.
- Completed restoration activities on Island 2. Activities included the installation of topsoil, coir logs, restoration seed, and erosion control blankets.
- Completed the removal of resuspension controls from around Island 2.
- Completed the removal of access roads on Island 2.
- Completed demobilization activities associated with the temporary floating bridge used to access Island 2.
- Continued loading and transporting tree stumps and staged soil material from Staging Area 2 to Allied Waste's C&C Landfill and Ottawa County Farms Landfill.


Estimated Weekly Volume Hauled to Non-TSCA Landfill Facilities		
Date	Estimated Quantity Non-TSCA material (cubic yards)	Number of Truck Loads Non-TSCA material
Weekly Total	665	19
2010 Total	4,550	130

Note: All values are unofficial, estimated quantities, subject to revision/verification.

Work Planned: July 22 – July 28, 2010

- Continue restoration activities in Removal Area 3B. Activities will include the installation of topsoil, coir logs, restoration seed, and erosion control blankets.
- Begin restoration activities in Removal Area 4B. Initial activities will include the installation of river run rock.
- Complete the installation of resuspension controls at Removal Area 5B.
- Begin the excavation of targeted top-of-bank and floodplain soils from Removal Area 5B.
- Complete construction of Staging Area 1.
- Continue loading and transporting tree stumps and staged soil material from Staging Area 2 to Allied Waste's C&C Landfill and Ottawa County Farms Landfill.


Removal Progress – 2010

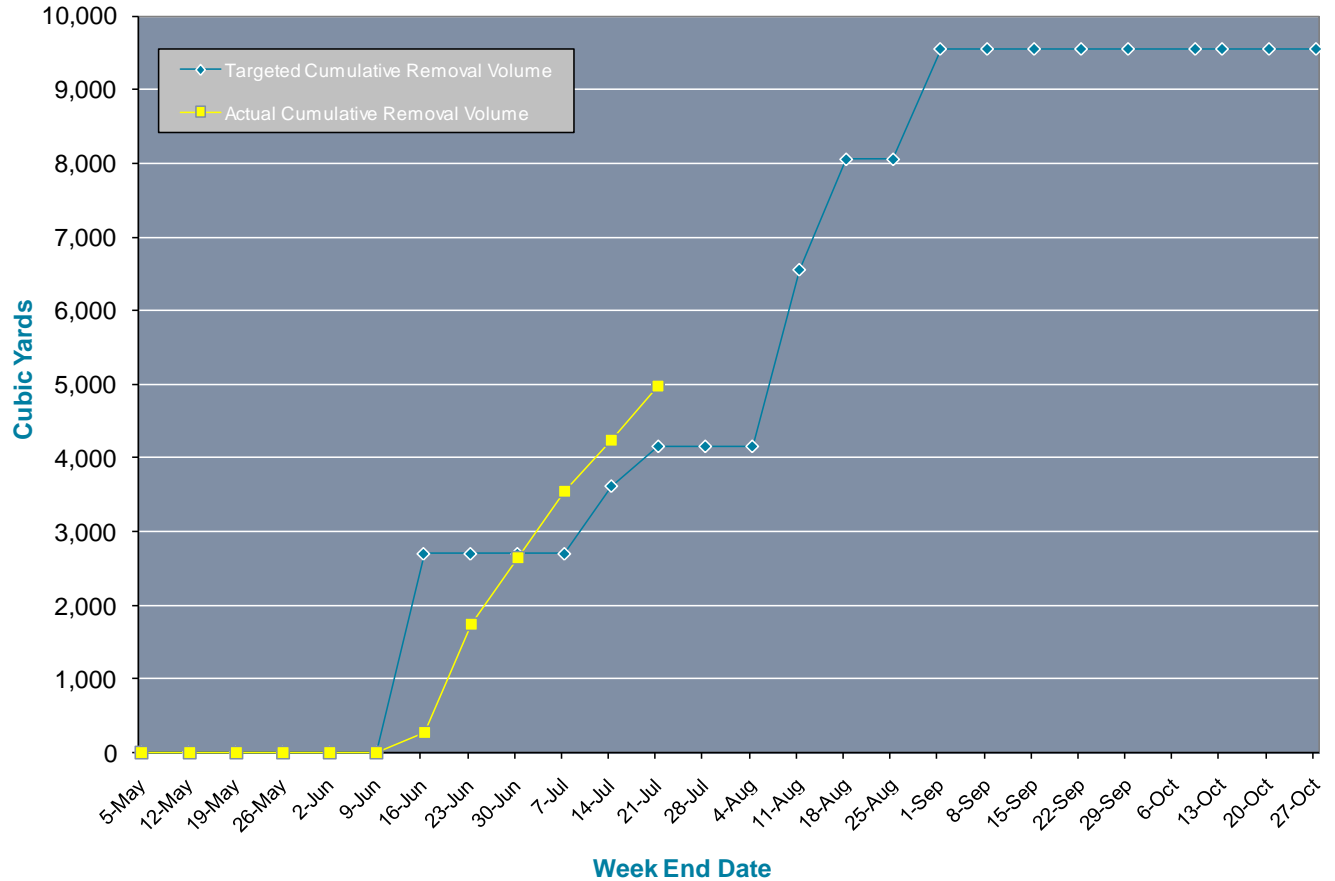

Notes:

Targeted volumes are neat and subject to change due to additional excavation done at request of USEPA.

Removal Progress – 2010

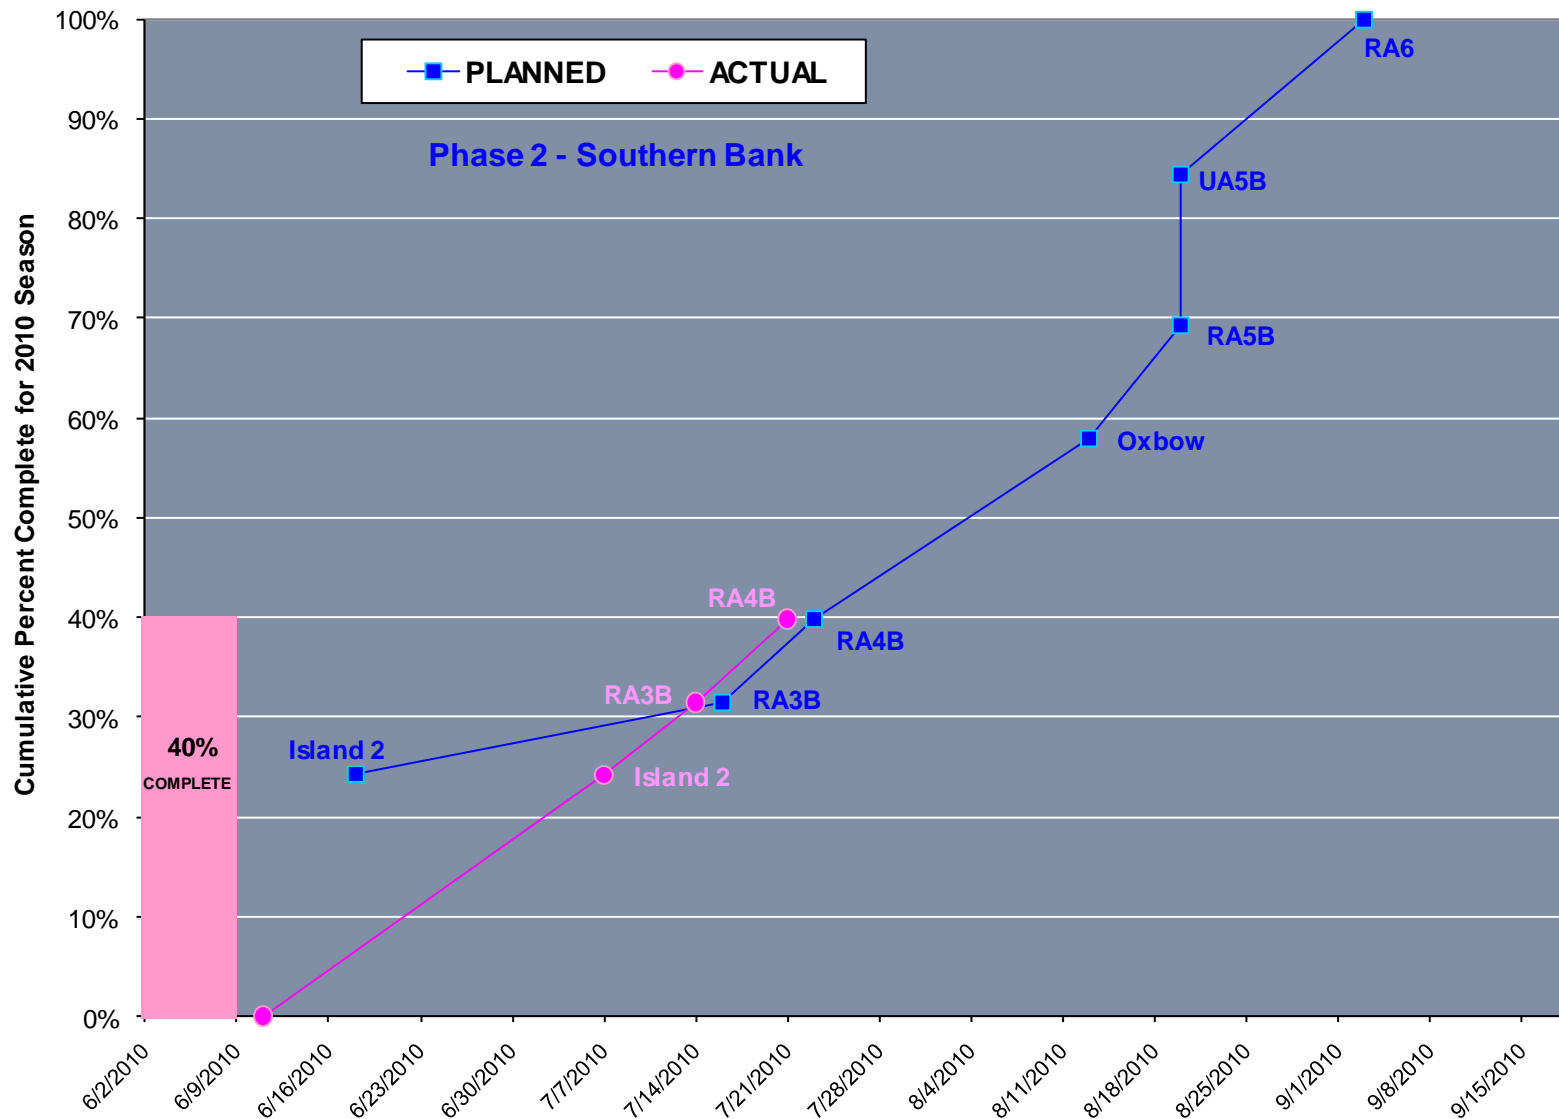

Notes:

'Complete' is defined as removal of all targeted materials as detailed in the Plainwell No. 2 Dam Area Design Report.

Health & Safety Update

- 4 Loss Prevention Observations (LPOs) were completed during this period.
A total of 89 LPOs have been completed for the project to date.

Weather Summary

- No weather delays encountered.

Environmental Monitoring and Construction Quality Assurance Testing

Resuspension/Turbidity Monitoring:

Testing Performed this Week? No ☐ Yes ☒

Exceedances? N/A ☐ No ☒ Yes ☐ If yes, explain:

Dewatering System Discharge Monitoring:

Discharge Flow: 0 gallons (Staging Areas 1 and 2)

Testing Performed this Week? No ☒ Yes ☐

Exceedances? N/A ☒ No ☐ Yes ☐ If yes, explain:

Excavation Verification Sampling:

Testing Performed this Week? No ☐ Yes ☒ Location: Removal Areas 3B and 4B.

Cleanup Standard Achieved? N/A ☐ Yes ☒ No ☐

Issues Encountered/Solutions Advanced

- None.

Equipment on Site

Equipment List	Number Onsite
Komatsu PC-300 Long Reach	1
Komatsu PC-300 w/ bucket	1
Komatsu PC-300 w/ shear	1
HM-300 Off Road Truck	3
Komatsu 320 Loader	1
2,000 Gallon Water Truck	1
FAVCO 40-Ton Crane	1
John Deere 51x Dozer	1
JD Tractor	1

**Plainwell No. 2 Dam Area
Time-Critical Removal Action
Weekly Construction Update
Progress Report #27
Page 5 of 7**

Personnel, Regulatory Staff, and Visitors on Site

Individual/Affiliation	07/15/10	07/16/10	07/17/10	07/18/10	07/19/10	07/20/10	07/21/10
Terra Contracting Staff	14	14	14		14	14	14
American Environmental Group							
JF New	2	2			3	3	3
Georgia-Pacific Staff							
Garry Griffith	X						X
ARCADIS Staff							
Matt Bowman							X
EJ Suardini	X					X	X
Michelle Rumler	X	X					
Caitlin Mahon					X	X	X
Nick Harmer	X				X	X	X
Mike Kohagen	X	X			X	X	X
Steve Garbaciak							X
Anthony Esposito							X
Oversight Personnel							
Sam Borries/USEPA OSC	X				X	X	X
Weston Personnel	X	X	X		X	X	X
Other Agency Staff							
Paul Bucholtz/MDNRE							X
Sharon Hanshue/MDNRE							X
John Lerg/MDNRE							X

Photos from July 15 – July 21, 2010



Demobilizing the temporary floating bridge used to access Island 2.



Removing targeted top-of-bank material in Removal Area 4B.




Seeding and mulching as part of restoration activities on Island 2.



Loading staged material for transportation and disposal at Staging Area 2.

Targeted Removal Areas – Plainwell No. 2 Dam Area

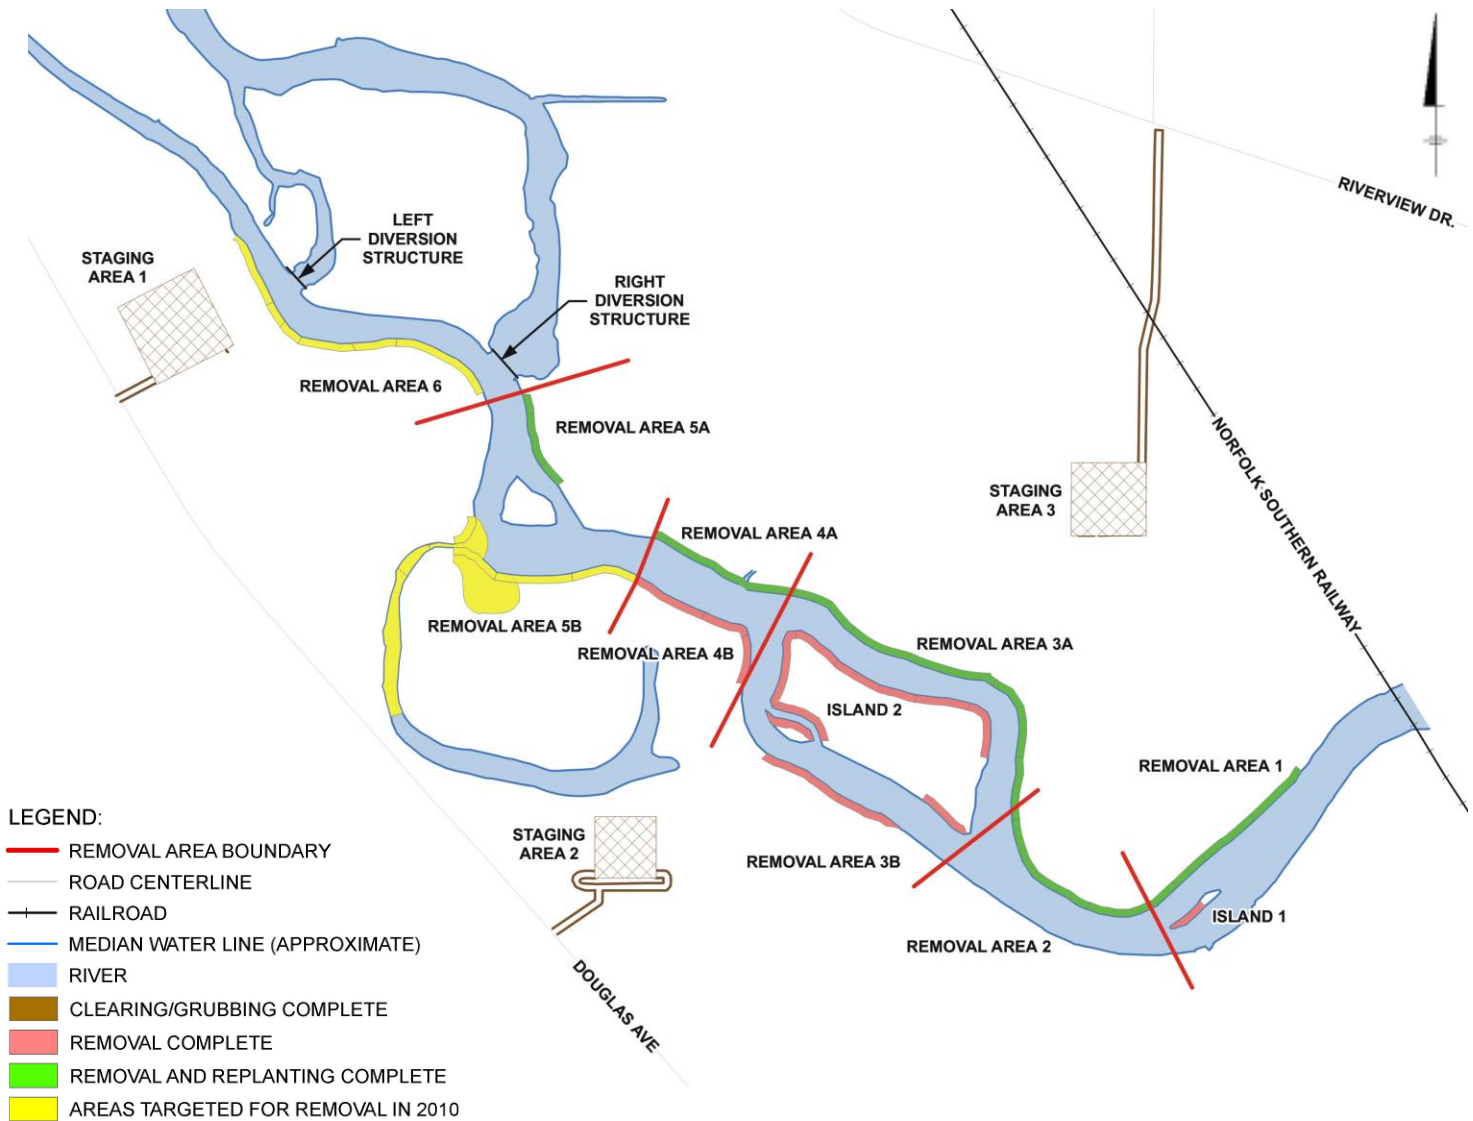

Notes:

All dimensions and features represented on this map are approximate. Actual locations of access roads and staging areas and final boundaries of removal areas will be determined at the time of construction.
