



2007 Cleanup Schedule

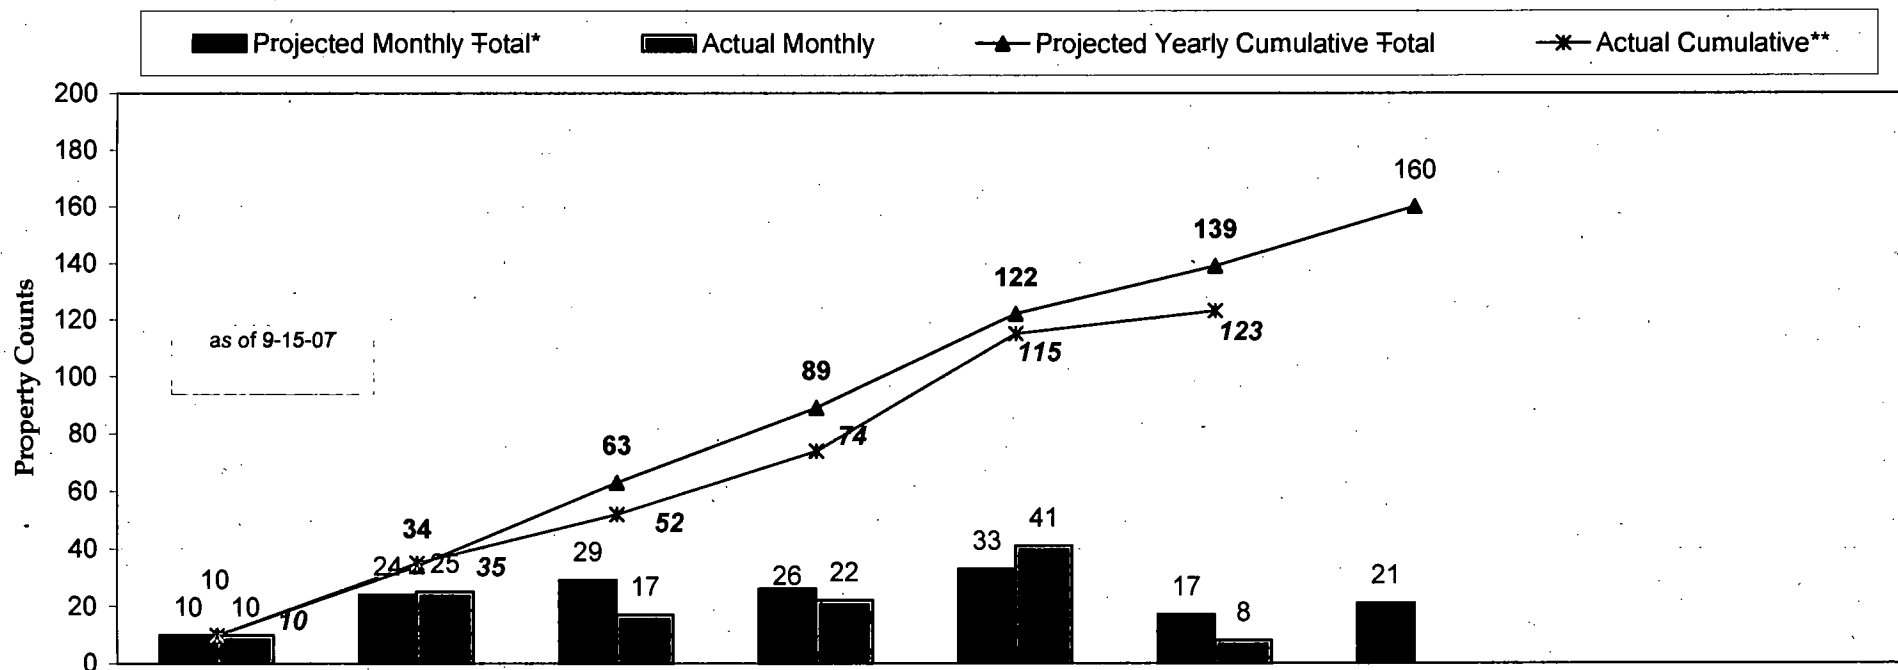


TO Construction Schedule Progress	April	May	June	July	August	September	October	November	December
	TO 42 - (28 properties)								
	Completed 28 of 28								
		TO 43 - (26 properties)							
		Completed 26 of 26							
			TO 44 - (30 properties)						
			Completed 30 of 30						
				TO 45 - (26 properties)					
				Completed 26 of 26					
					TO 46 - (13 properties)				
					Completed 10 of 13				
						TO 47 - (13 properties)			
						Completed 2 of 13			
						TO 48 - (20 properties)			
						Awarded			
						TO 49 - (4 properties)			
						Completed 1 of 4			

2007 Cleanup Schedule

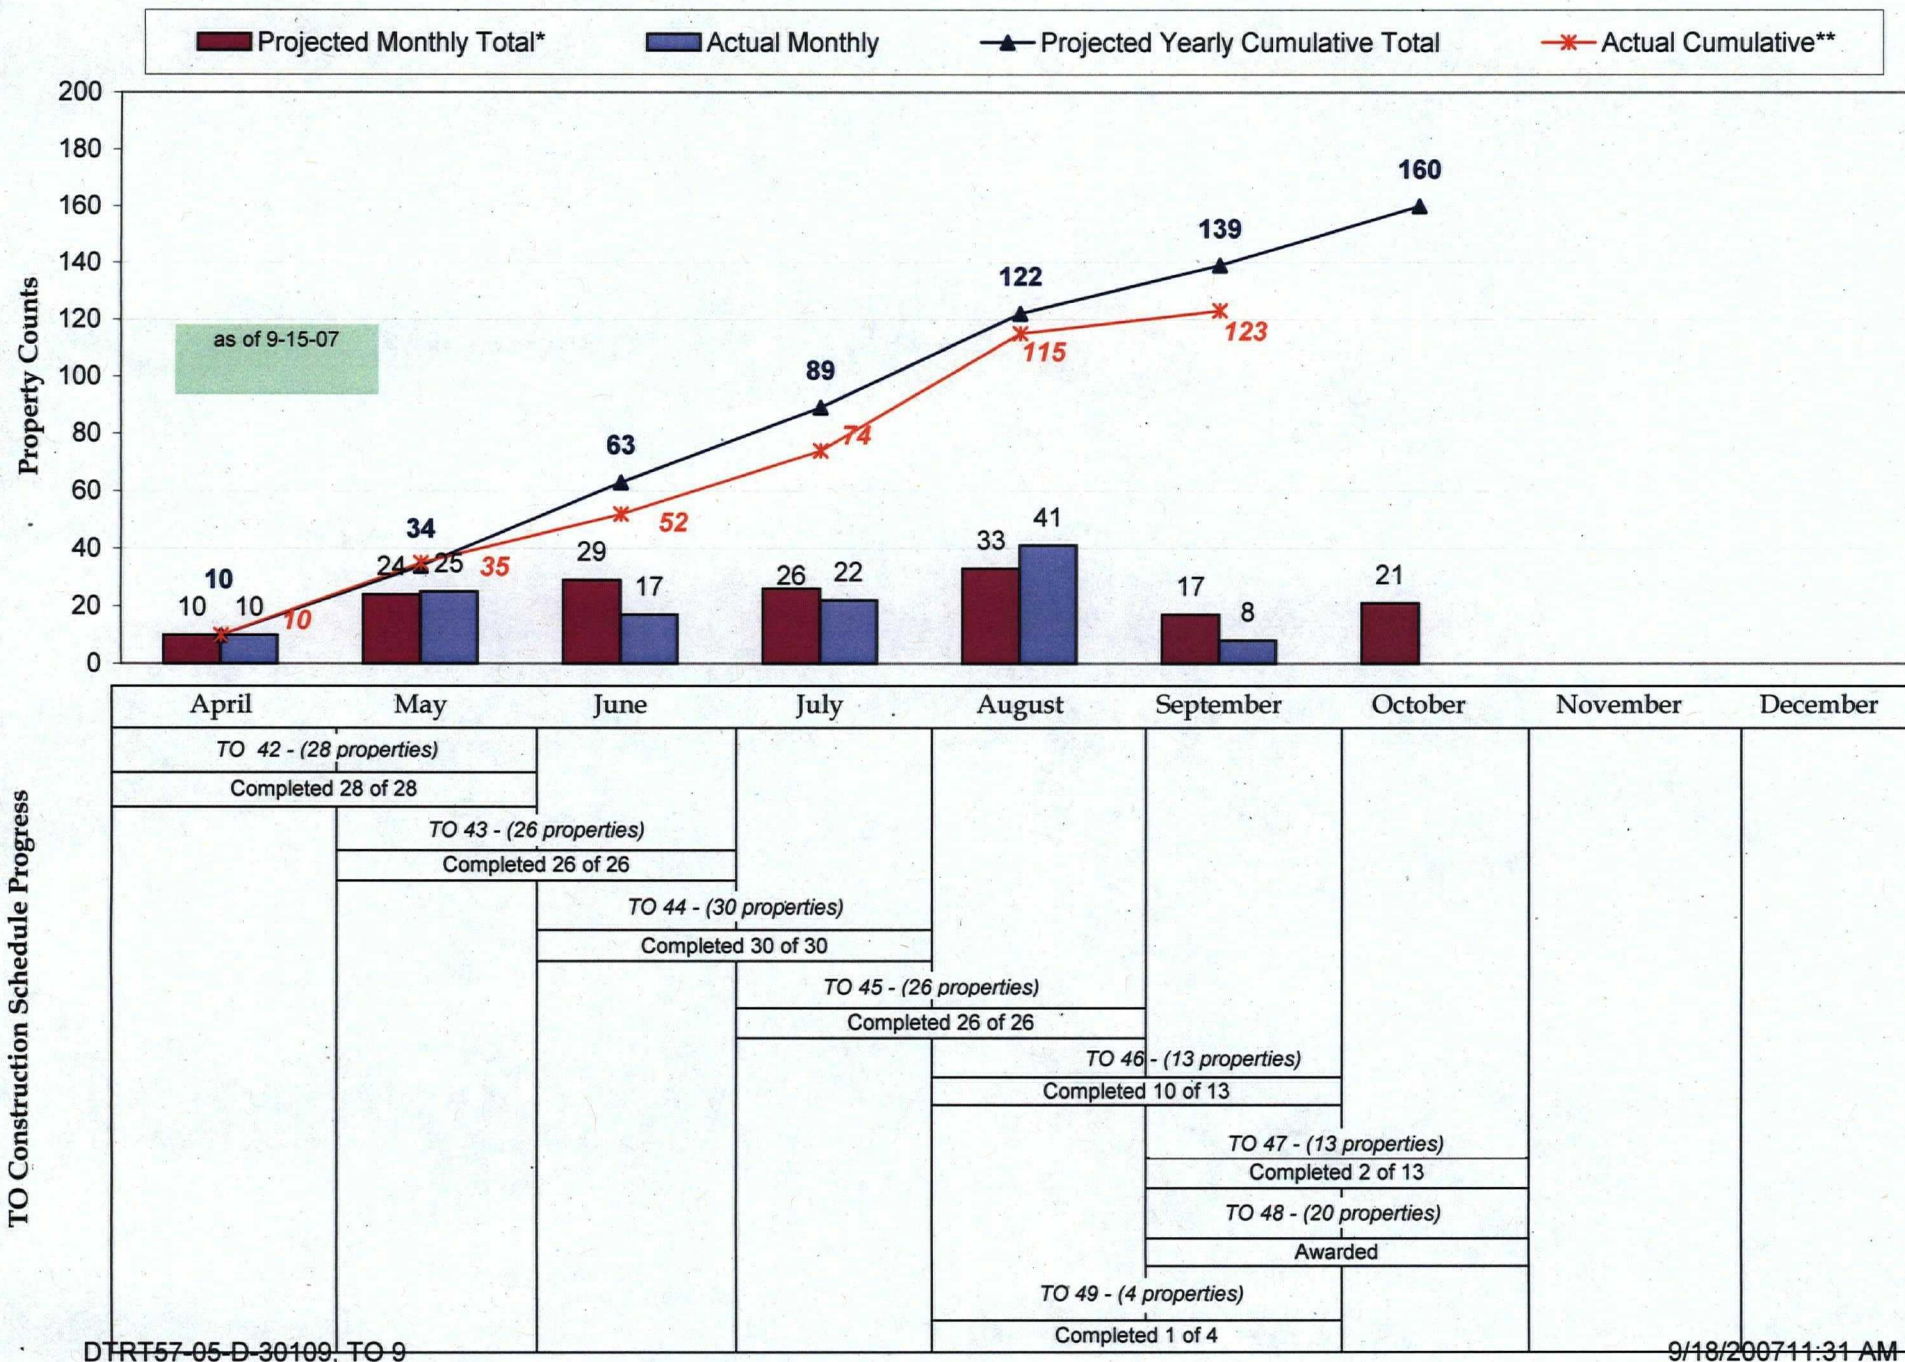

Projected VCI Removals

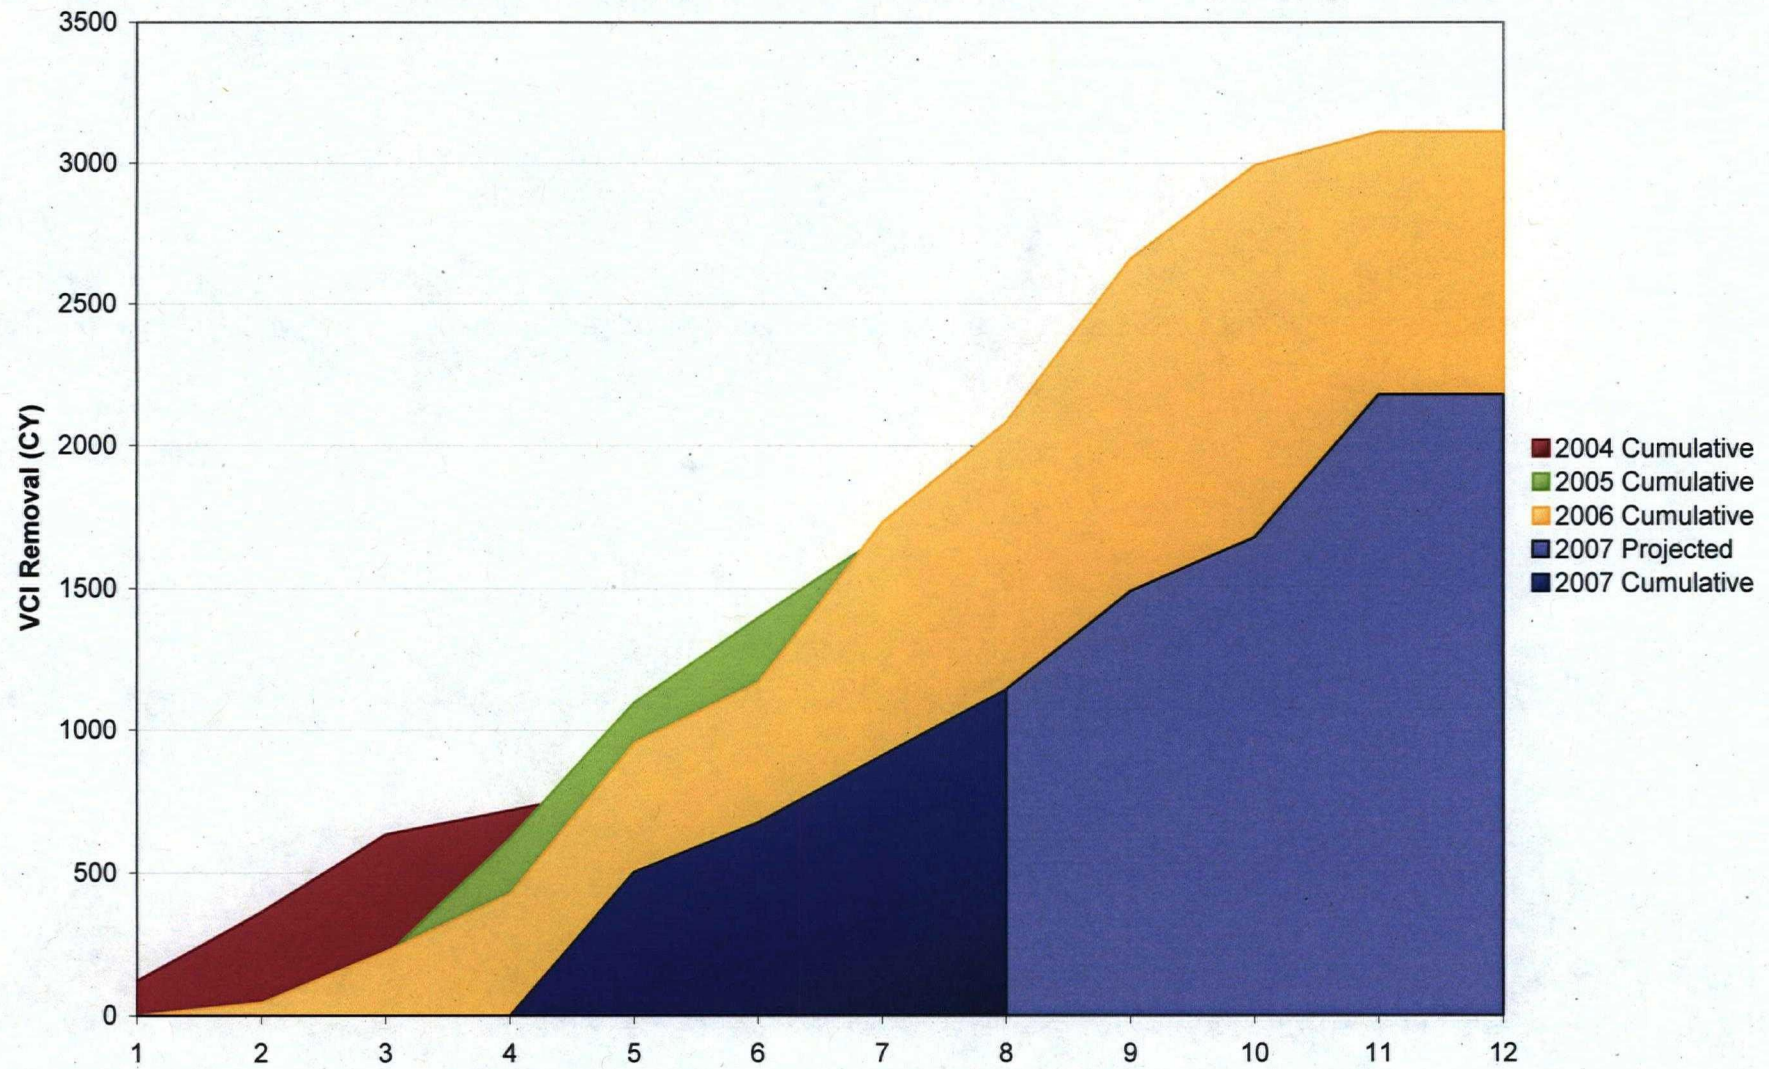

Projected Cumulative Soil Removal

