

Parcel C Remedial Action



Project Update for RU-C2 Hunters Point Naval Shipyard San Francisco, California

Tony Konzen


Project Manager
Contracted Support to NAVFAC BRAC PMO
BRAC Program Management Office West


BCT Meeting September 26, 2013



Parcel C Map



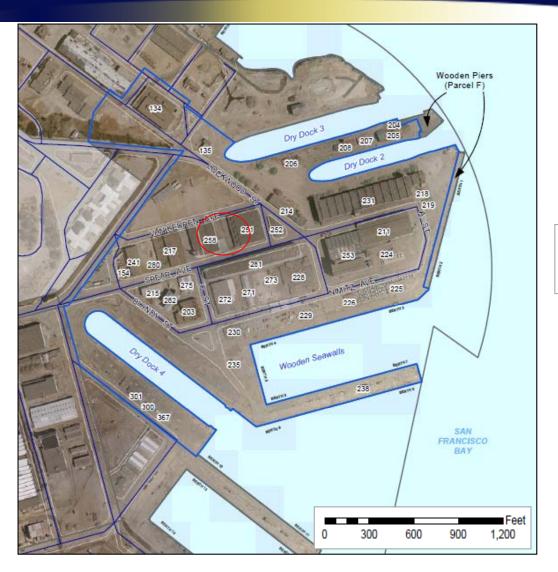






Approximate RU-C2 Boundary



RU-C2 Map



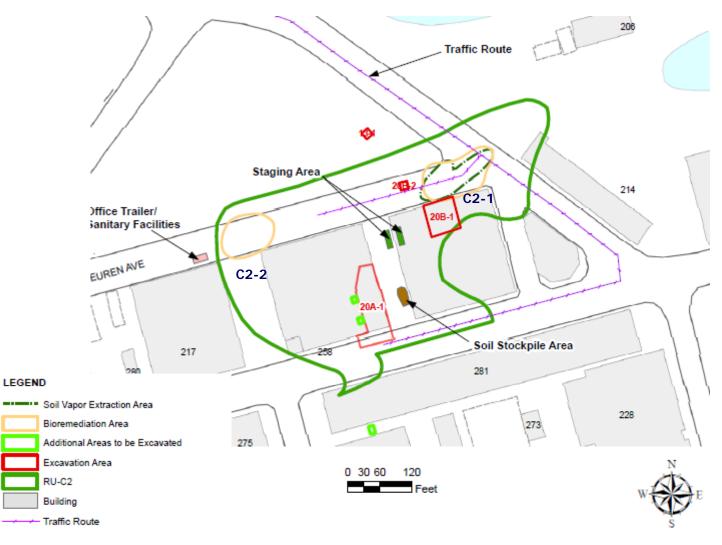



RU-C2 Update




Completed 1-month post injection sampling and started receiving data.

• Began planning for excavations (kick-off meeting held on September 24th).



RU-C2 One Month Post Injection Results – Building 258




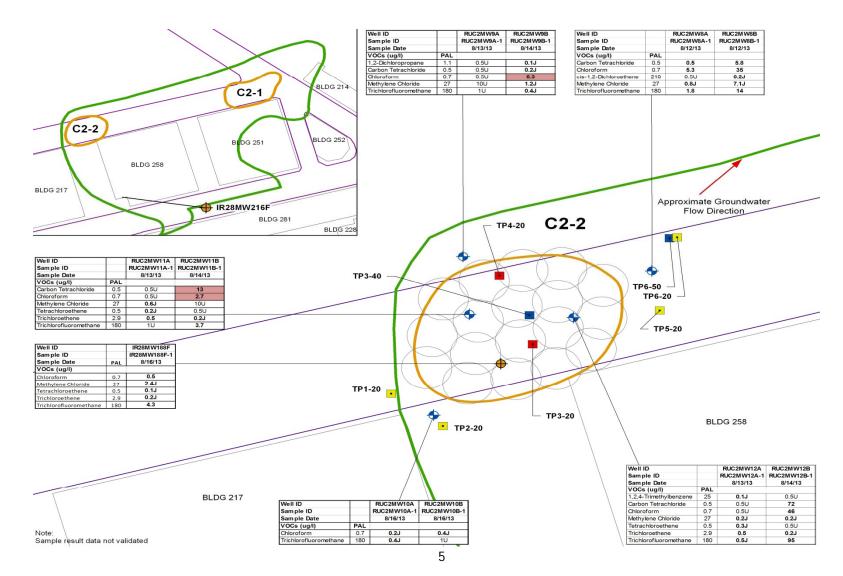



RU-C2 One Month Post Injection Results - Building 251



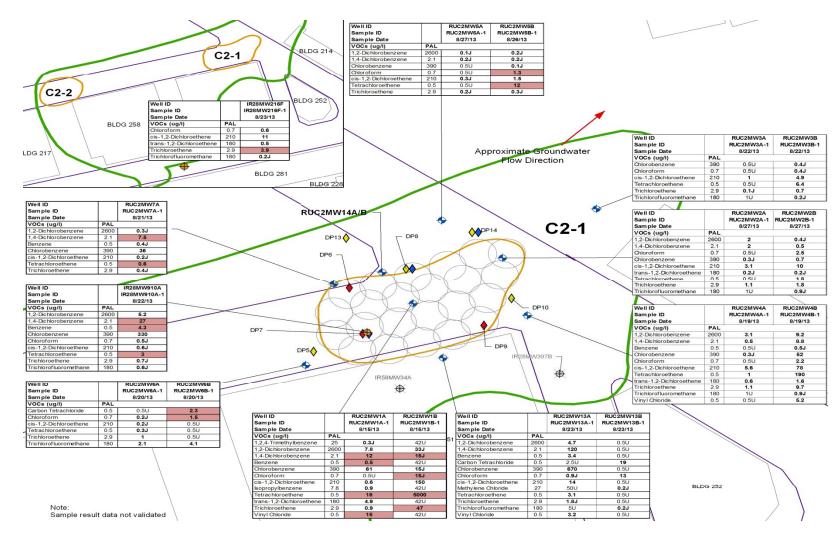



RU-C2 -Schedule



Schedule

• Excavations – 10/1/2013 - 11/9/2013

Groundwater sampling (1 month post injection event) –
 (additional events 3, 6, 9, and 12 months after injections)

8/12/2013 (1-month) Oct 2013 (3-month)

Jan 2014 (6-month)

April 2014 (9-month)

July 2014 (12-month)

Installation of SVE system –
 (following excavation 20B-1 which is adjacent to the SVE area)

11/15/2013
