



Fw: CF GTC RAP Phase II Schedule and Projected Site Inspection Schedule

Douglas.Tanner

to:

Bruce.Olenick, lwasniewski, jmende, Greg Weigel, Lynn.Vanevery, Greg.Mladenka

06/03/2010 09:49 PM

Cc:

Mark.Jeffers

Hide Details

From: <Douglas.Tanner@deq.idaho.gov> Sort List...

To: <Bruce.Olenick@deq.idaho.gov>, <lwasniewski@fs.fed.us>, <jmende@idfg.idaho.gov>, Greg Weigel/R10/USEPA/US@EPA, <Lynn.Vanevery@deq.idaho.gov>, <Greg.Mladenka@deq.idaho.gov>, <Mark.Jeffers@deq.idaho.gov>

Cc: <Mark.Jeffers@deq.idaho.gov>

1 Attachment



CF GTC Phase II Master Schedule 052210.pdf

All,

Let Mark or I know if you would like to take visit and we would be happy to set it up for you. We have high hopes for completing a great project. Dt

---

**From:** john brown <strater4@comcast.net>

**To:** Douglas Tanner; Mark Jeffers

**Cc:** mhart@agrium.com <mhart@agrium.com>; cemmons@norwestcorp.com <cemmons@norwestcorp.com>; kritter@norwestcorp.com <kritter@norwestcorp.com>; pkos@norwestcorp.com <pkos@norwestcorp.com>; JBWillia@agrium.com <JBWillia@agrium.com>

**Sent:** Thu Jun 03 17:18:52 2010

**Subject:** CF GTC RAP Phase II Schedule and Projected Site Inspection Schedule

Doug/Mark,

Please find attached the current schedule to perform the Phase II remedial actions at the Central Farmers site in Georgetown Canyon. We anticipate mobilization to the site towards the end of next week, with a preconstruction meeting to be held at the site on the morning of June 14, 2010. I recommend that you inspect the site at some point during the excavation of the stream channel and again at some point during the placement of the weirs, random boulders, filter gravel and rip rap. The IDWR will also be making at least one inspection of the construction activities, most likely just prior to diversion of the water from the bypass pipe to the new stream channel. Excavation is scheduled to occur throughout July and most of August, with the placement of the stream materials currently scheduled to begin on August 5th. I will keep you apprised of the construction progress in a manner consistent with Phase I reporting, or whenever you require updating on our progress.

Please let me know if you need anything else. I sincerely look forward to working with you on this project!

Best Regards,


JB

USEPA SF



1414695

# CENTRAL FARMERS FERTILIZER FACILITY GEORGETOWN CANYON REMEDIAL ACTION PHASE II

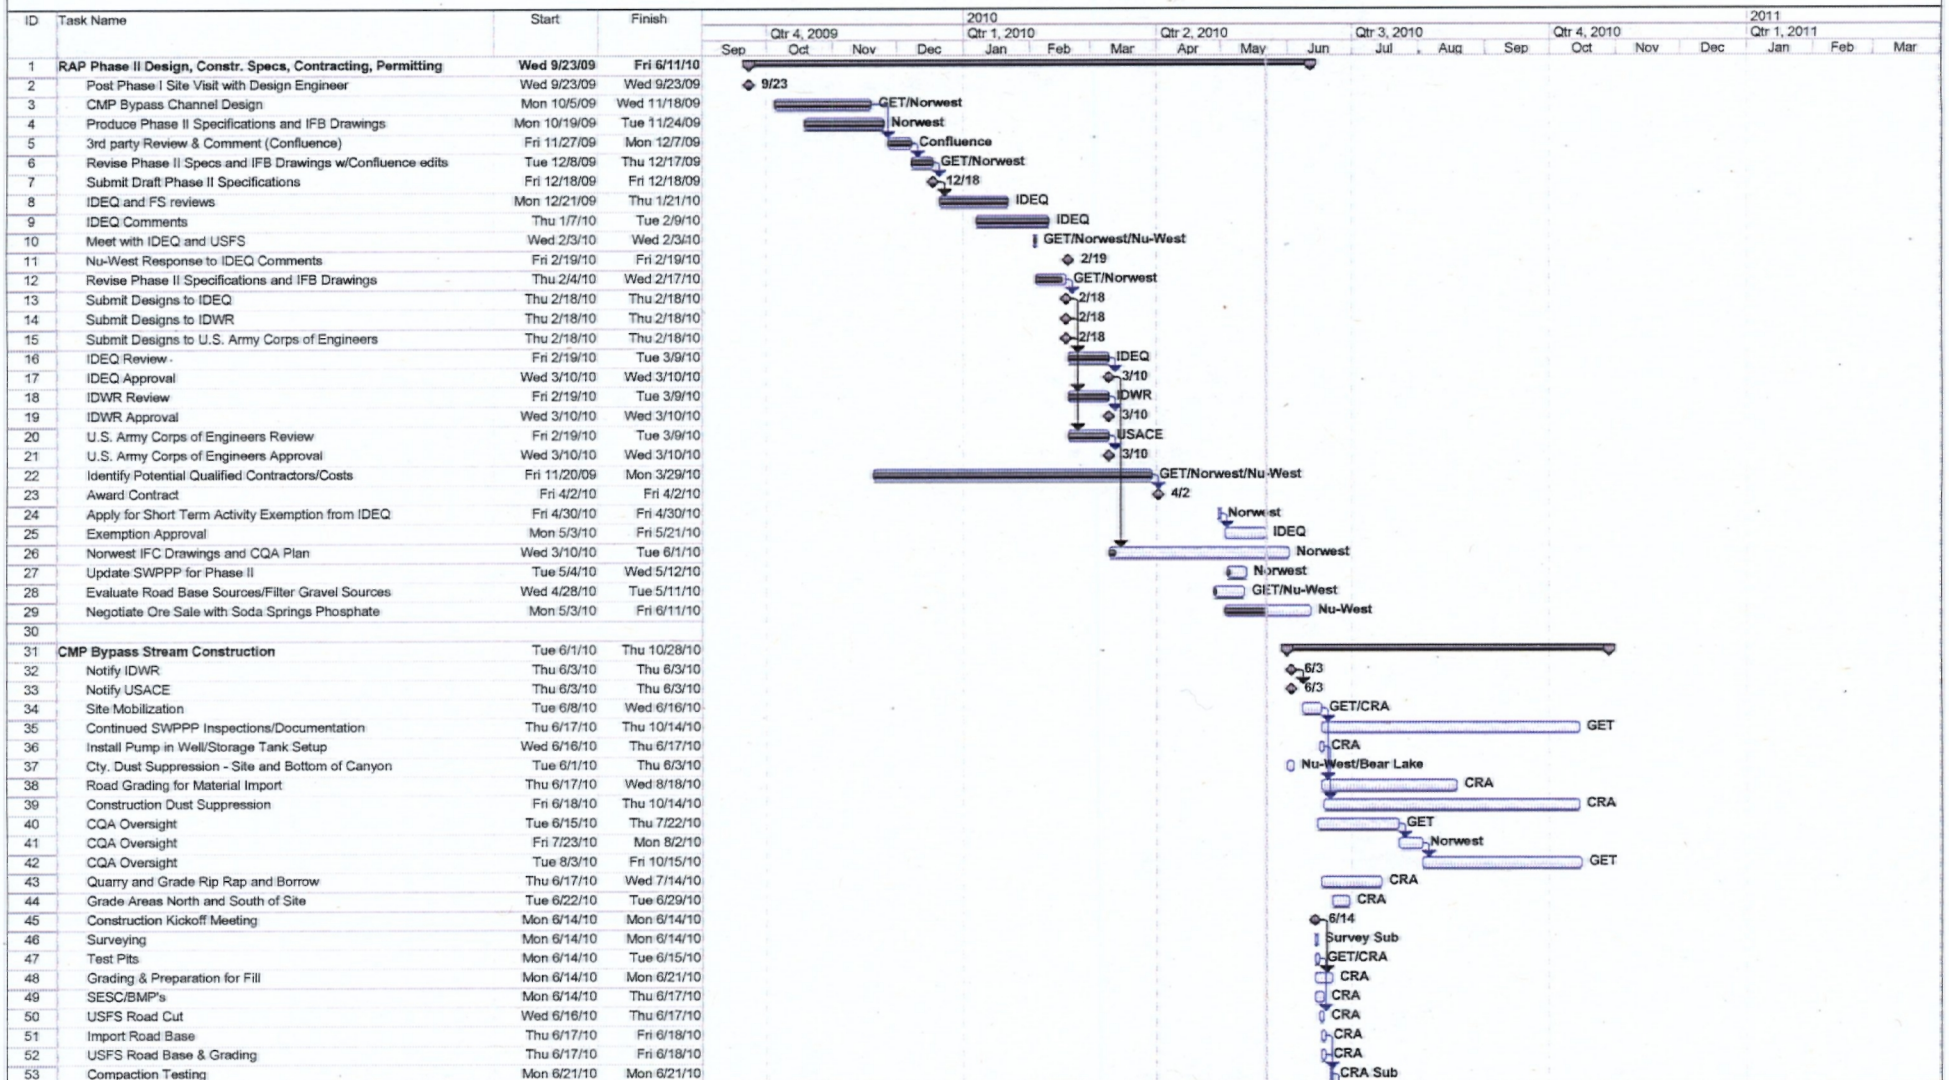

Project: Phase II CMP Bypass Channel Schedule  
Date: Sat 5/22/10

Task Progress Summary External Tasks Deadline  
Split Milestone Project Summary External Milestone



# CENTRAL FARMERS FERTILIZER FACILITY GEORGETOWN CANYON REMEDIAL ACTION PHASE II

ID	Task Name	Start	Finish	2010												2011											
				Qtr 4, 2009				Qtr 1, 2010				Qtr 2, 2010				Qtr 3, 2010				Qtr 4, 2010				Qtr 1, 2011			
				Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar					
54	Surveying	Tue 6/22/10	Tue 6/22/10																								
55	Clean out Sediment Pond	Wed 6/23/10	Thu 6/24/10																								
56	Sedimentation Basin Construction	Mon 6/21/10	Fri 6/25/10																								
57	Compaction Testing	Wed 6/23/10	Thu 6/24/10																								
58	Ore Haul to Soda Springs	Fri 6/25/10	Thu 8/5/10																								
59	Bulk Select Fill Production	Wed 6/23/10	Tue 6/29/10																								
60	Compacted Fill Placement at Sed Pond	Tue 6/29/10	Mon 7/5/10																								
61	Compaction Testing	Wed 6/30/10	Fri 7/2/10																								
62	Surveying	Mon 7/5/10	Mon 7/5/10																								
63	Fence Removal	Mon 6/28/10	Fri 7/2/10																								
64	Bldg Foundation Removal & Misc Debris	Tue 6/29/10	Tue 7/6/10																								
65	Construct Dewatering Sediment Pond	Wed 6/30/10	Thu 7/1/10																								
66	Grubbing/Prestrip Slag on Channel Excavation Areas	Tue 6/29/10	Fri 7/9/10																								
67	Improve On-site Roads	Thu 6/24/10	Mon 6/28/10																								
68	Channel Excavation & Fill Placement	Fri 7/2/10	Tue 8/24/10																								
69	Obtain Geotechnical Samples	Wed 7/14/10	Thu 7/15/10																								
70	Surveying	Fri 7/16/10	Fri 7/16/10																								
71	Surveying	Fri 8/6/10	Fri 8/6/10																								
72	Obtain Soil Samples for Nutrient Amendment	Wed 8/4/10	Wed 8/4/10																								
73	Surveying	Fri 8/27/10	Fri 8/27/10																								
74	Cover C&D landfill	Mon 8/23/10	Fri 8/27/10																								
75	Rip Rap Screening, Sorting, and Stockpiling	Fri 7/9/10	Thu 7/22/10																								
76	Import Filter Stone & Stockpile	Wed 7/21/10	Wed 7/28/10																								
77	Obtain/Testing Geotechnical Samples	Thu 7/22/10	Fri 7/23/10																								
78	Rock Placement - Filter Stone, Weirs, Sills, & Boulders	Thu 8/5/10	Wed 9/15/10																								
79	Notify IDWR Prior to Channel Diversion from CMP	Wed 9/15/10	Wed 9/15/10																								
80	IDWR Inspection	Wed 9/15/10	Wed 9/15/10																								
81	Topsoil (Channel)	Thu 9/16/10	Wed 9/29/10																								
82	Surveying	Thu 9/30/10	Fri 10/1/10																								
83	Tank Spring Channel Excavation	Mon 9/13/10	Mon 9/13/10																								
84	Abandon Tank Spring Drop Inlet	Mon 9/13/10	Mon 9/13/10																								
85	Bypass System Setup and Cofferdam	Fri 9/10/10	Thu 9/16/10																								
86	Survey New ROW for Easement Fence Alignment	Wed 9/1/10	Wed 9/1/10																								
87	Install Fence and Gates	Thu 9/16/10	Tue 9/21/10																								
88	CMP Abandonment	Thu 9/16/10	Thu 9/16/10																								
89	CMP Crossings	Thu 9/16/10	Thu 9/23/10																								
90	Remove Power Poles	Mon 9/13/10	Wed 9/15/10																								
91	Bypass System Removal	Tue 9/28/10	Mon 10/4/10																								
92	Tank Spring Filter Stone & Rip Rap	Fri 10/1/10	Mon 10/4/10																								
93	Syncline Spring Filter Stone & Rip Rap	Mon 10/4/10	Mon 10/4/10																								
94	Culverts	Mon 10/4/10	Tue 10/5/10																								
95	Willow, Alder, Dogwood, & Snowberry Planting	Fri 10/1/10	Tue 10/5/10																								
96	Hydro seeding (Spoil Areas)	Tue 9/14/10	Tue 9/21/10																								
97	Reclaim Borrow Areas	Tue 9/14/10	Wed 9/15/10																								
98	Hydro seeding & ECS (Channel)	Tue 10/5/10	Thu 10/14/10																								
99	Surveying	Fri 10/1/10	Mon 10/4/10																								
100	Controlled Burn with County Permit	Mon 10/11/10	Tue 10/12/10																								
101	Stormwater Inspection	Fri 10/15/10	Fri 10/15/10																								
102	Project Complete	Fri 10/15/10	Fri 10/15/10																								
103	Demobilization	Mon 10/18/10	Tue 10/19/10																								
104	Completion Certificate to USACE	Wed 10/20/10	Thu 10/21/10																								
105	Post Construction Photos to USACE	Fri 10/22/10	Thu 10/28/10																								
106	Notice of SWPPP Termination to EPA	Tue 10/19/10	Tue 10/19/10																								

Project: Phase II CMP Bypass Channel Schedule	Task	Progress	Summary	External Tasks	Deadline
Date: Sat 5/22/10	Split	Milestone	Project Summary	External Milestone	



# CENTRAL FARMERS FERTILIZER FACILITY GEORGETOWN CANYON REMEDIAL ACTION PHASE II



Project: Phase II CMP Bypass  
Channel Schedule  
Date: Sat 5/22/10

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone
