



## **Site 12 Field Work Update**

## **Former Naval Station Treasure Island**

**October 2018 BCT Meeting**


# Site 12 Field Work Update



- **Remaining Chemical Excavations**
  - **41 excavations on the northern end of Site 12**
    - Excavation locations being surveyed currently
    - Pre-excavation sampling to begin next week
    - Excavations start 11-26-18



Direct Push Drill Rig for  
Pre-excavation Sampling

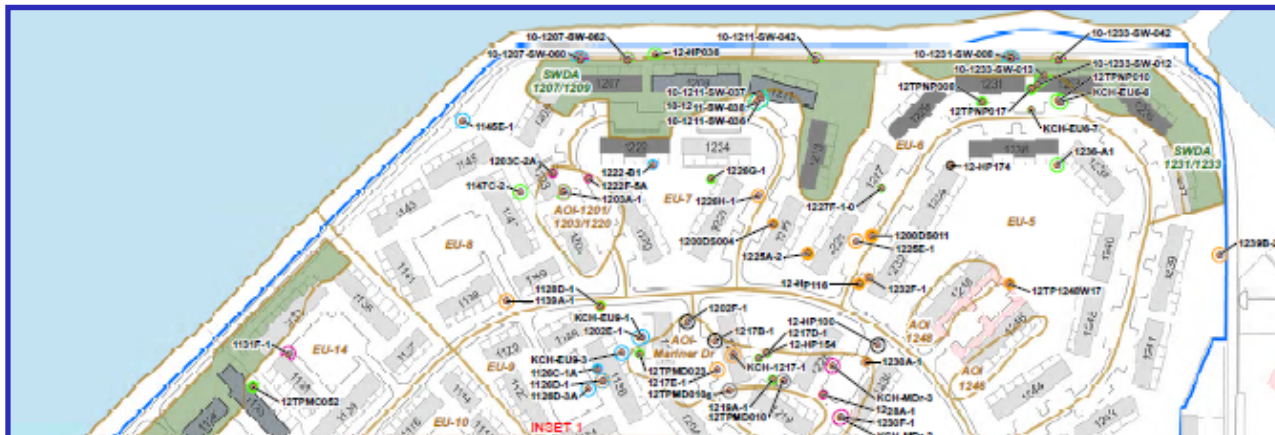

41 Discrete Chemical Excavation Locations



Surveying of Discrete  
Excavation Locations

# Site 12 Field Work Update



## • Building Demolitions

### – Buildings 1126 & 1217

- ACM survey complete and materials removed from buildings
- Radiological scanning ongoing
- Demolition to begin November 26, 2018



Buildings 1127 & 1217



Radiological Scanning at Building 1217

## Site 12 Field Work Update



- **Monitored groundwater wells in the Gateview Arsenic/TPH Area**
  - Sampling event concluded October 11, 2018
  - Results will be reported in the Q3Q4 Basewide Groundwater Report (March, 2019)



## Upcoming Field Work




- **Extension of previous excavation**
  - Additional 4000 cubic yards of soil for debris
  - Extends from southern margin of previous excavation
  - November-February
  - Rad scanning due to debris to be conducted at Site 32




# Upcoming Field Work



- **Removal of 2 Underground Storage Tanks**
  - Discovered in 2016 Remedial Action
  - Lot next to Building 225 (East of Site 20)
  - 2 Tanks, approximately 1000 gallons
  - Gilbane to remove in December

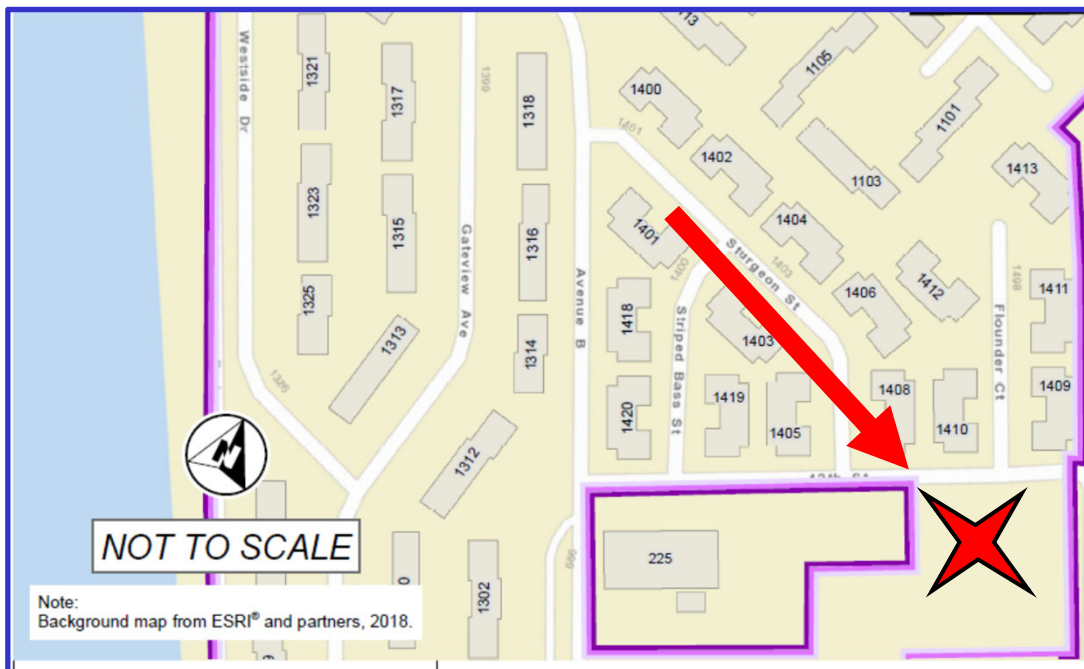

# Site 12 Project Schedule

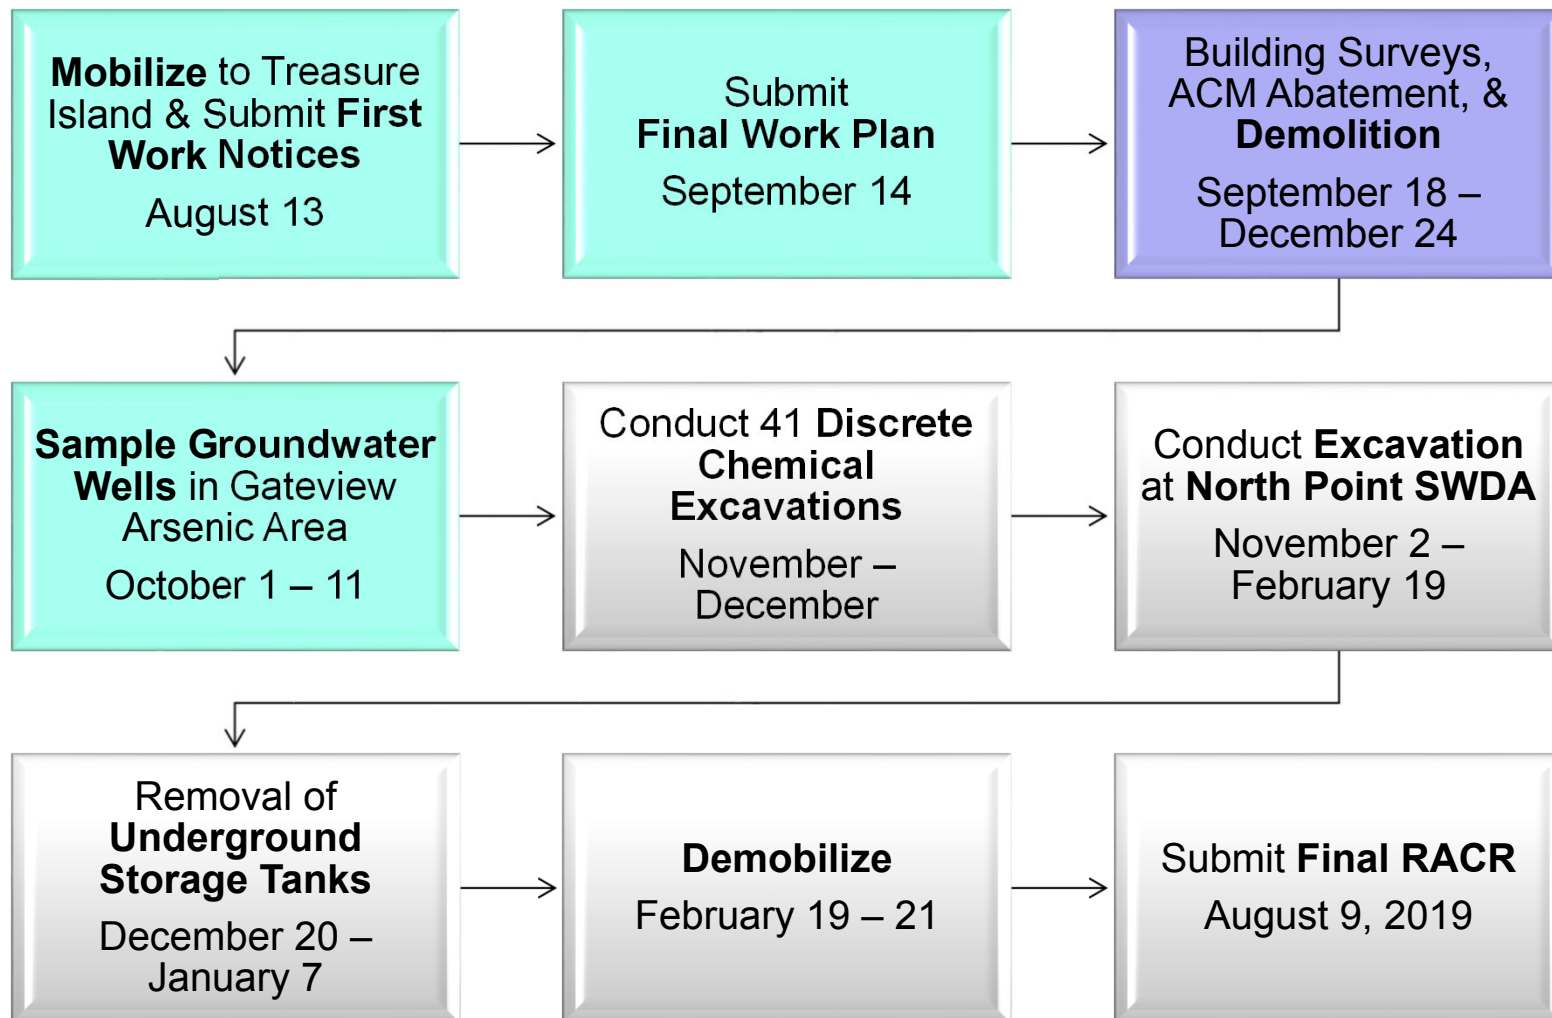

# QUESTIONS?
