


2/22/06
Mtg w/ Dufont
ANDER

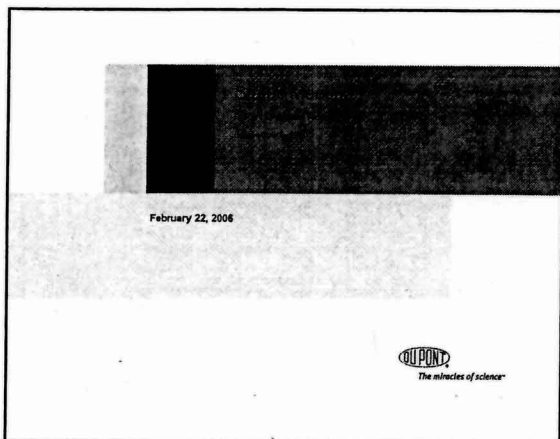

Agenda	
Agenda review/revision	5 min
SWMU 52 ISM Project Review	40 min
Salem Canal pre-design investigation status and workplan review status	10 min
Delaware River groundwater to surface water workplan overview and review status	10 min
SWMU 8:	
• Additional well installation, sampling and reporting status	10 min
• Surface water sampling and workplan review status	10 min
RFI Phase IVa workplan review status	5 min
Conceptual Model status	5 min
Science Advisory Board	5 min
Environmental Indicators CA 400 and 550	10 min
Overall project schedule and other activities	10 min
adjourn	Total 2 hours

201006 DUPONT CONFIDENTIAL

Salem Canal Pre-design investigation and work plan review status	
Pre-design work plan submitted 15 November 2005	
Under Agency Review	
• Groundwater and geotechnical investigation along length of canal for cut off wall design - Field work completed in advance of agency review	
• 45 Day water level monitoring	
• 25 of borings	
• 17 of groundwater samples	
• 3 of wells	
• Groundwater model of cut off wall -	
• Incorporated into site wide optimization model - ongoing - May completion	
• Sediment investigation	
• Proposed sediment investigation/delineation plan	
• Proposed sediment quality benchmarks based on contemporary published information	
• Field work pending agency review	
• Pre design started	
• Design report anticipated December	

201006 DUPONT CONFIDENTIAL
