



Project Summary Report

SDMS Document ID



2022518

Contractor's Name: Project Resources Inc.
Contract Number: DACA45-01-D-0001 Task Order 014
Site Name & Location: VB I-70 Superfund Site

Time Period:	06MAR04	12MAR04	Report #	034
--------------	---------	---------	----------	-----

Project Safety Report

Days Worked To Date:	205	Date of Last Accident:	01MAR04
Project Man-hours To Date:	35,121.00	Hours Worked w/o Accident:	1,651.50
Comments/Issues:	None.		

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

**PUBLIC
DOCUMENT**

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Site Set-up	21JUL03	11AUG03		21JUL03*	12AUG03*		100
Remediation	12AUG03	24AUG03		13AUG03*	12DEC03		100
Property Close-Out	15SEP03	20FEB04		16SEP03*	20FEB04		70
Final Report	02FEB04	20Feb04					0
PROJECT	21JUL03	20FEB04		21JUL03*	20FEB04		95

* Actual dates.

Conditions/Events which have/may result in delayed progress

None.

Current Project Activities

- Five homes remediated, with a total of 150 to date.
- Procurement of transportation and disposal underway.
- Property owners were contacted and restoration appointments were scheduled.
- Restoration appointments were completed at 12 properties, for a total of 70 restoration appointments to date.
- Digital copies of property files were created and property completion packets composed.
- Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, March 10, 2004 for a weekly meeting.
- Crew rotated back 08MAR04.

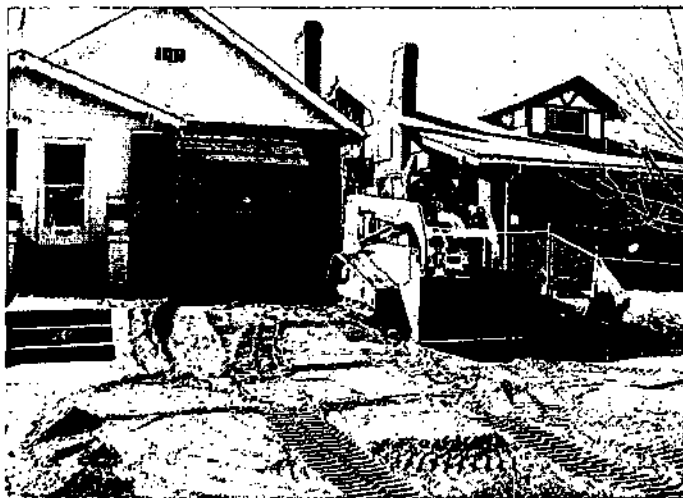
Upcoming Project Activities

- Five properties scheduled for remediation next week.
- Ten restoration appointments scheduled for next week.

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	145	150	
Square Footage Excavated	SF	478,784	492,924*	

*Approximate totals. Adjusted to reflect actual final square footage.

Project Photos**Additional Comments/Observations**

☐ None

Signed: _____

Date: _____

13MAR04
