

## **Project Summary Report**



Contractor's Name:

Project Resources Inc.

Contract Number:

W9128F-04-D-0016

Site Name & Location:

**VB I-70 Superfund Site** 

Time Period: 15MAYU4 21MAYU4 Report# UU8:	Time Period:	15MAY04	21MAY04	Report #	800
---	--------------	---------	---------	----------	-----

**Project Safety Report** 

Days Worked To Date:	51	Date of Last Accident:	28APR04	
Project Man-hours To Date:	11,675.50	Hours Worked w/o Accident:	5,432	
Comments/Issues: None.				

Project QC/QA Report

Project QC/QA Repo	PL	
Project Deficiencies:	None.	- OCUMENT
Comments/Issues:	None.	

**Project Schedule Report** 

Task	Scheduled			Current			%
I dSK	Start	Finished D	DUR	Start	Finished	DUR	Complete
Remediation	01APR04	15JUN04		1APR04*	15JUN04		65
Property Close-Out	01MAY04	30SEP04		01MAY04*	30SEP04		25
Final Report	01DEC04	15JAN05	-				0
PROJECT	01APR04	28JAN05		01APR04*	28JAN05		50

<sup>\*</sup> These dates are actual dates.

	Conditions/Event	ts which	have/may	result (n	delayed	l progress
--	------------------	----------	----------	-----------	---------	------------

N	o	n	e	

## **Current Project Activities**

- Thirteen homes remediated, with a total of fifty-nine to date.
- Property owners were contacted and restoration appointments were scheduled.
- Restoration appointments were completed at 5 properties, for a total of 186 restoration appointments year to date.
- Digital copies of property files were created and property completion packets composed.
- Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, May 19, 2004 for a weekly meeting.
- Site Coordination team attended Xeriscape Training with the Denver Water Board May 21, 2004.
- Site Coordination team composing Access Agreements to be sent to all candidate properties.

## **Upcoming Project Activities**


Crew scheduled to remediate 8 homes next week.

**Project Quantities** 

ltem	Unit	Last Report	To Date	Comment
Completed Properties	Property	46	59	
Square Footage Excavated	\$F	198,469	238,969	

**Project Photos** 



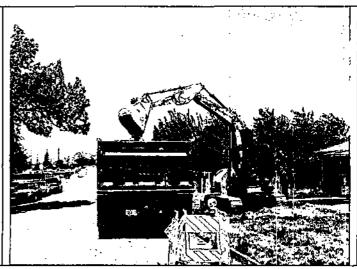

## **Additional Comments/Observations**

□ None

Signed: Michelle Smith \_\_\_\_\_\_\_ Date:
