



Project Summary Report

Contractor's Name: **Project Resources Inc.**
Contract Number: **W9128F-04-D-0029**
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	19JUN04	25JUN04	Report #	002
--------------	----------------	----------------	----------	------------

Project Safety Report

Days Worked To Date:	10	Date of Last Accident:	N/A
Project Man-hours To Date:	2,822.50	Hours Worked w/o Accident:	2,822.50
Comments/Issues: None.			

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		10
Property Close-Out	31OCT05	15MAR05					0
Final Report	01DEC04	15JAN05					0
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		5

* These dates are actual dates.

Conditions/Events which have/may result in delayed progress

None.

Current Project Activities

- Property owners were contacted and restoration appointments were scheduled.
- Eleven properties remediated to backfill this week.
- Eleven restoration appointments completed for a total of 218 to date.
- Four completion appointments completed.
- Digital copies of property files were created and property completion packets composed.
- Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, June 16, 2004 for a weekly meeting.
- Procurement of materials and subcontractors for new Contract.
- IHI, air monitoring subcontractor, on site 6/25/04 to conduct random community air monitoring.

Upcoming Project Activities


- Remediation of 10 homes scheduled for next week.
- IHI, air monitoring subcontractor, will be on site to conduct two days of monitoring.

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	0	11	
Square Footage Excavated	SF	0	43,383*	

*Approximate totals

Project Photos

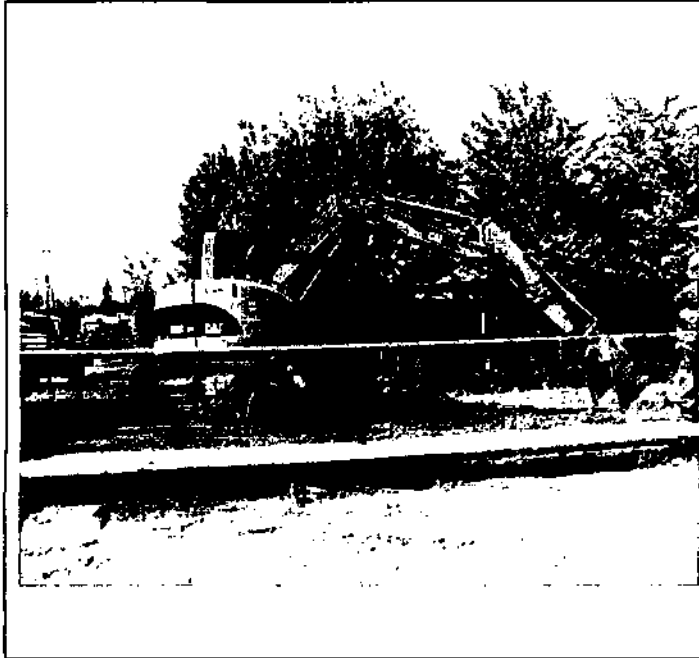

Additional Comments/Observations

☐ None

Signed: *Michelle Smith*

Date:

25JUN04
