



Project Summary Report

SDMS Document ID



2027805

Contractor's Name: **Project Resources Inc.**
Contract Number: **W9128F-04-D-0029**
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	26JUN04	02JUL04	Report #	003
--------------	----------------	----------------	----------	------------

Project Safety Report

Days Worked To Date:	17	Date of Last Accident:	N/A
Project Man-hours To Date:	4,664.25	Hours Worked w/o Accident:	4,664.25
Comments/Issues:	None.		

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		15
Property Close-Out	31OCT05	15MAR05					0
Final Report	01DEC04	15JAN05					0
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		5

* These dates are actual dates.

Conditions/Events which have/may result in delayed progress

None.

Current Project Activities

<ul style="list-style-type: none">Property owners were contacted and restoration appointments were scheduled.Ten properties remediated to backfill this week.Ten restoration appointments completed for a total of 228 to date.Seventeen completion appointments completed.Digital copies of property files were created and property completion packets composed.Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, June 30, 2004 for a weekly meeting.Procurement of sprinkler system subcontract underway.
--

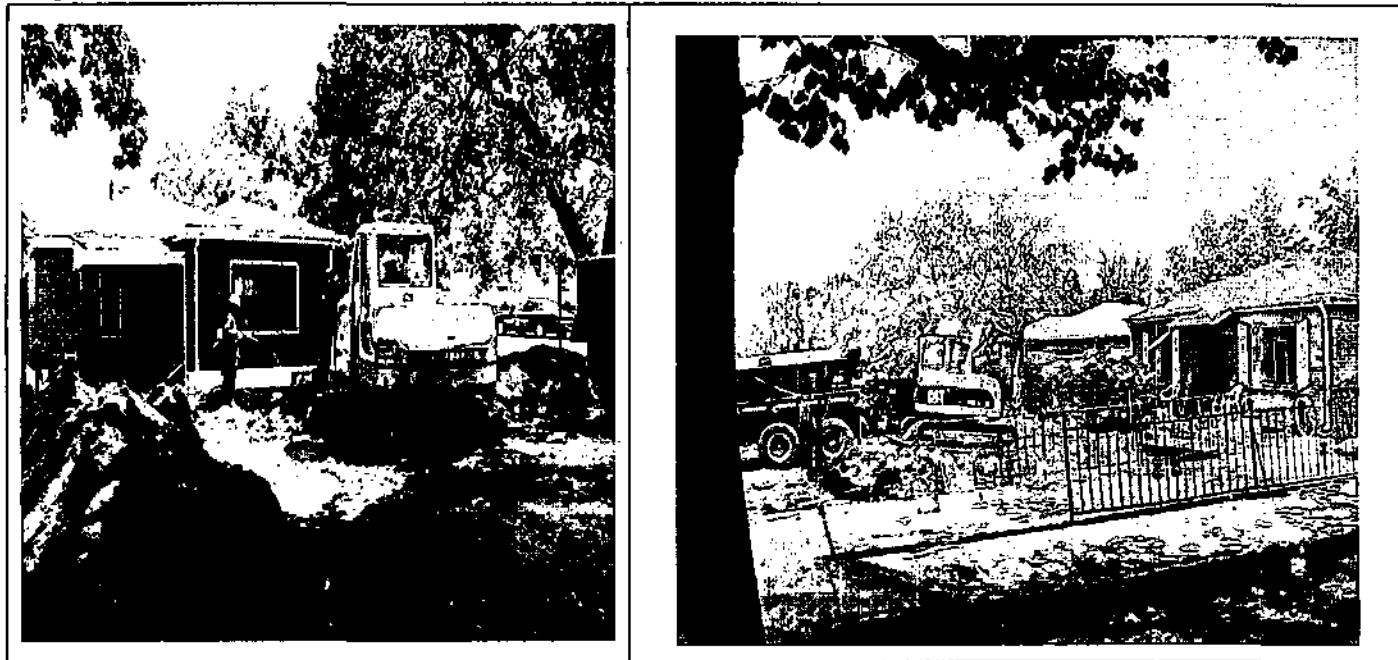
Upcoming Project Activities

<ul style="list-style-type: none">Remediation of 10 homes scheduled for next week.Restoration appointments to continue, with fifteen scheduled for next week.Site walk for sprinkler system subcontractors scheduled for July 8, 2004.
--

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	10	21	
Square Footage Excavated	SF	43,383	84,884*	

*Approximate totals

Project Photos**Additional Comments/Observations**

☐ None

Signed: *Michelle Smith*

Date:

02JUL04
