

Project Summary Report



Contractor's Name:

Project Resources Inc.

Contract Number:

W9128F-04-D-0029

Site Name & Location:

VB I-70 Superfund Site

Time Period:	24JUL04	30JUL04	Report #	007
				1

Project Safety Report

Days Worked To Date:	45	Date of Last Accident:	N/A
Project Man-hours To Date:	12,621.75	Hours Worked w/o Accident:	12,621.75
Comments/Issues: None.		<u> </u>	

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			%
	Start	Finished	DUR	Start	Finished	DUR	Complete
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		35
Property Close-Out	310CT05	15MAR05		·	-		0
Final Report	01DEC04	15JAN05					0
 -	 			· ·	 -		 -
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		20

^{*} These dates are actual dates.

Conditions/Events which have/may result in delayed progress

М	_	_	_	
ľ	u	•	ш	

Current Project Activities

- Property owners were contacted and restoration appointments were scheduled.
- · Nine properties remediated to backfill this week.
- Twelve restoration appointments completed for a total of 282 to date.
- Ten completion appointments completed.
- Digital copies of property files were created and property completion packets composed.
- Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, July 28, 2004 for a weekly meeting.
- Out of town crew rotated this weekend and returned on Monday July 26, 2004.


Upcoming Project Activities

- Remediation of 9 homes scheduled for next week.
- Restoration appointments to continue, with 12 scheduled for next week.

Project Quantities

item	Unit	Last Report	To Date	Comment
Completed Properties	Property	47	56	
Square Footage Excavated	SF	189,976	235,837*	

^{*}Approximate totals
Project Photos

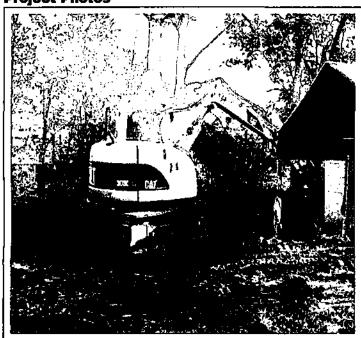



Additional Comments/Observations

□ None		

	30JUL04	
Signed: Michelle Smith Date:		
