



Project Summary Report

SDMS Document ID



2027812

Contractor's Name: **Project Resources Inc.**
Contract Number: **W9128F-04-D-0029**
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	14AUG04	20AUG04	Report #	010
--------------	----------------	----------------	----------	------------

Project Safety Report

Days Worked To Date:	66	Date of Last Accident:	8/12/04
Project Man-hours To Date:	20,004.25	Hours Worked w/o Accident:	2,292.00
Comments/Issues: None.			

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		50
Property Close-Out	31OCT05	15MAR05					10
Final Report	01DEC04	15JAN05					0
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		30

* These dates are actual dates.

Conditions/Events which have/may result in delayed progress

None.

Current Project Activities

- Property owners were contacted and restoration appointments were scheduled.
- Nine properties remediated to backfill this week.
- Nine restoration appointments completed for a total of 314 to date.
- Ten completion appointments completed.
- Digital copies of property files were created and property completion packets composed.
- Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on-site Wednesday, August 18, 2004 for a weekly meeting.
- Subcontract sent to NE Denver Housing to conduct lead-based paint assessment of 15 initial homes for review and signature.
- Out of town crew rotated back on August 16, 2004.

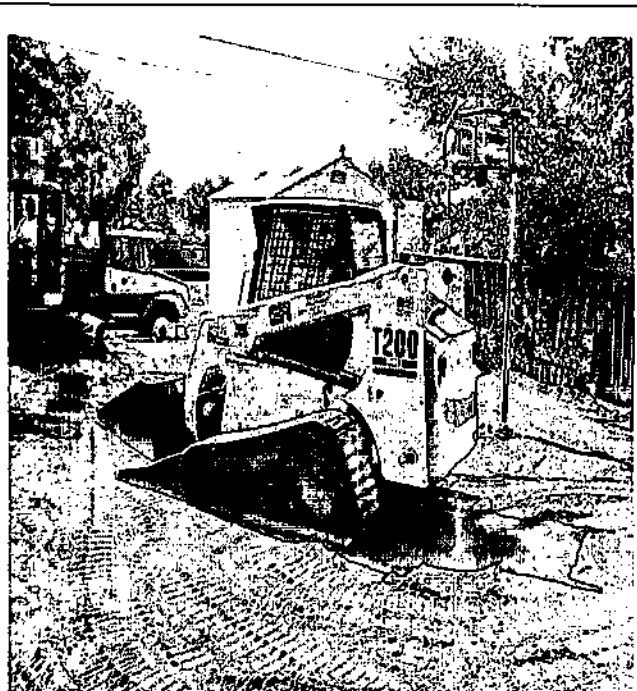
Upcoming Project Activities

- Remediation of 10 homes scheduled for next week.
- Restoration appointments to continue, with 9 scheduled for next week.

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	77	86	
Square Footage Excavated	SF	331,364	373,108*	

*Approximate totals

Project Photos**Additional Comments/Observations**

☐ None

Signed: *Michelle Smith*

Date:

20AUG04
