



## Project Summary Report

SDMS Document ID



2027821

Contractor's Name: **Project Resources Inc.**  
Contract Number: **W9128F-04-D-0029**  
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	<b>30OCT04</b>	<b>05NOV04</b>	Report #	<b>021</b>
--------------	----------------	----------------	----------	------------

### Project Safety Report

Days Worked To Date:	<b>142</b>	Date of Last Accident:	<b>8/12/04</b>
Project Man-hours To Date:	<b>37,638.25</b>	Hours Worked w/o Accident:	<b>20,405.50</b>
Comments/Issues: <b>None.</b>			

### Project QC/QA Report

Project Deficiencies:	<b>None.</b>
Comments/Issues:	<b>None.</b>

### Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
<b>Remediation</b>	16JUN04	30DEC04		16JUN04*	15DEC04		87
<b>Property Close-Out</b>	31OCT05	15MAR05		30JUN04*	30JAN04		47
<b>Final Report</b>	01DEC04	15JAN05					0
<b>PROJECT</b>	16JUN04	15MAR05		16JUN04*	15MAR05		65

\* These dates are actual dates.

### Conditions/Events which have/may result in delayed progress

<ul style="list-style-type: none"><li>• <b>None.</b></li></ul>
----------------------------------------------------------------

### Current Project Activities

<ul style="list-style-type: none"><li>• Property owners were contacted and completion appointments were scheduled. Access agreements have been arriving via mail for the 2005 remediation. Site Coordination is scheduling restoration appointments.</li><li>• Seven properties remediated to backfill this week for a total of 185 properties.</li><li>• Ten completion appointments completed.</li><li>• Digital copies of property files were created and property completion packets composed.</li><li>• Weekly meeting with Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on Wednesday, November 3, 2004. Mr. Ketellapper informed PRI that only homes that qualified for removal under lead impact will be candidates for the lead-based paint abatement.</li><li>• Out of town crew rotated back on 11/02/04.</li></ul>
---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------

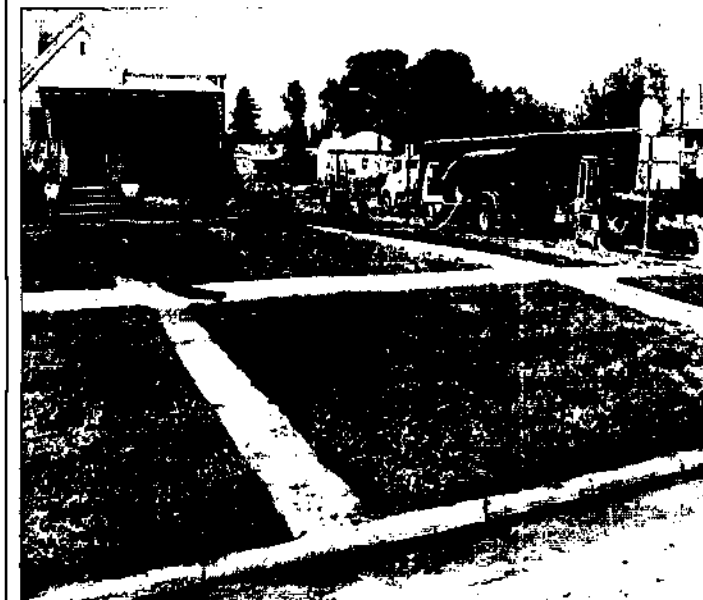
### Upcoming Project Activities

<ul style="list-style-type: none"><li>• Ten properties scheduled for remediation next week.</li></ul>
-------------------------------------------------------------------------------------------------------

**Project Quantities**

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	178	185*	
Square Footage Excavated	SF	698,901	729,247*	

\*Approximate totals

**Project Photos****Additional Comments/Observations**

☐ None

Signed: *Michelle Smith*

Date:

05NOV04
