



Project Summary Report

SDMS Document ID



2027822

Contractor's Name: **Project Resources Inc.**
Contract Number: **W9128F-04-D-0029**
Site Name & Location: **VB I-70 Superfund Site**

Time Period:	06NOV04	12NOV04	Report #	022
--------------	----------------	----------------	----------	------------

Project Safety Report

Days Worked To Date:	149	Date of Last Accident:	8/12/04
Project Man-hours To Date:	39,288.75	Hours Worked w/o Accident:	22,056.00
Comments/Issues:	None.		

Project QC/QA Report

Project Deficiencies:	None.
Comments/Issues:	None.

Project Schedule Report

Task	Scheduled			Current			% Complete
	Start	Finished	DUR	Start	Finished	DUR	
Remediation	16JUN04	30DEC04		16JUN04*	15DEC04		89
Property Close-Out	31OCT05	15MAR05		30JUN04*	30JAN04		49
Final Report	01DEC04	15JAN05					0
PROJECT	16JUN04	15MAR05		16JUN04*	15MAR05		70

* These dates are actual dates.

Conditions/Events which have/may result in delayed progress

- Adverse cold weather caused early shut-downs a couple of days this week.

Current Project Activities

- Property owners were contacted and completion appointments were scheduled. Access agreements have been arriving via mail for the 2005 remediation. Site Coordination is scheduling restoration appointments for end of Nov.
- Ten properties remediated to backfill this week for a total of 195 properties.
- Ten completion appointments completed.
- Digital copies of property files were created and property completion packets composed.
- Weekly meeting with Victor Ketellapper, EPA, and Barbara O'Grady, CDPHE, on Wednesday, November 10, 2004.
- Downsized the field crew to 25 people, configured into one large team.

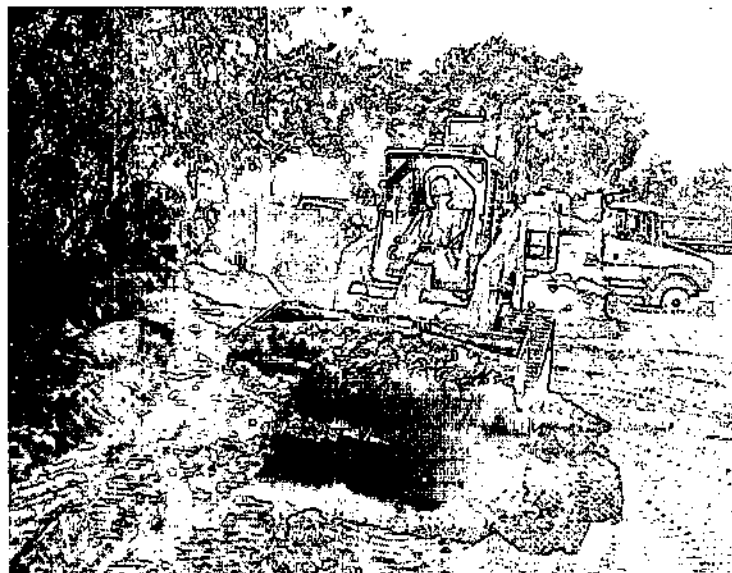
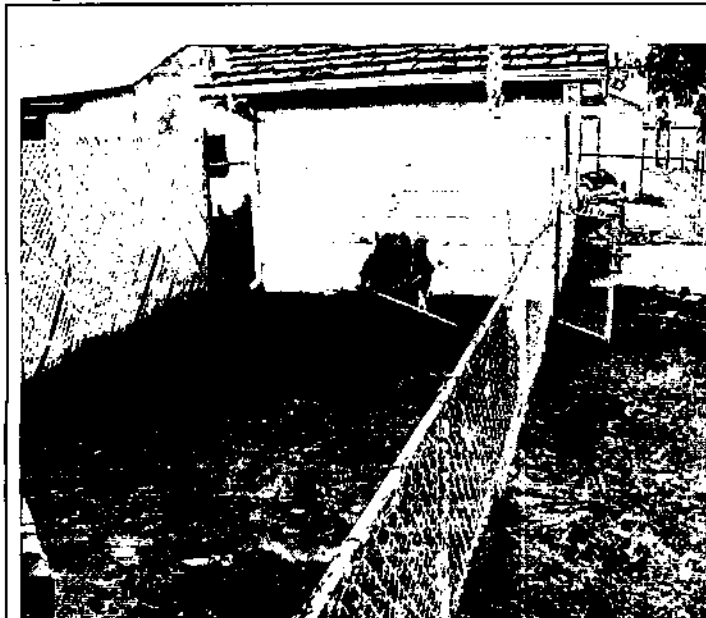
Upcoming Project Activities

- Ten properties scheduled for remediation next week.

Project Quantities

Item	Unit	Last Report	To Date	Comment
Completed Properties	Property	185	195*	
Square Footage Excavated	SF	729,247	760,246*	

*Approximate totals

Project Photos**Additional Comments/Observations**

☐ None

Signed: *Michelle Smith*

Date: **12NOV04**
