

Nicholas Clevett <Nicholas.Clevett@rmtinc.co m>

06/07/2005 11:42 AM

To ACINQUE@dep.state.nj.us, Stephen Cipot/R2/USEPA/US@EPA

cc George.Blyskun@dep.state.nj.us, John.Prendergast@dep.state.nj.us, Robert Alvey/R2/USEPA/US@EPA, Frances

bcc

Subject LEC Source Reduction Project - Progress Update No.@ 16

Please find attached the above-mentioned project update. Please contact me w/?s Regards,

Nicholas J. Clevett
Senior Project Manager
RMT, Inc., Michigan
2025 E. Beltline Ave. SE
Suite 402
Grand Rapids, MI 49546
(616) 975-5415 (Office)
(616) 975-1098 (Fax)
(616) 780-2398 (Mobile)
Nicholas Clevett@rmtinc.com

Outgoing messages, along with any attachments, are scanned for viruses prior to sending.

NOTICE-- This email may contain confidential and privileged information for the sole use of the intended recipient. Any review or distribution by others is strictly prohibited. If you are not the intended recipient, please contact the sender immediately and delete all copies.



Trans 00082_Progress Update No. 16_ May 25 to June 7 2005:pdf

RMT, Inc.

2025 E. Beltline Ave SE

Suite 402

Grand Rapids, MI 49546

TRANSMITTAL No. 00082

Phone: 616-975-5415 Fax: 616-975-1098

PROJECT: LEC Remediation Services

DATE: 6/7/2005

REF: PPU No. 16

TO:

NJDEP

Bureau of Federal Case Management Div. of Responsible Site Party Remed

WEARESEDING SUBMITTED FOR

CN028

Trenton, NJ 08625

ATTN: Anthony Cinque

			<u> </u>	Approve	ed as b	ubmiti	<u> </u>		
						4. 4	- 3		
					y.v	(4 H)			
4000000	erangen service merk	60°. 1554°.	Per PCL acc	mmarkitativ i	177	L T. A. A. A.	· 计数字数据 14	artenes estatement	(A) (A) (A) (A)
			•						
		1,							
.*		,				,			

Shop Drawings		Approval	Approved as Submitted
Letter		Your Use	Approved as Noted
Prints		As Requested	Returned After Loan
Change Order		Review and Comment	Resubmit
Plans			Submit
Samples	S	CNTTIME	Returned
Specifications		Attached	Returned for Corrections
Other: Project Progress Update No. 16		Separate Cover Via: Email 6/7/05	Due Date:

ELEM N	o. copi	ES DATE : ITEM	NUMBER REV. NO DESCRIPTION STATES OF THE PERSONS AND ADDRESS AN	SAN
01	1	6/7/2005	Project Progress Update No. 16	APP
02	1	6/7/2005	Project Progress Update No. 16 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team Signed: Nick Clevett

Expedition (

L.E. CARPENTER & COMPANY ~ NJD002168748 BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY

SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 16

Date:

June 7, 2005

To:

Stephen Cipot, USEPA
Anthony Cinque, NJDEP

From:

Nicholas J. Clevett, RMT

cc:

Robert Alvey, USEPA Frances Zizila, USEPA John Prendergast, NJDEP George Blyskun, NJDEP

Jim Lewis, LEC Cris Anderson, LEC Ernie Schaub, LEC

Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton

Dan Oman, RMT Jim Dexter, RMT Walter Kurzeja, RMT Jeff Macri, RMT Dave Pratt, RMT Nakia Addison, RMT

Project No.:

00-06527.09

Subject:

SOURCE REDUCTION REMEDIAL ACTION

Project Progress Update No. 16

I. SOURCE REDUCTION REMEDIAL ACTIONS - MAY 25TH THROUGH JUNE 7TH 2005

- 1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
- 2. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.). Initiated demobilization of some equipment following completion of the smear zone excavation and waste loading.
- 3. Performed and documented daily inspections on the silt fence as outlined in the certified SESCP
- 4. Cleaned all paved areas with a skid steer broom attachment and manual sweeping
- Terminated receipt of cement kiln dust (CKD) to facilitate ex-situ drying of smear zone soils prior to screening, stockpiling, and off-site disposal as the smear zone excavation is now complete. A total of 3,959 tons of CKD were delivered and utilized at the site.
- 6. Completed the smear zone excavation utilizing the slurry mix. Loading and transportation of smear zone soils began on March 28, 2005. A total of 34,052 tons of smear zone soils have been transported and disposed off-site.
- 7. Initiated backfilling of the wetland, transition zones and main excavation areas.
- 8. As built surveying of the excavation areas, wetland areas, and transition zones is complete. Surveying will be performed on the site wide final grade in the wetland, transition zones and main excavation areas once backfilling is complete and final grade has been established.
- II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS JUNE 7TH THROUGH JUNE 14TH 2005
- 1. Continue backfilling wetland, transition zones and main excavation areas.
- 2. Survey final grades and initiate site restoration in the main excavation area.



Photographic Log Progress Update No. 16

Client Name: Site Location: Project No.:

L.E. CARPENTER & COMPANY Wharton, Morris County, NJ 00-06527.09

Photo No. Date 1 6/4/05

Description

Backfilling and grading wetland area. Subgrade established in main portion of the excavation area.

View looking west northwest

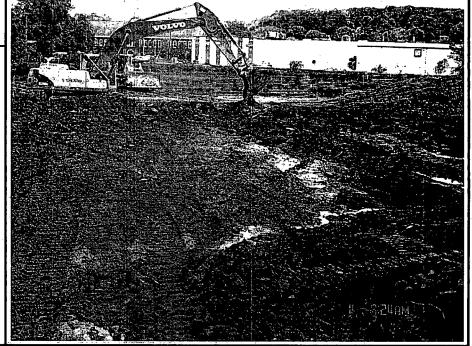


Photo No. Date 2 6/4/05

Description

Establishing grade between main portion of the excavation area and the transition zone and wetland areas.

View looking west.





Photographic Log Progress Update No. 16

Client Name:		Site Location:	Project No.:		
L.E. CARPENTER & COMPANY			Wharton, Morris County, NJ	00-06527.09	
Photo No.	Date			W WY X	
3	6/4/05				
Description Wetland area gr	rading.				
View looking ea	ist				
		046			

Photo No.	Date	
4	6/4/05	
Description		
Wetland area gi	rading.	
, , , , , , , , , , , , , , , , , , ,		
View looking ea	ast southeast	
VICW ROOKING CO	15t 50utileast	
	•	
	,	
·		
•		
	•	
	3. <u>2.</u> 3. 2. 2.	The state of the s



Photographic Log Progress Update No. 16

	Client Name:	Site Location:	Project No.:	
L.E. CARF	PENTER & COMPANY	Wharton, Morris County, NJ	00-06527.09	
Photo No.	Date			
5	6/4/05			
Description Surveying wetlan grades.	d area final			
View looking eas				
		-500		
