

RMT, Inc.

2025 E. Beltline Ave SE
Suite 402
Grand Rapids, MI 49546

Phone: 616-975-5415
Fax: 616-975-1098

TRANSMITTAL**No. 00065****PROJECT:** LEC Remediation Services**DATE:** 3/11/2005

TO: NJDEP
Bureau of Federal Case Management
Div. of Responsible Site Party Remed
CN028
Trenton, NJ 08625

REF: PPU No. 7**ATTN:** Anthony Cinque

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	SENT VIA:	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Update No. 7	<input checked="" type="checkbox"/> Separate Cover Via: Email 3/11/05	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	1	3/11/2005			Project Progress Update No. 7	APP
02	1	3/11/2005			Project Progress Update No. 7 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis
C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

Signed: 

Nick Clavett



L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 7

Date: March 11, 2005

To: Stephen Cipot, USEPA
Anthony Cinque, NJDEP

From: Nicholas J. Clevett, RMT

cc: Robert Alvey, USEPA
Frances Zizila, USEPA
John Prendergast, NJDEP
George Blyskun, NJDEP
Jim Lewis, LEC
Cris Anderson, LEC
Ernie Schaub, LEC
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton
Dan Oman, RMT
Jim Dexter, RMT
Walter Kurzeja, RMT
Jeff Macri, RMT
Dave Pratt, RMT
Nakia Addison, RMT

Project No.: 00-06527.09

Subject: SOURCE REDUCTION REMEDIAL ACTION
Project Progress Update No. 7

I. SOURCE REDUCTION REMEDIAL ACTIONS - THROUGH MARCH 3RD THROUGH MARCH 10TH 2005

1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
4. Performed and documented daily inspections on the silt fence as outlined in the certified SESCO
5. Cleaned all paved areas with a skid steer broom attachment
6. Additional silt fence was installed around the large rock pile to be used during smear zone excavation activities so the smear zone excavation footprint is fully enclosed
7. The fence was removed along the western (LEC) side of the drainage ditch. Silt fence and snow fence were installed in preparation for smear zone soil excavation in this area in accordance with the SESCO plan and Wetland GP4 permit
8. Finalized excavation of the B-1 process waste areas. All materials were placed on and covered with poly sheeting. An additional 142 tons of B-1 process wastes were loaded and transported off-site as hazardous waste for disposal. To date a total of 288 tons of B-1 process wastes have been removed from the site
9. Finalized excavation of the B-2 process waste area. Materials were screened and disposed off-site as non-hazardous waste
10. Continued to collect and submit for analysis confirmatory samples (base and sidewall samples) for lead, copper and antimony in both the B-1 and B-2 process wastes areas as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
11. Installed additional silt fence and snow fence in the wetland area as required by the GP4 permit

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 7

12. Initiated PCB impacted soil excavation and stockpiling of in those areas inside and outside [west] of the delineated wetland areas. A total of 795 tons of PCB impacted soils were excavated, loaded and transported off-site for disposal as non TSCA PCB wastes. CKD was utilized to dry the excavated PCB soils prior to transportation and off-site disposal.
13. Collected and submitted for analysis confirmatory samples (base and sidewall samples) for total PCBs in the PCB area as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
14. Continued to set up the batch plant and ancillary equipment to prepare slurry to facilitate the smear zone excavation within the saturated zone
15. Initiated preparation of test slurry mix to ensure the correct mix and consistency prior to smear zone excavation activities
16. Set up survey control for smear zone excavation (depth master)

II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS - MARCH 11TH THROUGH MARCH 17TH 2005

1. Continue to stockpile, load, transport and dispose of PCB impacted soils within permitted wetlands areas existing within the Wharton Enterprise property east of the LEC site, and conduct confirmatory sampling as required in the RAWP
2. Establish final grade in the wetland area as required by the GP4 permit
3. Initiate smear zone excavation activities



Photographic Log Progress Update No. 7



Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 1	Date 3/4/05		
Description Waste drum removal activities			

Photo No. 2	Date 3/7/05	 03/07/2005
Description Survey control for excavation activities (depth master) View looking southeast towards the Rockaway River		



Photographic Log Progress Update No. 7

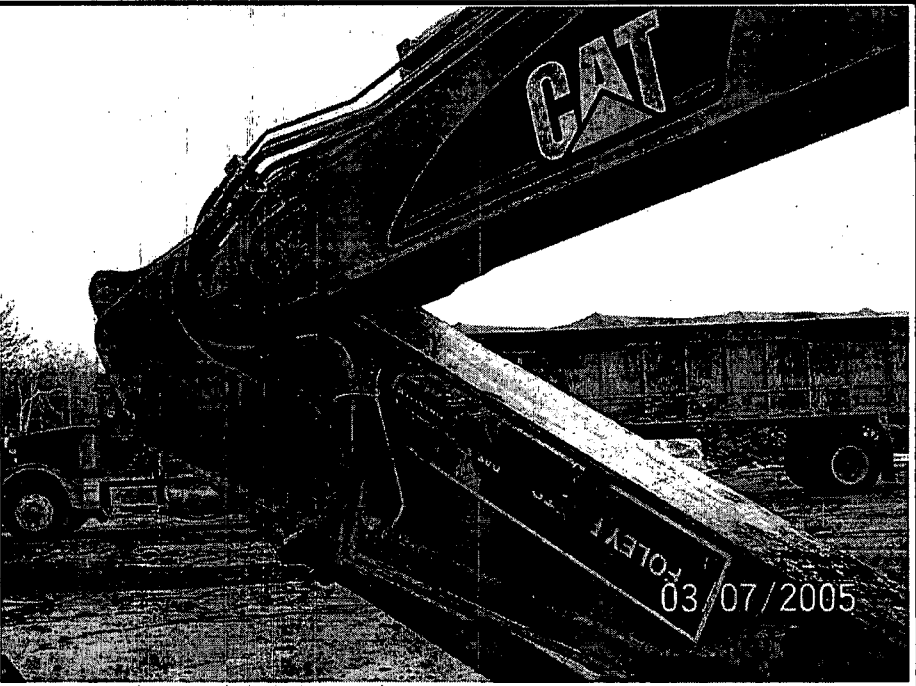



Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 3	Date 3/7/05		
Description Survey control for excavation activities Depth master located on excavation equipment to ensure target depth is achieved			

Photo No. 4	Date 3/7/05	
Description The PCB excavation area. Flooded due to inclement weather and location within the floodplain View looking east		



Photographic Log Progress Update No. 7

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 5	Date 3/7/05		
Description Loading PCB soils			
Photo No. 6	Date 3/7/05		
Description Sampling PCB soils			
