

To: ACINQUE@dep.state.nj.us, Stephen Cipot/R2/USEPA/US@EPA
cc: George.Blyskun@dep.state.nj.us, John.Prendergast@dep.state.nj.us,
Robert Alvey/R2/USEPA/US@EPA, Frances
Zizila/R2/USEPA/US@EPA, morrissoil@optonline.net,
cristopher.anderson@Polyone.com, Emie.Schaub@Polyone.com,
James.Lewis@Polyone.com, Dan Oman <Dan.Oman@rmtinc.com>,
David Pratt <David.Pratt@rmtinc.com>; Jeff Macri
<Jeff.Macri@rmtinc.com>, Jim Dexter <Jim.Dexter@rmtinc.com>,
Nakia Addison <Nakia.Addison@rmtinc.com>, Wally Kurzeja
<Wally.Kurzeja@rmtinc.com>, jrheinhardt@whartonnj.com
Subject: LEC Source Reduction Progress Update No.@ 6

See attached Please contact me with questions. Regards,

Nicholas J. Clevett Senior Project Manager RMT, Inc., Michigan 2025 E. Beltline Ave. SE Suite 402 Grand Rapids, MI 49546 (616) 975-5415 (Office) (616) 975-1098 (Fax) (616) 780-2398 (Mobile) Nicholas Clevett@rmtinc.com

Outgoing messages, along with any attachments, are scanned for viruses prior to sending.

NOTICE-- This email may contain confidential and privileged information for the sole use of the intended recipient. Any review or distribution by others is strictly prohibited. If you are not the intended recipient, please contact the sender immediately and delete all copies.

Trans 00064 Progress Update No. 6 Feb 26 to Mar 2 20

RMT, Inc. 2025 E. Beltline Ave SE Suite 402 Grand Rapids, MI 49546 Phone: 616-975-5415 Fax: 616-975-1098 PROJECT: LEC Remediation Services DATE: 3/3/2005

REF: PPU No. 6

TO: NJDEP
Bureau of Federal Case Management
Div. of Responsible Site Party Remed

CN028

Trenton, NJ 08625

ATTN: Anthony Cinque

4	Al 114. Initiony Chique					
1	WATER TO THE STREET, OF THE STREET, ST		ON INTERNAL DESCRIPTION DE LA COMPANSION DE		(60 a) (6) \$ (9) \$ (40 b) \$ (40	
	Shop Drawings		Approval		Approved as Submitted	
	Letter	1	Your Use		Approved as Noted	
	Prints		As Requested		Returned After Loan	
	Change Order		Review and Comment		Resubmit	
	Plans				Submit	
	Samples	10	ENT VIALE VILLE		Returned	
	Specifications		Attached		Returned for Corrections	
	Other: Project Progress Update No. 6		Separate Cover Via: Bmail 3/3/05		Due Date:	

TTEM.	(O. CÓPII	SIDATE TIEM	NUMBER	REV. N	O DESCRIBITION :	STATUS
01	1.	3/3/2005	,		Project Progress Update No. 6	APP
02	1 1	3/3/2005			Project Progress Update No. 6 Photos	NEW

CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyakun, J. Lewis C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

Signed: Nick Clevett

Barredition 4

L.E. CARPENTER & COMPANY ~ NJD002168748 BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY

SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 6

Jon Rheinhardt, Borough of Wharton

Dan Oman, RMT

Jim Dexter, RMT

Dave Pratt, RMT Nakia Addison, RMT

Walter Kurzeja, RMT Jeff Macri, RMT

Date:

March 3, 2005

To:

Stephen Cipot, USEPA Anthony Cinque, NJDEP

From:

Nicholas J. Clevett, RMT

cc:

Robert Alvey, USEPA Frances Zizila, USEPA

John Prendergast, NJDEP George Blyskun, NJDEP Cris Anderson, LEC

Colin Clavadetscher, Morris County

Jim Lewis, LEC

Ernie Schaub, LEC

Project No.:

00-06527.09

Subject:

SOURCE REDUCTION REMEDIAL ACTION

Project Progress Update No. 6

SOURCE REDUCTION REMEDIAL ACTIONS - FEBRUARY 26TH THROUGH MARCH 2ND 2005

- 1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
- 2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
- 3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
- 4. Performed and documented daily inspections on the silt fence as outlined in the certified SESCP
- 5. Continued excavation of the B-1 process waste area. All materials were placed on and covered with poly sheeting. An additional 50 tons of B-1 process wastes were excavated, screened, loaded and transported off-site as hazardous waste for disposal. To date a total of 146 tons of B-1 process wastes have been removed form the site
- 6. Continued excavation of the B-2 process waste area. Materials were screening and stockpiled pending offsite disposal as non-hazardous waste
- 7. Continued to collect and submit for analysis confirmatory samples (base and sidewall samples) for lead, copper and antimony in both the B-1 and B-2 process wastes areas as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
- 8. Initiated PCB impacted soil excavation and stockpiling of in those areas outside [west] of the delineated wetland areas
- 9. Continued to set up the batch plant and ancillary equipment to prepare slurry to facilitate the smear zone excavation within the saturated zone
- 10. Secured the Freshwater Wetland General Permit No. 4 (GP4). Based on the receipt of both NJDEP LURP permits, excavation, screening, loading, transportation and disposal of PCB impacted soils existing within delineated wetland areas are tentatively scheduled to begin in March 3, 2005. Sediment generating

L.E. CARPENTER & COMPANY ~ NJD002168748 BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY

SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 6

activities (i.e., excavation, backfilling and grading) will completed on or before March 15, 2005. Wetland restoration (i.e., seeding, planting) will be performed once appropriate weather conditions permit

- II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS MARCH 3RD THROUGH MARCH 9TH 2005
- 1. Continue with excavation, screening, loading, off-site transportation, disposal, and confirmatory sampling of the B-1 and B-2 process waste areas
- 2. Excavate, screen, stockpile, load, transport and disposal of PCB impacted soils within permitted wetlands areas existing within the Wharton Enterprise property east of the LEC site



Photographic Log Progress Update No. 6

Client Name: Site Location: Project No.:

L.E. CARPENTER & COMPANY Wharton, Morris County, NJ 00-06527.09

Photo No. Date

1 3/2/05

Description

Exterior batch plant equipment [Silo and PIG] utilized to prepare slurry to facilitate smear zone soil excavation in the saturated zone.

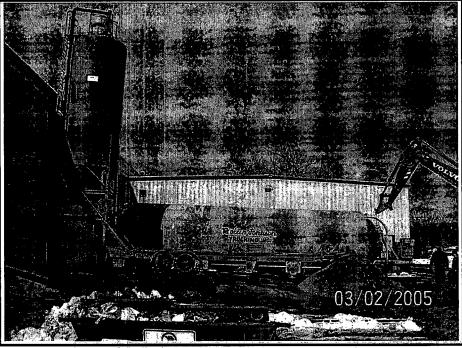


Photo No.	Date	
2	3/1/05	
Description Interior batch putilized to prepfacilitate smear excavation in the	zone soil	
zone.		

03/01/2005



Photographic Log Progress Update No. 6

	Client Name:	- L	Site Location:	Project No.:
L.E. CAI	RPENTER & COM	/IPANY	Wharton, Morris County, NJ	00-06527.09
Photo No.	Date	*1:	A second the second	
3	3/1/05		grise la company of the second	
Description Stored bentonit preparation.	te used for slurry	; ;		
		Common amountainers		0 3/01/2005

Photo No.		Date
4	4	3/2/05

Description

Continued excavation and confirmatory sampling of the B-2 process waste area.

View looking southeast towards the Rockaway River





Photographic Log Progress Update No. 6

Client Name: L.E. CARPENTER & COMPANY			Site Locat	Project No.: 00-06527.09	
			Wharton, Morris		
Photo No.	Date		NAME OF STREET		
5	3/2/05				
Description PCB soil excava			LANGUE AND		
= ,	rmitted wetland				
areas.	•				
View looking east southeast					
towards the Wh	narton Enterprise				
property and the Rockaway					
River		10 mars			
				rivers I was a	
				03/02/2005 ~	
		F			

Photo No.	Date
6	3/2/05

Description

PCB soil excavation outside [west] of the permitted wetland areas.

View looking east southeast towards the Wharton Enterprise property and the Rockaway River

