



Nicholas Clevett
<Nicholas.Clevett@rmt
inc.com>

02/11/2005 02:27 PM

To: ACINQUE@dep.state.nj.us, Stephen Cipot/R2/USEPA/US@EPA
cc: George.Blyskun@dep.state.nj.us, John.Prendergast@dep.state.nj.us,
Robert Alvey/R2/USEPA/US@EPA, Frances
Zizila/R2/USEPA/US@EPA, morrissoil@optonline.net,
cristopher.anderson@Polyone.com, Ernie.Schaub@Polyone.com,
James.Lewis@Polyone.com, Dan Oman <Dan.Oman@rmtinc.com>,
David Pratt <David.Pratt@rmtinc.com>, Jeff Macri
<Jeff.Macri@rmtinc.com>, Jim Dexter <Jim.Dexter@rmtinc.com>,
Nakia Addison <Nakia.Addison@rmtinc.com>, Wally Kurzeja
<Wally.Kurzeja@rmtinc.com>, jrheinhardt@whartonnj.com
Subject: Progress Update No. @ 3

See attached.
Please contact me with questions.

Nicholas J. Clevett
Senior Project Manager
RMT, Inc., Michigan
2025 E. Beltline Ave. SE
Suite 402
Grand Rapids, MI 49546
(616) 975-5415 (Office)
(616) 975-1098 (Fax)
(616) 780-2398 (Mobile)
Nicholas.Clevett@rmtinc.com

Outgoing messages, along with any attachments, are scanned for
viruses prior to sending.

NOTICE-- This email may contain confidential and privileged
information for the sole use of the intended recipient. Any
review or distribution by others is strictly prohibited. If you
are not the intended recipient, please contact the sender
immediately and delete all copies.



Trans 00051 Progress Update No. 3 Feb 4 to Feb 10 20

346424



RMT, Inc.

2025 E. Beltline Ave SE
Suite 402
Grand Rapids, MI 49546

Phone: 616-975-5415
Fax: 616-975-1098

TRANSMITTAL**No. 00051****PROJECT:** LEC Remediation Services**DATE:** 2/11/2005

TO: NJDEP
Bureau of Federal Case Management
Div. of Responsible Site Party Remed
CN028
Trenton, NJ 08625

REF: Project Progress Update No. 3**ATTN:** Anthony Cinque

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	SENT VIA:	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input checked="" type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Report Update No. 3	<input type="checkbox"/> Separate Cover Via:	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	01	2/11/2005			Project Progress Update No. 3	AAN

Remarks: Please find Project Progress Update No. 3 for the Source Reduction Remedial Project.

CC: S. Cipot, R. Alvey, F. Zizilia, J. Predergast, G. Blyskun, J. Lewis,
C. Anderson, E. Schaub, C. Clavedetscher, J. Rheinhardt, RMT Project Team

Signed: 
Nick Clevett

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 3

Date: February 11, 2005

To: Stephen Cipot, USEPA
Anthony Cinque, NJDEP

From: Nicholas J. Clevett, RMT

cc: Robert Alvey, USEPA
Frances Zizila, USEPA
John Prendergast, NJDEP
George Blyskun, NJDEP
Jim Lewis, LEC
Cris Anderson, LEC
Ernie Schaub, LEC
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton
Dan Oman, RMT
Jim Dexter, RMT
Walter Kurzeja, RMT
Jeff Macri, RMT
Dave Pratt, RMT
Nakia Addison, RMT

Project No.: 00-06527.09

Subject: SOURCE REDUCTION REMEDIAL ACTION
Project Progress Update No. 3

I. SOURCE REDUCTION REMEDIAL ACTIONS - FEBRUARY 4TH THROUGH FEBRUARY 10TH 2005

1. Continued morning safety briefings (e.g., discussion of daily work scope and associated health and safety procedures)
2. Maintained air monitoring equipment (e.g., Weather Station, Miniram, PID, data loggers etc.) and air monitoring program (e.g., data log download, grab sampling)
3. Maintained all on-site heavy equipment (e.g., excavators, skid steer, off-road truck, screen, etc.)
4. Performed and documented daily inspections on the silt fence as outlined in the certified SSCP
5. Continued the excavation, screening, stockpiling and loading of the primary lead soil area (A-1) soils.
6. Managed former LEC operation infrastructure as encountered (e.g., former Bldg 13 sump and water line). The sump was excavated and removed, and the water line was capped, excavated and removed.
7. Encountered two (2) 55-gallon drums while excavating the lead soil around the MW-11 well cluster, and encountered another nine (9) 55-gallon drums while excavating lead soils overlaying the B-1 process waste area. The drums contained a latex and white glue looking substance, and general debris. All drums were over packed, and samples were collected and submitted for characterization. Off-site disposal is pending the results of waste analyses.
8. Completed excavation, confirmatory sampling, screening, stockpiling and loading of the A-2 lead soil area.
9. Initiated excavation, stockpiling and loading of the A-3 lead area soils.
10. Collected and submitted for analysis confirmatory lead soil samples (base and sidewall samples) as outlined in the RAWP documents (e.g., RAWP and regulatory response letters)
11. Performed additional lead soil excavation and re-confirmatory sampling (if required) as outlined in the RAWP in those area which exhibited a lead soil concentration > 400 mg/kg
12. Laid stakes to survey the C-1 area clean soil and smear zone excavations.

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 3

13. Laid stakes to survey the northern end of the A-1 lead soil excavation area, and the completed A-2 lead soil excavation area.

14. Conducted the monthly on-site meeting on February 10, 2005 at 10am.



To date (Jan 31st to Feb 10th), a total of **251 trucks** have hauled **5,656 tons** of lead impacted soils off-site for disposal [averaging **628 tons/day** of lead soils removed from the site].

II. PROPOSED SOURCE REDUCTION REMEDIAL ACTIONS - FEBRUARY 11TH THROUGH FEBRUARY 17TH 2005

1. Continue with excavation, screening, loading, off-site transportation and disposal, confirmatory sample collection and analysis in the primary lead soils area (A-1) and the A-3 lead soil area.
2. Initiate excavation of process waste area B-1 and the clean soils area C-1.



Photographic Log Progress Update No. 3

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 1	Date 2/04/04		
Description Excavating the waterline running through the footprint of the excavation View looking south towards the Rockaway River			
Photo No. 2	Date 2/04/05		
Description The cut waterline with new flange and thrust block framing			



Photographic Log Progress Update No. 3


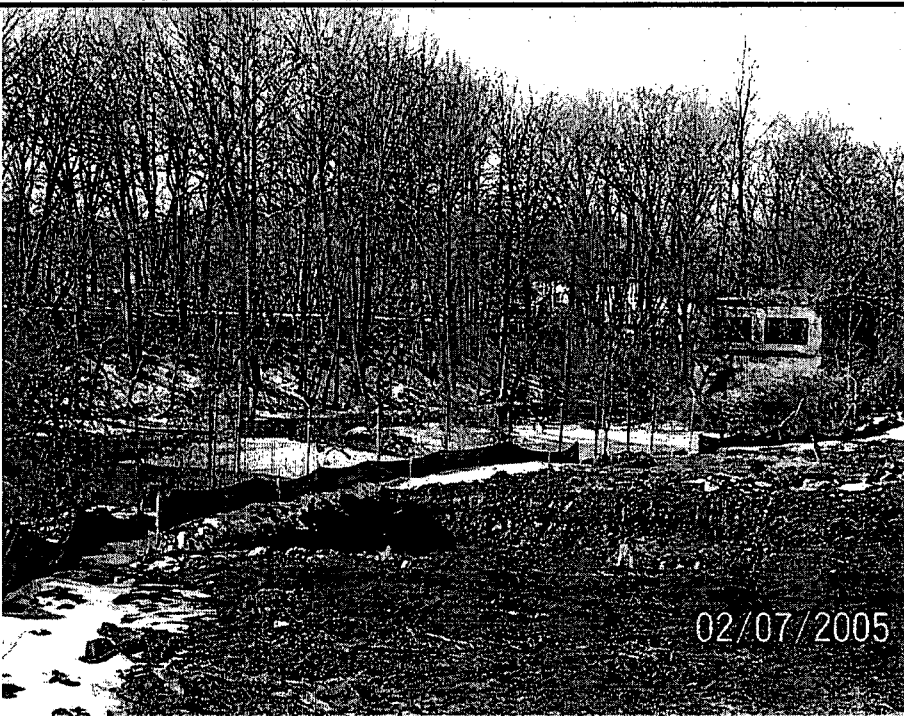
Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 3	Date 2/05/05		
Description Former Building 13 sump pit View looking southeast			

Photo No. 4	Date 2/07/05	
Description Excavated lead soil area A-2 View looking southwest		



Photographic Log Progress Update No. 3





Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 5	Date 2/07/05		
Description Screening A-3 soils into a separate pile View looking south.			

Photo No. 6	Date 2/07/05	
Description Two 50 gal drums buried at the northeastern corner of A-1 zone (adjacent to the former MW-11 cluster).		



Photographic Log Progress Update No. 3

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 7	Date 2/02/05		
Description The excavated lead soil area A-1 View looking west			
Photo No. 8	Date 2/05/05		
Description Excavated lead areas A-1 and A-3 View looking west			
