

DEPARTMENT OF THE ARMY HEADQUARTERS CAMP EDWARDS BEAMAN STREET BUILDING 3468 CAMP EDWARDS, MA 02542

Commander Camp Edwards

05 November 2012

Lynne A. Jennings MMR Team Leader U. S. Environmental Protection Agency 5 Post Office Square, Suite 100 Mail Code OSRR07-3 Boston, MA 02109-3912

Subject: Supplemental Environmental Project 1st Quarterly Report, Consent Order Final Agreement, Docket No. SDWA 01-2012-0021

Dear Lynne Jennings,

As outlined in the Consent Order Final Agreement (CAFO) with the MAARNG please consider this our first quarterly report.

The CAFO Paragraph 52, states that the "Respondent shall submit quarterly written reports outlining work completed to date and funds spent to date. The quarterly reports will include copies of invoices documenting funds spent towards completion of the SEP. The reports shall be submitted to EPA by the 30th day of the month following each quarter (January, April, July, October)."

All areas to be removed have been delineated in the field, the area has had a Dig Safe completed, and all Groundwater Monitoring wells have been identified and marked. Work commenced on this project on November 3, 2012 in compliance with the CAFO requiring work begin within 90 days of the approval (August 29, 2012) of the CAFO, making the deadline to start work 29 November 2012. Due to funding constraints, the initial work was conducted in a drill status, with Camp Edwards resources which is a smaller work crew than projected for the project. The attached map, enclosure 1, indicates the areas designated as SEP asphalt areas to be removed in yellow. The area completed on the November 3-4 weekend is indicated in green. Our plan of execution has a larger work force with much higher rates of production anticipated. The actual rates will be validated as funding becomes available to support the full work crew.

The total production was 10,252 sf, or 0.235 acres. This was accomplished with 51-Man hours, 32 equipment hours, and 69 gallons of fuel. Enclosure 2 breaks down the cost of this initial work effort.

As required by the CAFO, attachment 1 paragraph C., we will be contacting you again after approximately 5 acres of impervious surface removal is complete so that USEPA can... "review

implementation to date, issues encountered, and issues anticipated with the remaining acres of impervious surface removal."

Please let us know if you have any questions.


I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, the information is, to the best of my knowledge and belief, true, accurate and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fines and imprisonment.

Respectfully,

RICHARD V. CRIVELLO

COL, EN Commanding

Enclosure (2)

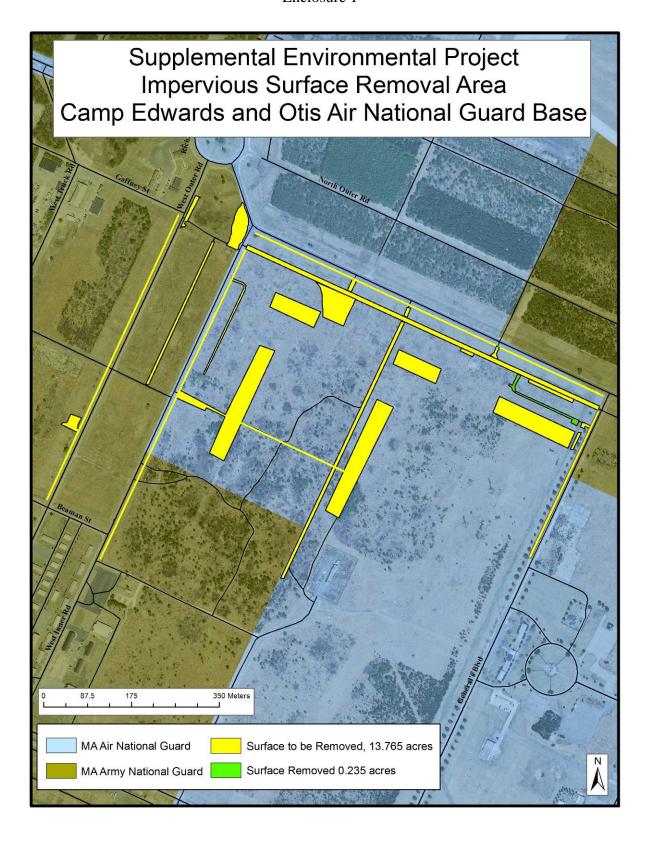

Enclosure 2

SEP Production Report Impervious Surface Removal Project Report Period 03-04 NOVEMBER 2012

	3-4NOV 12				YTD
MANPOWER					
Personnel	5				5
Manhours	51				51
Cost	\$ 1,048.43			\$	1,048.43

EQUIPMENT		
Hours	32	32
Gallons (JP-8)	69	69
Cost	\$ 272.55	\$ 272.55

PRODUCTION		
SQ FT	10252	10252
ACRES	0.235353535	0.235353535
COST/Acre	\$ 5,612.73	\$ 5,612.73

	_	
TOTALS		
Production		1.689
Cos	s	1,320.98

Man Power cost is derived from Grade and Time-In-Service (TIS), hours worked on the project and Pay Status (IDT or ADOS)

Equipment Cost is based soley on Gallons of JP-8 fuel consumed.

Production is as a percentage against the 14 acre requirement
