



614 Magnolia Avenue
Ocean Springs, Mississippi 39564
Phone 228.818.9626
Fax 228.818.9631

February 14, 2011

Mr. Stephen Tzhone, Remedial Project Manager
U.S. Environmental Protection Agency, Region 6
Superfund Division (6SF-RA)
1445 Ross Avenue, Suite 1200
Dallas, Texas 75202-2733

Re: San Jacinto River Waste Pits Superfund Site RI/FS Schedule

Project Number: 090557-01


Dear Steve:

As requested, the attached provides an updated schedule for the Remedial Investigation and Feasibility Study for the San Jacinto River Waste Pits Superfund Site. We previously provided a schedule with the Draft and Final RI/FS Work Plan as required in UAO 06-03-10 for the Site. The original schedule was provided for Pre-Preliminary Site Characterization Report (PSCR) activities and deliverables, and Post-PSCR activities and deliverables. The post-PSCR schedule remains unchanged, and the revised schedule only includes changes to Pre-PSCR activities and deliverables. It should be noted however, that the draft submittal date of the PSCR to the USEPA has not changed from July 20, 2011.

The revised schedule reflects actual completion dates for those tasks and deliverables that are completed at this time, and shows expected completion dates for the remaining activities and deliverables leading up to delivery of the PSCR. Some of the remaining activities, specifically for groundwater and soil sampling, and fate and transport field work have shifted from the original schedule, primarily because the final approval dates of the work plans for those efforts were delayed due to the extended comment/response cycles on those work plans.

As you are aware, this revised schedule is subject to change as additional requests from the USEPA on the scopes of work, access issues related to field implementation, weather delays, equipment failure, etc. We will keep the USEPA fully informed of our progress through our daily communication and monthly reports for the RI/FS. At this time, we respectfully request your approval of this revised schedule.

Sincerely,

A handwritten signature in blue ink that reads "David C. Keith". The signature is written in a cursive style with a large initial 'D'.

David C. Keith
Project Coordinator

Attachment(s)

cc: Philip Slowiak, IP
Andrew Shafer, MIMC
March Smith, MIMC

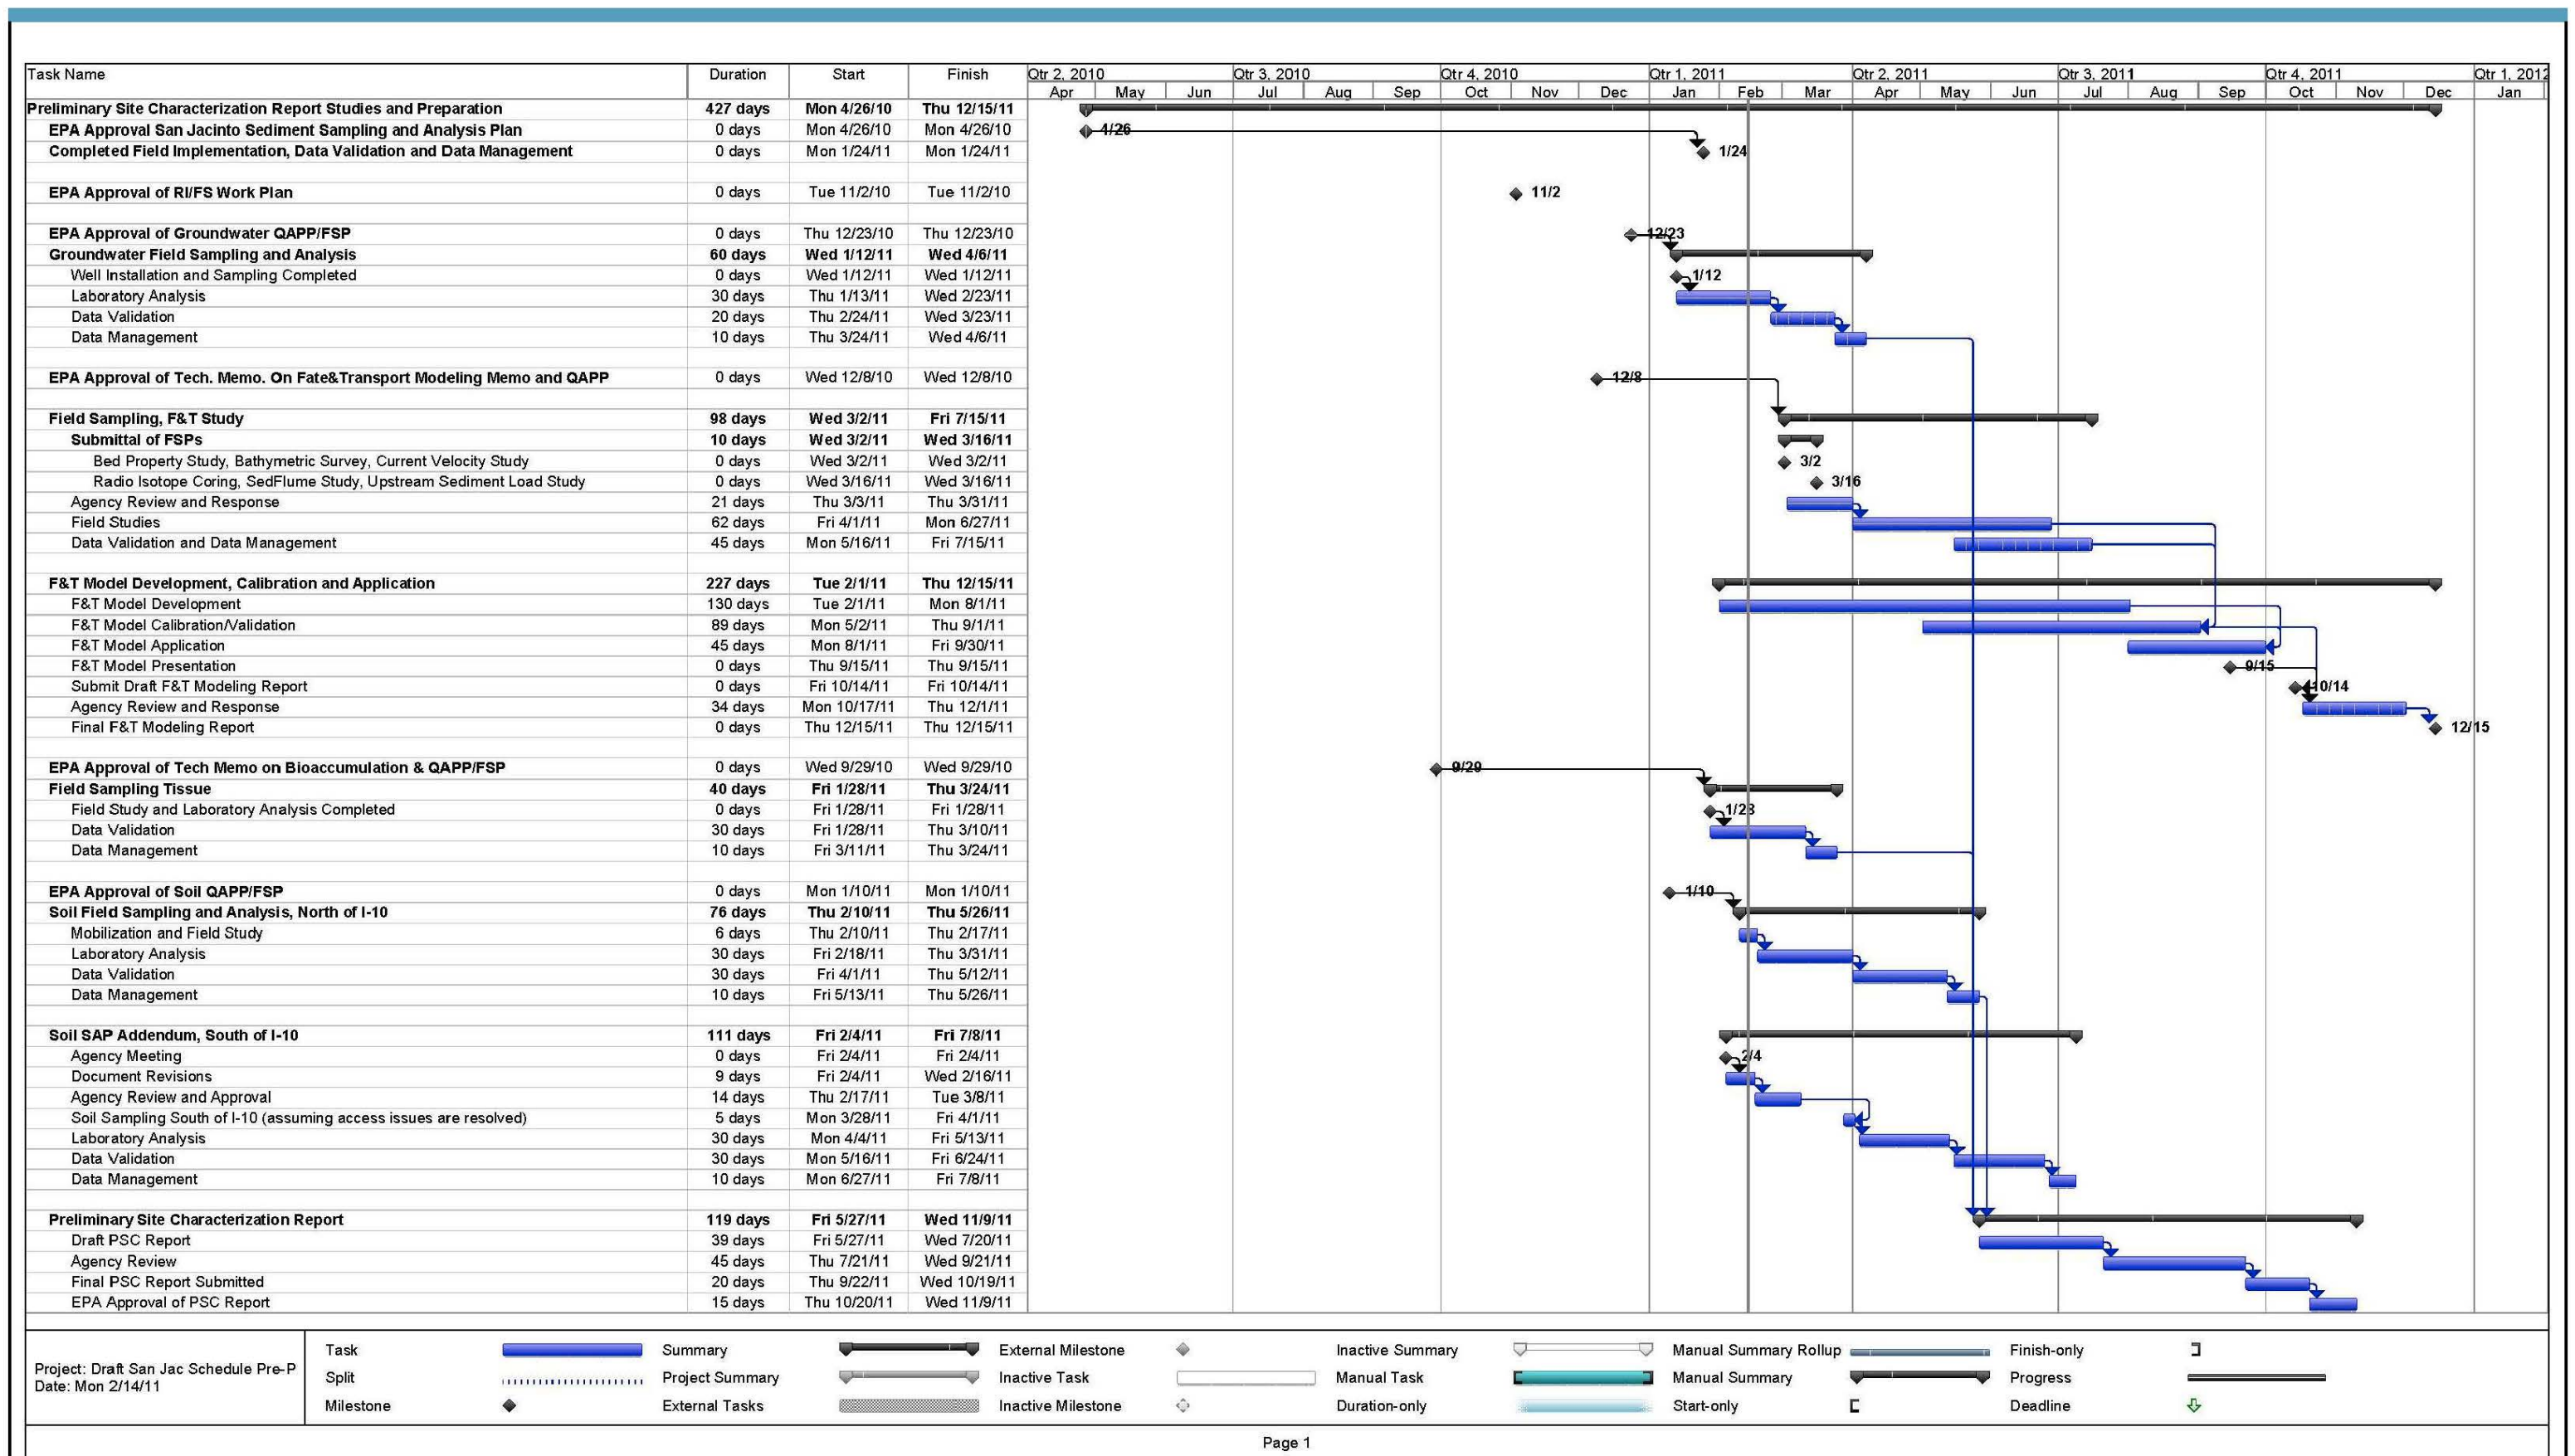


Figure 8-1a
Schedule of Deliverables Pre-Preliminary Site Characterization Report
SJRWPF RI/FS Work Plan
SJRWPF Superfund/MIMC and IPC

