



Photo 13 (DAY 1): 8/24/20 Excavation progress, moving the excavation southward, within Brown Polygon; view to WSW.



Photo 14 (DAY 1): 8/24/20 PID measuring ambient air quality (volatile organics) at 0.0ppm; view to WSW, Blue Polygons (A) and (B) in background.



Photo 15 (DAY 1): 8/24/20 Day-end progress showing Blue Polygons (A) and (B); view to NW.



Photo 16 (DAY 1): 8/24/20 Day-end progress showing Blue Polygons (A) and (B); view to WNW.



Photo 17 (DAY 1): 8/24/20 Day-end progress showing Brown Polygon; view to WSW.



Photo 18 (DAY 1): 8/24/20 Day-end site excavation progress; view to SE, Spinnaker in background.



Photo 49 (DAY 2): 8/25/20 Moving Brown Polygon excavation toward East Water Street; view to SSW.

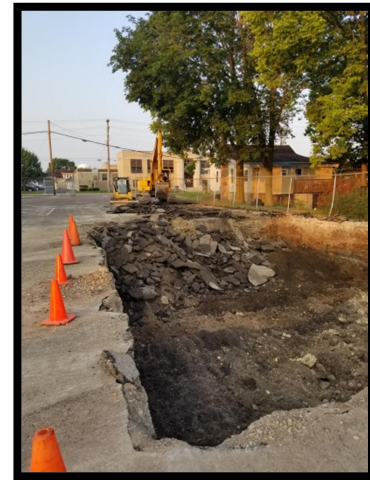


Photo 20 (DAY 2): 8/25/20 Progress of Brown Polygon excavation to 8ft depth; view to SSW.

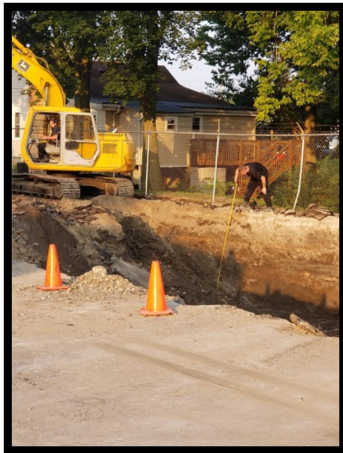


Photo 21 (DAY 2): 8/25/20 Gauging depth of Brown Polygon excavation to 8ft depth; view to SW, offsite/residential home in background.



Photo 22 (DAY 2): 8/25/20 Gauging depth of Brown Polygon excavation to 8ft depth; view to SW, offsite/residential home in background.



Photo 23 (DAY 2): 8/25/20 Tree demo at corner fencepost begins at 1130; view to WSW.



Photo 24 (DAY 2): 8/25/20 Trees in Brown Polygon excavation; beginning demo of front three street trees at 1215; view to S.

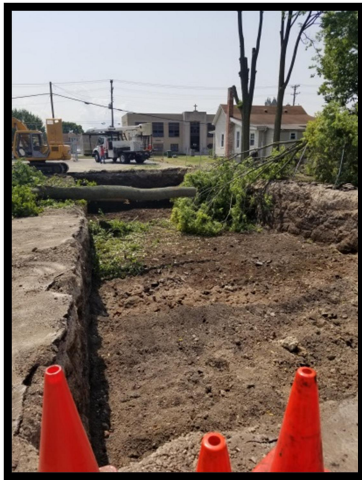


Photo 25 (DAY 2): 8/25/20 Brown Polygon excavation now complete at 1420; view to S (East Water Street).

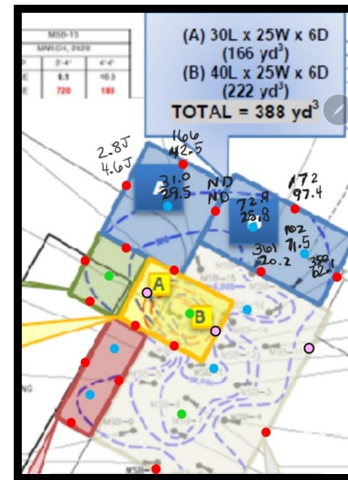


Photo 26 (DAY 2): 8/25/20 Field Map showing initial/preliminary analytical data of soil samples collected in Blue Polygons (A) and (B).



Photo 27 (DAY 2): 8/25/20 An additional 2 feet of soil is excavated (to collect additional samples) from Blue Polygon areas, due to initial sample results in exceedance of site PRGs.



Photo 28 (DAY 2): 8/25/20 Day-end progress, showing tree demo nearly complete, and Brown Polygon excavation complete; view to SW.



Photo 29 (DAY 3): 8/26/20 Removal of corner fencepost, begin excavation of off-site Blue Polygon (A) (residential property); soils simultaneously staged within on-site/Spinnaker Blue Polygon (A) area; view to SW.



Photo 30 (DAY 3): 8/26/20 Continue excavation offsite within off-site Blue Polygon (A); view to SW.



Photo 31 (DAY 3): 8/26/20 Begin excavating Green Polygon (offsite, backyard of residential home) at 0945; view to SSE.



Photo 32 (DAY 3): 8/26/20 Excavating Green Polygon (offsite, backyard of residential home); view to SE.



Photo 33 (DAY 3): 8/26/20 Removal of remaining tree stump at corner property boundary; view to SW.



Photo 34 (DAY 3): 8/26/20 Progress of Green Polygon excavation; view to S.



Photo 35 (DAY 3): 8/26/20 Progress of Green Polygon excavation to 6ft depth; view to S.



Photo 36 (DAY3): 8/26/20 View of completed on-site Brown Polygon (depth 8ft.) and continuing excavation of off-site Green Polygon (depth 6ft.); view to SSW.



Photo 37 (DAY 3): 8/26/20 Soil collected from the Green Polygon excavation and used for field PID screenings to measure the potential presence of volatile organic compounds in site soils.



Photo 38 (DAY 3): 8/26/20 View to Brown Polygon (left), completed Green Polygon (right, at track hoe, out of frame), and beginning excavation of Yellow Polygon excavation (center); view to WSW.



Photo 39 (DAY 3): 8/26/20 Progress of Green and Yellow Polygon excavation areas (center right); view to E.



Photo 40 (DAY 3): 8/26/20 Progress of Green and Yellow Polygon excavation areas (center right), residential home in and East Water Street in background; view to S.



Photo 41 (DAY3): 8/26/20 Completing excavation of Yellow Polygon area (center); view to S.



Photo 42 (DAY 4): 8/27/20 Completing excavation of Red Polygon area (soil staging in Brown Polygon (left); view to S.



Photo 43 (DAY 4): 8/27/20 Completing excavation of Red Polygon area (front left), as shown in Photo 42; view to NE.



Photo 44 (DAY 4): 8/27/20 Loading soil from adjacent Red Polygon excavation area; view to WSW.



Photo 45 (DAY 4): 8/27/20 Loading soil (truck #13 for today) from adjacent Blue Polygon (A) and Green Polygon (residential backyard); view to WSW.



Photo 46 (DAY 4): 8/27/20 Completed excavations of Brown Polygon (foreground), Yellow Polygon (center), and Green Polygon (background); view to WSW.



Photo 47 (DAY 4): 8/27/20 Northern boundary wall of Blue Polygon (A) excavation; view to NW.



Photo 48 (DAY 4): 8/27/20 Southern boundary wall of Brown Polygon, offsite property in background; view to SW.



Photo 49 (DAY 4): 8/27/20 End-of-day continuing to load staged soil from on-site Blue Polygon (A) area; view to SW.



Photo 50 (DAY 5): 8/28/20 Continue clearing and loading staged soil from Blue Polygon (A); view to WNW.



Photo 51 (DAY 5): 8/28/20 On-site/off-site view of all excavation areas complete, except ongoing soil loading at on-site Blue Polygon (A) (right, out of frame); view to SW.



Photo 52 (DAY 5): 8/28/20 Western sidewall of final excavated on-site Blue Polygon (A) area; view to WSW.



Photo 53 (DAY 5): 8/28/20 Northern sidewalls (left) of on-site Blue Polygons (A) and (B), eastern sidewall of on-site Brown Polygon (background); view to ENE.



Photo 54 (DAY 5): 8/28/20 First backfill (gravel) loaded into Blue Polygon (B); view to S toward East Water Street.



Photo 55 (DAY 5): 8/28/20 Continue to backfill (gravel) into Blue Polygon (B); view to ESE.



Photo 56 (DAY 5): 8/28/20 Continue to backfill (gravel) into Blue Polygon (B) and Brown Polygon; view to S.



Photo 57 (DAY 5): 8/28/20 Truck #22 gravel backfill into Brown Polygon excavation area at 1435; view to N.



Photo 58 (DAY 5): 8/28/20 End -of-day photo of gravel in Brown Polygon and Blue (B) Polygon excavations; view to S.



Photo 59 (DAY 6): 9/01/20 Begin bracing/placing fence posts along property boundary; view to S.



Photo 60 (DAY 6): 9/01/20 Begin bracing/placing fence posts along property boundary; view to SE.



Photo 61 (DAY 6): 9/01/20 Continue to spread gravel backfill across on-site/Spinnaker excavation areas.



Photo 62 (DAY 6): 9/01/20 Spreading gravel backfill into off-site/residential backyard area; view to SSE.



Photo 63 (DAY 6): 9/01/20 Complete grading gravel today (approx. 35 trucks of backfill deposited); view to SSW.



Photo 64 (DAY 7): 9/02/20 View to S and along property boundary, with reinstallation of fenceline, and access road in background, adjacent to orange safety cones.



Photo 65 (DAY 7): 9/02/20 Gravel-asphalt mix covers surfaces of on-site/Spinnaker excavation areas; view to S.



Photo 66 (DAY 7): 9/02/20 Truck arriving with topsoil backfill for backyard; view to W.



Photo 67 (DAY 7): 9/02/20 Truck arriving with topsoil backfill for backyard; view to WNW.



Photo 68 (DAY 7): 9/02/20 Spreading and grading topsoil backfill for backyard; view to SW.



Photo 69 (DAY 7): 9/02/20 Southern boundary of access road, tree stumps, and residence (left); view to NNW.



Photo 70 (DAY 7): 9/02/20 Spreading, grading, and mounding topsoil in backyard residence; view to S.



Photo 71 (DAY 7): 9/02/20 Spreading, grading, and mounding topsoil in backyard residence; view to S, along fenceline property boundary.



Photo 72 (DAY 7): 9/02/20 Spreading and grading topsoil load #1 within off-site property backyard; view to SSW.



Photo 73 (DAY 7): 9/02/20 Spreading and grading topsoil load #2 within off-site property backyard; view to W.



Photo 74 (DAY 7): 9/02/20 Status of residential backyard, prior to backfill of topsoil, view to N.



Photo 75 (DAY 7): 9/02/20 Status of residential backyard, prior to backfill of topsoil, view to NNE.



Photo 76 (DAY 7): 9/02/20 Access road, southern boundary, adjacent to off-site residence; view to N.

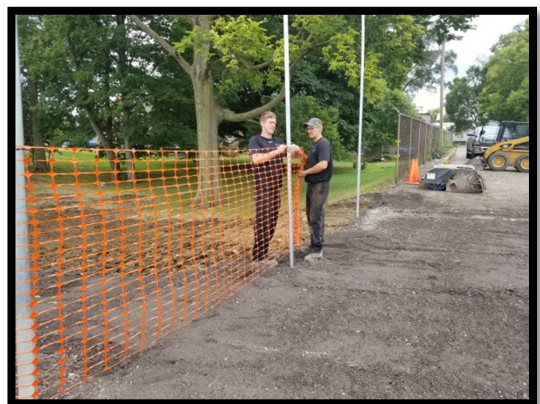


Photo 77 (DAY 7): 9/02/20 Installing remaining orange safety fencing; view to W.



Photo 78 (DAY 7): 9/02/20 Surficial cleanup and sweep;
view to S.



Photo 79 (DAY 7): 9/02/20 Tamping surfaces with track
hoe as partial compaction; view to SW.



Photo 80 (DAY 7): 9/02/20 Tangential view along southern
boundary of Spinnaker Brown Polygon and Red Polygon
(access road) excavations; view to W.



Photo 81 (DAY 7): 9/02/20 View of smooth surficial gravel-
asphalt mix across site; view to SW.

APPENDIX B

Phase B LSI Laboratory Analytical Data Reports



Analytical Data Package

Prepared by:

Pace Analytical Services

Pace Project No.: 5249143
