

| ID | Task Mode | Task Name | Duration | Start | Finish | April | | | | | May | | | |
|----|-----------|---|----------|-------------|-------------|-------|-----|------|------|------|-----|-----|------|------|
| | | | | | | 3/27 | 4/3 | 4/10 | 4/17 | 4/24 | 5/1 | 5/8 | 5/15 | 5/22 |
| 1 | | Project Work Plan | 6 days | Wed 4/6/11 | Wed 4/13/11 | | | | | | | | | |
| 2 | | Work Plan Review - EPA | 2 days | Thu 4/14/11 | Fri 4/15/11 | | | | | | | | | |
| 3 | | ACTA Data Request | 14 days | Tue 5/24/11 | Fri 6/10/11 | | | | | | | | | |
| 4 | | ACTA Data Review | 20 days | Mon 6/27/11 | Fri 7/22/11 | | | | | | | | | |
| 5 | | Prepare/Update Work Plan for Site Assessment | 5 days | Mon 4/25/11 | Fri 4/29/11 | | | | | | | | | |
| 6 | | Work Plan Review - EPA | 2 days | Mon 5/2/11 | Tue 5/3/11 | | | | | | | | | |
| 7 | | Revise Work Plan (Renamed Project Plan) | 9 days | Tue 5/3/11 | Fri 5/13/11 | | | | | | | | | |
| 8 | | EPA Review of Project Plan | 24 days | Fri 5/13/11 | Wed 6/15/11 | | | | | | | | | |
| 9 | | Prepare Work Activity Plan (WAP) #1 for Technical Data Review | 3 days | Fri 6/17/11 | Tue 6/21/11 | | | | | | | | | |
| 10 | | EPA Review of WAP #1 | 2 days | Tue 6/21/11 | Wed 6/22/11 | | | | | | | | | |
| 11 | | Prepare WAP #2 Oil Charaterization | 5 days | Thu 6/16/11 | Wed 6/22/11 | | | | | | | | | |
| 12 | | EPA Review of WAP #2 | 12 days | Wed 6/29/11 | Thu 7/14/11 | | | | | | | | | |
| 13 | | Prepare WAP #3 Waste Disposal Plan | 5 days | Thu 6/23/11 | Wed 6/29/11 | | | | | | | | | |
| 14 | | EPA Review of WAP #3 | 2 days | Thu 6/30/11 | Fri 7/1/11 | | | | | | | | | |
| 15 | | Prepare WAP #4 Collection Area Operations and Maintenance | 1 day | Tue 7/12/11 | Tue 7/12/11 | | | | | | | | | |
| 16 | | EPA Review of WAP #4 | 4 days | Wed 7/13/11 | Mon 7/18/11 | | | | | | | | | |










Project: Dominguez Channel Oil S
Date: Tue 9/13/11

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |



















| ID | Task Mode | Task Name | Duration | Start | Finish | April | | | | | May | | | |
|----|-----------|--|----------|-------------|-------------|-------|-----|------|------|------|-----|-----|------|------|
| | | | | | | 3/27 | 4/3 | 4/10 | 4/17 | 4/24 | 5/1 | 5/8 | 5/15 | 5/22 |
| 17 | | Transfer Collection Area Operations and Maintenance to Crimson | | Mon 7/25/11 | | | | | | | | | | |
| 18 | | Prepare WAP #5 Shell Lubes Plant and French Drain Soil Investigation | 7 days | Mon 7/25/11 | Tue 8/2/11 | | | | | | | | | |
| 19 | | EPA Review of WAP #5 | 6 days | Tue 8/2/11 | Tue 8/9/11 | | | | | | | | | |
| 20 | | Prepare WAP #6 Youngstown Lateral Pipeline Removal | 51 days | Wed 6/15/11 | Wed 8/24/11 | | | | | | | | | |
| 21 | | EPA, OSFM, ACTA Review of WAP #6 | 14 days | Thu 8/25/11 | Tue 9/13/11 | | | | | | | | | |
| 22 | | Prepare WAP #7 French Drain Investigation | 14 days | Tue 8/30/11 | Fri 9/16/11 | | | | | | | | | |
| 23 | | EPA Review of WAP #7 | 2 days | Mon 9/19/11 | Tue 9/20/11 | | | | | | | | | |
| 24 | | Revision of SAP for WAP #5 | 11 days | Wed 8/31/11 | Wed 9/14/11 | | | | | | | | | |
| 25 | | Project Coordination w/ ACTA for WAP #5 Activities - Pending EPA approval to initiate activities | 9 days | Tue 9/13/11 | Fri 9/23/11 | | | | | | | | | |
| 26 | | Begin onsite work for WAP #5 - Initial Oil Removal and Investigation | 2 days | Tue 9/27/11 | Wed 9/28/11 | | | | | | | | | |


Project: Dominguez Channel Oil S
Date: Tue 9/13/11

| | | | | | |
|-----------------|--|--------------------|--|-----------------------|--|
| Task | | External Milestone | | Manual Summary Rollup | |
| Split | | Inactive Task | | Manual Summary | |
| Milestone | | Inactive Milestone | | Start-only | |
| Summary | | Inactive Summary | | Finish-only | |
| Project Summary | | Manual Task | | Deadline | |
| External Tasks | | Duration-only | | Progress | |

| ID | Task Mode | Task Name | Duration | Start | Finish | April | | | | | May | | | |
|----|---|--|----------|--------------|--------------|-------|-----|------|------|------|-----|-----|------|------|
| | | | | | | 3/27 | 4/3 | 4/10 | 4/17 | 4/24 | 5/1 | 5/8 | 5/15 | 5/22 |
| 27 |  | Prepare summary report of WAP #5 activities | 10 days | Mon 10/3/11 | Fri 10/14/11 | | | | | | | | | |
| 28 |  | Revise WAP #6 w/ provided comments (ACTA, OSFM) | 2 days | Mon 9/19/11 | Tue 9/20/11 | | | | | | | | | |
| 29 |  | Initiate WAP #6 | 18 days | Tue 10/4/11 | Thu 10/27/11 | | | | | | | | | |
| 30 |  | Initiate WAP #7 - pending EPA approval | 64 days | Mon 10/24/11 | Thu 1/19/12 | | | | | | | | | |
| 31 |  | Prepare WAP #8 Water Treatment System | 22 days | Mon 8/29/11 | Tue 9/27/11 | | | | | | | | | |
| 32 |  | EPA review WAP #8 | 2 days | Wed 9/28/11 | Thu 9/29/11 | | | | | | | | | |
| 33 |  | Construct Water Treatment System for Collection Area | 37 days | Thu 9/29/11 | Fri 11/18/11 | | | | | | | | | |
| 34 |  | Prepare WAP #9 Investigate Drain System on Shell Lubes Plant | 3 days | Mon 10/3/11 | Wed 10/5/11 | | | | | | | | | |
| 35 |  | EPA review of WAP #9 | 2 days | Thu 10/6/11 | Fri 10/7/11 | | | | | | | | | |





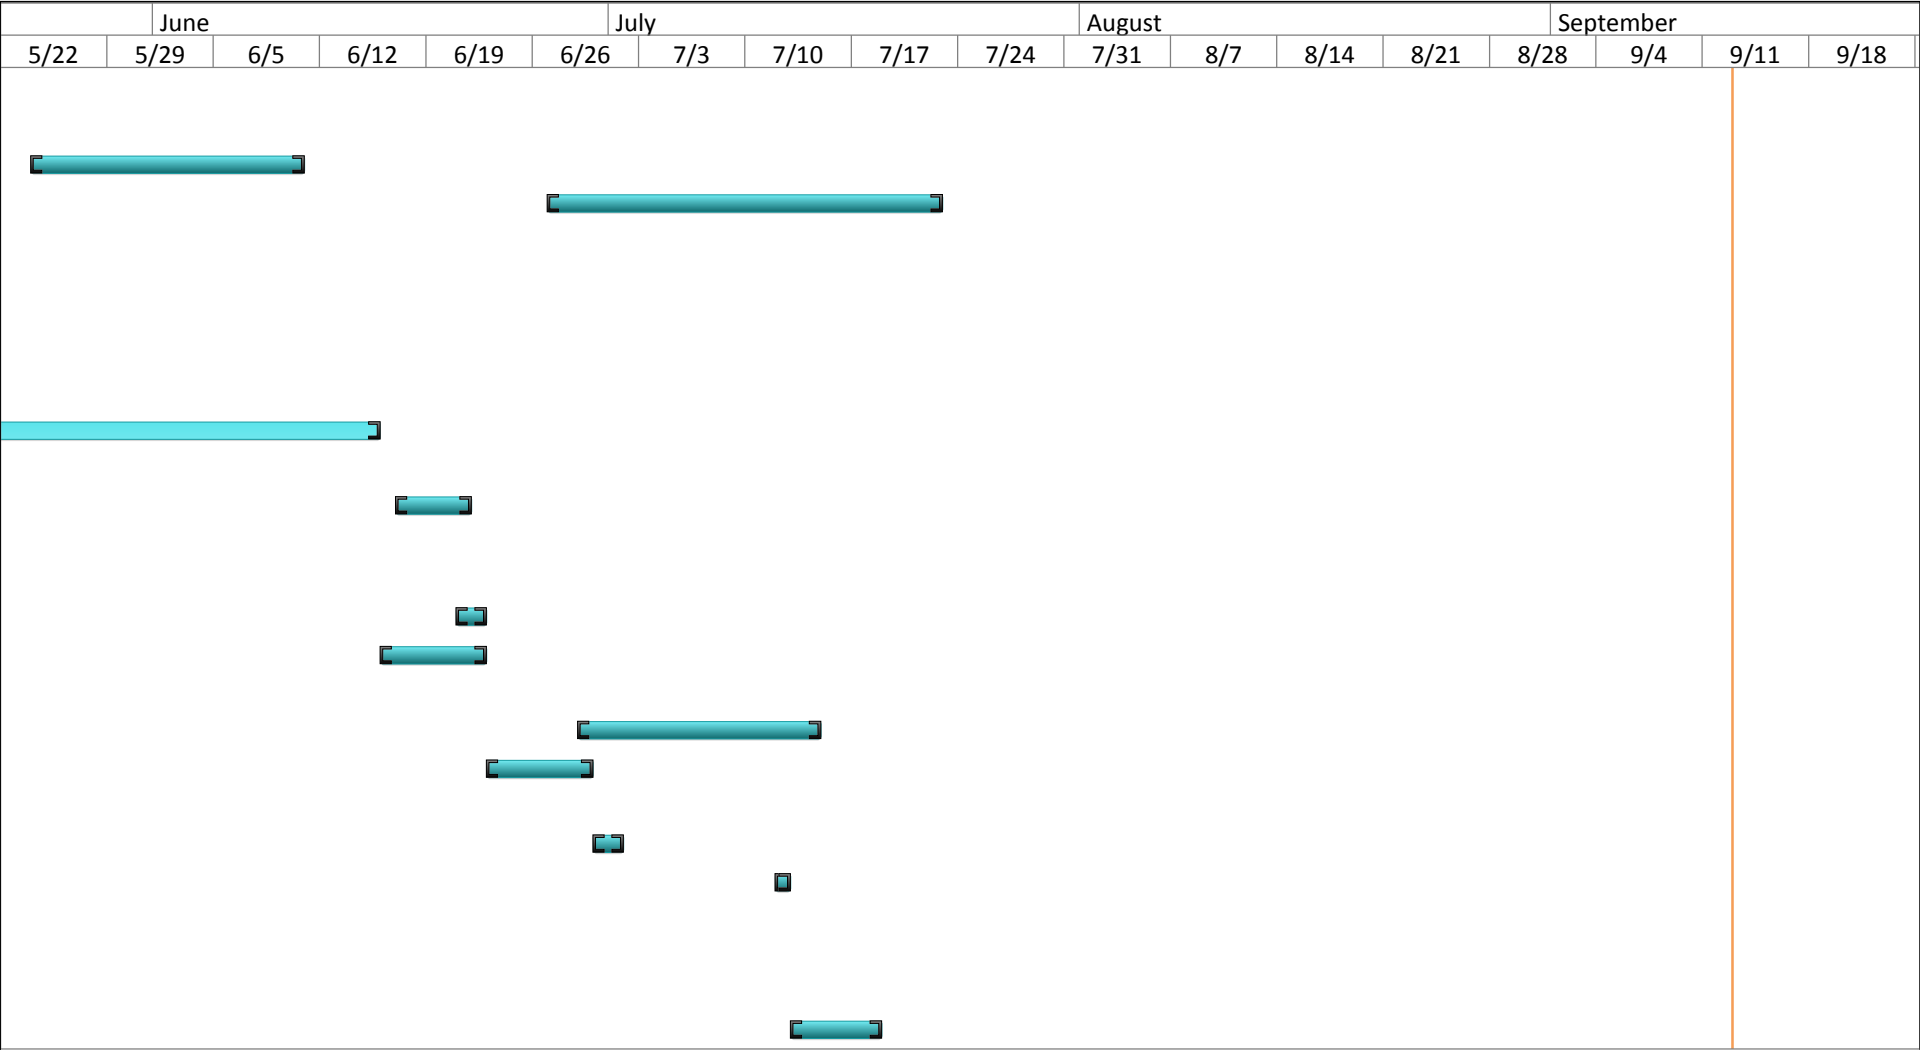













Project: Dominguez Channel Oil S
Date: Tue 9/13/11

| | | | | | |
|-----------------|---|--------------------|---|-----------------------|---|
| Task |  | External Milestone |  | Manual Summary Rollup |  |
| Split |  | Inactive Task |  | Manual Summary |  |
| Milestone |  | Inactive Milestone |  | Start-only |  |
| Summary |  | Inactive Summary |  | Finish-only |  |
| Project Summary |  | Manual Task |  | Deadline |  |
| External Tasks |  | Duration-only |  | Progress |  |



| | | | | | | |
|---|-----------------|--|--------------------|--|-----------------------|--|
| Project: Dominguez Channel Oil S Date: Tue 9/13/11 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |



| October | | | | | November | | | | | December | | | | | January | | | |
|---------|------|------|-------|-------|----------|------|-------|-------|-------|----------|-------|-------|-------|-----|---------|------|------|--|
| 9/25 | 10/2 | 10/9 | 10/16 | 10/23 | 10/30 | 11/6 | 11/13 | 11/20 | 11/27 | 12/4 | 12/11 | 12/18 | 12/25 | 1/1 | 1/8 | 1/15 | 1/22 | |
| | | | | | | | | | | | | | | | | | | |

| | | | | | | |
|---|-----------------|---|--------------------|---|-----------------------|---|
| Project: Dominguez Channel Oil S Date: Tue 9/13/11 | Task |  | External Milestone |  | Manual Summary Rollup |  |
| | Split |  | Inactive Task |  | Manual Summary |  |
| | Milestone |  | Inactive Milestone |  | Start-only |  |
| | Summary |  | Inactive Summary |  | Finish-only |  |
| | Project Summary |  | Manual Task |  | Deadline |  |
| | External Tasks |  | Duration-only |  | Progress |  |

| | October | | | | | November | | | | | December | | | | | January | | | |
|------|---------|------|-------|-------|-------|----------|-------|-------|-------|------|----------|-------|-------|-----|-----|---------|------|--|--|
| 9/25 | 10/2 | 10/9 | 10/16 | 10/23 | 10/30 | 11/6 | 11/13 | 11/20 | 11/27 | 12/4 | 12/11 | 12/18 | 12/25 | 1/1 | 1/8 | 1/15 | 1/22 | | |



| | | | | | | |
|---|-----------------|--|--------------------|--|-----------------------|--|
| Project: Dominguez Channel Oil S Date: Tue 9/13/11 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |

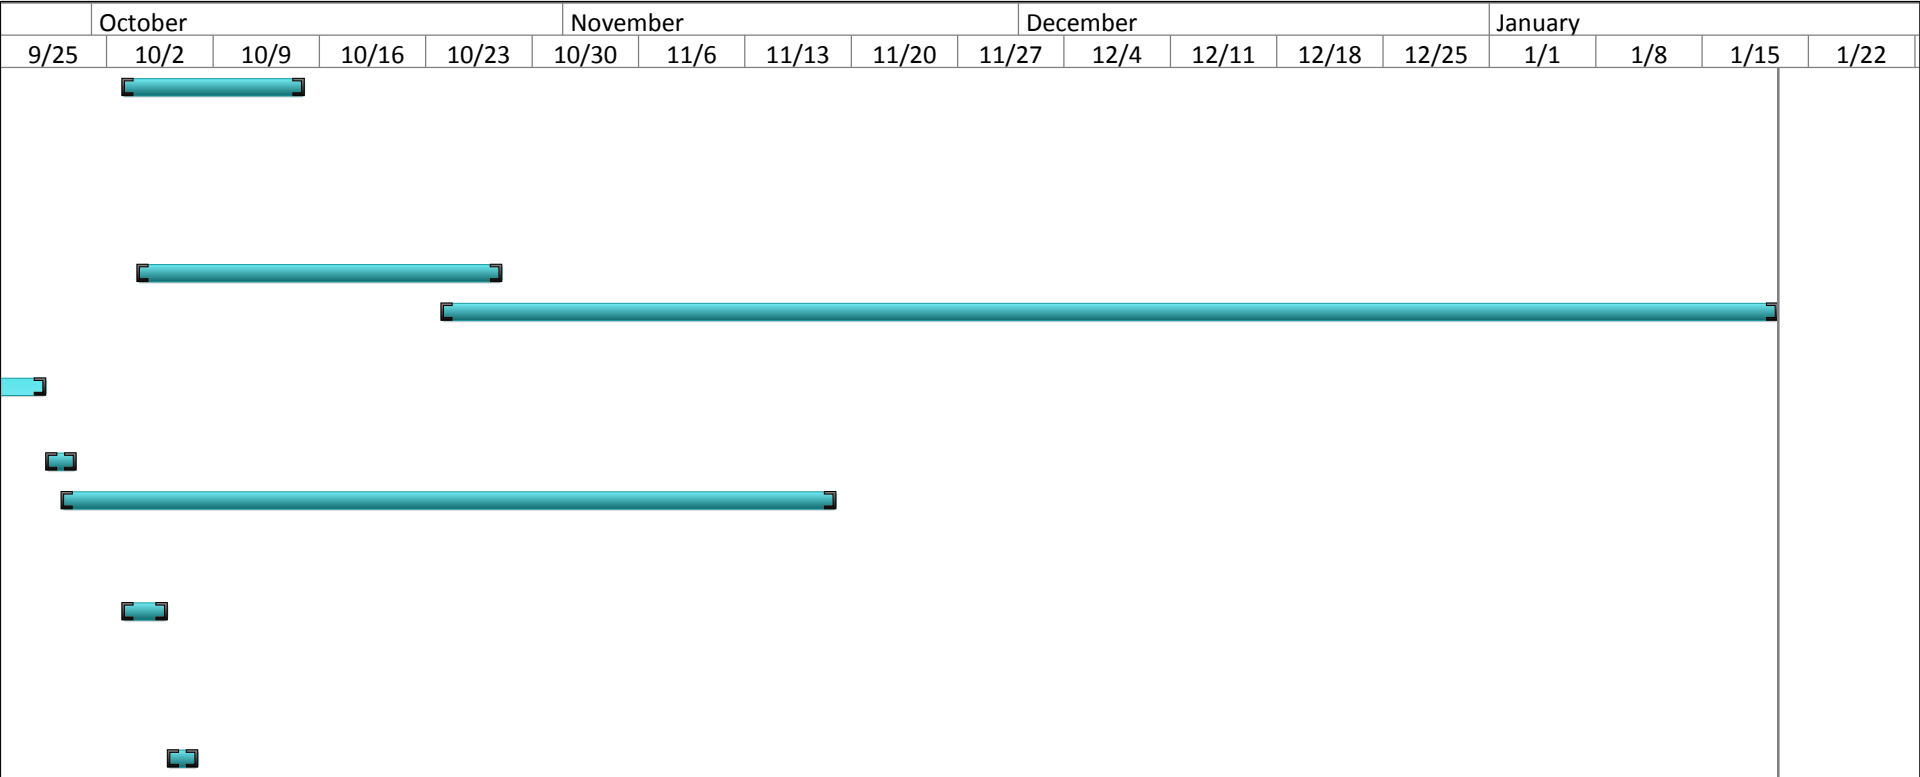

| | | | | | | |
|---|-----------------|--|--------------------|--|-----------------------|--|
| Project: Dominguez Channel Oil S Date: Tue 9/13/11 | Task | | External Milestone | | Manual Summary Rollup | |
| | Split | | Inactive Task | | Manual Summary | |
| | Milestone | | Inactive Milestone | | Start-only | |
| | Summary | | Inactive Summary | | Finish-only | |
| | Project Summary | | Manual Task | | Deadline | |
| | External Tasks | | Duration-only | | Progress | |
