

Remedial Action Contract 2
for Remedial Response, Enforcement Oversight, and
Non-Time-Critical Removal Activities in EPA Region 8

U.S. EPA Contract Number EP-W-05-049

Monthly Progress Report

June 2017

359 – Columbia Falls Aluminum Plant

Prepared for:
U.S. Environmental Protection Agency
Region 8
1595 Wynkoop Street
Denver, CO 80202-1129

Prepared by:
CDM Federal Programs Corporation
555 17th Street, Suite 1100
Denver, CO 80202

Business Confidential Information

This monthly report includes data that shall not be disclosed outside the government and shall not be duplicated, used, or disclosed—whole or in part—for any purpose other than the purpose it was intended. The government shall have the right to duplicate, use, or disclose this report to the extent provided in U.S. Environmental Protection Agency Contract No.: EP-W-05-049. This restriction does not limit the government's right to use information contained in this report if it is obtainable from another source without restriction. This restriction applies to all sheets marked as such in this report.

Standard Form 1035

September 1973 &
Treasury FRM 2000
1035-110

PUBLIC VOUCHER FOR PURCHASES AND
SERVICES OTHER THAN PERSONAL

CONTINUATION SHEET

Voucher No.

Schedule No.

Sheet No.

***** COMPANY CONFIDENTIAL *****

PBI / Ex. 4

**Work Assignment
Monthly Progress Report
June 2017
- Region VIII -
Columbia Falls Aluminum Plant
Work Assignment No. 359-RSBD-A882
Contract No. EP-W-05-049**

Monthly Work Assignment Status Report (Technical)

Prepared by: Gunnar Emilsson

Date: July 20, 2017

Period: May 28 – July 1, 2017

1. PROGRESS MADE THIS REPORTING PERIOD:

Task 1 – Project Planning and Support

- Performed monthly invoice preparation, weekly financial tracking, and general work assignment correspondence for the U.S. Environmental Protection Agency (EPA).
- Completed review of Columbia Falls Aluminum Company (CFAC), Glencore, and their contractor, Roux & Associates, (the CFAC team) response to comments to the *Screening Level Ecological Risk Assessment* and the *Phase I Site Characterization Data Summary Report*.
- Reviewed and provided EPA comments to the CFAC team's proposed Modifications 10 (slug testing) and 11 (asbestos sampling) to the Phase I sampling and analysis plan. Supported EPA during calls with the CFAC team, which led to the modifications being revised and approved by EPA.

2. UPCOMING ACTIVITIES:

- Review revised *Phase I Site Characterization Data Summary Report* and *Screening Level Ecological Risk Assessment* upon receipt.
- Other activities as directed by EPA.

3. SUBCONTRACTING:

- None.

4. POTENTIAL PROBLEMS AND PROPOSED SOLUTIONS:

- None.

5. CRITICAL ACTION ITEMS:

- None.

6. BUDGET HIGHLIGHTS:

- See burn chart and forecasted expenditures in Attachment 2.
- Detail for Remedial Action Contract program support allocation and other direct costs:

PBI / Ex. 4

7. TRAVEL:

- None.

8. DELIVERABLE SCHEDULE HIGHLIGHTS:


- See Attachment 1 for deliverable submittal schedule.

ATTACHMENT I
CDM Federal Programs
Deliverable Schedule Tracking
Columbia Falls Aluminum Plant
Work assignment: 359-RSBD-A882

Deliverable	Original Planned Completion Date	Current Planned Completion Date	Actual Completion Date	Explanation of Delay
PBI / Ex. 4				

ATTACHMENT 2
CDM Federal Programs Corporation
RAC 8 Burn Rate and Projections Summary
Contract No. EP-W-05-049
Columbia Falls Aluminum Plant
Work Assignment 359-RSBD-A882


WA 359
Expenditures

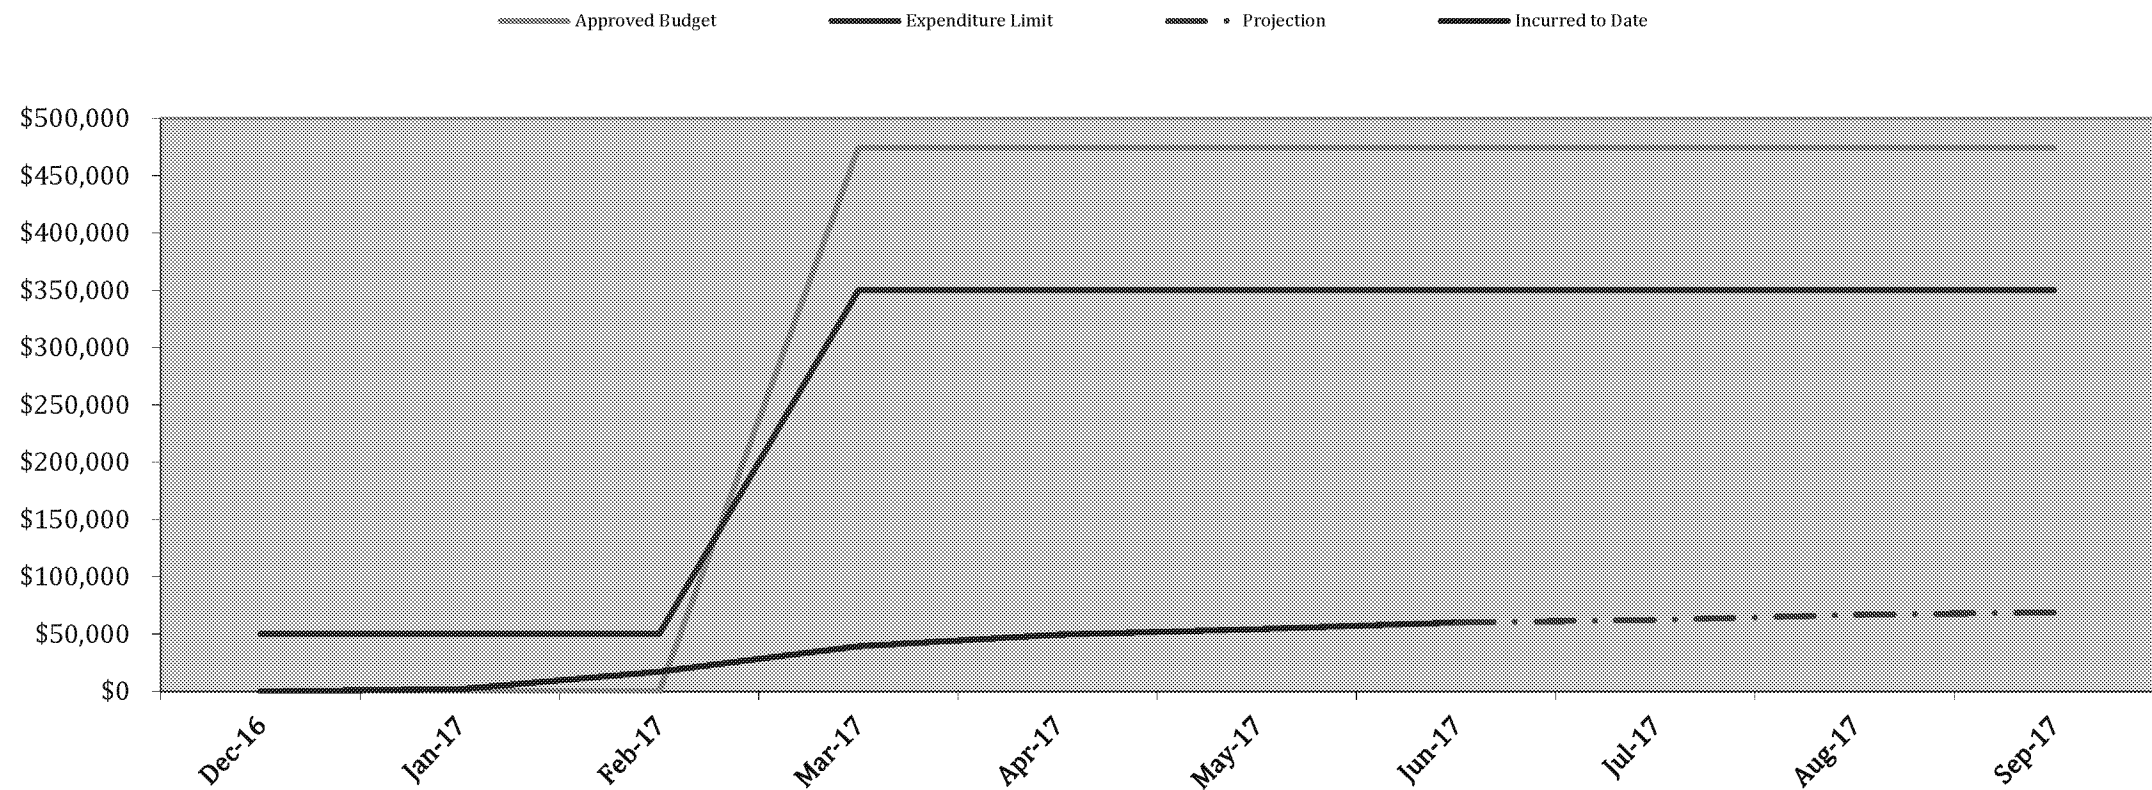

Expenditure Limit \$350,000
 Budget \$474,147

	2016	2017								
	December	January	February	March	April	May	June	July	August	September
Projections			\$6,600	\$26,400	\$11,000	\$8,000	\$11,000	\$2,200	\$4,400	\$2,200
Actual	\$50	\$1,848	\$15,309	\$22,150	\$10,047	\$4,851	\$5,903			
Cumulative	\$50	\$1,898	\$17,207	\$39,358	\$49,405	\$54,256	\$60,160	\$62,360	\$66,760	\$68,960
% Spent	0%	4%	34%	11%	14%	16%	17%	18%	19%	20%
Funding Balance	\$49,950	\$48,102	\$32,793	\$310,642	\$300,595	\$295,744	\$289,840	\$287,640	\$283,240	\$281,040

ATTACHMENT 2
CDM Federal Programs Corporation
RAC 8 Burn Rate and Projections Summary
Contract No. EP-W-05-049
Columbia Falls Aluminum Plant
Work Assignment 359-RSBD-A882

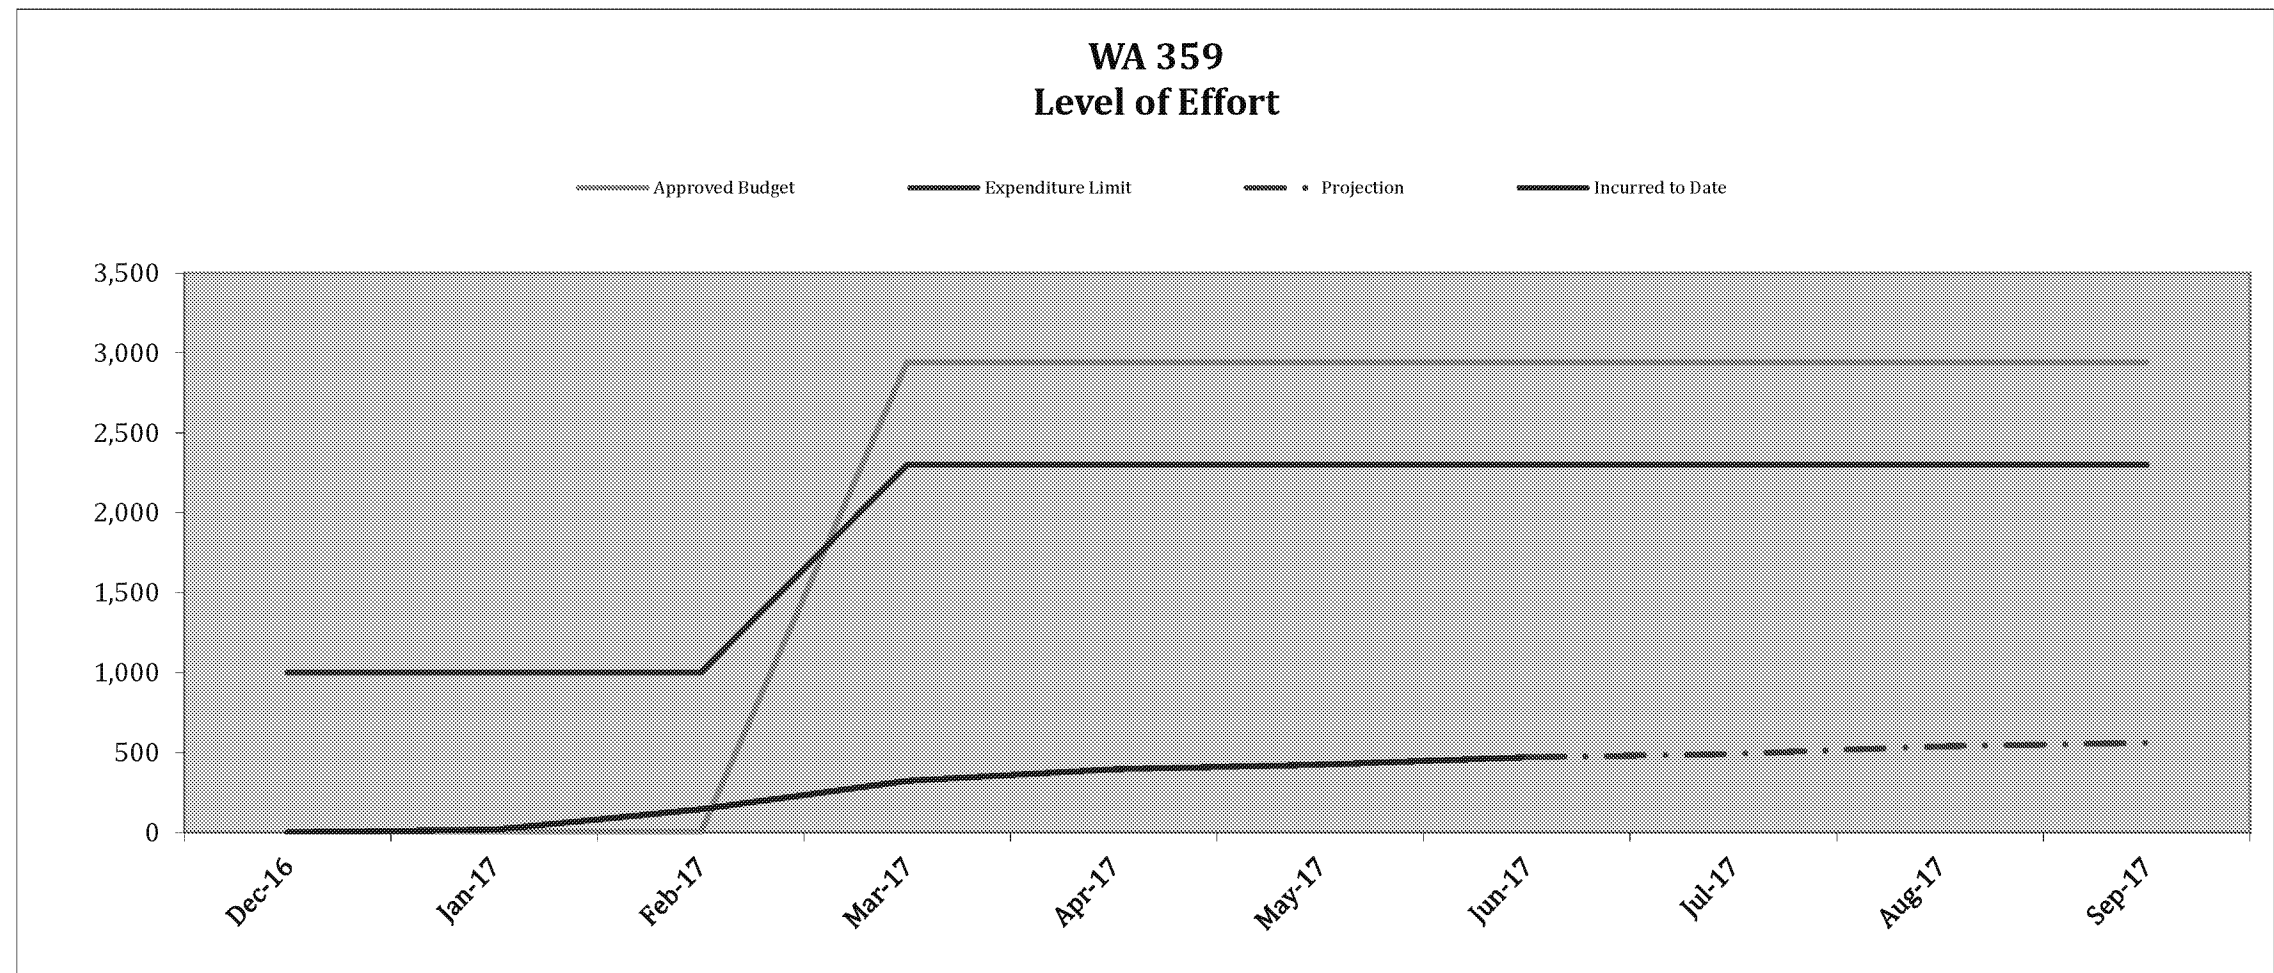

Expenditure Limit 2,300
 Budget 2,943

	2016	2017								
	December	January	February	March	April	May	June	July	August	September
Projections			70	240	100	50	100	20	50	20
Actual	2	16	128	178	73	29	46			
Cumulative	2	18	146	323	396	425	471	491	541	561
% Spent	0%	2%	15%	14%	17%	18%	20%	21%	24%	24%
Funding Balance	999	983	855	1,977	1,904	1,876	1,830	1,810	1,760	1,740

Report 1:

Work Assignment - Task Level Specific Detail Report

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

Region: 70

Task Number: 2 Task Title: COMMUNITY INVOLVEMENT Task Category: CR

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4

PBI / Ex. 4
