

Remedial Action Contract 2
for Remedial Response, Enforcement Oversight, and
Non-Time-Critical Removal Activities in EPA Region 8

U.S. EPA Contract Number EP-W-05-049

Monthly Progress Report

April 2017

359 – Columbia Falls Aluminum Plant

Prepared for:
U.S. Environmental Protection Agency
Region 8
1595 Wynkoop Street
Denver, CO 80202-1129

Prepared by:
CDM Federal Programs Corporation
555 17th Street, Suite 1100
Denver, CO 80202

Business Confidential Information

This monthly report includes data that shall not be disclosed outside the government and shall not be duplicated, used, or disclosed—whole or in part—for any purpose other than the purpose it was intended. The government shall have the right to duplicate, use, or disclose this report to the extent provided in U.S. Environmental Protection Agency Contract No.: EP-W-05-049. This restriction does not limit the government's right to use information contained in this report if it is obtainable from another source without restriction. This restriction applies to all sheets marked as such in this report.

Standard Form 1035 September 1973 & Treasury FRM 2000 1035-110	PUBLIC VOUCHER FOR PURCHASES AND SERVICES OTHER THAN PERSONAL CONTINUATION SHEET	Voucher No. <hr/> Schedule No. <hr/> Sheet No.																																																																																																							
***** COMPANY CONFIDENTIAL *****																																																																																																									
ARTICLES OR SERVICES <small>(Enter Description, Item Number of contractor Federal supply schedule, and other information deemed necessary)</small>	Quan- tity	Unit Price <hr/> COST PER																																																																																																							
RAC Contract Invoice Backup Report Contract Summary (CORP - 1) Contractor Name: CDM FEDERAL PROGRAMS CORPORATION Invoice Number: B09100 Contract Number: EP_W_05_049_O Invoice Date: 4/29/2017 Contract Period: OPTION																																																																																																									
<table style="width: 100%; border-collapse: collapse;"> <tr> <td style="width: 30%;">Work Assignment Number:</td> <td style="width: 30%;">359-RSBD-A882</td> <td style="width: 30%;">CDM Federal Project No.:</td> <td style="width: 10%;">3383.359</td> </tr> <tr> <td>Work Assignment Name:</td> <td colspan="3">Columbia Falls Aluminum Plant</td> </tr> </table> <table style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 30%;"></th> <th style="width: 10%; text-align: center;">Current</th> <th style="width: 10%;"></th> <th style="width: 10%; text-align: center;">Cumulative</th> <th style="width: 10%;"></th> </tr> <tr> <th></th> <th style="text-align: center;">LOE</th> <th style="text-align: center;">Dollars</th> <th style="text-align: center;">LOE</th> <th style="text-align: center;">Dollars</th> </tr> </thead> <tbody> <tr> <td>Direct Labor P1</td> <td style="text-align: right;">0.00</td> <td style="text-align: right;">0.00</td> <td style="text-align: right;">2.00</td> <td style="text-align: right;">57.74</td> </tr> <tr> <td> P2</td> <td style="text-align: right;">10.50</td> <td style="text-align: right;">438.06</td> <td style="text-align: right;">110.00</td> <td style="text-align: right;">4,528.61</td> </tr> <tr> <td> P3</td> <td style="text-align: right;">58.50</td> <td style="text-align: right;">3,018.07</td> <td style="text-align: right;">255.00</td> <td style="text-align: right;">12,426.62</td> </tr> <tr> <td> P4</td> <td style="text-align: right;">1.00</td> <td style="text-align: right;">67.04</td> <td style="text-align: right;">6.00</td> <td style="text-align: right;">392.62</td> </tr> <tr> <td> T1</td> <td style="text-align: right;">0.00</td> <td style="text-align: right;">0.00</td> <td style="text-align: right;">1.00</td> <td style="text-align: right;">15.26</td> </tr> <tr> <td></td> <td style="text-align: right; border-top: 1px solid black;">70.00</td> <td style="text-align: right; border-top: 1px solid black;">3,523.17</td> <td style="text-align: right; border-top: 1px solid black;">374.00</td> <td style="text-align: right; border-top: 1px solid black;">17,420.85</td> </tr> <tr> <td>Fringe 39.50% (of Labor)</td> <td></td> <td style="text-align: right;">1,391.67</td> <td></td> <td style="text-align: right;">6,881.19</td> </tr> <tr> <td>Overhead - Office 54.20% (of Lbr&Frnge)</td> <td></td> <td style="text-align: right;">2,646.82</td> <td></td> <td style="text-align: right;">11,639.05</td> </tr> <tr> <td>Overhead - Field 16.00% (of Lbr&Frnge)</td> <td></td> <td style="text-align: right;">5.03</td> <td></td> <td style="text-align: right;">452.57</td> </tr> <tr> <td>G&A 18.30% (All Excl Subs)</td> <td></td> <td style="text-align: right;">1,384.71</td> <td></td> <td style="text-align: right;">6,660.03</td> </tr> <tr> <td>Total Cost</td> <td style="text-align: right; border-top: 1px solid black;">70.00</td> <td style="text-align: right; border-top: 1px solid black;">8,951.40</td> <td style="text-align: right; border-top: 1px solid black;">374.00</td> <td style="text-align: right; border-top: 1px solid black;">43,053.69</td> </tr> <tr> <td>Base Fee</td> <td></td> <td style="text-align: right;">602.00</td> <td></td> <td style="text-align: right;">3,216.40</td> </tr> <tr> <td>Prog Support Alloc</td> <td style="text-align: right;">3.00</td> <td style="text-align: right;">494.05</td> <td style="text-align: right;">22.00</td> <td style="text-align: right;">3,134.99</td> </tr> <tr> <td>Total Amount Claimed</td> <td style="text-align: right; border-top: 1px solid black;">73.00</td> <td style="text-align: right; border-top: 1px solid black;">10,047.45</td> <td style="text-align: right; border-top: 1px solid black;">396.00</td> <td style="text-align: right; border-top: 1px solid black;">49,405.08</td> </tr> <tr> <td>Amount Reimbursed</td> <td></td> <td></td> <td></td> <td style="text-align: right;">39,357.63</td> </tr> <tr> <td>(Withhold)/Rebill</td> <td></td> <td style="text-align: right; border-top: 1px solid black;">0.00</td> <td></td> <td style="text-align: right; border-top: 1px solid black;">0.00</td> </tr> <tr> <td>Current Amount Claimed</td> <td></td> <td style="text-align: right; border-top: 1px solid black; border-bottom: 3px double black;">10,047.45</td> <td></td> <td style="text-align: right; border-top: 1px solid black; border-bottom: 3px double black;">10,047.45</td> </tr> </tbody> </table>			Work Assignment Number:	359-RSBD-A882	CDM Federal Project No.:	3383.359	Work Assignment Name:	Columbia Falls Aluminum Plant				Current		Cumulative			LOE	Dollars	LOE	Dollars	Direct Labor P1	0.00	0.00	2.00	57.74	P2	10.50	438.06	110.00	4,528.61	P3	58.50	3,018.07	255.00	12,426.62	P4	1.00	67.04	6.00	392.62	T1	0.00	0.00	1.00	15.26		70.00	3,523.17	374.00	17,420.85	Fringe 39.50% (of Labor)		1,391.67		6,881.19	Overhead - Office 54.20% (of Lbr&Frnge)		2,646.82		11,639.05	Overhead - Field 16.00% (of Lbr&Frnge)		5.03		452.57	G&A 18.30% (All Excl Subs)		1,384.71		6,660.03	Total Cost	70.00	8,951.40	374.00	43,053.69	Base Fee		602.00		3,216.40	Prog Support Alloc	3.00	494.05	22.00	3,134.99	Total Amount Claimed	73.00	10,047.45	396.00	49,405.08	Amount Reimbursed				39,357.63	(Withhold)/Rebill		0.00		0.00	Current Amount Claimed		10,047.45		10,047.45
Work Assignment Number:	359-RSBD-A882	CDM Federal Project No.:	3383.359																																																																																																						
Work Assignment Name:	Columbia Falls Aluminum Plant																																																																																																								
	Current		Cumulative																																																																																																						
	LOE	Dollars	LOE	Dollars																																																																																																					
Direct Labor P1	0.00	0.00	2.00	57.74																																																																																																					
P2	10.50	438.06	110.00	4,528.61																																																																																																					
P3	58.50	3,018.07	255.00	12,426.62																																																																																																					
P4	1.00	67.04	6.00	392.62																																																																																																					
T1	0.00	0.00	1.00	15.26																																																																																																					
	70.00	3,523.17	374.00	17,420.85																																																																																																					
Fringe 39.50% (of Labor)		1,391.67		6,881.19																																																																																																					
Overhead - Office 54.20% (of Lbr&Frnge)		2,646.82		11,639.05																																																																																																					
Overhead - Field 16.00% (of Lbr&Frnge)		5.03		452.57																																																																																																					
G&A 18.30% (All Excl Subs)		1,384.71		6,660.03																																																																																																					
Total Cost	70.00	8,951.40	374.00	43,053.69																																																																																																					
Base Fee		602.00		3,216.40																																																																																																					
Prog Support Alloc	3.00	494.05	22.00	3,134.99																																																																																																					
Total Amount Claimed	73.00	10,047.45	396.00	49,405.08																																																																																																					
Amount Reimbursed				39,357.63																																																																																																					
(Withhold)/Rebill		0.00		0.00																																																																																																					
Current Amount Claimed		10,047.45		10,047.45																																																																																																					

**Work Assignment
Monthly Progress Report
April 2017
- Region VIII -
Columbia Falls Aluminum Plant
Work Assignment No. 359-RSBD-A882
Contract No. EP-W-05-049**

Monthly Work Assignment Status Report (Technical)

Prepared by: Gunnar Emilsson

Date: May 19, 2017

Period: April 2 – 29, 2017

1. PROGRESS MADE THIS REPORTING PERIOD:

Task 1 – Project Planning and Support

- Performed monthly invoice preparation, weekly financial tracking, and general work assignment correspondence for the U.S. Environmental Protection Agency (EPA).
- Provided EPA comments to the *Screening Level Ecological Risk Assessment*. Also attached to the comments an example Ecological Screening Values workbook to guide revising the document.
- Finalized comments to the *Phase I Site Characterization Data Summary Report* and sent them to EPA for transmittal to the Columbia Falls Aluminum Company (CFAC), Glencore, and their contractors, Roux & Associates (the CFAC team).
- Met with EPA, Montana Department of Environmental Quality, and the CFAC team to review the transmitted comments and tour the CFAC site.
- Reviewed and provided EPA comments to a sampling and analysis plan addendum to collect concrete cores from the CFAC plant buildings for additional fluoride analysis. Prior to submitting the comments, CDM Smith participated in a call with EPA and the CFAC team to review the purpose behind the request.

Task 2 – Community Involvement

- At EPA's request, CDM Smith attended two public meetings. A city council meeting was held April 17, 2017 and included a progress update presentation by EPA. An April 19, 2017 public meeting was presented by the CFAC team to the Community Liaison Panel.

2. UPCOMING ACTIVITIES:

- Finalize comments to the *Phase I Site Characterization Data Summary Report* and *Screening Level Ecological Risk Assessment*.
- Support EPA during public meetings scheduled for the week of April 17, 2017.
- Other activities as directed by EPA.

3. SUBCONTRACTING:

- None.

4. POTENTIAL PROBLEMS AND PROPOSED SOLUTIONS:

- None.

5. CRITICAL ACTION ITEMS:

- None.

6. BUDGET HIGHLIGHTS:

- See burn chart and forecasted expenditures in Attachment 2.
- Detail for Remedial Action Contract program support allocation and other direct costs:

Name	Transaction Description	Amount
ALLOCATION, RAC	R2R8 APR PROG. SUPP. ALLOC.	\$494.05

7. TRAVEL:

- Gunnar Emilsson traveled to Columbia Falls to attend public and technical meetings April 17 through 19, 2017. These charges will appear on the May 2017 invoice.

8. DELIVERABLE SCHEDULE HIGHLIGHTS:


- See Attachment 1 for deliverable submittal schedule.

ATTACHMENT I
CDM Federal Programs
Deliverable Schedule Tracking
Columbia Falls Aluminum Plant
Work assignment: 359-RSBD-A882

Deliverable	Original Planned Completion Date	Current Planned Completion Date	Actual Completion Date	Explanation of Delay
Task 1 - Project Planning				
Work plan	2/17/2017	2/22/2017	2/28/2017	Change in project management
Comments to DSR and SLERA	4/6/2017	4/6/2017	4/6/2017	
Task 11 - Work Assignment Closeout				
Closeout report	9/27/2017	9/27/2017		

ATTACHMENT 2
CDM Federal Programs Corporation
RAC 8 Burn Rate and Projections Summary
Contract No. EP-W-05-049
Columbia Falls Aluminum Plant
Work Assignment 359-RSBD-A882


WA 359
Expenditures

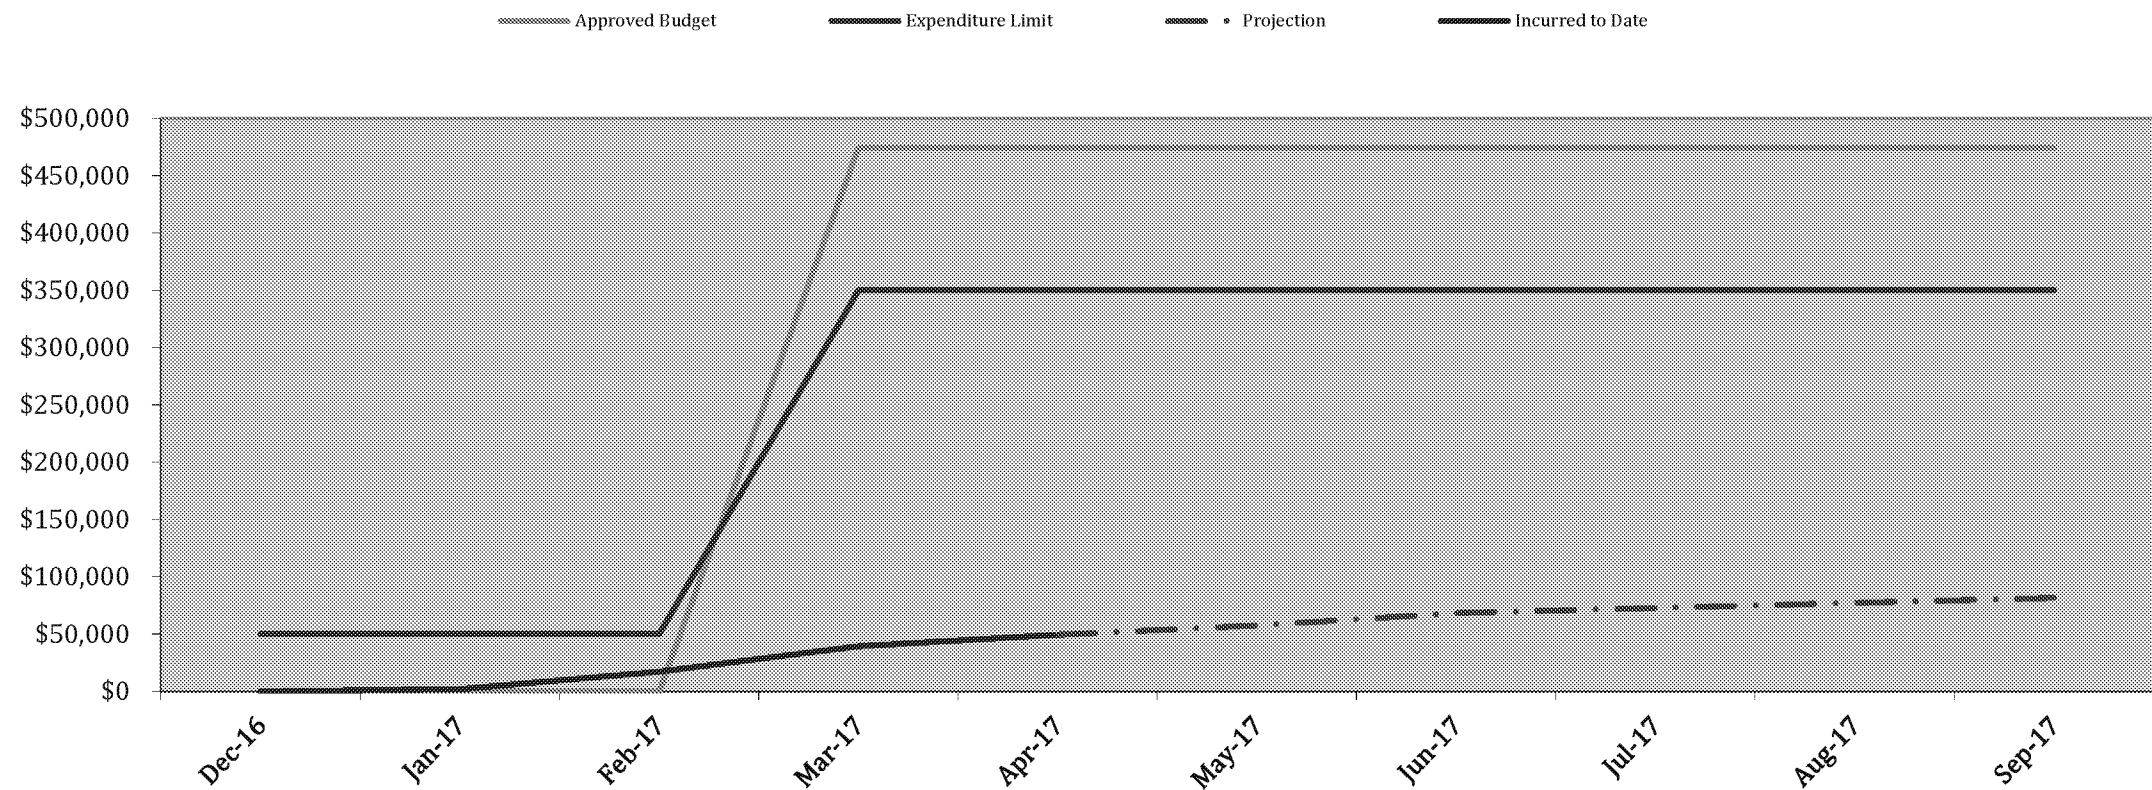

Expenditure Limit \$350,000
 Budget \$474,147

	2016	2017								
	December	January	February	March	April	May	June	July	August	September
Projections			\$6,600	\$26,400	\$11,000	\$8,000	\$11,000	\$4,400	\$4,400	\$4,400
Actual	\$50	\$1,848	\$15,309	\$22,150	\$10,047					
Cumulative	\$50	\$1,898	\$17,207	\$39,358	\$49,405	\$57,405	\$68,405	\$72,805	\$77,205	\$81,605
% Spent	0%	4%	34%	11%	14%	16%	20%	21%	22%	23%
Funding Balance	\$49,950	\$48,102	\$32,793	\$310,642	\$300,595	\$292,595	\$281,595	\$277,195	\$272,795	\$268,395

ATTACHMENT 2
CDM Federal Programs Corporation
RAC 8 Burn Rate and Projections Summary
Contract No. EP-W-05-049
Columbia Falls Aluminum Plant
Work Assignment 359-RSBD-A882

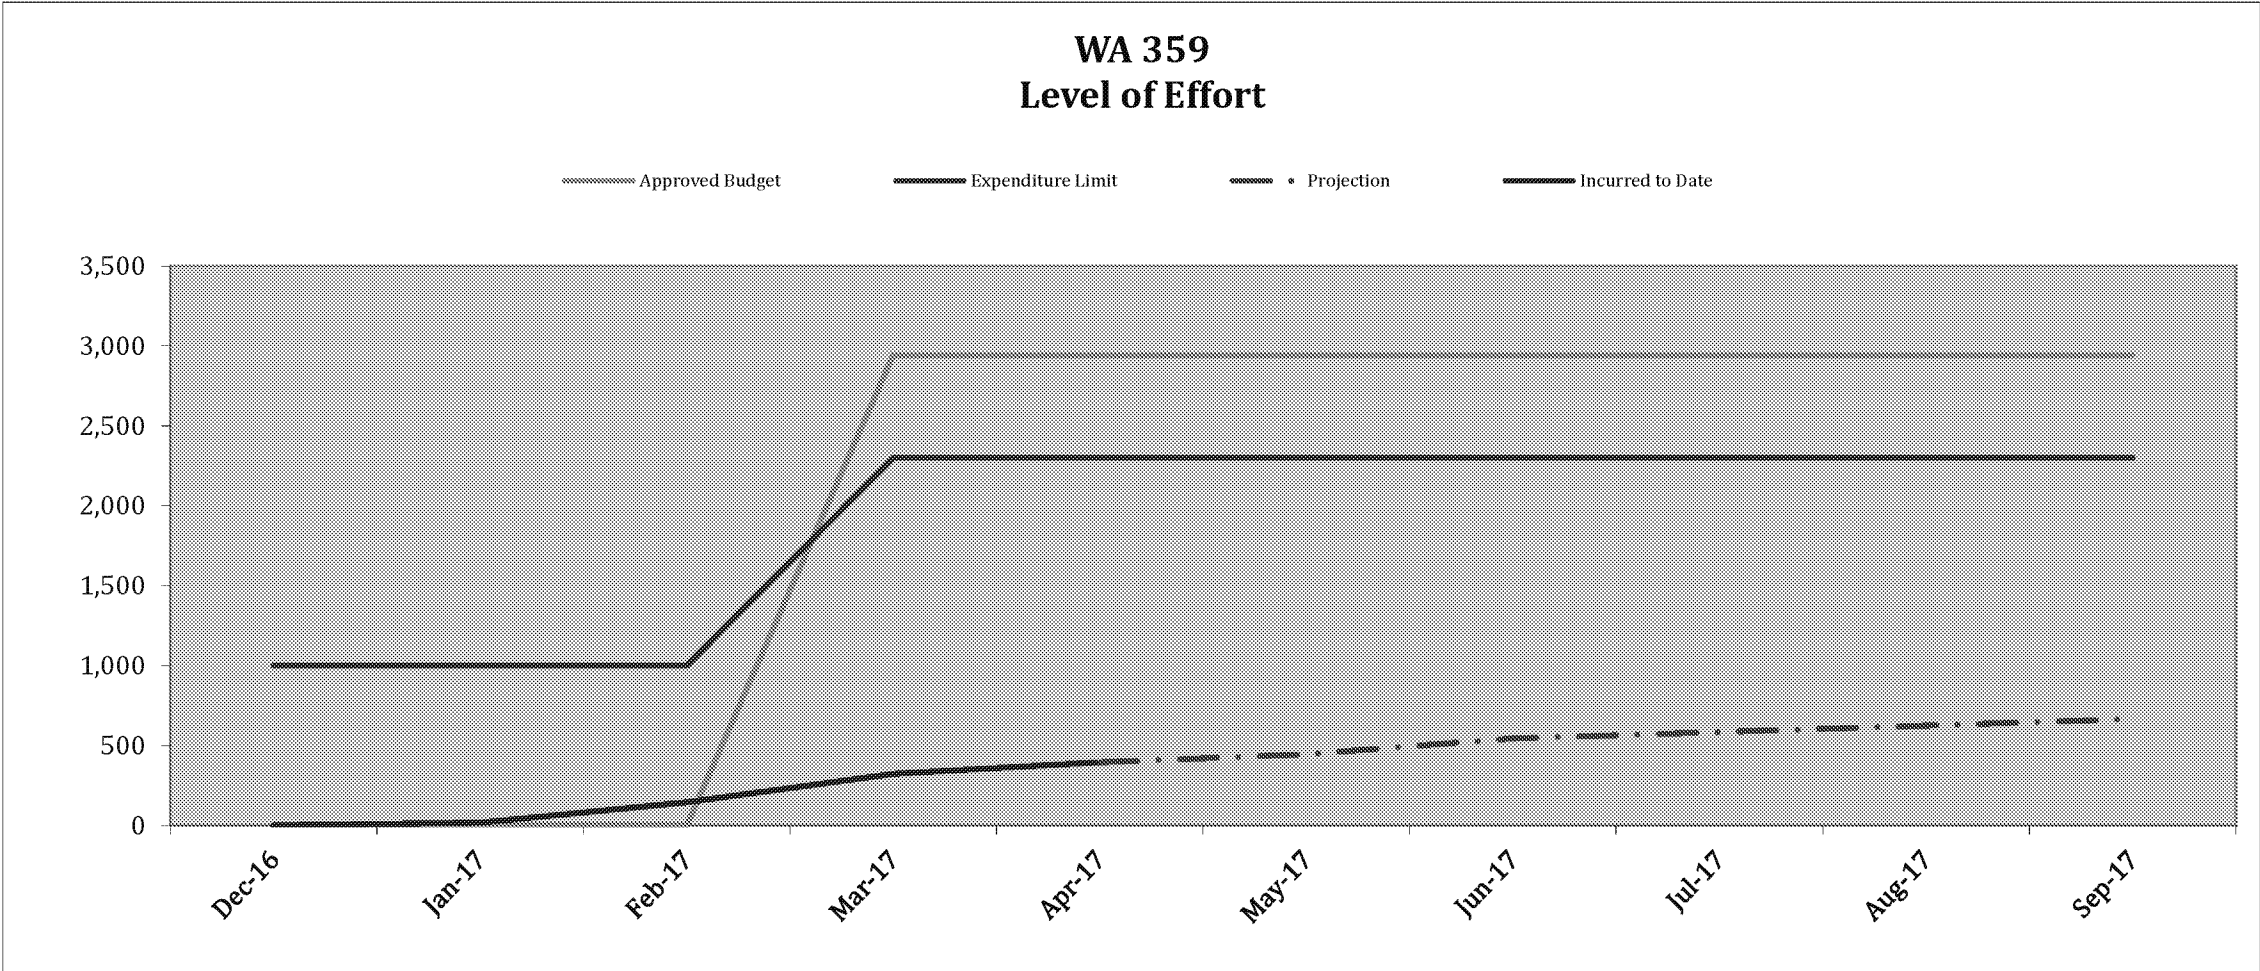

Expenditure Limit 2,300
Budget 2,943

	2016	2017								
	December	January	February	March	April	May	June	July	August	September
Projections			70	240	100	50	100	40	40	40
Actual	2	16	128	178	73					
Cumulative	2	18	146	323	396	446	546	586	626	666
% Spent	0%	2%	15%	14%	17%	19%	24%	25%	27%	29%
Funding Balance	999	983	855	1,977	1,904	1,854	1,754	1,714	1,674	1,634

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 1 Task Title: PROJECT PLANNING AND SUPPORT Task Category: PP

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-4**

Chapman, Kristine E (Kris	1.00		4.00			
Woodbury, Lynn	0.00		2.00			
Subtotal	1.00	\$67.04	6.00	\$392.62	82.00	\$5,823.00

P-3

Adamek, Scott H	0.00		2.00			
Alexander, Robert R	0.00		4.00			
Ekstrom, Karen L	0.00		18.00			
Emilsson, Gunnar R	30.00		49.00			
Formanek, Erin K	24.00		109.00			
Love, Catherine A	0.00		6.00			
Repine, Damon L	0.50		44.50			
Shanight, David T	0.00		5.00			
Zaczkowski, Talia N	1.00		9.50			
Zakowski, Cherie A	0.00		5.00			
Subtotal	55.50	\$2,855.29	252.00	\$12,263.84	865.00	\$45,922.00

P-2

Coan, Sean M	10.50		109.00			
Repine, Damon L	0.00		0.50			
Robadey, Sheila G	0.00		0.50			
Subtotal	10.50	\$438.06	110.00	\$4,528.61	475.00	\$19,247.00

P-1

Hamblock, Sarah	0.00		0.50			
Mordell, Traci L	0.00		1.00			
Ross, Natalie	0.00		0.50			
Subtotal	0.00	\$0.00	2.00	\$57.74	12.00	\$404.00

T-1

Rabanal, Christopher M	0.00		1.00			
Subtotal	0.00	\$0.00	1.00	\$15.26	16.00	\$366.00
Total, Professional	67.00	\$3,360.39	371.00	\$17,258.07	1450.00	\$71,762.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 1 Task Title: PROJECT PLANNING AND SUPPORT Task Category: PP

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****Prog Support Alloc**

PROGRAM SUPPORT ALLOCATIO	3.00		22.00			\$17,791.00
Subtotal	3.00	\$494.05	22.00	\$3,134.99	127.00	\$17,791.00

Clerical

Subtotal					14.00	\$371.00
Total Direct Labor	70.00	\$3,854.44	393.00	\$20,393.06	1,591.00	\$89,924.00

Direct Costs**ODCs**

Subtotal					0.00	\$1,233.00
----------	--	--	--	--	------	------------

Other ODCs

Travel					0.00	\$2,171.00
Subtotal					0.00	\$2,171.00
Total Direct Costs					0.00	\$3,404.00
Total LOE & Cost	70.00	\$3,854.44	393.00	\$20,393.06	1,591.00	\$93,328.00

Indirect Costs

Fringe		\$1,327.37		\$6,816.89		
G&A		\$1,320.63		\$6,595.95		

Overhead		\$2,528.77		\$11,968.54		
Subtotal	0.00	\$5,176.77	0.00	\$25,381.38	0.00	\$112,052.00

Fee

Fixed Fee		\$576.20		\$3,190.60	0.00	\$12,468.00
Subtotal	0.00	\$576.20	0.00	\$3,190.60	0.00	\$12,468.00

Total Direct + Indirect + Fixed Fee	70.00	\$9,607.41	393.00	\$48,965.04	1,591.00	\$217,848.00
(FED)						

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 1 Task Title: PROJECT PLANNING AND SUPPORT Task Category: PP

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Task Summary Information:**

Total, Direct Labor (Professional)	67.00	\$3,360.39	371.00	\$17,258.07	1,450.00	\$71,762.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	14.00	\$371.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$1,233.00
Travel		\$0.00		\$0.00		\$2,171.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$5,176.77		\$25,381.38		\$112,052.00
Total, Fixed Fee (Prime)		\$576.20		\$3,190.60		\$12,468.00
Program Support Allocation	3.00	\$494.05	22.00	\$3,134.99	127.00	\$17,791.00
Total, Task Costs	70.00	\$9,607.41	393.00	\$48,965.04	1,577.00	\$217,848.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 2 Task Title: COMMUNITY INVOLVEMENT Task Category: CR

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-3**

Emilsson, Gunnar R	3.00		3.00			
Subtotal	3.00	\$162.78	3.00	\$162.78	148.00	\$7,858.00

T-1

Subtotal					16.00	\$365.00
Total, Professional	3.00	\$162.78	3.00	\$162.78	164.00	\$8,223.00

Clerical

Subtotal					56.00	\$1,480.00
Total Direct Labor	3.00	\$162.78	3.00	\$162.78	220.00	\$9,703.00

Direct Costs**ODCs**

Subtotal					0.00	\$3,040.00
----------	--	--	--	--	------	------------

Other ODCs

Travel					0.00	\$892.00
Subtotal					0.00	\$892.00
Total Direct Costs					0.00	\$3,932.00
Total LOE & Cost	3.00	\$162.78	3.00	\$162.78	220.00	\$13,635.00

Indirect Costs

Fringe		\$64.30		\$64.30		
G&A		\$64.08		\$64.08		
Overhead		\$123.08		\$123.08		
Subtotal	0.00	\$251.46	0.00	\$251.46	0.00	\$15,709.00

Fee

Fixed Fee		\$25.80		\$25.80	0.00	\$1,410.00
-----------	--	---------	--	---------	------	------------

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 2 Task Title: COMMUNITY INVOLVEMENT Task Category: CR

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Fee						
Fixed Fee		\$25.80		\$25.80		\$1,410.00
Subtotal	0.00	\$25.80	0.00	\$25.80	0.00	\$1,410.00
Total Direct + Indirect + Fixed Fee						
(FED)	3.00	\$440.04	3.00	\$440.04	220.00	\$30,754.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 2 Task Title: COMMUNITY INVOLVEMENT Task Category: CR

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Task Summary Information:**

Total, Direct Labor (Professional)	3.00	\$162.78	3.00	\$162.78	164.00	\$8,223.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	56.00	\$1,480.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$3,040.00
Travel		\$0.00		\$0.00		\$892.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$251.46		\$251.46		\$15,709.00
Total, Fixed Fee (Prime)		\$25.80		\$25.80		\$1,410.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	3.00	\$440.04	3.00	\$440.04	164.00	\$30,754.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 3 Task Title: FIELD INVESTIGATION Task Category: FI

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-3**

Subtotal			53.00	\$2,813.00
----------	--	--	-------	------------

P-2

Subtotal			519.00	\$21,029.00
----------	--	--	--------	-------------

P-1

Subtotal			223.00	\$7,501.00
----------	--	--	--------	------------

Total, Professional			795.00	\$31,343.00
---------------------	--	--	--------	-------------

Clerical

Subtotal			36.00	\$952.00
----------	--	--	-------	----------

Total Direct Labor			831.00	\$32,295.00
--------------------	--	--	--------	-------------

Direct Costs**ODCs**

Subtotal			0.00	\$2,865.00
----------	--	--	------	------------

Other ODCs

Equipment			0.00	\$2,400.00
-----------	--	--	------	------------

Travel			0.00	\$14,118.00
--------	--	--	------	-------------

Subtotal			0.00	\$16,518.00
----------	--	--	------	-------------

Total Direct Costs			0.00	\$19,383.00
--------------------	--	--	------	-------------

Total LOE & Cost			831.00	\$51,678.00
------------------	--	--	--------	-------------

Indirect Costs

Subtotal			0.00	\$53,441.00
----------	--	--	------	-------------

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 3 Task Title: FIELD INVESTIGATION Task Category: FI

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Fee			
Fixed Fee		0.00	\$6,836.00
Subtotal		0.00	\$6,836.00
Total Direct + Indirect + Fixed Fee		831.00	\$111,955.00
(FED)			

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 3 Task Title: FIELD INVESTIGATION Task Category: FI

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Task Summary Information:**

Total, Direct Labor (Professional)	0.00	\$0.00	0.00	\$0.00	795.00	\$31,343.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	36.00	\$952.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$2,865.00
Travel		\$0.00		\$0.00		\$14,118.00
Equipment		\$0.00		\$0.00		\$2,400.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$0.00		\$0.00		\$53,441.00
Total, Fixed Fee (Prime)		\$0.00		\$0.00		\$6,836.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	0.00	\$0.00	0.00	\$0.00	795.00	\$111,955.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 4 Task Title: SAMPLE ANALYSIS Task Category: SN

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Direct Costs

Other ODCs

Subpool			0.00	\$55,426.00
Subtotal			0.00	\$55,426.00
Total Direct Costs			0.00	\$55,426.00
Total LOE & Cost			0.00	\$55,426.00

Indirect Costs

Subtotal			0.00	\$2,820.00
Fee				
Fixed Fee			0.00	\$2,743.00
Subtotal			0.00	\$2,743.00

Total Direct + Indirect + Fixed Fee			0.00	\$60,989.00
(FED)				

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 4 Task Title: SAMPLE ANALYSIS Task Category: SN

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Task Summary Information:

Total, Direct Labor (Professional)	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$0.00
Travel		\$0.00		\$0.00		\$0.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$55,426.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$0.00		\$0.00		\$2,820.00
Total, Fixed Fee (Prime)		\$0.00		\$0.00		\$2,743.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	0.00	\$0.00	0.00	\$0.00	0.00	\$60,989.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 5 Task Title: ANALYTICAL SUPPORT AND DATA VALIDATION Task Category: AN

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-4**

Subtotal			2.00	\$142.00
----------	--	--	------	----------

P-3

Subtotal			58.00	\$3,079.00
----------	--	--	-------	------------

P-2

Subtotal			114.00	\$4,619.00
----------	--	--	--------	------------

P-1

Subtotal			14.00	\$471.00
----------	--	--	-------	----------

Total, Professional			188.00	\$8,311.00
---------------------	--	--	--------	------------

Clerical

Subtotal			12.00	\$318.00
----------	--	--	-------	----------

Total Direct Labor			200.00	\$8,629.00
--------------------	--	--	--------	------------

Direct Costs**ODCs**

Subtotal			0.00	\$160.00
----------	--	--	------	----------

Total Direct Costs			0.00	\$160.00
--------------------	--	--	------	----------

Total LOE & Cost			200.00	\$8,789.00
------------------	--	--	--------	------------

Indirect Costs

Subtotal			0.00	\$13,358.00
----------	--	--	------	-------------

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 5 Task Title: ANALYTICAL SUPPORT AND DATA VALIDATION Task Category: AN

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Fee			
Fixed Fee		0.00	\$1,617.00
Subtotal		0.00	\$1,617.00
Total Direct + Indirect + Fixed Fee		200.00	\$23,764.00
(FED)			

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 5 Task Title: ANALYTICAL SUPPORT AND DATA VALIDATION Task Category: AN

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Task Summary Information:

Total, Direct Labor (Professional)	0.00	\$0.00	0.00	\$0.00	188.00	\$8,311.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	12.00	\$318.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$160.00
Travel		\$0.00		\$0.00		\$0.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$0.00		\$0.00		\$13,358.00
Total, Fixed Fee (Prime)		\$0.00		\$0.00		\$1,617.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	0.00	\$0.00	0.00	\$0.00	188.00	\$23,764.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 6 Task Title: DATA EVALUATION Task Category: DE

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-4**

Subtotal			12.00	\$852.00
----------	--	--	-------	----------

P-3

Subtotal			78.00	\$4,141.00
----------	--	--	-------	------------

P-2

Subtotal			90.00	\$3,646.00
----------	--	--	-------	------------

P-1

Subtotal			19.00	\$639.00
----------	--	--	-------	----------

Total, Professional			199.00	\$9,278.00
---------------------	--	--	--------	------------

Clerical

Subtotal			5.00	\$132.00
----------	--	--	------	----------

Total Direct Labor			204.00	\$9,410.00
--------------------	--	--	--------	------------

Direct Costs**ODCs**

Subtotal			0.00	\$170.00
----------	--	--	------	----------

Total Direct Costs			0.00	\$170.00
--------------------	--	--	------	----------

Total LOE & Cost			204.00	\$9,580.00
------------------	--	--	--------	------------

Indirect Costs

Subtotal			0.00	\$14,570.00
----------	--	--	------	-------------

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 6 Task Title: DATA EVALUATION Task Category: DE

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Fee			
Fixed Fee		0.00	\$1,711.00
Subtotal		0.00	\$1,711.00
Total Direct + Indirect + Fixed Fee		204.00	\$25,861.00
(FED)			

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 6 Task Title: DATA EVALUATION Task Category: DE

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Task Summary Information:**

Total, Direct Labor (Professional)	0.00	\$0.00	0.00	\$0.00	199.00	\$9,278.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	5.00	\$132.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$170.00
Travel		\$0.00		\$0.00		\$0.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$0.00		\$0.00		\$14,570.00
Total, Fixed Fee (Prime)		\$0.00		\$0.00		\$1,711.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	0.00	\$0.00	0.00	\$0.00	199.00	\$25,861.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 15 Task Title: WORK ASSIGNMENT CLOSEOUT Task Category: CO

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)**Direct Labor****P-4**

Subtotal			6.00	\$426.00
----------	--	--	------	----------

P-3

Subtotal			8.00	\$425.00
----------	--	--	------	----------

P-2

Subtotal			6.00	\$243.00
----------	--	--	------	----------

Total, Professional			20.00	\$1,094.00
---------------------	--	--	-------	------------

Total Direct Labor			20.00	\$1,094.00
--------------------	--	--	-------	------------

Direct Costs**ODCs**

Subtotal			0.00	\$17.00
----------	--	--	------	---------

Total Direct Costs			0.00	\$17.00
--------------------	--	--	------	---------

Total LOE & Cost			20.00	\$1,111.00
------------------	--	--	-------	------------

Indirect Costs

Subtotal			0.00	\$1,693.00
----------	--	--	------	------------

Fee

Fixed Fee			0.00	\$172.00
-----------	--	--	------	----------

Subtotal			0.00	\$172.00
----------	--	--	------	----------

Total Direct + Indirect + Fixed Fee			20.00	\$2,976.00
--	--	--	--------------	-------------------

(FED)

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-O	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Task Number: 15 Task Title: WORK ASSIGNMENT CLOSEOUT Task Category: CO

	Current		Cumulative		Approved Budget	
Name	LOE	Dollars	LOE	Dollars	LOE	Dollars

Prime Contractor - CDM FEDERAL PROGRAMS CORP (FED)

Task Summary Information:

Total, Direct Labor (Professional)	0.00	\$0.00	0.00	\$0.00	20.00	\$1,094.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$17.00
Travel		\$0.00		\$0.00		\$0.00
Equipment		\$0.00		\$0.00		\$0.00
Subpool		\$0.00		\$0.00		\$0.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$0.00		\$0.00		\$1,693.00
Total, Fixed Fee (Prime)		\$0.00		\$0.00		\$172.00
Program Support Allocation	0.00	\$0.00	0.00	\$0.00	0.00	\$0.00
Total, Task Costs	0.00	\$0.00	0.00	\$0.00	20.00	\$2,976.00

Report 1: Work Assignment - Task Level Specific Detail Report

Contractor Name:	CDM Federal Programs Corporation	Work Area Code:	RS	Contract Period:	Option
Contract No.:	EP-W-05-049-C	Action Code:	BD	WA POP Start:	12/20/16
Work Assignment Number:	359-RSBD-A882	WA Form:	T	WA POP End:	09/27/17
Work Assignment Title:	Columbia Falls Aluminum P	Type Funding:	WA	Invoice Date:	04/29/17
SSID:	82	Work Assign Status:	Ongoing	Invoice No.:	B09100
State:	MT			Purpose:	Monthly Invoice
Region:	A8				

Cost Element	Current		Cumulative		Approved Budget	
	LOE	Dollars	LOE	Dollars	LOE	Dollars
Total, Direct Labor (Professional)	70.00	\$3,523.17	374.00	\$17,420.85	2,816.00	\$130,011.00
Total, Direct Labor (Clerical)	0.00	\$0.00	0.00	\$0.00	123.00	\$3,253.00
Total, Direct Costs						
Other Direct Costs		\$0.00		\$0.00		\$7,485.00
Travel		\$0.00		\$0.00		\$17,181.00
Equipment		\$0.00		\$0.00		\$2,400.00
Subpool		\$0.00		\$0.00		\$55,426.00
Insurance		\$0.00		\$0.00		\$0.00
Total, Indirect Costs (Fringe, O/H, G&A)		\$5,428.23		\$25,632.84		\$213,643.00
Total, Fixed Fee (Prime)		\$602.00		\$3,216.40		\$26,957.00
Program Support Allocation	3.00	\$494.05	22.00	\$3,134.99	127.00	\$17,791.00
Total, LOE, Work Assignment Costs	73.00	\$10,047.45	396.00	\$49,405.08	2,943.00	\$474,147.00
Average Hourly Rate		\$50.33		\$46.58		
Expenditure Limit LOE			2,300.00			
Expenditure Limit Dollars				\$350,000.00		
