

Lower Passaic River Restoration Project RIFS – PRP Oversight – 17 Mile: April 2018

IA #	942125	IA Exp	Mar 20	P2#	147757	EPA ID	NJD980528996	Funding Req'd	25 May 2018
RPM	Diane Salkie		PM	Beth Franklin		Contractor		CDM Smith	

PROJECT/INFORMATION:

Location: Newark, NJ

Address: Site is 17 river miles; see PM

Primary Contaminant: dioxin (plus others)

Scope: Oversight of the Responsible Parties (who refer to themselves as the Cooperating Parties Group - CPG) as they implement a study of the 17-miles of the Lower Passaic River from the Dundee Dam to Newark Bay. Sediments contaminated with hazardous substances exist along the entire 17-mile tidal stretch of the LPR,

CONTRACT DATA: CDM Federal Programs

Contract	W912DQ-15-D-3013/0007	Type	CPFF
Initial Award	Nov 30, 2016	POP Exp:	Dec 28, 2018

Special Account Funding

	Inhouse	Contract	Total	Date Req'd
IA Amt**	1,120,000	14,940,000	16,060,000	
IA Avail	~65,000	~1,321,000	~1,386,000	
FY 18	80,000	950,000	1,030,000	25 May 18
FY 19; Q1	70,000	750,000	825,000	Nov 2018
EAC	TBD	TBD	TBD	


SCHEDULE/MILESTONES

- 29 June 2018; FY 18 Mod award projected. Funds expected to cover work ~July-December 2018, depending on CPG level of activity. Mod process currently on schedule.
- Dec 2018; FY 19 Mod required to extend POP/add funds. **Planning figure** at this time.
- If new Task Order is required;** process will start in June/July for AE selection and base task order contracting efforts.
- 30 Apr 18; LBG Contract Mod planned for award. Mod supports coordination of LPR 8 mile team with LPR 17 mile team.
- Interim Remedy (IR) plan being discussed with the CPG; schedule dates are proposed by CPG but have not been finalized at this time. NOTE: new dates are being discussed with CPG; anticipate updated schedule next reporting period.
 - Winter - Complete 17-mile RI
 - Winter - Complete BERA
 - 28 Feb/1 Mar 2018 - CSTAG (complete)
 - 2018 - Draft and Finalize Upper 9-mile FS
 - 2020 - Proposed Plan/ROD 1/AOC

EPA Target Milestones:

- Working with CPG to finalize milestones with consideration of the Interim Action.

NOTE: Update provided prior to end of April as PM is out of office in early May.

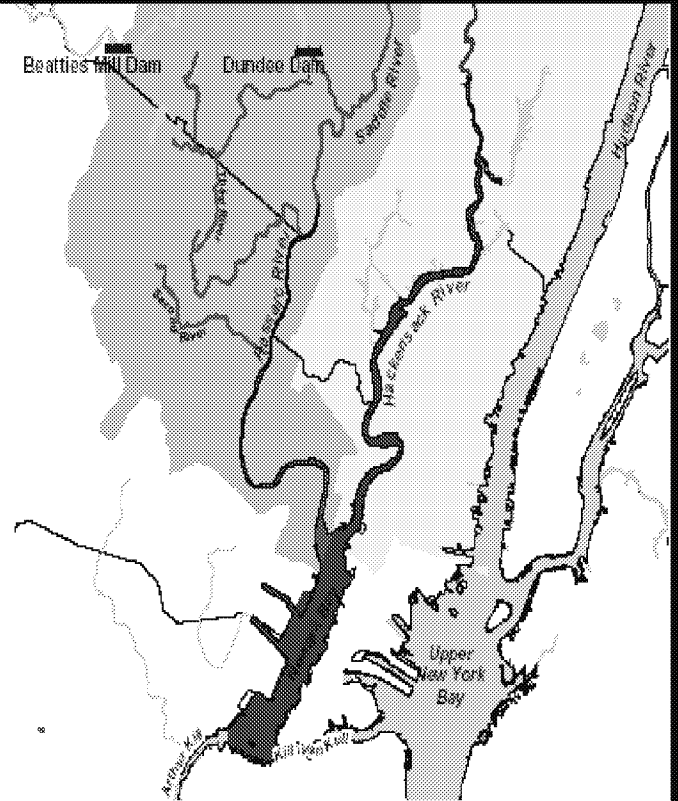

CURRENT STATUS & UPCOMING ACTIVITIES

- Interim Action planning continues.
- Expedited schedule discussions in progress.
- RI/Risk Assessment documents being revised and finalized.
- Models are in progress and CPG is providing regular updates of progress.
- Anticipate FS completion in 2018/early 2019.

ISSUES/CHALLENGES

Funding:

- None

Schedule:

- None.

Technical:

- Discussed with CPG as appropriate.

PROJECT DELIVERY TEAM

COR	Matt Dolly
Specialist	Gary Rizzolo
KO	Michael Dolly
Budget	Shelly Allen
