

Lower Passaic River Restoration Project RIFS – PRP Oversight – 17 Mile: March 2018

IA #	942125	IA Exp	Mar 20	P2#	147757	EPA ID	NJD980528996	Funding Req'd	25 May 2018
RPM	Diane Salkie	PM	Beth Franklin	Contractor	CDM Smith				

PROJECT/INFORMATION:

Location: Newark, NJ

Address: Site is 17 river miles; see PM

Primary Contaminant: dioxin (plus others)

Scope: Oversight of the Responsible Parties (who refer to themselves as the Cooperating Parties Group - CPG) as they implement a study of the 17-miles of the Lower Passaic River from the Dundee Dam to Newark Bay. Sediments contaminated with hazardous substances exist along the entire 17-mile tidal stretch of the LPR,

CONTRACT DATA: CDM Federal Programs

Contract	W912DQ-15-D-3013/0007	Type	CPFF
Initial Award	Nov 30, 2016	POP Exp:	Dec 28, 2018

Special Account Funding

	Inhouse	Contract	Total	Date Req'd
IA Amt**	1,120,000	14,940,000	16,060,000	
IA Avail	~93,000	~1,653,000	~1,746,000	
FY 18	70,000	900,000	970,000	25 May 18
EAC	TBD	TBD	TBD	

FY 18 request is earlier than last update based on higher monthly burn rate. Interim action efforts and CSTAG have required substantial consultant efforts.

SCHEDULE/MILESTONES


- CDM Contract Mod being initiated. Anticipate June 2018 award.
- LBG Contract Mod underway; supports Kern, Battelle and sample storage using IA 2125 (funds in KC for this effort; no funds needed). Award planned in April.
- Interim Remedy (IR) plan being discussed with the CPG; schedule dates are proposed by CPG but most have not been finalized at this time:
 - Winter - Complete 17-mile RI
 - Winter – Complete BERA
 - 28 Feb/1 Mar 2018 – CSTAG (complete)
 - 2018 – Draft and Finalize Upper 9-mile FS
 - 2020 – Proposed Plan/ROD 1/AOC

EPA Target Milestones:

- Working with CPG to finalize milestones with consideration of the Interim Action.

PROJECT DELIVERY TEAM

COR	Matt Dolly
Specialist	Gary Rizzolo
KO	Michael Dolly
Budget	Shelly Allen

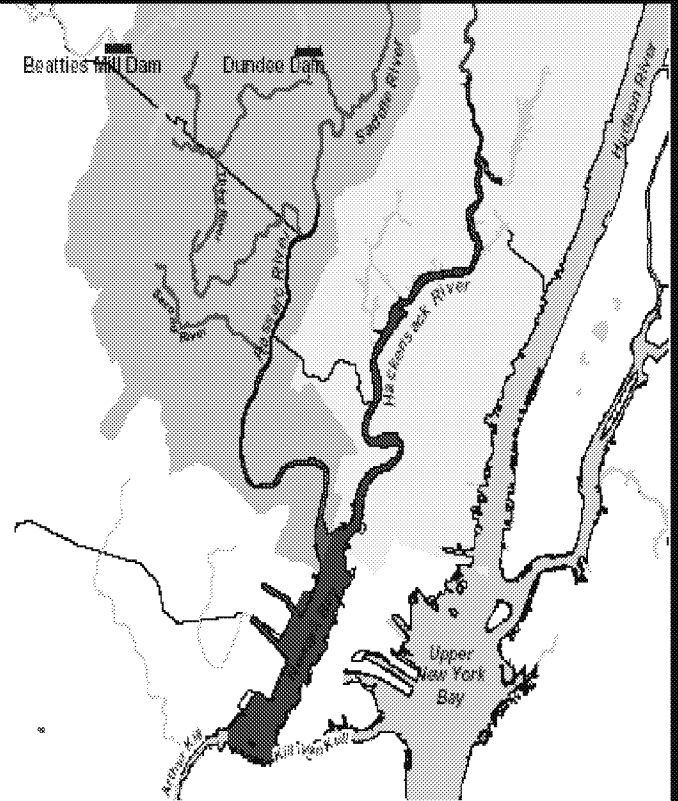

CURRENT STATUS & UPCOMING ACTIVITIES

- Interim Action planning continues.
- CSTAG Complete.
- Expedited schedule discussions in progress.
- RI/Risk Assessment documents being revised and finalized.
- Models are in progress and CPG is providing regular updates of progress.
- Anticipate FS completion in 2018.

ISSUES/CHALLENGES

Funding:

- None

Schedule:

- None.

Technical:

- Discussed with CPG as appropriate.
