

February 10, 2020

Project 8619192590

Ms. Bianca Handley U.S. Environmental Protection Agency 75 Hawthorne Street San Francisco, California 94105 Wood Environment & Infrastructure Solutions, Inc. 180 Grand Avenue, Suite 1100 Oakland, California 94612-3066 USA

> T: (510) 663-4100 F: (510) 663-4141

www.woodplc.com

**Subject:** January 2020 Monthly Progress Report (electronic submittal)

North Hollywood Operable Unit

Second Interim Remedy

Groundwater Remediation Design

Dear Ms. Handley:

On behalf of Honeywell International Inc., attached is the January 2020 monthly progress report for North Hollywood Operable Unit (NHOU) Second Interim Remedy (2IR) treatment activities, pursuant to the October 2017 Unilateral Administrative Order for Remedial Action (U.S. EPA Region IX CERCLA Docket No. 2017-06; UAO) that became effective on February 1, 2018, and the First Amendment to the UAO (CERCLA Docket No. 2019-12) dated July 8, 2019.

Please contact either of the undersigned at (510) 663-4100 if you have questions regarding this submittal.

Sincerely,

Wood Environment & Infrastructure Solutions, Inc.

Mari Gilmore, PG CA 8492

Project Manager

Michael Taraszki, PG CA 6457, CHG CA 586, PMP

**Project Principal** 

willed

MG/MT/MR

Attachment: January 2020 Monthly Progress Report

Monthly Progress Schedule

cc: Mr. Benny Dehghi (Honeywell)

Mr. Vahe Dabbaghian (LADWP)

Ms. Nicole Alkov and Ms. Christina Humphreys (RWQCB-LA)

Mr. Chi Diep (SWRCB DDW)

Mr. John Wingate (OTIE)

Mr. Kevin Murdock (Jacobs)

Ms. Bianca Handley Monthly Progress Report – NHOU Second Interim Remedy February 10, 2020 Page 2

# **January 2020 NHOU Monthly Progress Report**

## **ACTIVITIES COMPLETED FOR THE REPORT PERIOD**

- Honeywell/Wood continued with modifications to the Phase 1B groundwater treatment system design for the "For Construction" drawing set based on comments received from U.S. EPA and Los Angeles Department of Water and Power (LADWP);
- Honeywell/Wood continued with procurement activities for major equipment for the Phase 1B groundwater treatment system;
- Honeywell received the NPDES permit that will facilitate the Phase 1B operations;
- Honeywell/Wood requested an extension on January 30 to submit the Transportation and Off-site Disposal Plan and Construction Quality Assurance/Quality Control Plan by end of February;
- Honeywell/Wood completed final activities associated with the Phase 2 groundwater extraction well installations (i.e., surveying, bollard install, final site cleanup, and waste transport and disposal); LADWP observed the construction activities regularly;
- Honeywell/Wood initiated plan check activities at the Los Angeles Department of Building and Safety (LADBS) and Bureau of Engineering (LABOE) to support Phase 1B construction; and,
- Honeywell/Wood completed survey activities to support Phase 2 conveyance design.

## **ISSUES AND CORRECTIVE ACTIONS**

None.

#### ANTICIPATED ACTIVITIES FOR THE NEXT SIX WEEKS

- Honeywell/Wood actions:
  - Continue with the Phase 1B groundwater treatment system procurement, plan check and permitting processes;
  - Continue supporting LADWP with the DDW 97-005 process;
  - Submit the following additional deliverables before Phase 1B construction begins (by end of February):
    - Transportation and Off-Site Disposal Plan; and,
    - Construction Quality Assurance/Quality Control Plan.

ED 013425 00000048-00002

## **January 2020 NHOU Monthly Progress Report (continued)**

## ANTICIPATED ACTIVITIES FOR THE NEXT SIX WEEKS (CONTINUED)

- LADWP actions (anticipated):
  - Continue development and submittal of documents associated with the DDW 97-005 process.
- U.S. EPA actions (anticipated):
  - Review of the Final Revised RAWP Revision 1 submitted by Honeywell/Wood on December 20.

## ANTICIPATED ACTIVITIES FOR THE NEXT SIX MONTHS

- Honeywell/Wood actions:
  - Continue to support LADWP with the DDW 97-005 process, including meeting with DDW;
  - Submit a well installation report for the Phase 2 groundwater extraction wells;
  - Host a Pre-Construction Conference with U.S. EPA before beginning construction of the Phase 1B Groundwater Treatment System; and,
  - Initiate construction of the Phase 1B Groundwater Treatment System.
- LADWP actions (anticipated):
  - Continue development and submittal of documents associated with the DDW 97-005 process, including meeting with DDW;
  - Participate in a Pre-Construction Conference with Honeywell/Wood for the Phase 1B
    Groundwater Treatment System and subsequent construction meetings, as required.
- U.S. EPA actions (anticipated):
  - Review and approve (as needed) the additional Honeywell/Wood deliverables noted above; and
  - Participate in a Pre-Construction Conference with Honeywell/Wood for the Phase 1B
    Groundwater Treatment System and subsequent construction meetings, as required.

## UNRESOLVED ISSUES/POTENTIAL IMPACTS TO SCHEDULE/WORK PLAN


• Construction schedule has been revised to reflect an update to the anticipated start of construction (attached).

## **DESIGN CHANGES OF NOTE**

None.

# APPENDIX A PROPOSED PHASE 1B CONSTRUCTION SCHEDULE

North Hollywood Operable Unit Second Interim Remedy

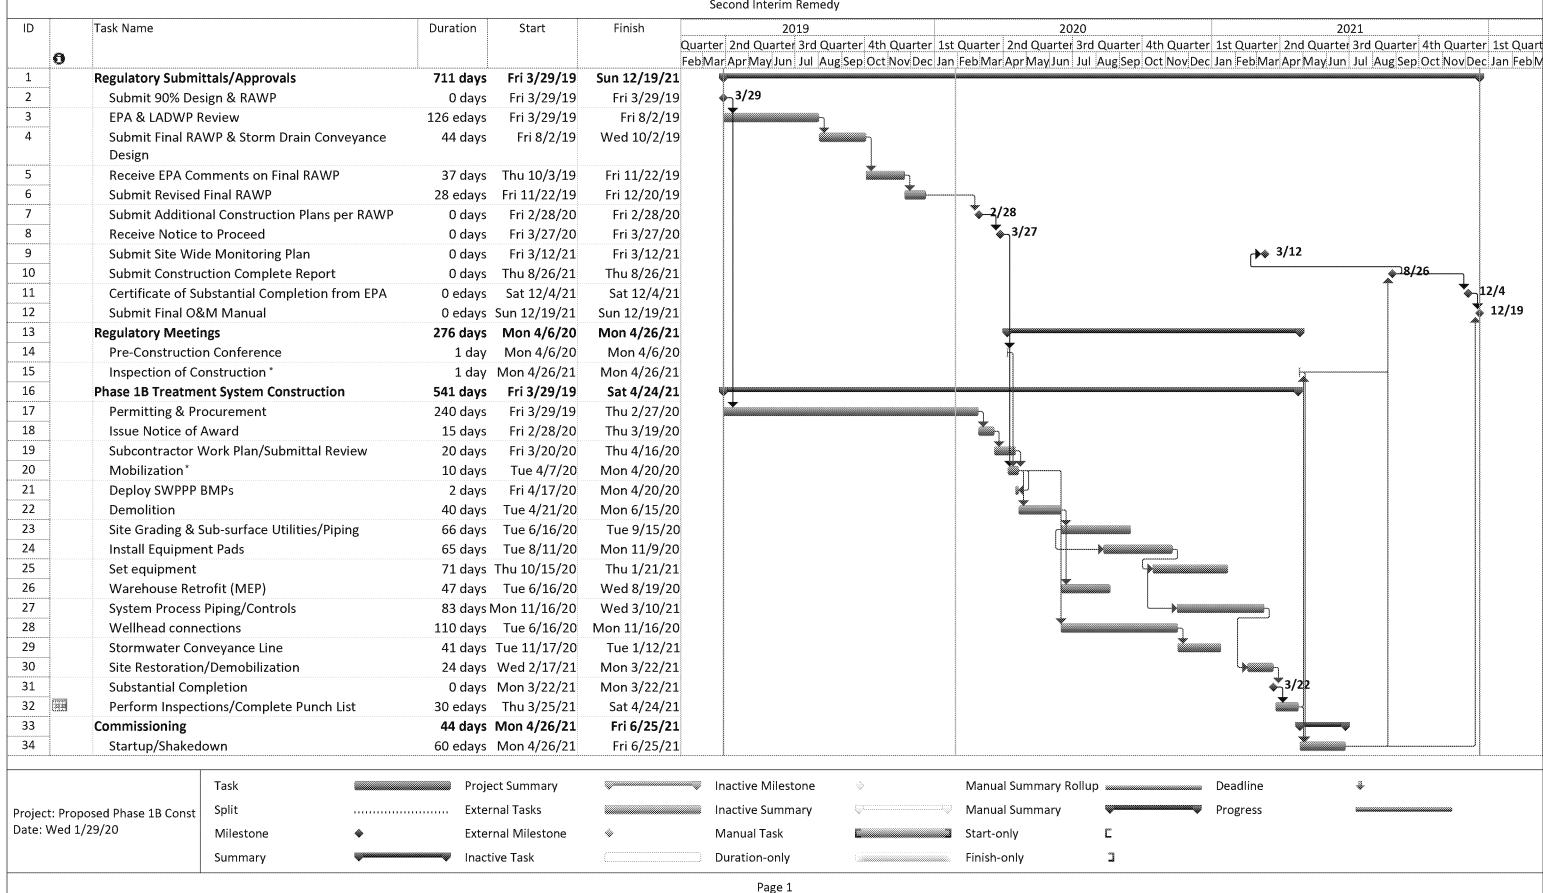

<sup>\*</sup> Note construction mobilization date is contingent on the procurement process being finalized as anticipated.
