Date: Wednesday, December 03, 2019

#### **Personnel On-Site:**

EPA OSC - Peter Lisichenko

START V – Sean Quinn, & Thomas O'Donnell

ERRS Contractor: Guardian Environmental Services (GES)

Weather: Scattered flurries, 20% rain, Lo: 29°F, High: 37°F, Winds: 10 to 20 mph, due W, 82% humidity.

**Health and Safety:** Safety topics included: being aware of slips, trips, and falls, site traffic and heavy equipment awareness, cold stress, using proper personal protective equipment (PPE), high winds, and radiation hazards.

#### **Activities Completed:**

- 1. ERRS continued loading trucks with waste material for offsite disposal.
- 2. ERRS continued to move items from GNBC warehouse 2 to warehouse 3 and into ST-04.
- 3. ERRS began breaking up the concrete floor in warehouse 2.
- 4. START V conducted calibration check of the Ludlum 2241-2
- 5. START V scanned trucks to ensure they were within the predetermined permissible limits.
- 6. At the end of the work day, START V uploaded field data to the EPA internet SharePoint site designated for the Site.

#### Planned Activities for December 05, 2019:

- 1. ERRS continued to move items from GNBC warehouse 2 to warehouse 3 and into ST-04.
- 2. ERRS will continue breaking up the concrete floor in warehouse 2 and begin removing concrete from the area.
- 3. START V will continue to troubleshoot HPGe with the EPA health physicist.
- 4. START V will continue scanning trucks to ensure they are within the predetermined permissible limits.

Page 1 of 4 12/04/2019

#### **Soil Excavation & Backfill Data:**

Soil Volume Excavated Today (In Cubic Yards)	0
Cumulative Soil Volume Excavated (In Cubic Yards) <sup>1</sup>	3,492.5
Total Number of Disposal Trucks Today	25
Total Number of Disposal Trucks to Date	171
Soil Volume Transferred to Disposal Trucks	575
Cumulative Disposal Volume Removed To Date (In Tons)	3,910
Number of Backfill Trucks Today	0
Number of Backfill Trucks to Date	243
Backfill Received Today (In Tons)	604.71
Cumulative Backfill Volume to Date (In Tons)	8737.72


<sup>&</sup>lt;sup>1</sup> Corrected value based on ERRS reported totals for each area.

Page 2 of 4 12/04/2019

# **Site Photographs**



View of items being staged in ST-04 of GNBC by ERRS.

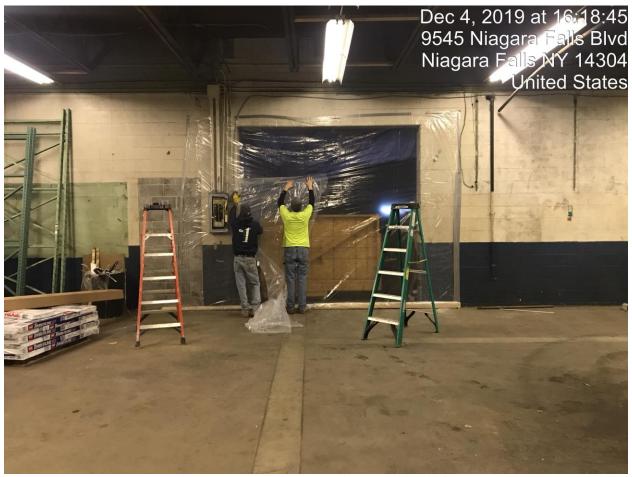

View of ERRS preparing warehouse 2 in GNBC for the removal of concrete.
