

**Niagara Falls Boulevard  
Niagara County, New York  
2019 Removal Action Daily Report**

**Date:** Tuesday, December 10, 2019

**Personnel On-Site:**

EPA OSC – Peter Lisichenko

START V – Sean Quinn, & Thomas O'Donnell

ERRS Contractor: Guardian Environmental Services (GES)

**Weather:** Rain, 80% chance of rain, Lo: 37°F, High: 47°F, Winds: 15 to 25 mph, due S, 65% humidity.

**Health and Safety:** Safety topics included: being aware of slips, trips, and falls, site traffic and heavy equipment awareness, cold stress, using proper personal protective equipment (PPE), high winds, and radiation hazards.

**Activities Completed:**

1. ERRS completed backfilling the first half WH-2.
2. ERRS completed removal of concrete from WH-2.
3. START V began to process samples in the HGPe.
4. START V continued air monitoring in warehouse 2 with a RadeCo, AreaRae and Dataram.
5. START V conducted calibration check of the Ludlum 2241-2
6. At the end of the work day, START V uploaded field data to the EPA internet SharePoint site designated for the Site.

**Planned Activities for December 11, 2019:**

1. ERRS will begin removal of soil WH-2 staging it on the south west side of the soil pile.
2. START V will conduct waste classification sampling from two test pits in WH-2.
3. START V will continue to process samples in HPGe.
4. Air monitoring will continue in work areas.

**Niagara Falls Boulevard  
Niagara County, New York  
2019 Removal Action Daily Report**

**Soil Excavation & Backfill Data:**

Soil Volume Excavated Today (In Cubic Yards)	<b>0</b>
Cumulative Soil Volume Excavated (In Cubic Yards) <sup>1</sup>	<b>3,492.5</b>
Total Number of Disposal Trucks Today	<b>25</b>
Total Number of Disposal Trucks to Date	<b>171</b>
Soil Volume Transferred to Disposal Trucks	<b>575</b>
Cumulative Disposal Volume Removed To Date ( In Tons)	<b>3,910</b>
Number of Backfill Trucks Today	<b>0</b>
Number of Backfill Trucks to Date	<b>243</b>
Backfill Received Today (In Tons)	<b>604.71</b>
Cumulative Backfill Volume to Date (In Tons)	<b>8737.72</b>

<sup>1</sup> Corrected value based on ERRS reported totals for each area.


**Niagara Falls Boulevard  
Niagara County, New York  
2019 Removal Action Daily Report**

**Site Photographs**



View of ERRS placing backfill in WH-2.

**Niagara Falls Boulevard  
Niagara County, New York  
2019 Removal Action Daily Report**

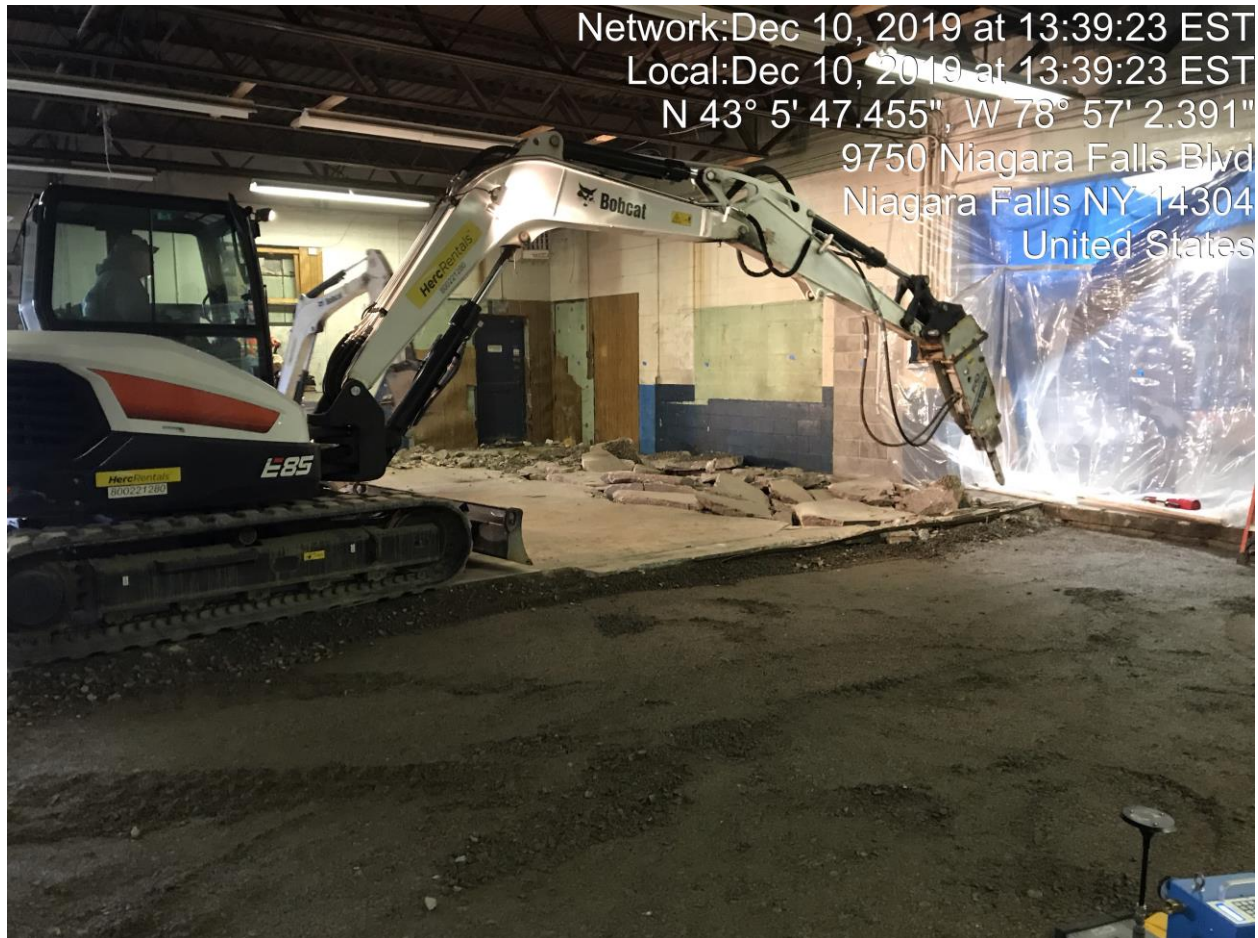

View of ERRS removing concrete in the second half of WH-2.
