

**Niagara Falls Boulevard  
Niagara County, New York  
2020 Removal Action Daily Report**

**Date:** Monday, January 06, 2020

**Personnel On-Site:**

EPA OSC – Peter Lisichenko

START V – Sean Quinn, & Patrick Ahern

ERRS Contractor: Guardian Environmental Services (GES)

**Weather:** Snow showers, 30% chance of snow, Lo: 26°F, High: 35°F, Winds: 5 to 10 mph, due NW, 83% humidity.

**Health and Safety:** Safety topics included: being aware of slips, trips, and falls, site traffic and heavy equipment awareness, cold stress, using proper personal protective equipment (PPE), high winds, and radiation hazards.

**Activities Completed:**

1. ERRS completed removing concrete from WH3.
2. ERRS began excavating soil in WH3.
3. START V began to scan excavations in WH3.
4. START V continued to process samples in HPGe.
5. At the end of the work day, START V uploaded field data to the EPA internet SharePoint site designated for the Site.

**Planned Activities for January 7, 2020:**

1. START V will continue to process samples in HPGe.
2. ERRS will continue soil removal in WH3.
3. START V will collect waste characterization samples from two test pits in WH3.
4. START V will conduct air monitoring in work zones.

**Niagara Falls Boulevard  
Niagara County, New York  
2020 Removal Action Daily Report**


**Soil Excavation & Backfill Data:**

Soil Volume Excavated Today (In Cubic Yards)	<b>0</b>
Cumulative Soil Volume Excavated (In Cubic Yards) <sup>1</sup>	<b>3,492.5</b>
Total Number of Disposal Trucks Today	<b>21</b>
Total Number of Disposal Trucks to Date	<b>314</b>
Soil Volume Transferred to Disposal Trucks	<b>483</b>
Cumulative Disposal Volume Removed To Date ( In Tons)	<b>7,199</b>
Number of Backfill Trucks Today	<b>0</b>
Number of Backfill Trucks to Date	<b>243</b>
Backfill Received Today (In Tons)	<b>604.71</b>
Cumulative Backfill Volume to Date (In Tons)	<b>8737.72</b>

<sup>1</sup> Corrected value based on ERRS reported totals for each area.

**Niagara Falls Boulevard  
Niagara County, New York  
2020 Removal Action Daily Report**

**Site Photographs**

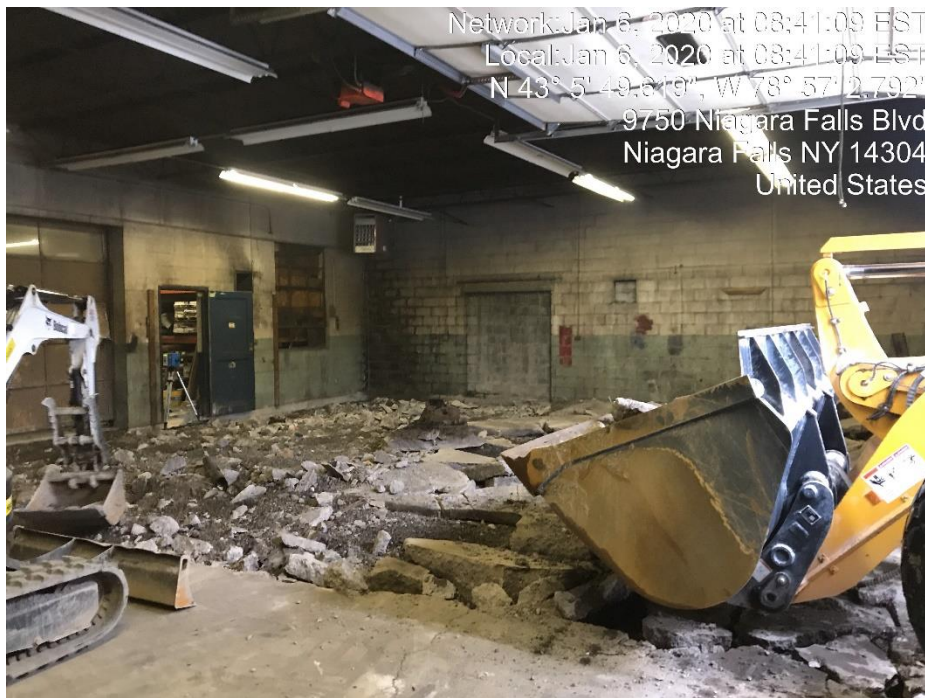

View ERRS removing concrete from WH3.



View ERRS conducting excavation activities in WH3.
