



ENVIRON

March 11, 1999

Mr. Augusto Chavarriaga
500 Garibaldi Avenue
South Plainfield, New Jersey 07080

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Mr. Chavarriaga:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).

Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. Work on your property is scheduled to begin on March 25, 1999 as shown on the enclosed schedule. It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.
4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all

of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

Handwritten signature of J. Mark Nielsen in cursive, followed by the initials 'lel'.

J. Mark Nielsen, P.E.
Manager

JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:01PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

Removal Action Implementation Schedule - Revised (Tier I Properties - Spicer Avenue)

ID	Task Name	Work Days	Start	Finish	Feb				Mar				Apr				May				Jun				Ju		
					1/31	2/7	2/14	2/21	2/28	3/7	3/14	3/21	3/28	4/4	4/11	4/18	4/25	5/2	5/9	5/16	5/23	5/30	6/6	6/13	6/20	6/27	7/4
101	Additional Verification Sampling	7 days	Fri 3/5/99	Mon 3/15/99																							
102	Sampling collection	1 day	Fri 3/5/99	Fri 3/5/99																							
103	Laboratory Analysis	5 days	Mon 3/8/99	Fri 3/12/99																							
104	Statistical Analysis (draft data)	5 days	Tue 3/9/99	Mon 3/15/99																							
105	Final delineation of Excavation Areas	5 days	Tue 3/9/99	Mon 3/15/99																							
106	Mobilization	4 days	Wed 3/10/99	Mon 3/15/99																							
107	Initiate field activities	1 day	Fri 3/12/99	Fri 3/12/99																							
108	Utility notifications & markout	4 days	Wed 3/10/99	Mon 3/15/99																							
109	Set up work zones/security	2 days	Fri 3/12/99	Mon 3/15/99																							
110	Contractor briefing	1 day	Mon 3/15/99	Mon 3/15/99																							
111	Soil Excavation & Initial Restoration	19 days	Mon 3/15/99	Thu 4/8/99																							
112	Property E Excavation	4 days	Mon 3/15/99	Thu 3/18/99																							
113	Property E Restoration	2 days	Thu 3/18/99	Fri 3/19/99																							
114	Property F Excavation	3 days	Thu 3/18/99	Mon 3/22/99																							
115	Property F Restoration	2 days	Tue 3/23/99	Wed 3/24/99																							
116	Property B Excavation	3 days	Tue 3/23/99	Thu 3/25/99																							
117	Property B Restoration	2 days	Thu 3/25/99	Fri 3/26/99																							
118	Property C Excavation	3 days	Thu 3/25/99	Mon 3/29/99																							
119	Property C Restoration	2 days	Mon 3/29/99	Tue 3/30/99																							
120	Property N Excavation	4 days	Mon 3/29/99	Thu 4/1/99																							
121	Property N Restoration	2 days	Thu 4/1/99	Fri 4/2/99																							
122	Property I Excavation	4 days	Thu 4/1/99	Tue 4/6/99																							
123	Property I Restoration	2 days	Wed 4/7/99	Thu 4/8/99																							
124	Waste Soil Disposal	25 days	Wed 3/10/99	Tue 4/13/99																							
125	Notification to EPA & receiving state of planne	1 day	Wed 3/10/99	Wed 3/10/99																							
126	Waste soil loading and off-site disposal	21 days	Tue 3/16/99	Tue 4/13/99																							
127	Demobilization	4 days	Mon 4/12/99	Thu 4/15/99																							
128																											
129	REPORTING	79 days	Mon 2/1/99	Thu 5/20/99																							
130	Laboratory Reporting & Validation	60 days	Mon 2/1/99	Fri 4/23/99																							
131	Report Preparation	25 days	Fri 4/16/99	Thu 5/20/99																							
132	Submittal of Final Report to EPA		Thu 5/20/99	Thu 5/20/99																							
133																											

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone



Summary



Recurring Task



Completed Task



h:\nielsen\02-5840c\schedules\Rra_wpin.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "*") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "*" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed _____

Date _____

Address _____

ENVIRON

March 11, 1999

Ms. Cindy Kane
501 Garibaldi Avenue
South Plainfield, New Jersey 07080

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Ms. Kane:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).

Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. Work on your property is scheduled to begin on March 23, 1999 as shown on the enclosed schedule. It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.

4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

A handwritten signature in black ink, appearing to read "J. Mark Nielsen" followed by a stylized flourish or initials.

J. Mark Nielsen, P.E.
Manager


JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:05PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

**Removal Action Implementation Schedule - Revised
(Tier I Properties - Spicer Avenue)**

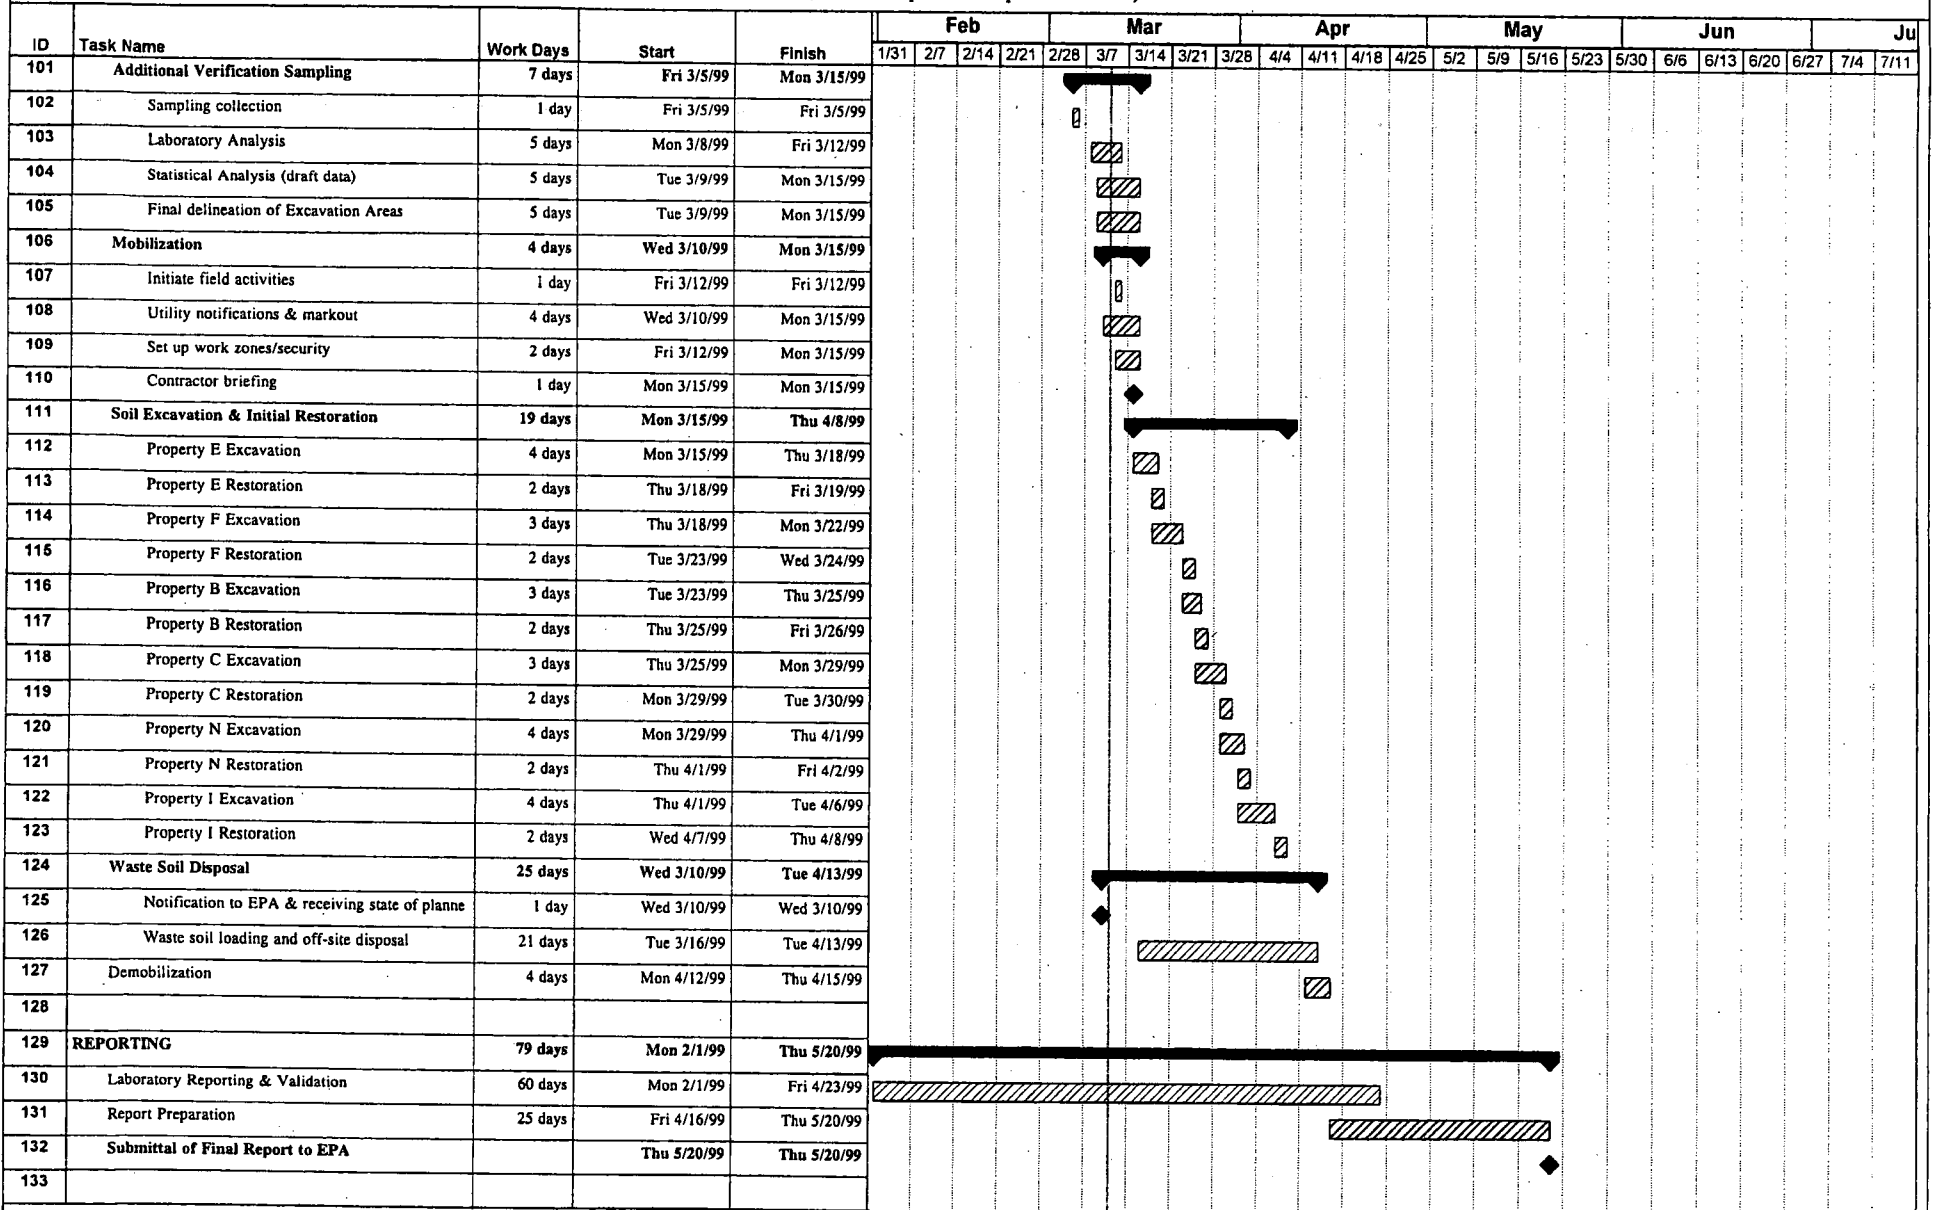

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone



Summary



Recurring Task



Completed Task



h:\nielsen\02-5840\cschedules\Rra_wpln.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "*") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "*" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed _____

Date _____

Address _____

ENVIRON

March 11, 1999

Mr. Frank Riccardi
305 Spicer Avenue
South Plainfield, New Jersey 07080

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Mr. Riccardi:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).


Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. Work on your property is scheduled to begin on April 1, 1999 as shown on the enclosed schedule. It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.
4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all

of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

A handwritten signature in black ink that reads "J. Mark Nielsen / lel". The signature is written in a cursive, flowing style.

J. Mark Nielsen, P.E.
Manager

JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:05PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

Removal Action Implementation Schedule - Revised (Tier I Properties - Spicer Avenue)

ID	Task Name	Work Days	Start	Finish	Feb				Mar				Apr				May				Jun				Ju		
					1/31	2/7	2/14	2/21	2/28	3/7	3/14	3/21	3/28	4/4	4/11	4/18	4/25	5/2	5/9	5/16	5/23	5/30	6/6	6/13		6/20	6/27
101	Additional Verification Sampling	7 days	Fri 3/5/99	Mon 3/15/99																							
102	Sampling collection	1 day	Fri 3/5/99	Fri 3/5/99																							
103	Laboratory Analysis	5 days	Mon 3/8/99	Fri 3/12/99																							
104	Statistical Analysis (draft data)	5 days	Tue 3/9/99	Mon 3/15/99																							
105	Final delineation of Excavation Areas	5 days	Tue 3/9/99	Mon 3/15/99																							
106	Mobilization	4 days	Wed 3/10/99	Mon 3/15/99																							
107	Initiate field activities	1 day	Fri 3/12/99	Fri 3/12/99																							
108	Utility notifications & markout	4 days	Wed 3/10/99	Mon 3/15/99																							
109	Set up work zones/security	2 days	Fri 3/12/99	Mon 3/15/99																							
110	Contractor briefing	1 day	Mon 3/15/99	Mon 3/15/99																							
111	Soil Excavation & Initial Restoration	19 days	Mon 3/15/99	Thu 4/8/99																							
112	Property E Excavation	4 days	Mon 3/15/99	Thu 3/18/99																							
113	Property E Restoration	2 days	Thu 3/18/99	Fri 3/19/99																							
114	Property F Excavation	3 days	Thu 3/18/99	Mon 3/22/99																							
115	Property F Restoration	2 days	Tue 3/23/99	Wed 3/24/99																							
116	Property B Excavation	3 days	Tue 3/23/99	Thu 3/25/99																							
117	Property B Restoration	2 days	Thu 3/25/99	Fri 3/26/99																							
118	Property C Excavation	3 days	Thu 3/25/99	Mon 3/29/99																							
119	Property C Restoration	2 days	Mon 3/29/99	Tue 3/30/99																							
120	Property N Excavation	4 days	Mon 3/29/99	Thu 4/1/99																							
121	Property N Restoration	2 days	Thu 4/1/99	Fri 4/2/99																							
122	Property I Excavation	4 days	Thu 4/1/99	Tue 4/6/99																							
123	Property I Restoration	2 days	Wed 4/7/99	Thu 4/8/99																							
124	Waste Soil Disposal	25 days	Wed 3/10/99	Tue 4/13/99																							
125	Notification to EPA & receiving state of planne	1 day	Wed 3/10/99	Wed 3/10/99																							
126	Waste soil loading and off-site disposal	21 days	Tue 3/16/99	Tue 4/13/99																							
127	Demobilization	4 days	Mon 4/12/99	Thu 4/15/99																							
128																											
129	REPORTING	79 days	Mon 2/1/99	Thu 5/20/99																							
130	Laboratory Reporting & Validation	60 days	Mon 2/1/99	Fri 4/23/99																							
131	Report Preparation	25 days	Fri 4/16/99	Thu 5/20/99																							
132	Submittal of Final Report to EPA		Thu 5/20/99	Thu 5/20/99																							
133																											

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone

Summary

Reoccurring Task

Completed Task

h:\nielsen\02-5840\cschedules\lrra_wpln.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "*") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "*" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed

Date

Address

ENVIRON

March 11, 1999

Mr. Mark Calderone
17 High Point Drive
Edison, New Jersey 08820

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Mr. Calderone:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).

Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. Work on your property is scheduled to begin on March 29, 1999 as shown on the enclosed schedule. It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.
4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all

of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

A handwritten signature in black ink, appearing to read "J. Mark Nielsen / lel".

J. Mark Nielsen, P.E.
Manager

JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:05PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

Removal Action Implementation Schedule - Revised
(Tier I Properties - Spicer Avenue)

ID	Task Name	Work Days	Start	Finish	Feb				Mar				Apr				May				Jun				Jul		
					1/31	2/7	2/14	2/21	2/28	3/7	3/14	3/21	3/28	4/4	4/11	4/18	4/25	5/2	5/9	5/16	5/23	5/30	6/6	6/13		6/20	6/27
101	Additional Verification Sampling	7 days	Fri 3/5/99	Mon 3/15/99																							
102	Sampling collection	1 day	Fri 3/5/99	Fri 3/5/99																							
103	Laboratory Analysis	5 days	Mon 3/8/99	Fri 3/12/99																							
104	Statistical Analysis (draft data)	5 days	Tue 3/9/99	Mon 3/15/99																							
105	Final delineation of Excavation Areas	5 days	Tue 3/9/99	Mon 3/15/99																							
106	Mobilization	4 days	Wed 3/10/99	Mon 3/15/99																							
107	Initiate field activities	1 day	Fri 3/12/99	Fri 3/12/99																							
108	Utility notifications & markout	4 days	Wed 3/10/99	Mon 3/15/99																							
109	Set up work zones/security	2 days	Fri 3/12/99	Mon 3/15/99																							
110	Contractor briefing	1 day	Mon 3/15/99	Mon 3/15/99																							
111	Soil Excavation & Initial Restoration	19 days	Mon 3/15/99	Thu 4/8/99																							
112	Property E Excavation	4 days	Mon 3/15/99	Thu 3/18/99																							
113	Property E Restoration	2 days	Thu 3/18/99	Fri 3/19/99																							
114	Property F Excavation	3 days	Thu 3/18/99	Mon 3/22/99																							
115	Property F Restoration	2 days	Tue 3/23/99	Wed 3/24/99																							
116	Property B Excavation	3 days	Tue 3/23/99	Thu 3/25/99																							
117	Property B Restoration	2 days	Thu 3/25/99	Fri 3/26/99																							
118	Property C Excavation	3 days	Thu 3/25/99	Mon 3/29/99																							
119	Property C Restoration	2 days	Mon 3/29/99	Tue 3/30/99																							
120	Property N Excavation	4 days	Mon 3/29/99	Thu 4/1/99																							
121	Property N Restoration	2 days	Thu 4/1/99	Fri 4/2/99																							
122	Property I Excavation	4 days	Thu 4/1/99	Tue 4/6/99																							
123	Property I Restoration	2 days	Wed 4/7/99	Thu 4/8/99																							
124	Waste Soil Disposal	25 days	Wed 3/10/99	Tue 4/13/99																							
125	Notification to EPA & receiving state of planne	1 day	Wed 3/10/99	Wed 3/10/99																							
126	Waste soil loading and off-site disposal	21 days	Tue 3/16/99	Tue 4/13/99																							
127	Demobilization	4 days	Mon 4/12/99	Thu 4/15/99																							
128																											
129	REPORTING	79 days	Mon 2/1/99	Thu 5/20/99																							
130	Laboratory Reporting & Validation	60 days	Mon 2/1/99	Fri 4/23/99																							
131	Report Preparation	25 days	Fri 4/16/99	Thu 5/20/99																							
132	Submittal of Final Report to EPA		Thu 5/20/99	Thu 5/20/99																							
133																											

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone

Summary

Reoccurring Task

Completed Task

h:\nielsen\02-5840\cschedules\VRa_wpin.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "*") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "*" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed _____

Date _____

Address _____

ENVIRON

March 11, 1999

Ms. Margaret Reidy
204 Spicer Avenue
South Plainfield, New Jersey 07080

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Ms. Reidy:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).

Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. Work on your property is scheduled to begin on March 15, 1999 as discussed on March 2, 1999. Cornell Dubilier Electronics, Inc. is agreeable to your contracting separately for the restoration work as specified in your contractor's bid and quoted at \$15,035. Please have your contractor submit his invoice to me directly for payment.

It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.
4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

A handwritten signature in black ink, appearing to read "J. Mark Nielsen / lel". The signature is fluid and cursive.

J. Mark Nielsen, P.E.
Manager


JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:05PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

**Removal Action Implementation Schedule - Revised
(Tier I Properties - Spicer Avenue)**

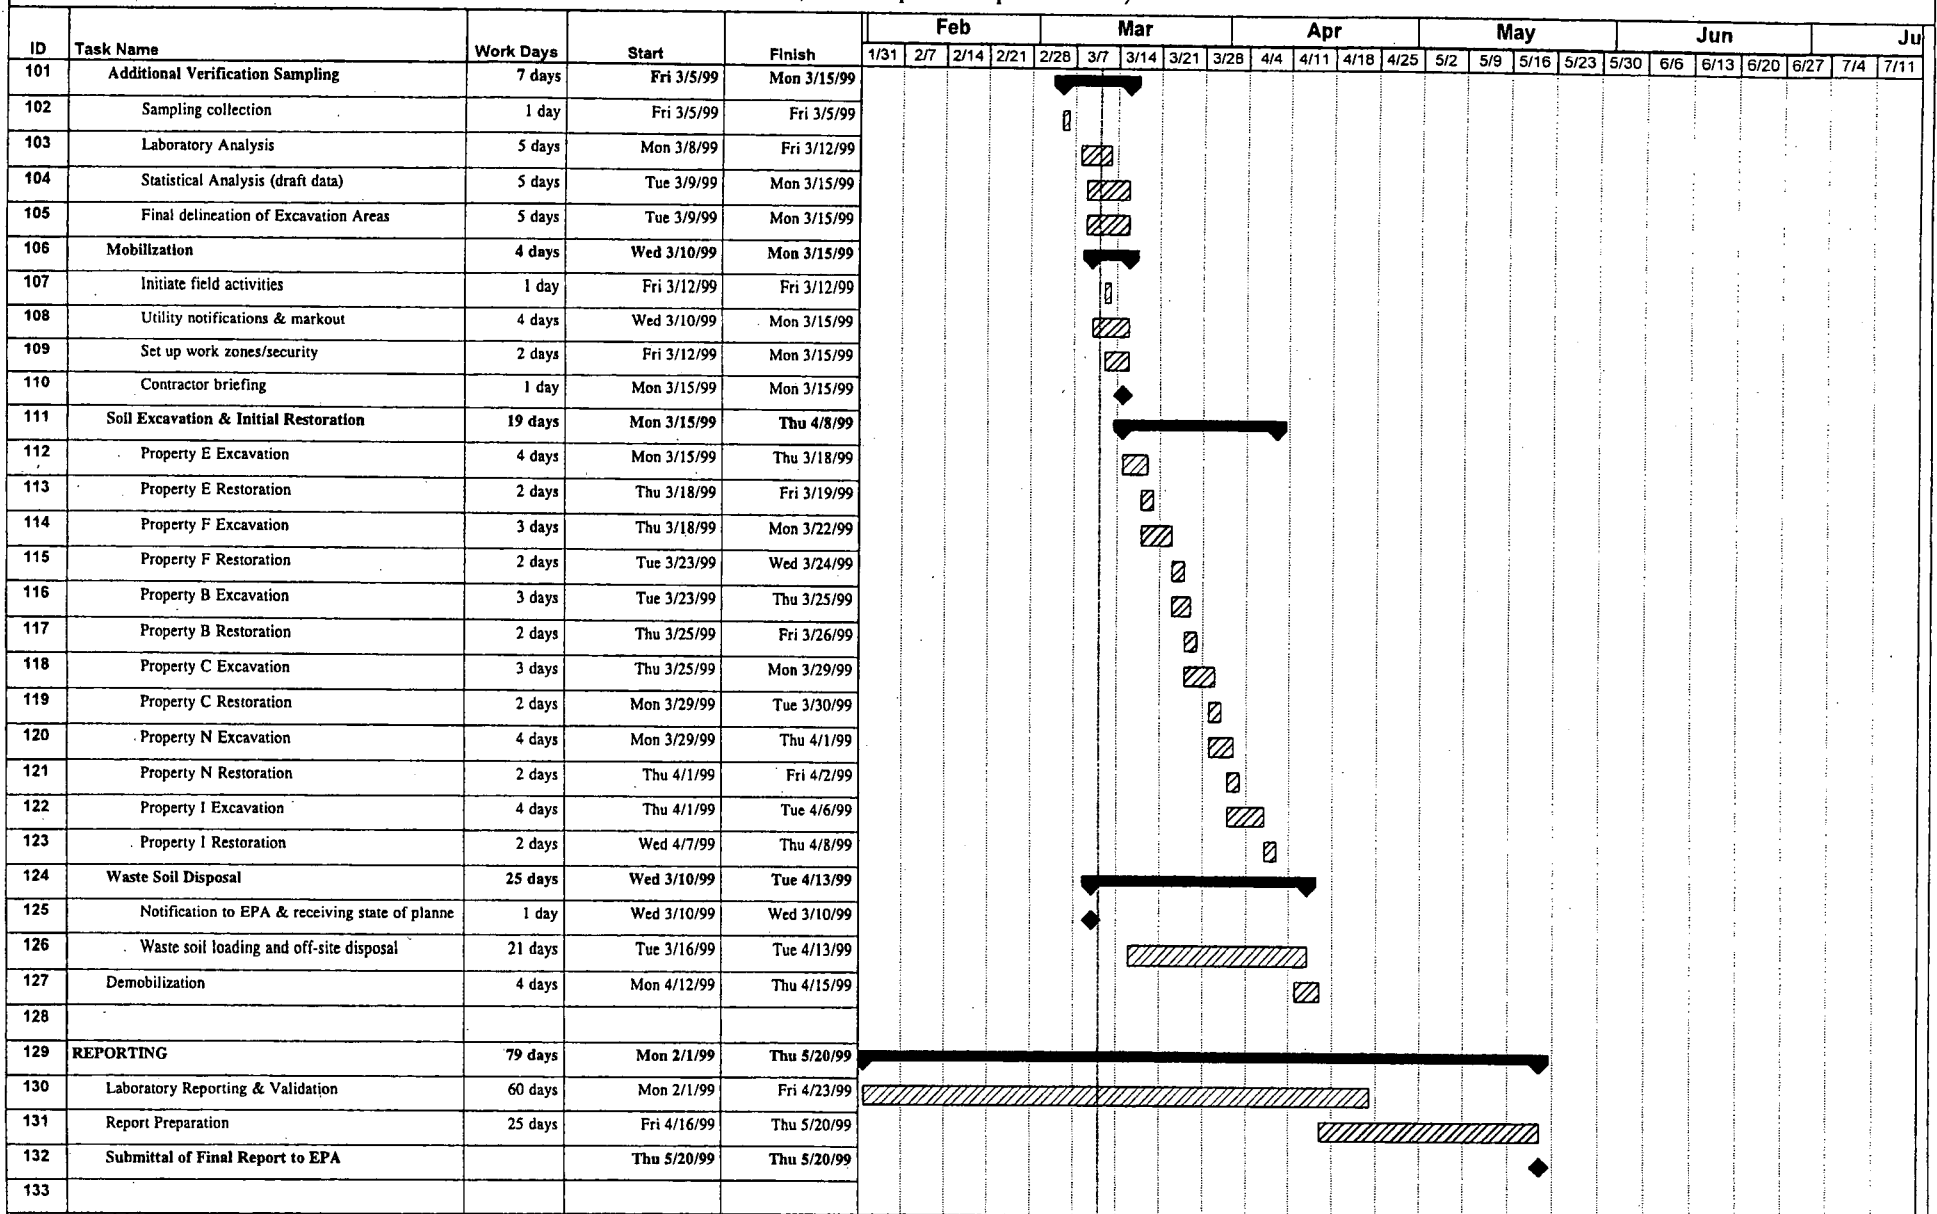

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone

Summary

Reoccurring Task

Completed Task

h:\nielsen\02-5840\cschedules\lra_wpin.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "*") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "*" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed

Date

Address

ENVIRON

March 11, 1999

Mr. Diwan Puar
210 Spicer Avenue
South Plainfield, New Jersey 07080

Re: Schedule of Construction Activities; Instructions and Landscape Plan Agreement

Dear Mr. Puar:

As you are aware, soil removal activities are to be conducted at six residential properties located on Spicer Avenue, South Plainfield, New Jersey, including your property, in response to an Administrative Order on Consent (AOC) issued by the United States Environmental Protection Agency (USEPA) pursuant to Comprehensive Environmental Response, Compensation and Liability Act (Superfund).

Integrated Technical Services, Inc. (ITS) has been selected to perform the soil removal and restoration activities. As we discussed on March 2, 1999, C & M Pools & Installation, Inc. (C & M) will dismantle your swimming pool prior to ITS beginning work on your property. Based on our discussion, I understand that the pool may be stored in your garage until restoration of your property is completed.

Excavation work on your property is scheduled to begin on March 18, 1999 as shown on the enclosed schedule. It is very important that you complete the following activities prior to this date:

1. Provide a list and location of any private utilities installed on your property (e.g., electrical lines for outdoor lighting fixtures, gas lines for grills or other appliances, pipes for sprinkler systems, etc.). Please mark the locations of these utilities on the enclosed plan or mark these utilities on the copy that was provided to you during the USEPA meeting on November 30, 1998 or hand delivered to you on December 1, 1998. You may list the names and types of utilities on the back of this map.
2. Remove all personal property and nonstructural items from the outside of your property (e.g., lawn ornaments, furniture, picnic tables, bicycles, unsecured playground equipment, etc.). The contractors cannot be responsible for damage to these items if they are not removed prior to the scheduled start date.
3. Review and provide written agreement to the enclosed landscape plan. Instructions and a form for completing this task are provided in Attachment 1.

4. During the excavation and restoration activities conducted on your property, it is requested that all pets be kept inside the house and that any gates be left unlocked during daylight hours. Please note that the contractors may need to remove part or all of the fencing on your property in order to complete the required work.

If you should have any questions regarding this notice or the excavation and restoration activities planned for your property, please call me at (609) 243-9859.

Sincerely,

A handwritten signature in black ink, appearing to read "J. Mark Nielsen", followed by a stylized flourish or initials.

J. Mark Nielsen, P.E.
Manager


JMN:lel

025840c:H:\NIELSEN\02-5840C\5840C_39.WPD/3-11-99/6:05PM

Enclosure

cc: Eric Wilson, USEPA
John Corica, Borough of South Plainfield
Mike Scott, ENVIRON

**Removal Action Implementation Schedule - Revised
(Tier I Properties - Spicer Avenue)**

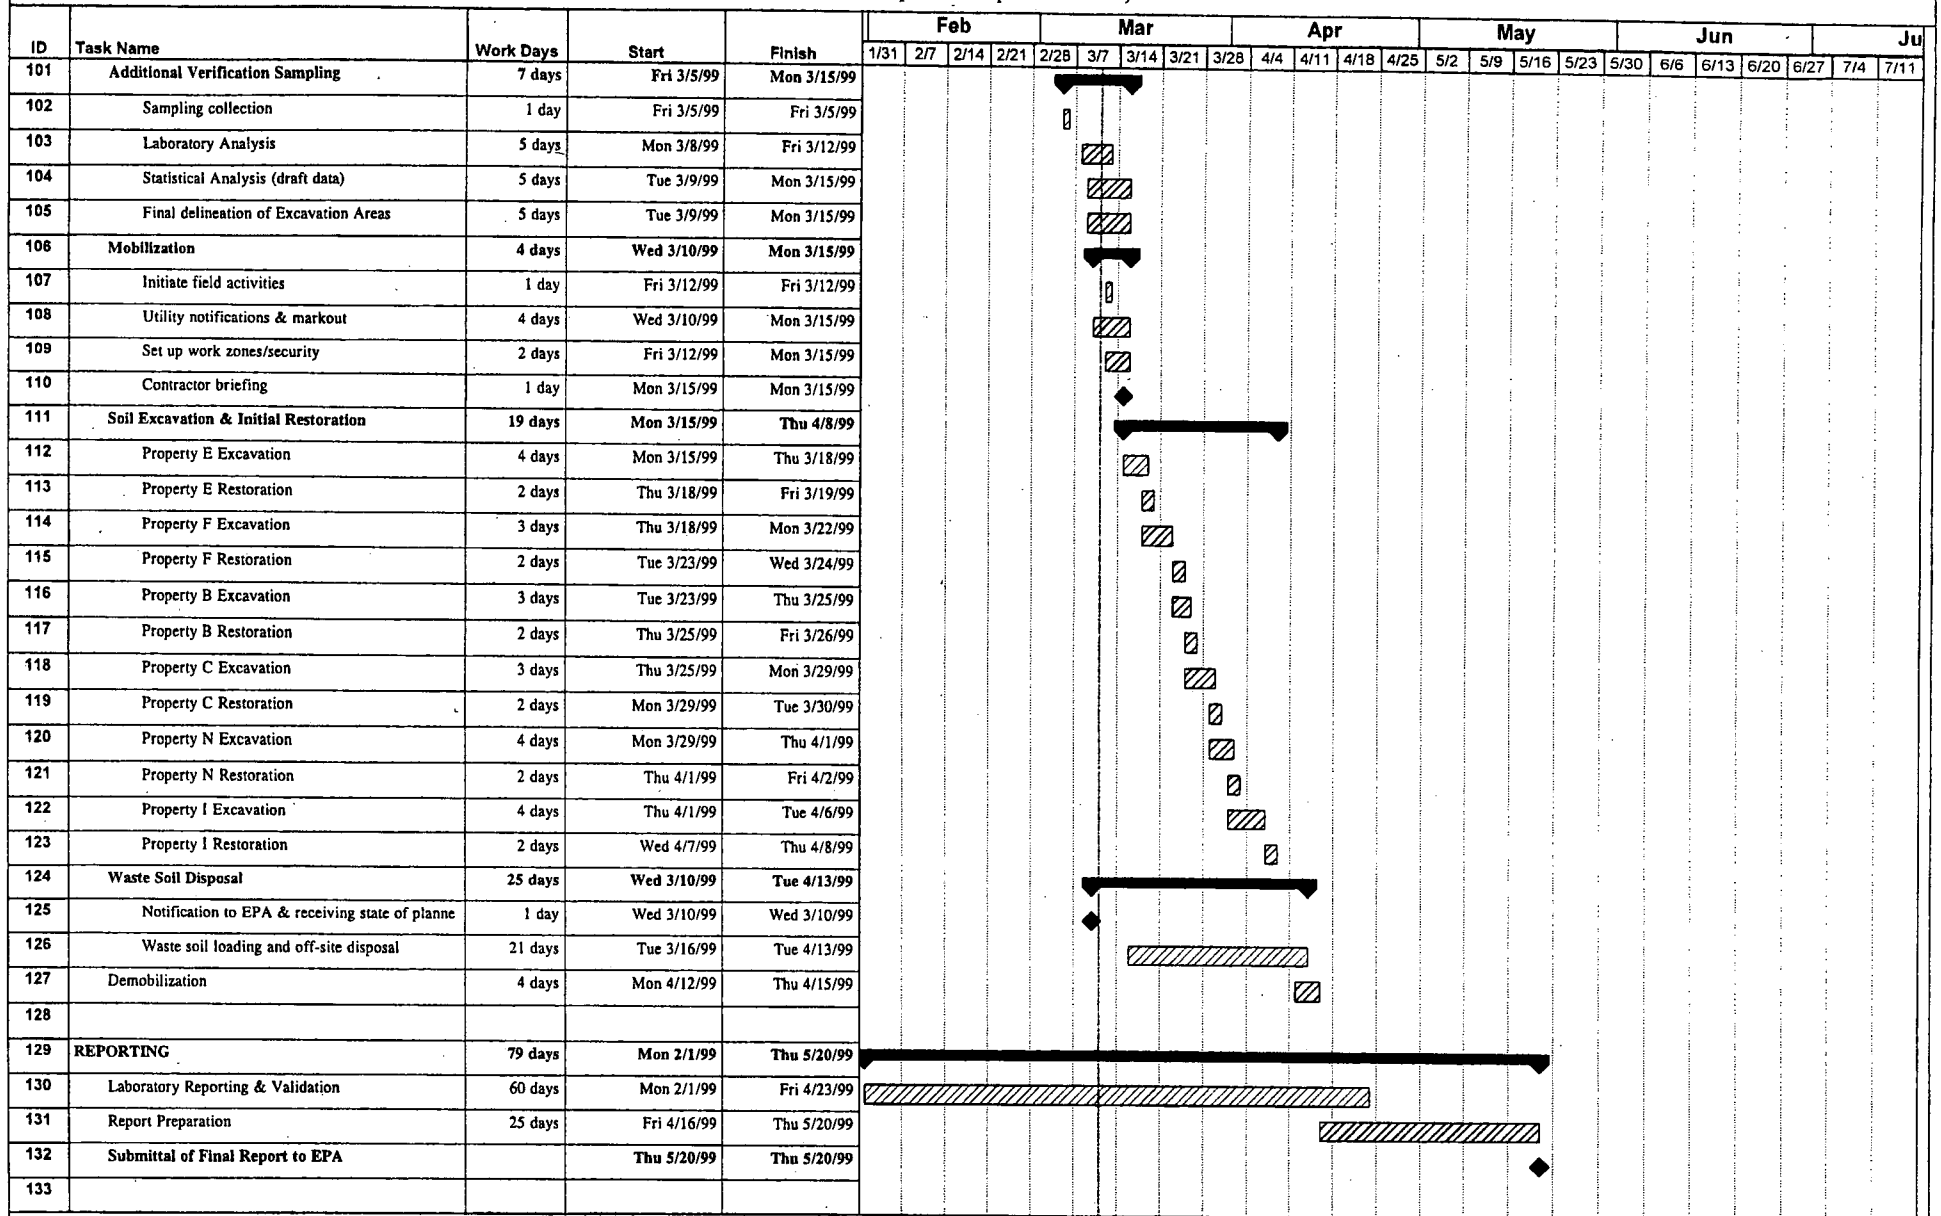

Project: Hamilton
Plot Date: Thu 3/11/99

Task

Milestone

Summary

Recurring Task

Completed Task

h:\nielsen\02-5840\lschedules\lra_wph.mpp

Last Saved Date: Thu 3/11/99 **5:34 PM

ATTACHMENT 1
INSTRUCTIONS AND FORM FOR AGREEMENT TO
LANDSCAPE RESTORATION PLAN

ATTACHMENT 1: INSTRUCTIONS

The landscape restoration plan contains tables labeled "Restoration Schedule" and "Alternate Plant Material". The Restoration Schedule lists the material that will replace plants or hardscape items that must be removed from your property by the contractor in order to complete soil excavation activities. The Alternate Plant Material schedule lists other plants on your property which have not yet been identified for removal during the soil excavation phase. Please review both schedules and verify that all plants on your property are included. Additional instructions for the Restoration Schedule are provided below.

Restoration Schedule

The Restoration Schedule includes certain trees (marked with a "**") which are too large to be replaced with a tree of equal size. This designation indicates that three smaller trees of the same species will be provided to you in order to restore the landscaping on your property to equivalent value of the original. However, before proceeding with the excavation and restoration, ENVIRON requests your input on this arrangement. Please select one of the following options and provide the requested information to ENVIRON:

1. If you would like to receive three trees in replacement of each "**" tree to be removed, please indicate on the enclosed landscape plan the locations in which you would like each tree to be planted. The enclosed landscape plan is a photocopy of the plan that was provided to you on November 30, 1998 or December 1, 1998. OR
2. If you would prefer one tree to replace the original, and would rather specify alternate planting in place of the two additional trees, please identify the types and locations of your preferred alternate plantings on the enclosed landscape plan. Note that alternate plantings will be provided as a substitute in equivalent value, to the extent practicable.

Signed

Date

Address
