


Sevenson Environmental Services Inc.
Cornell Dubilier Electronics Superfund Site
OU1 Residential Soils Remediation
Project Schedule Update (thru 12-30-12)

January 16, 2013

299000



**Cornell Dubilier Electronics Superfund Site
OU1 Schedule Narrative—Project Schedule Update (thru 12-30-12)**

Data Date

The schedule data date is 12-30-12. This is Project Schedule Update 6.

Project Schedule Update

Attached is the Cornell Dubilier Electronics Superfund Site, OU1 Residential Soils Remediation Schedule Update 5 compiled using the previously negotiated production rates and durations.

Some areas to note are as follows:

- All General Requirements items have been rolled into one activity for ease of tracking. Utility protection costs have been spread across the property groupings within the excavation activities
- There is no dewatering or water treatment associated with these groupings. Weather days are built into the production rates within this schedule. Should inclement weather show a further adverse effect on production, SES will revisit the situation accordingly and provide the necessary documentation.
- Additional duration will be necessary for excavation at 140 Harvard property as well as excavation at 1000 Giribaldi that has impacted areas outside of the original scope of work for this grouping. These excavations and associated restoration will be completed in the spring 2013 as shown on the attached update.
- Fixed fee cost is assigned to the General Requirements activity and is spread across the entire project.
- Due to slower production being encountered at the Delmore property grouping because of underground obstructions, Hurricane Sandy impacts, as well as additional excavation at the Harvard property grouping and increased scope for restoration at this grouping, the general requirements activities and closeout submittals are now projected at 4/15/13 from the previous scheduled end date of 1/21/13. SES will strive to increase production where available to decrease the remaining duration of the currently scheduled properties.

Any questions please contact me at 973-650-5995

Revisions to the OU1 Schedule – Cornell Dubilier Superfund Site

Logic Changes

No changes to the logic for this update.


Problems/Deficiencies

See deficiency log for any new deficiencies.

Future Potential Changes

SES's proposal for additional properties are being negotiated on 1/16/13 and will be added to the overall schedule once the negotiations are finalized.

Cornell Dubilier Electronics Superfund Site
Residential Schedule Update thru 12-30-12 (Group 1, 2, 3)

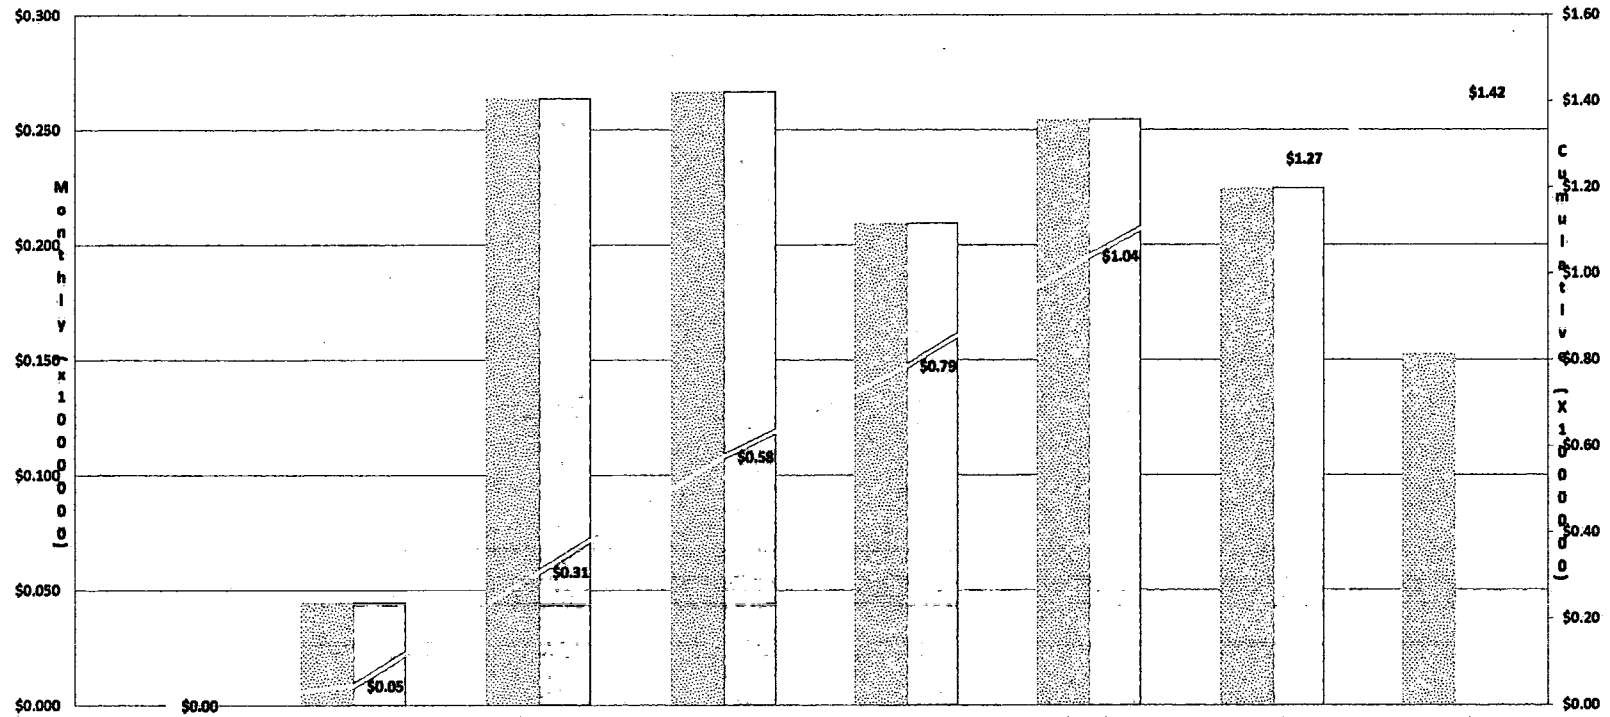

	Jun-12	Jul-12	Aug-12	Sep-12	Oct-12	Nov-12	Dec-12	Jan-13
At Completion	\$0.000	\$0.045	\$0.264	\$0.267	\$0.210	\$0.255	\$0.23	\$0.159
Actual Costs	\$0.00	\$0.05	\$0.26	\$0.27	\$0.21	\$0.26	\$0.23	\$0.00
At Completion Cum	\$0.00	\$0.05	\$0.31	\$0.58	\$0.79	\$1.04	\$1.27	\$1.42

Notes:

Current Budget Funding = \$1,366,348

Current Funding will be exhausted by 1/28/13
