

RMT, Inc.

2025 E. Beltline Ave SE
Suite 402
Grand Rapids, MI 49546

Phone: 616-975-5415
Fax: 616-975-1098

TRANSMITTAL**No. 00085****PROJECT:** LEC Remediation Services**DATE:** 6/30/2005

TO: NJDEP
Bureau of Federal Case Management
Div. of Responsible Site Party Remed
CN028
Trenton, NJ 08625

REF: PPU No. 17**ATTN:** Anthony Cinque

WE ARE SENDING:	SUBMITTED FOR:	ACTION TAKEN:
<input type="checkbox"/> Shop Drawings	<input type="checkbox"/> Approval	<input type="checkbox"/> Approved as Submitted
<input type="checkbox"/> Letter	<input checked="" type="checkbox"/> Your Use	<input type="checkbox"/> Approved as Noted
<input type="checkbox"/> Prints	<input type="checkbox"/> As Requested	<input type="checkbox"/> Returned After Loan
<input type="checkbox"/> Change Order	<input type="checkbox"/> Review and Comment	<input type="checkbox"/> Resubmit
<input type="checkbox"/> Plans		<input type="checkbox"/> Submit
<input type="checkbox"/> Samples	SENT VIA:	<input type="checkbox"/> Returned
<input type="checkbox"/> Specifications	<input type="checkbox"/> Attached	<input type="checkbox"/> Returned for Corrections
<input checked="" type="checkbox"/> Other: Project Progress Update No. 17	<input checked="" type="checkbox"/> Separate Cover Via: Email 6/30/05	<input type="checkbox"/> Due Date:

ITEM NO.	COPIES	DATE	ITEM NUMBER	REV. NO.	DESCRIPTION	STATUS
01	1	6/30/2005			Project Progress Update No. 17	APP
02	1	6/30/2005			Project Progress Update No. 17 Photos	NEW

471477



CC: S. Cipot, R. Alvey, F. Zizilia, J. Prendergast, G. Blyskun, J. Lewis
C. Anderson, E. Schaub, C. Clavadetscher, J. Rheinhardt, RMT Project Team

Signed: 

Nick Clevett

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 17

Date: June 30, 2005

To: Stephen Cipot, USEPA
Anthony Cinque, NJDEP

From: Nicholas J. Clevett, RMT

cc: Robert Alvey, USEPA
Frances Zizila, USEPA
John Prendergast, NJDEP
George Blyskun, NJDEP
Jim Lewis, LEC
Cris Anderson, LEC
Ernie Schaub, LEC
Colin Clavadetscher, Morris County

Jon Rheinhardt, Borough of Wharton
Dan Oman, RMT
Jim Dexter, RMT
Walter Kurzeja, RMT
Jeff Macri, RMT
Dave Pratt, RMT
Nakia Addison, RMT

Project No.: 00-06527.09

Subject: SOURCE REDUCTION REMEDIAL ACTION
Project Progress Update No. 17 ~ FINAL WEEKLY UPDATE

The Source Reduction Remedial Project is now considered substantially complete. As such, this will be the final weekly update prepared for the construction phase of this project. As required by USEPA and NJDEP following their respective reviews of the Remedial Action Work Plan (RAWP), a Remedial Action Report (RAR) documenting the construction activities completed during the period between January 6, 2005 [preconstruction meeting] and June 30, 2005 [final grade survey] will be presented 90-calendar days following the receipt of the final grade survey data. The final grade survey data is tentatively scheduled for receipt during the week of July 11, 2005. As such, the RAR is tentatively scheduled for submittal to both NJDEP and USEPA for review during the week of October 10, 2005. In addition, a Post Remedial Monitoring Plan (PRMP) outlining the groundwater and surface water monitoring proposed for the LEC site (*i.e.*, monitoring well network design and installation, sampling locations, frequency and analyses) will be submitted to NJDEP and USEPA for review 45-calendar days following completion of the source reduction project. As such, the PRMP is proposed for submittal to both NJDEP and USEPA for review during the week of August 22, 2005.

I. SOURCE REDUCTION REMEDIAL ACTIONS - JUNE 8TH THROUGH JUNE 30TH 2005

1. Completed backfilling activities in all site areas (*i.e.*, the main portion of the excavation, wetland areas, transition zones and along the Air Products drainage ditch).
2. Completed all site surveying (*i.e.*, as-built excavation and final grades).
3. Hydro-seeded the main portion of the source reduction excavation area in accordance with the Remedial Action Work Plan (RAWP).
4. Held the post final grade meeting with the NJDEP Land Use Regulation Program (LURP) on June 24, 2005 at 1pm EST in accordance with Special Condition No. 10 of the NJDEP LURP Freshwater Wetlands Statewide General Permit No. 4 [Permit No 1439-04-0001.1 (FWW 040001)]. Final grade was unconditionally approved by the LURP, and wetland restoration activities were authorized for completion.
5. All wetland and transition areas were restored between the dates of June 27th and June 29th 2005 in accordance with the LURP approved wetland restoration plan.

L.E. CARPENTER & COMPANY ~ NJD002168748
BOROUGH OF WHARTON, MORRIS COUNTY, NEW JERSEY
SOURCE REDUCTION REMEDIAL PROJECT PROGRESS UPDATE NO. 17

6. Demobilized all equipment and cleaned all paved areas with a skid steer broom attachment and manual sweeping.
7. Repaired the galvanized fencing along the rails-to-trails and the Wharton Enterprise Property.
8. Repaired the asphalt on the rails-to-trails.



Photographic Log Progress Update No. 17 ~ Final Update

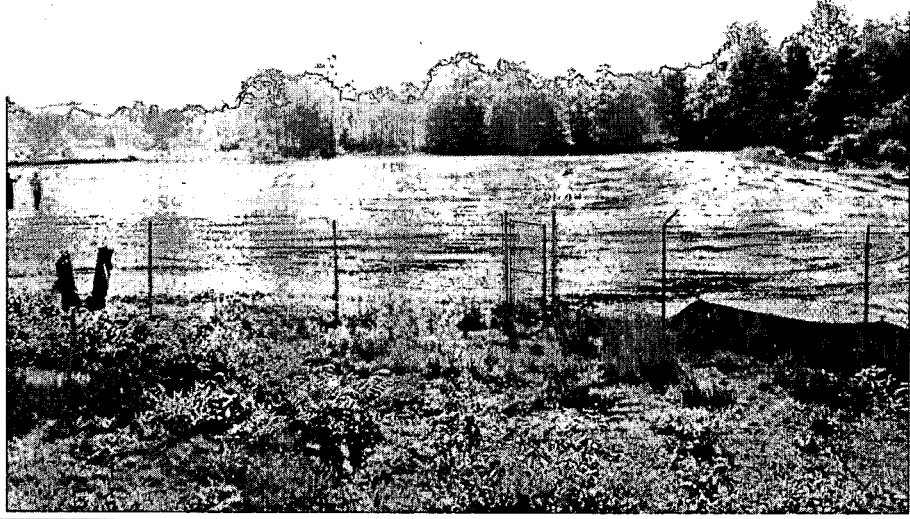
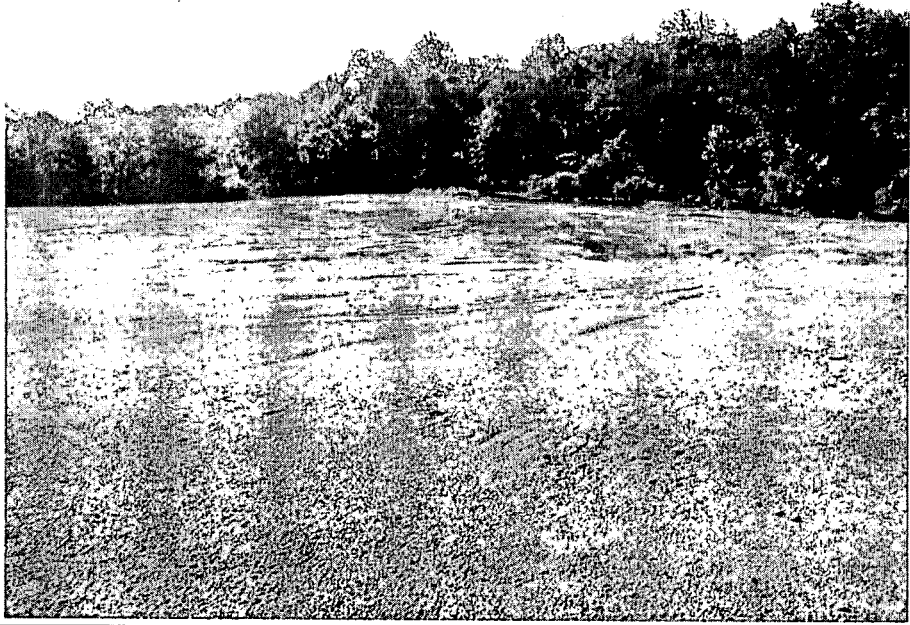

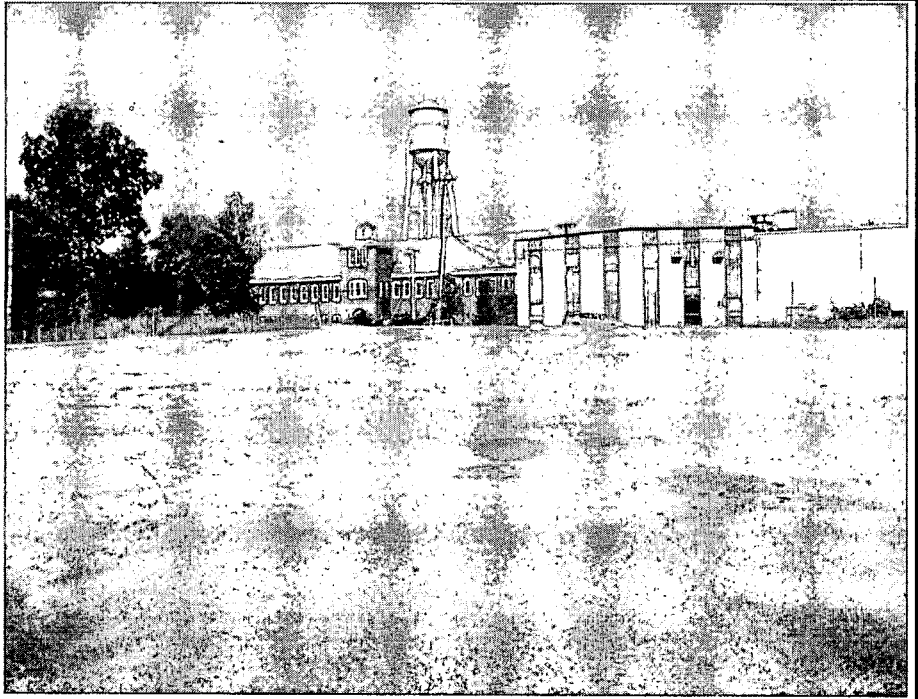
Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 1	Date 6/24/05		
Description Final grade. South end of the source reduction excavation area. View looking east from the rails-to-trails.			

Photo No. 2	Date 6/24/05	
Description Final grade. Central section of the source reduction excavation area. View looking southeast.		





Photographic Log Progress Update No. 17 ~ Final Update

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 3	Date 6/24/05		
Description Final grade. Central section of the source reduction excavation area. View looking east.			
Photo No. 4	Date 6/24/05		
Description Final grade. Western section of the source reduction excavation area. View looking west.			



Photographic Log Progress Update No. 17 ~ Final Update

Client Name:		Site Location:	Project No.:
L.E. CARPENTER & COMPANY		Wharton, Morris County, NJ	00-06527.09
Photo No.	Date		
5	6/24/05		
Description Hydro seed close-up.			
Photo No.	Date		
6	6/24/05		
Description Final grade. Wetland area. <u>Note</u> high quality topsoil (12.6% organic content) and eastern extent of hydro seed. The wetland area was not hydro seeded in preparation for wetland restoration with specific seed mixes and plantings. Wetland area and transition zone survey stakes are shown at the forefront of the picture. View looking east southeast.			



Photographic Log Progress Update No. 17 ~ Final Update



Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 7	Date 6/24/05		
Description Wetland area final grade. View looking east.			

Photo No. 8	Date 6/24/05	
Description Wetland area final grade. <u>Note</u> large trees were preserved during excavation activities. View looking west.		



Photographic Log Progress Update No. 17 ~ Final Update

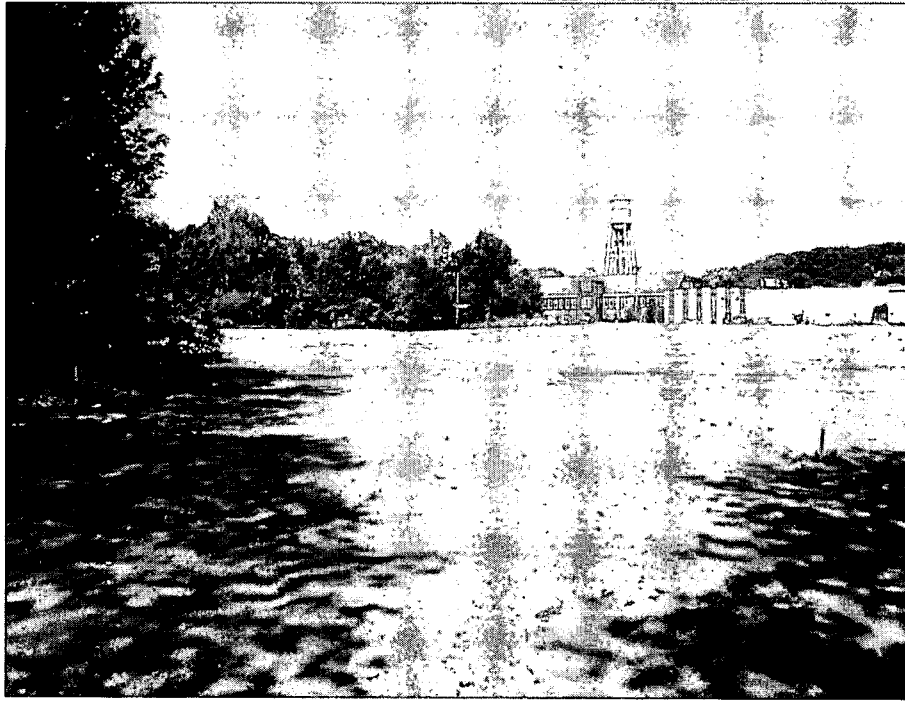


Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 9	Date 6/24/05		
Description Wetland and main excavation interface. View looking west.			

Photo No. 10	Date 6/24/05	
Description Reinstalling the rails to trails fence. View looking northeast		



Photographic Log Progress Update No. 17 ~ Final Update

Client Name: L.E. CARPENTER & COMPANY		Site Location: Wharton, Morris County, NJ	Project No.: 00-06527.09
Photo No. 11	Date 6/24/05		
Description Wetland and main excavation interface. View looking east.			
