



Avery Landing 008.JPG
09/15/2000
View of backside of coffer dam
Petroleum film evident




Avery Landing 009.JPG
09/15/2000
Viewing downstream at coffer dam

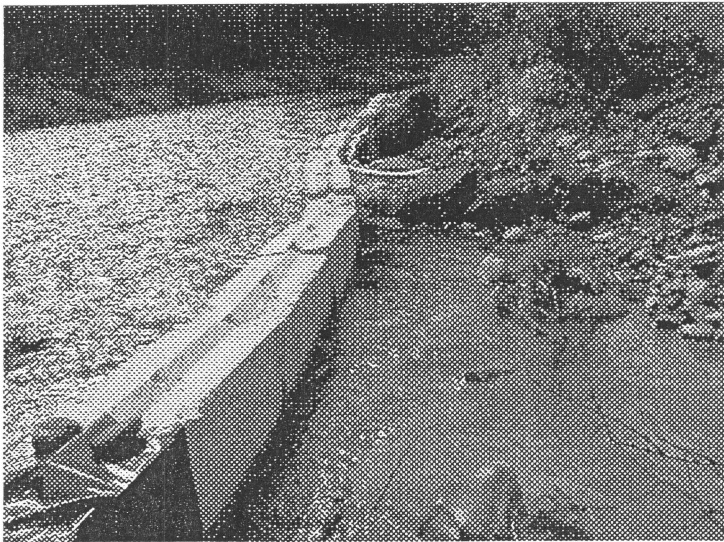

Avery Landing 010.JPG
09/15/2000
Viewing downstream at coffer dam

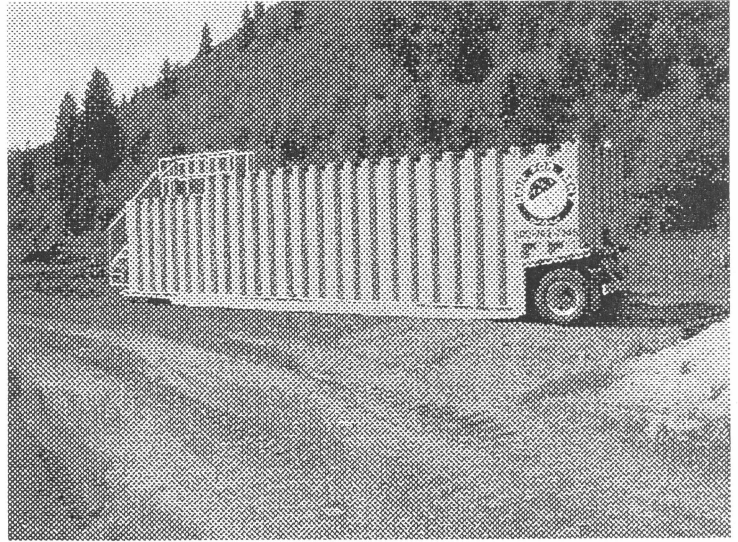


Avery Landing 011.JPG
09/15/2000
Oil/water separator being used on site

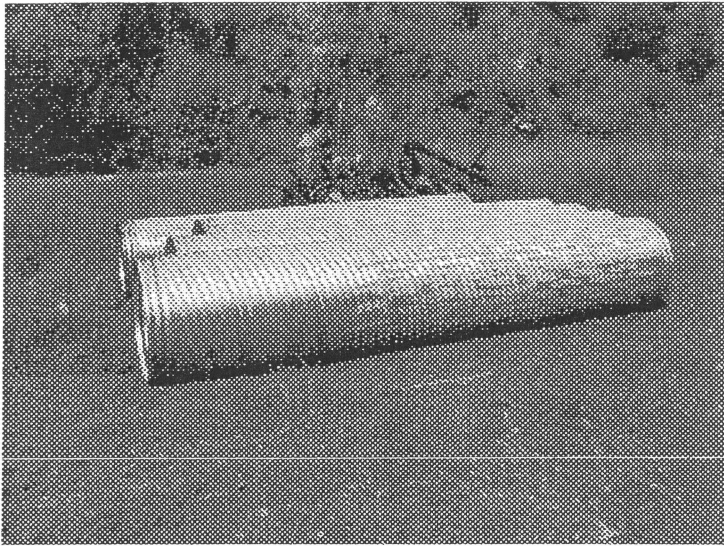

Avery Landing 012.JPG
09/15/2000


Photo of recovery wells that will be placed just upgradient of liner

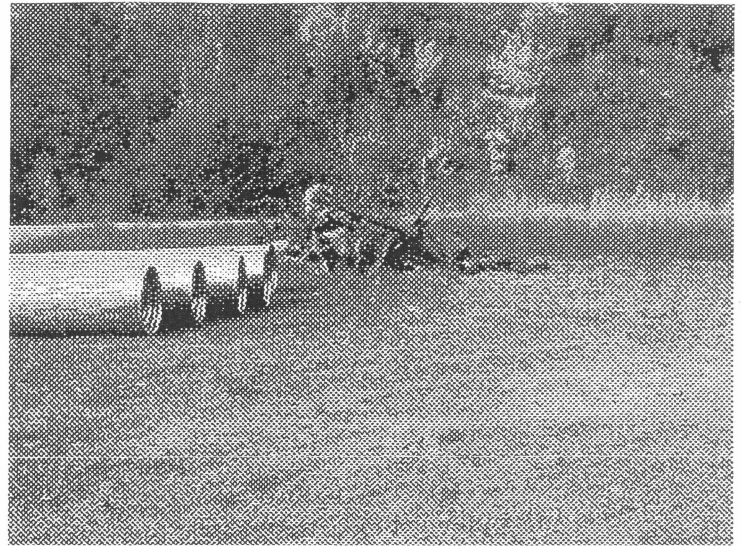

Avery Landing 013.JPG
09/15/2000


Photo of 3' diameter recover pipes

*& junk metal that has been excavated
from stream bank*

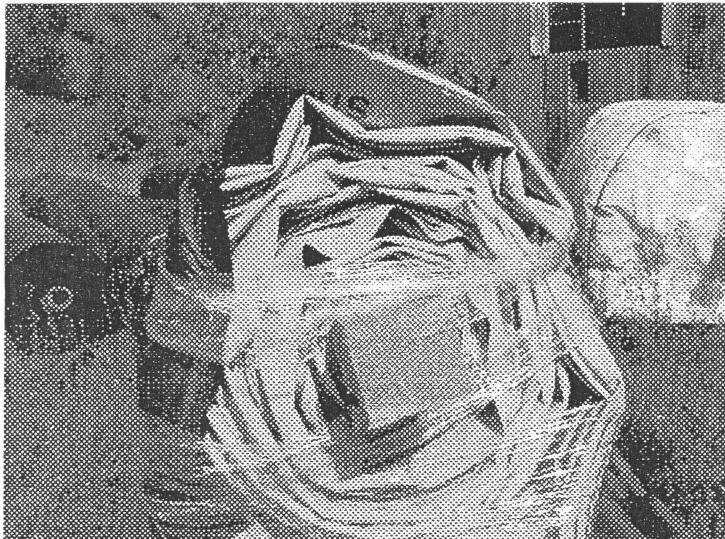


Avery Landing 014.JPG
09/15/2000

Photo of liner that will be placed along stream bank

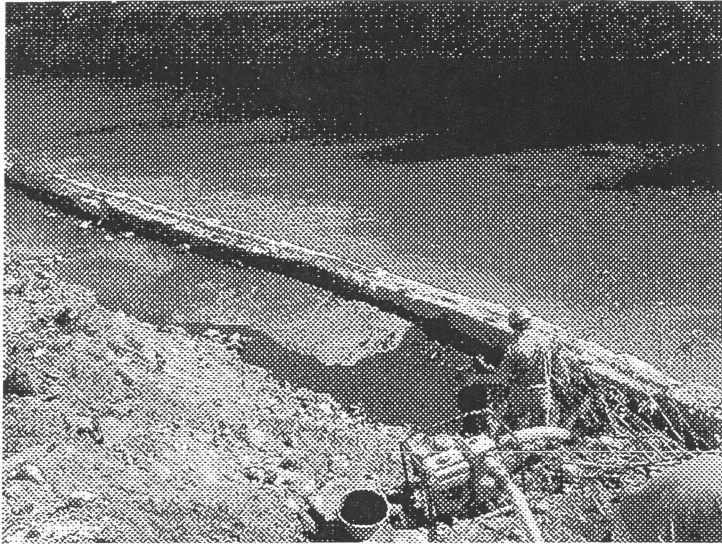

Avery 008.JPG
09/25/2000

Viewing upriver from W end of site. Lots of petroleum behind coffer dam;
some silting outside of dam

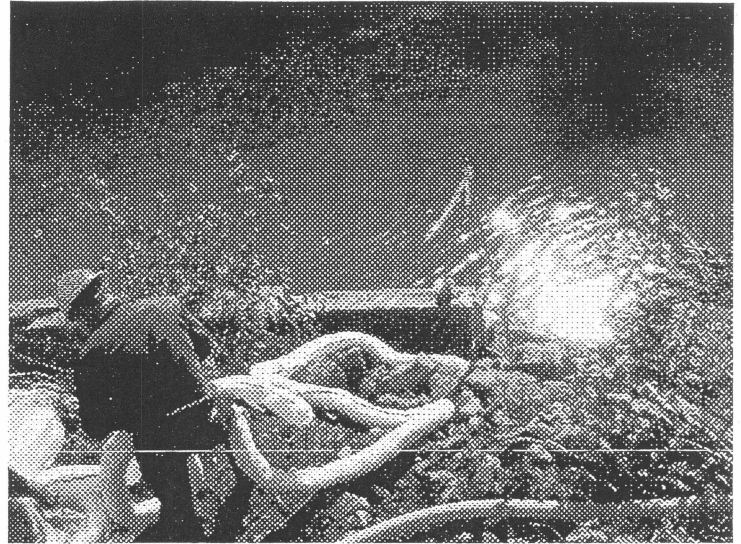

Avery 009.JPG
09/25/2000

Potlatch workers adding new boom to W end of site where minor amounts of
petroleum were escaping thru coffer dam




Avery 010.JPG
09/25/2000

Petroleum seep on bench in approx. center of site. Unknown whether this
came from heavy equip or ground




Avery 011.JPG
09/25/2000

Photo of silt and oil behind coffer dam on W end of site

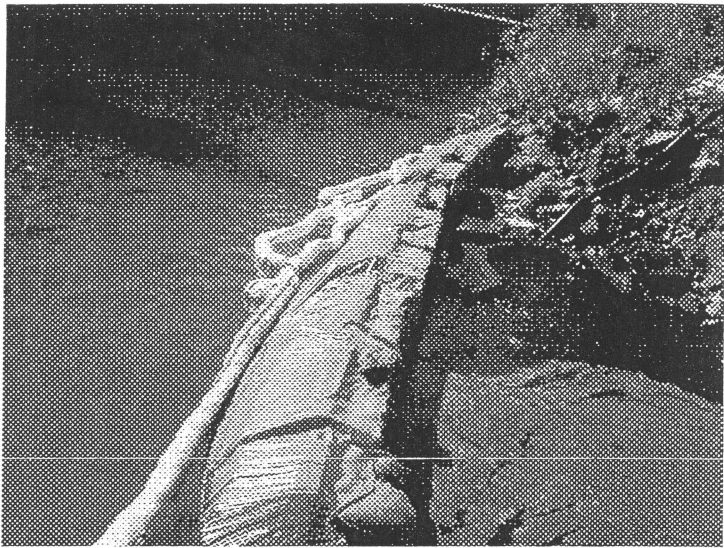


Avery 012.JPG
09/25/2000

Viewing downstream @ contaminated W end of site, behind coffer dam

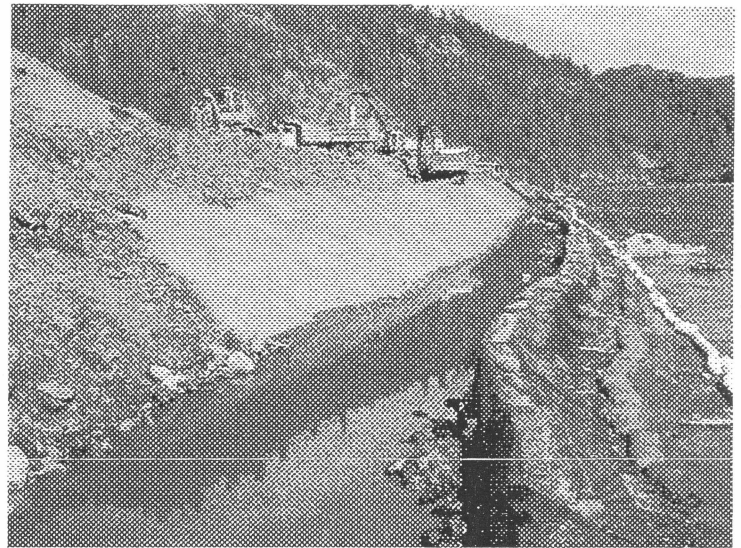


Avery 013.JPG
09/25/2000

Viewing upstream across entire coffer dam

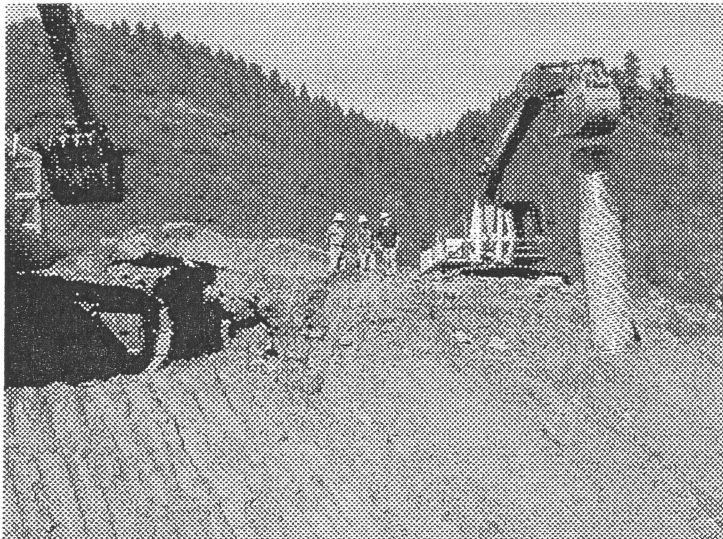


Avery 014.JPG
09/25/2000

Photo of one of the extraction wells being installed

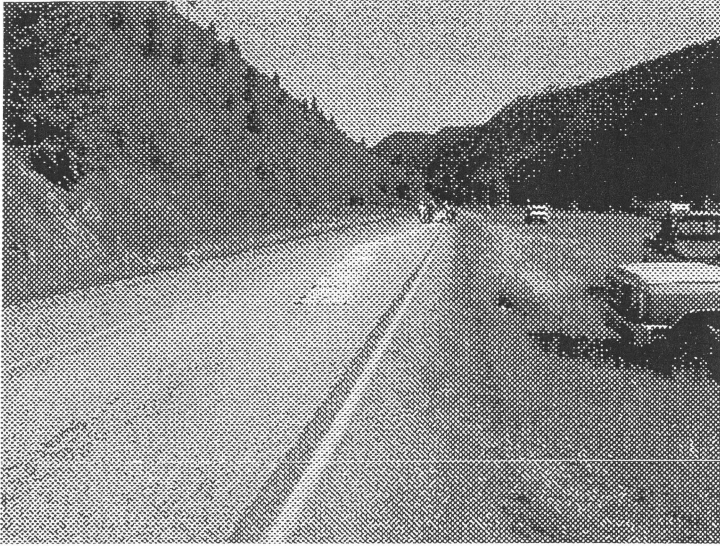


Avery Landing CAP 008.JPG
09/27/2000

Liner being rolled out on hwy to be unfolded and rolled back up on a long steel bar

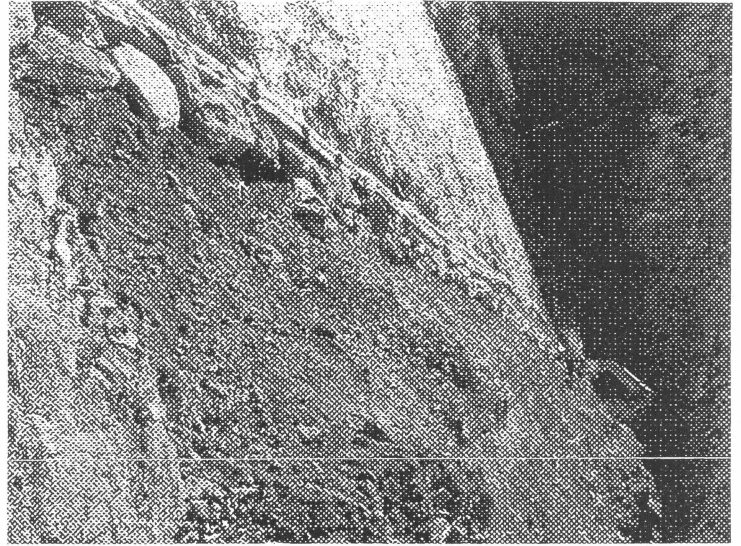


Avery Landing CAP 009.JPG
09/27/2000

Viewing downriver from E end of site. Liner and rip rap have already been installed in this area

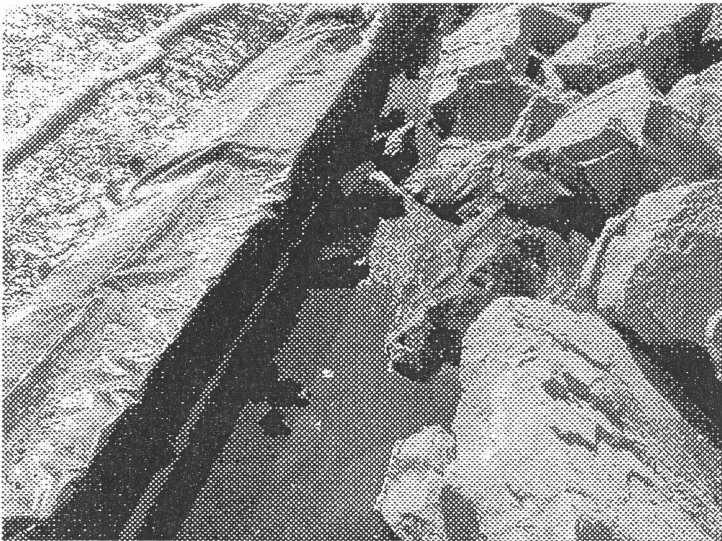

Avery Landing CAP 010.JPG
09/27/2000

Small area of petroleum scum forming behind coffer dam, about 1/3 of the way downstream from E end of site

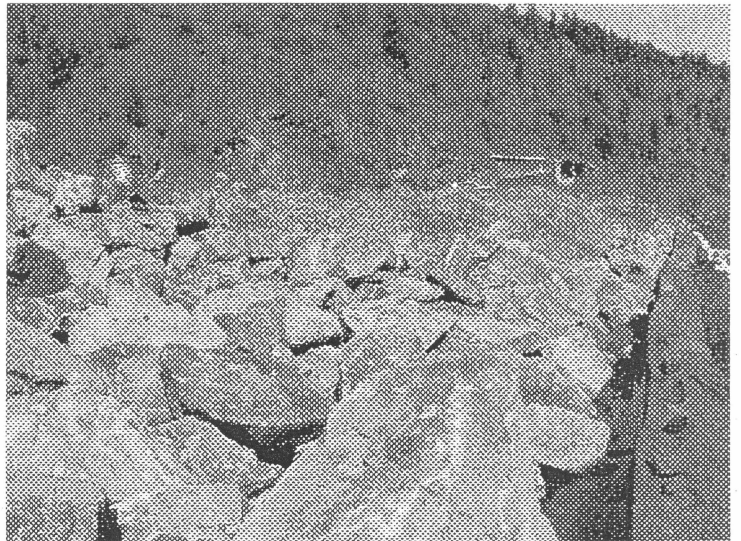


Avery Landing CAP 011.JPG
09/27/2000


Viewing upriver over eastern third of remediated stream bank. Photo shows smaller rock being overlayed by larger




Avery Landing CAP_012.JPG
09/27/2000
Photo of top layer of geofabric at toe of bank

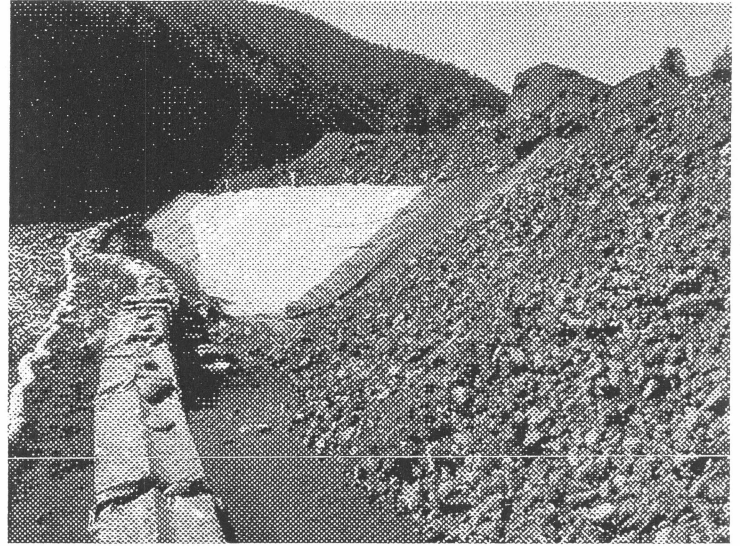


Avery Landing CAP_013.JPG
09/27/2000
Viewing downstream thru center portion of site. Photo shows the geofabric, liner, and rock cover

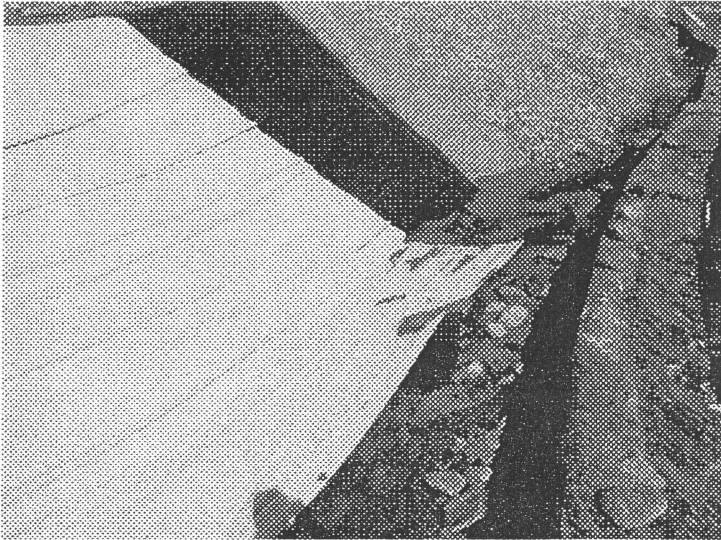


Avery Landing CAP_014.JPG
09/27/2000
Upstream view of same area as previous photo

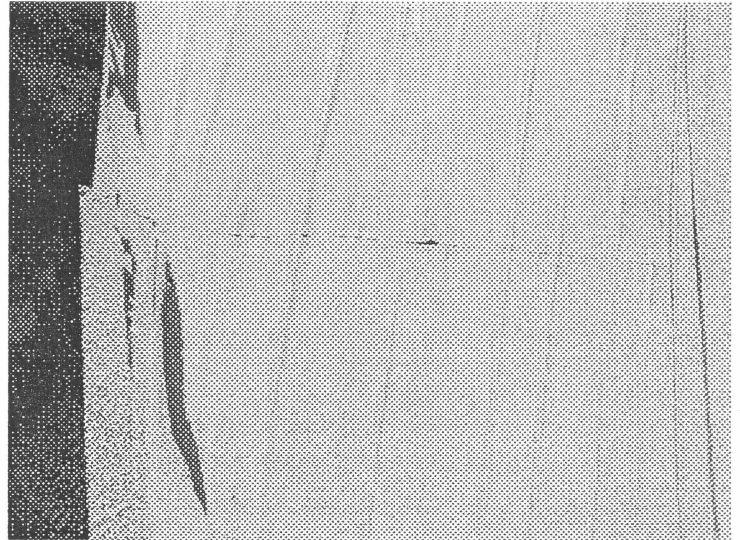


Avery Landing CAP_015.JPG
09/27/2000
Photo of a manufactured seam in the liner

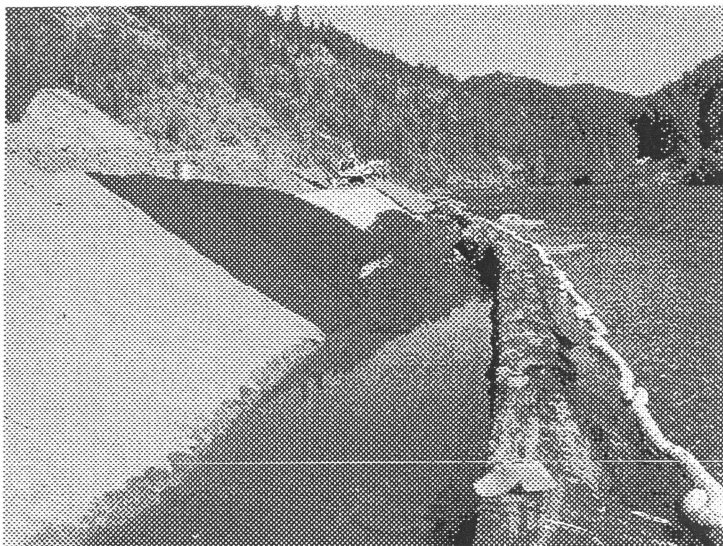


Avery Landing CAP 016.JPG
09/27/2000
Viewing upstream over eastern half of site

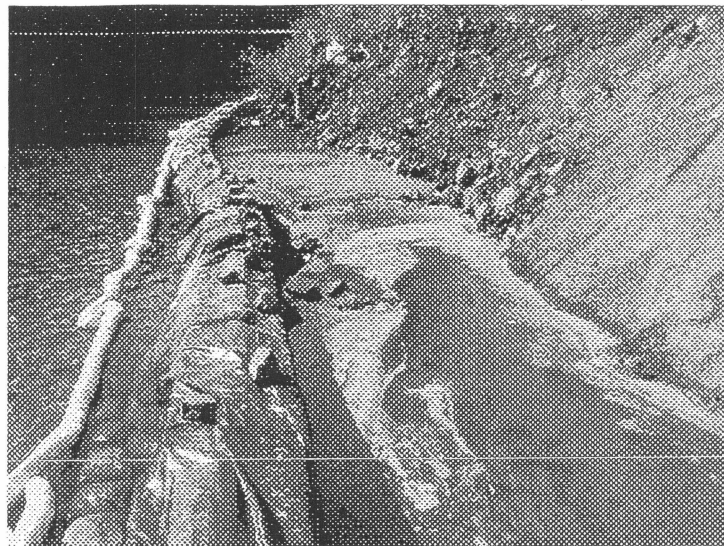


Avery Landing CAP 017.JPG
09/27/2000
Photo of petroleum scum buildup on extreme W end of site

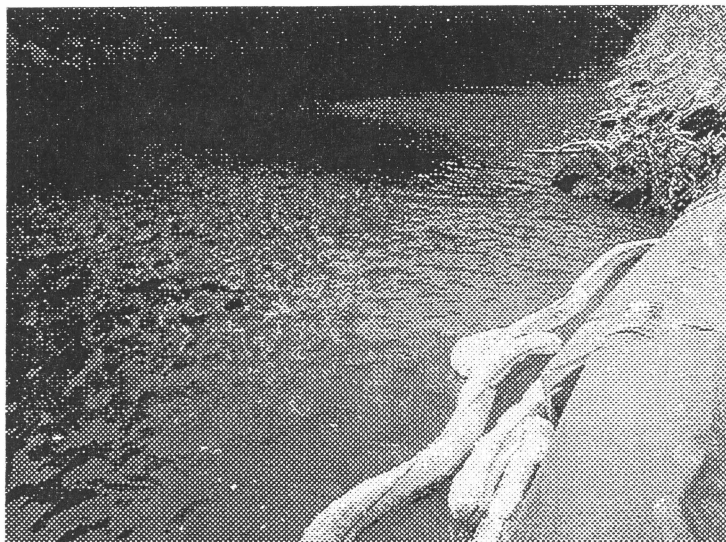

Avery Landing CAP 018.JPG
09/27/2000
Photo of river side of coffer dam at W end of site. Some silt but no petroleum was escaping past the dam

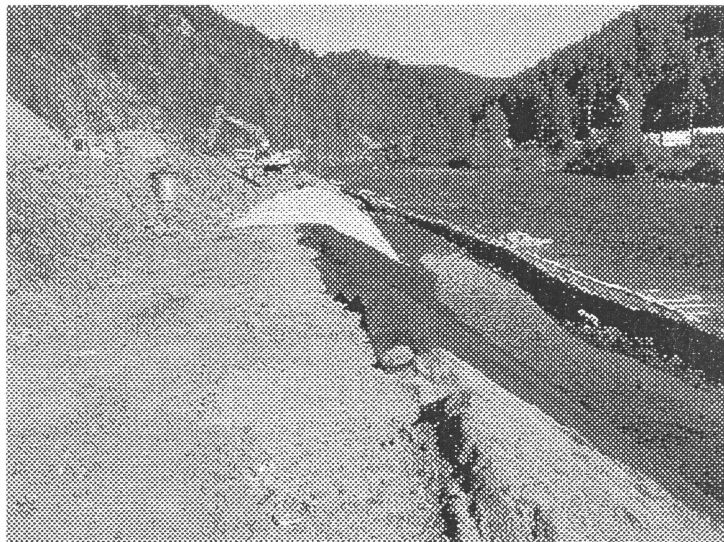


Avery Landing CAP 019.JPG
09/27/2000
Photo showing how geofabric is draped over top of slope

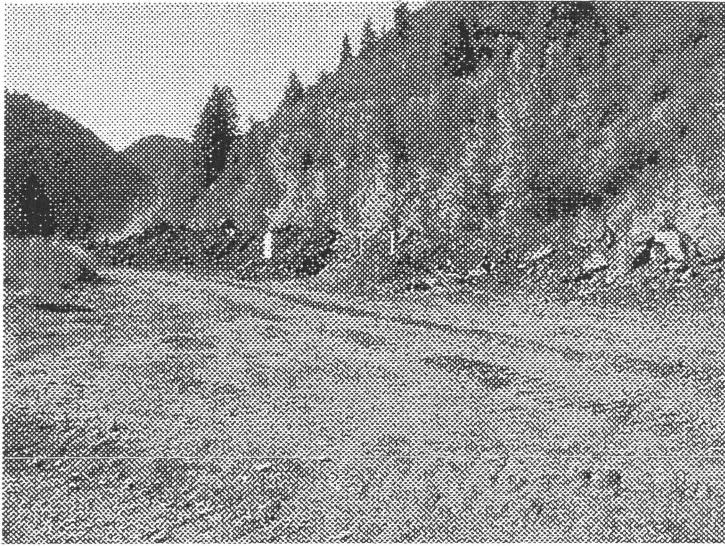


Avery Landing CAP 020.JPG
09/27/2000

Viewing E over a pile of rock and soil that was excavated and stockpiled along the hwy

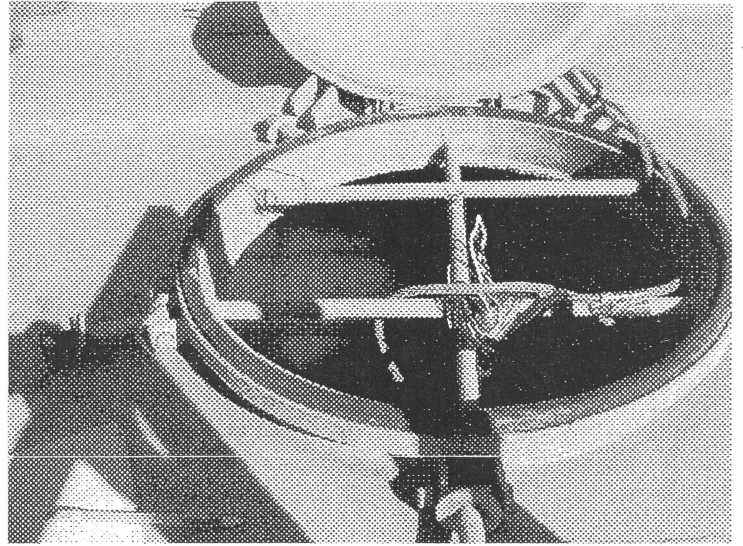


Avery Landing CAP 021.JPG
09/27/2000

Top entrance to O/W separator. Although not evident, tank was nearly full; very little petroleum film on top of water

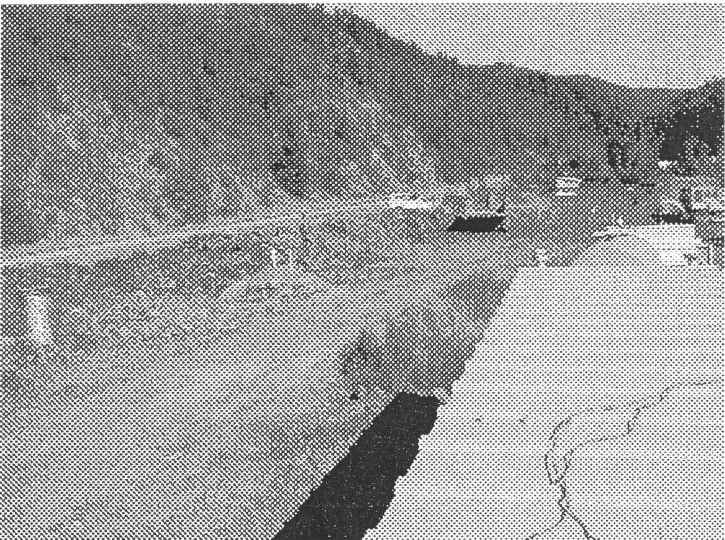


Avery Landing CAP 022.JPG
09/27/2000

Viewing E across stockpiled soils on N end of site

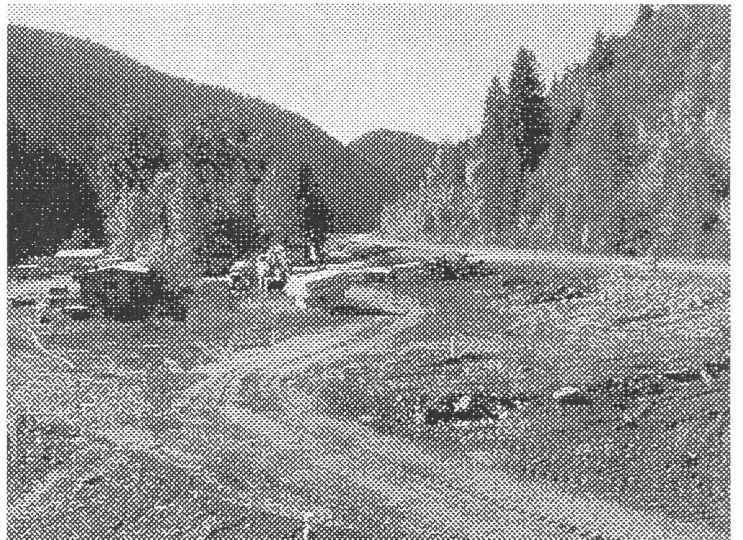

Avery Landing CAP 023.JPG
09/27/2000

Viewing W across W end of site. Crew working on liner, on hwy, in background

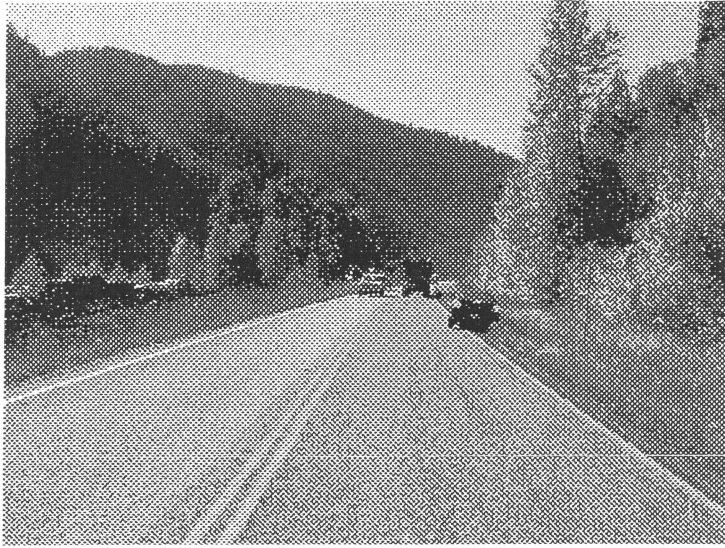


Avery Landing CAP 024.JPG
09/27/2000

Photo of re-rolled liner being brought back to site




Avery Landing CAP 025.JPG
09/27/2000

Photo showing how liner has been rolled onto long bar then is suspended to be pulled out along the bank

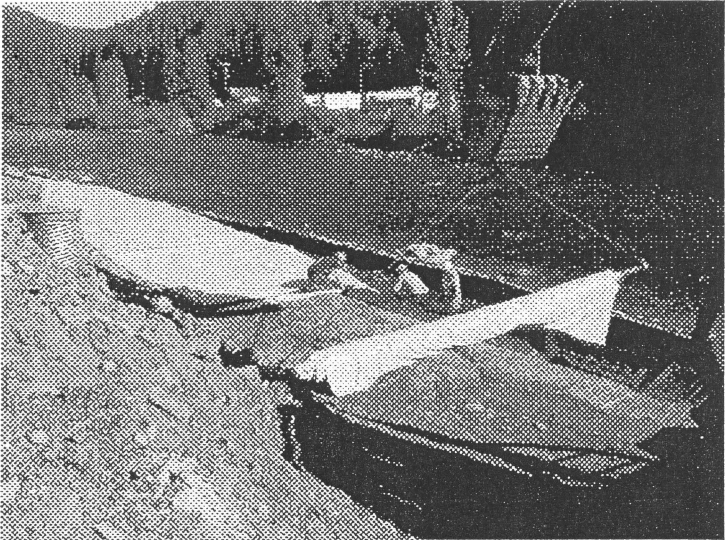


Avery Landing CAP 026.JPG
09/27/2000

Photo showing roll of liner positioned over band. Rock "barb" in background

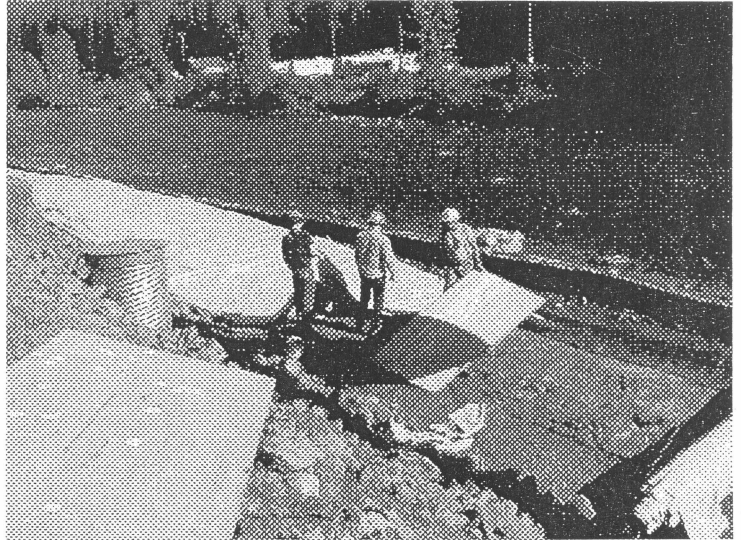


Avery Landing CAP 027.JPG
09/27/2000

Workers preparing to splice the 2, 400' rolls of liner. Wooden platform in bg shows how low river is

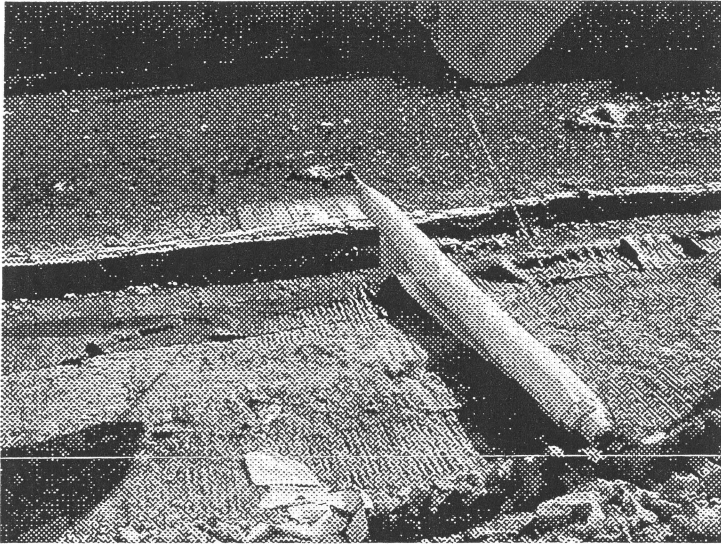

Avery Landing CAP 028.JPG
09/27/2000
Same as previous photo

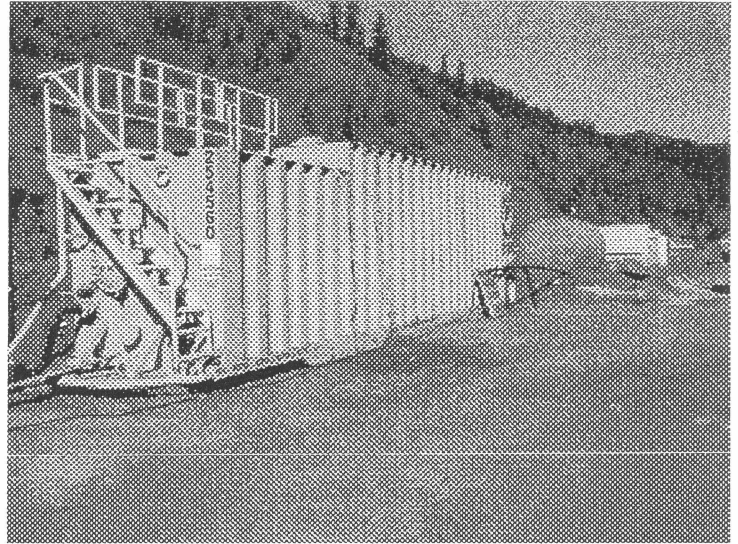

Avery Landing CAP 029.JPG
09/27/2000
O/W separator "overtopping". Workers turned on river pump but didn't turn on pump that delivers water to infil. tre
