



## **Pier Surveys and Removal**


Hunters Point Naval Shipyard BRAC Cleanup Team Meeting

April 26, 2011



### **Map of Work Areas**



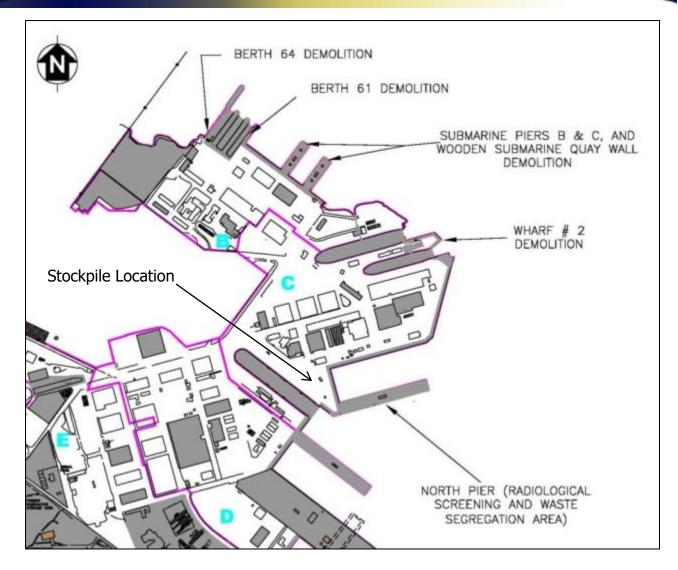



### **Scope of Work and Status Update**



#### ✓ Planning

Workplan – Final Pier Demolition Work Plan

#### ✓ Pre-Demolition Activities

- Pre-Demolition Surveys complete
- Equipment Mobilization

#### Pier Demolition Activities

Demolition and Radiological Screening Activities

#### Post-Demolition Activities

- Post-Demolition Surveys
- Equipment Decontamination (if necessary)
- Removal Action Completion Report (RACR) Preparation



## Field Activities: Monitoring & BMPs



#### Water quality monitoring:





#### **Debris control:**



Dust control

(@ North Pier material staging):





# Field Activities: Sub Piers B & C Demo Activities Update



#### **Submarine Pier B**






#### **Submarine Pier C**





## Field Activities: Sub Piers B & C Demo Activities Update



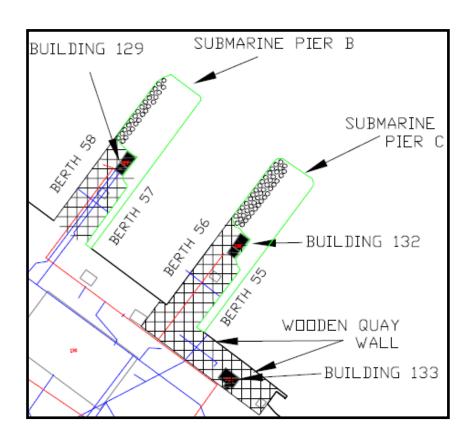

#### As of 4/15/2011:

- Sub Pier B
  - Approx demo qty:
     16,000 ft<sup>2</sup> (~ 40% complete)
- Sub Pier C
  - Approx demo qty:
     16,000 ft<sup>2</sup> (~ 27% complete)
- Notifications
  - BAAQ 4/11/2011



## **North Pier Debris Processing**













### **Project Schedule**



Mobilization: Week of March 14th

• **Demolition Activities Start:** Week of March 21st

Anticipated De-mobilization: September 2011

Project Completion: February 2012 – Final Report
