



# Parcel G Remedial Action Update

Hunters Point Naval Shipyard  
BCT Meeting  
January 24, 2013



# Overview










- Mobilized to the site January 4, 2013
- Upcoming field activities
- Overview of Project Milestones, including RACR preparation






# Site Location Map




- 
-  Parcel Boundary
  -  Parcel G Boundary
  -  Parcel F Boundary
  -  Building
  -  Non-Navy Property
  -  Road

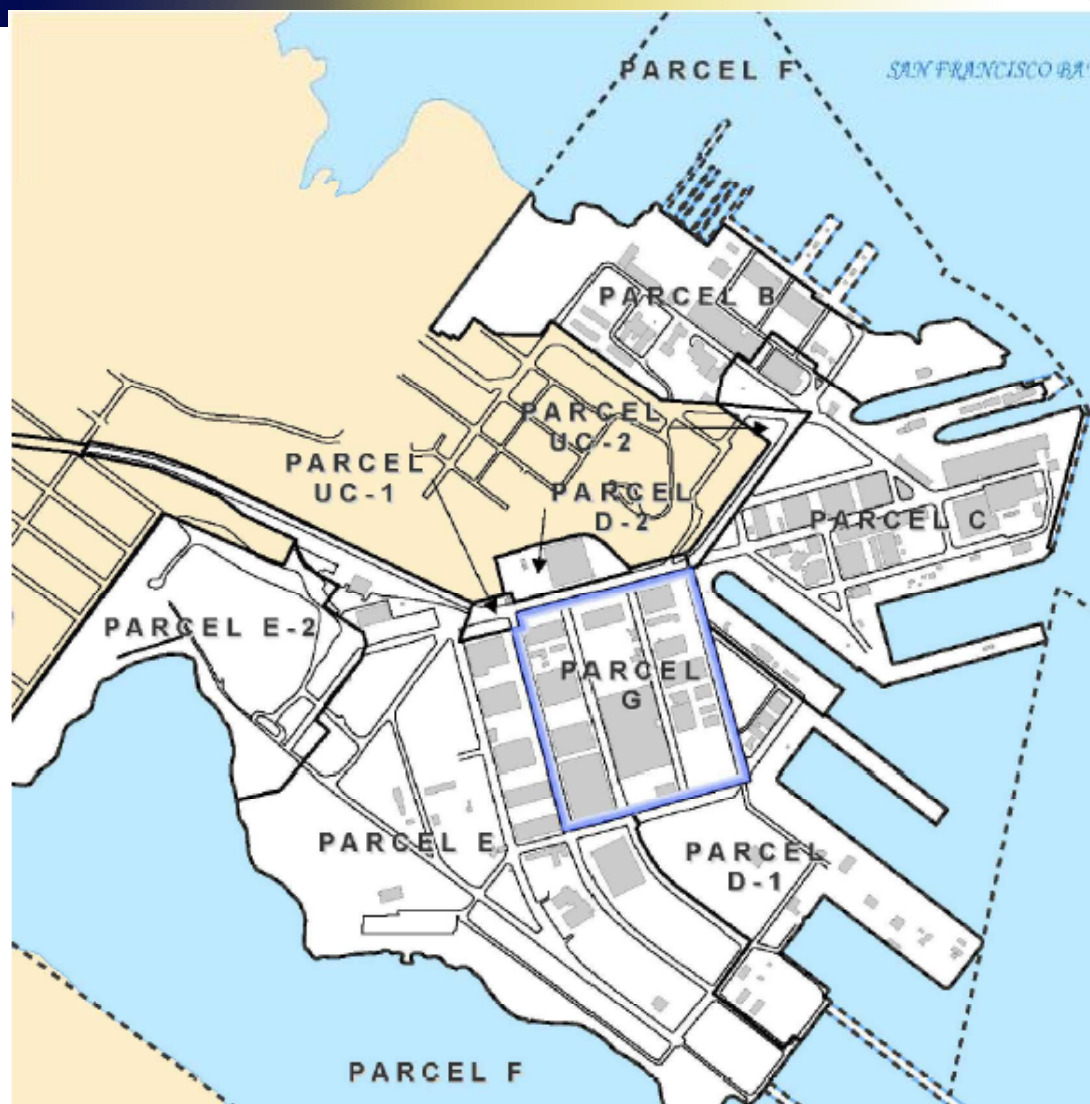



# Construction Schedule

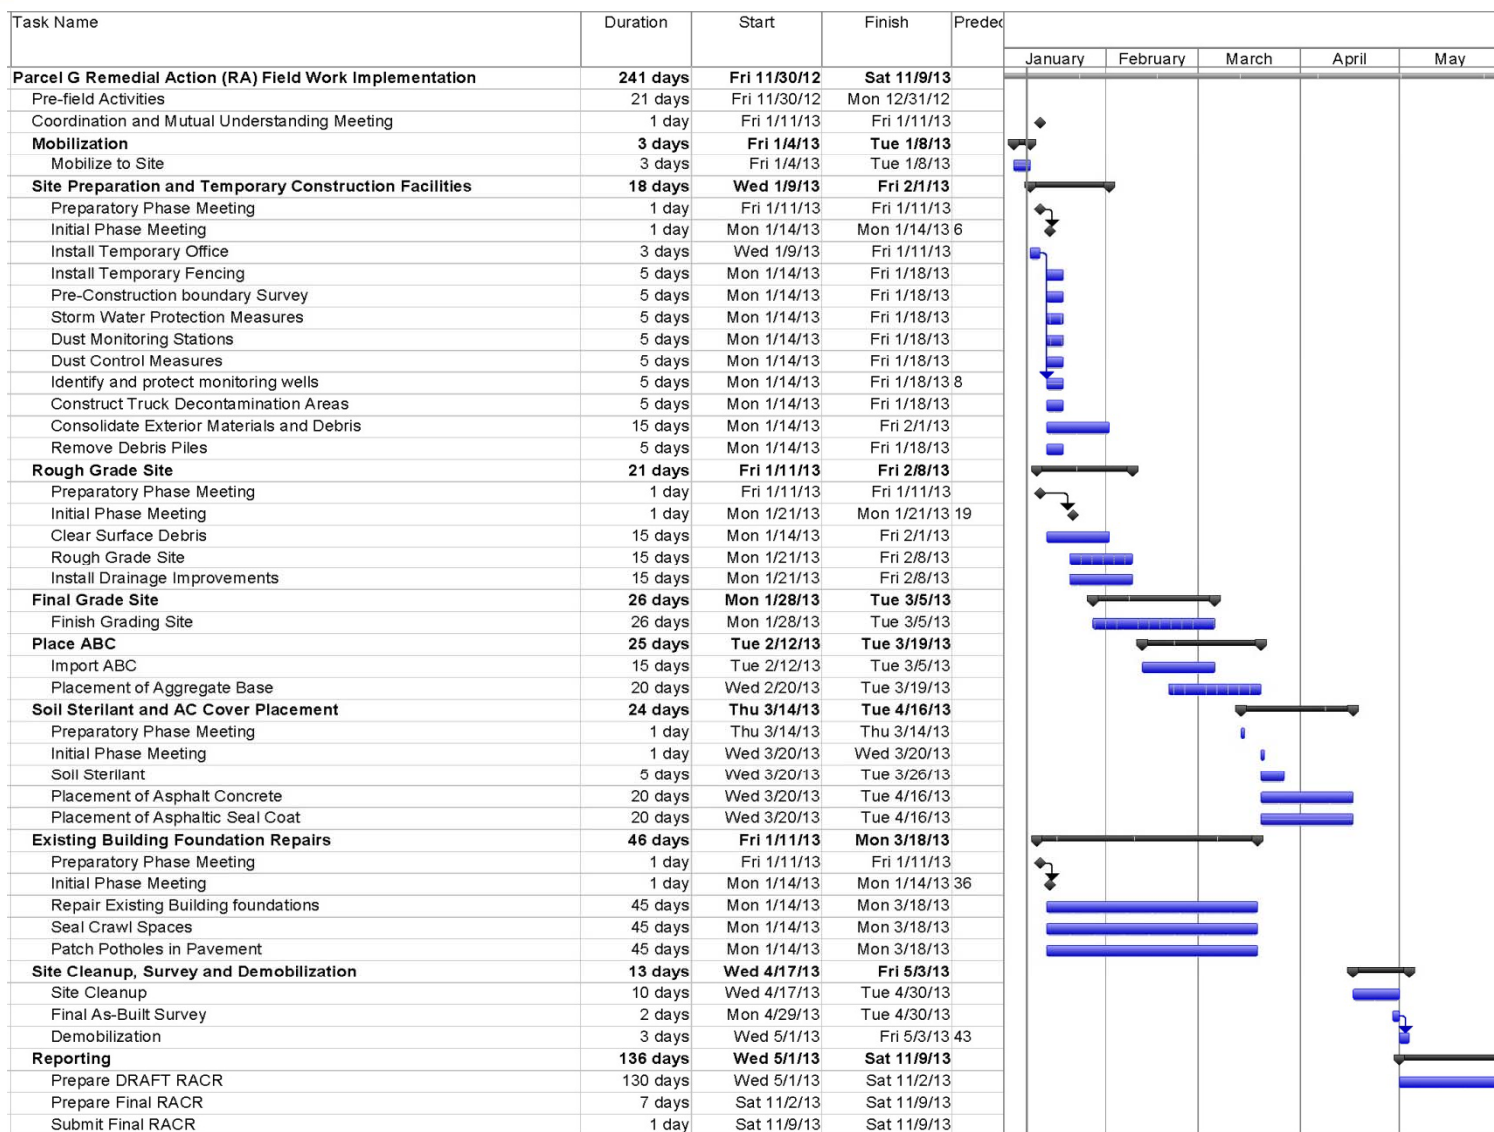



# Post Kick Off Meeting Site Walk



Hunters Point Naval Shipyard BCT Meeting, January 24, 2013





## Project Milestones



- Submit Final RAWP (completed) December 12, 2102
- Mobilization for Fieldwork (completed) January 4, 2013
- Construct Durable Cover (in progress) January-May 2013
- BCT review of Draft RACR July 22- Oct 7, 2013
- BCT review of DF RACR and RTC October 26, 2013
- Issue Final RACR November 28, 2013



## Hunters Point – Parcel G



# Questions?
