



Hunters Point Naval Shipyard



Parcel G Remedial Action Update Durable Cover Construction


BCT Meeting

May 29, 2013

05/13/2013




Agenda



- **Construction Progress Update**
 - Rough Grading
 - Aggregate Base Import and Placement
 - Finish Grading and Compaction
 - Laying Asphalt Pavement
 - Exterior Durable Cover Construction
 - Building Foundation Repairs
- **Work Remaining**
- **Schedule**




Project Location

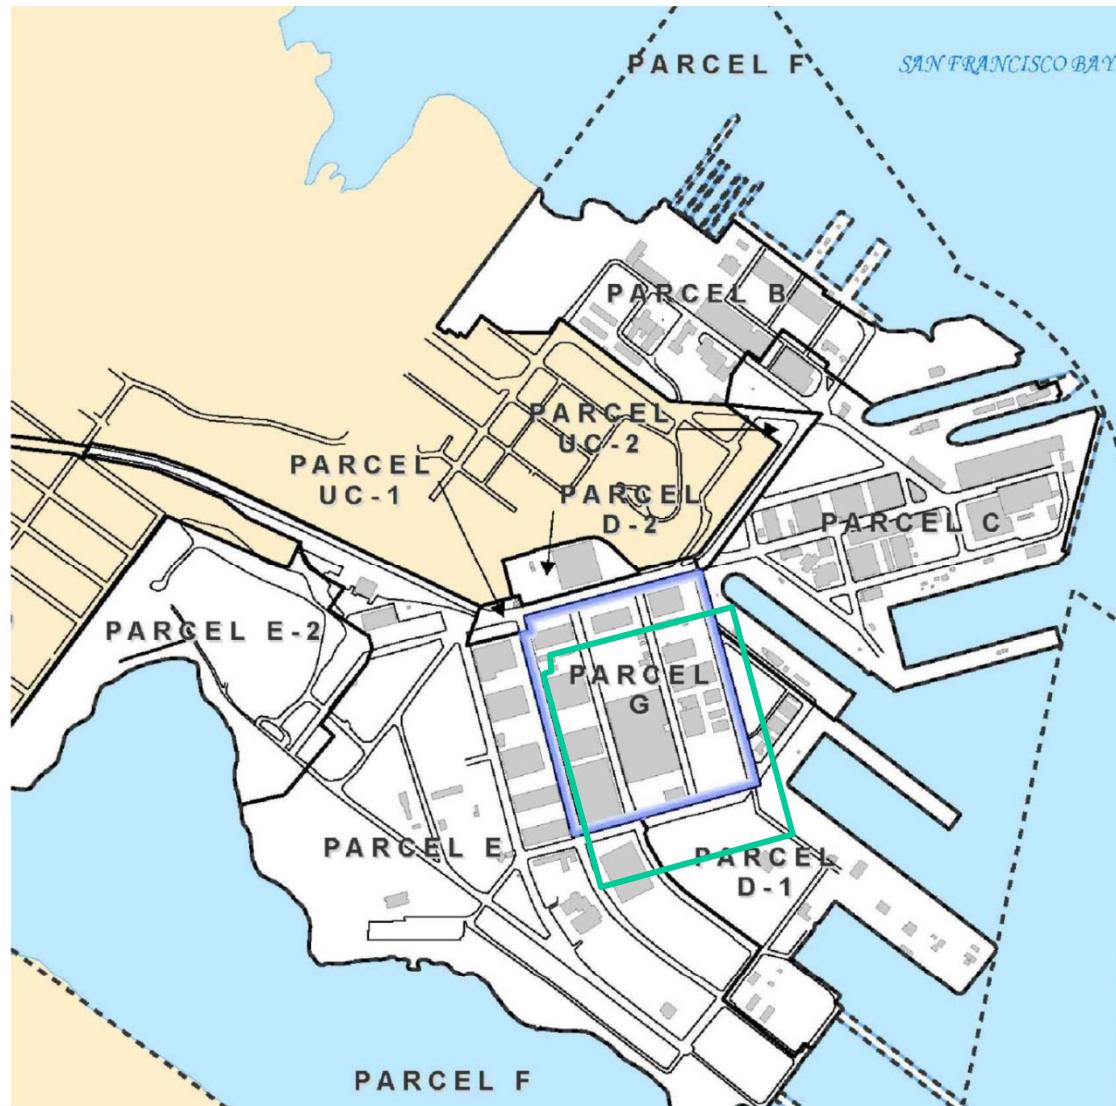



Project Site and Scope

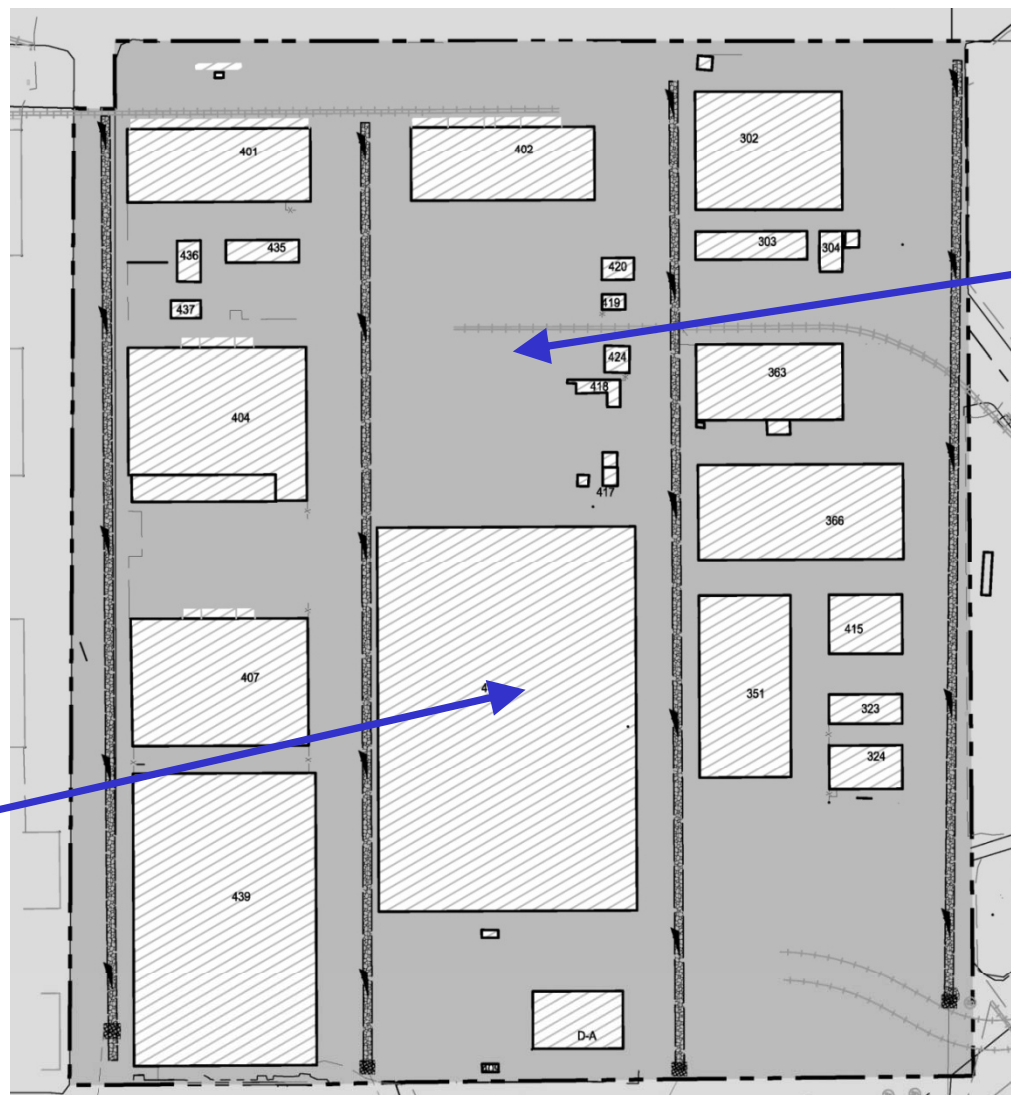


**Completed
Durable Cover
outside
buildings
(Gray areas)**

**Repaired
Concrete
Building Slabs
(White areas)**




Rough Grading






Delivery of Aggregate Base





Aggregate Base






Finish Grading






Finish Grading and Compaction





Compacting Swales






Asphalt Cover Placement






Asphalt Compaction Testing






Asphalt Placement and Compaction





Asphalt Placement and Compaction





Completed Asphalt Cover Placement






Drainage Improvements





Drainage Improvements






Building Slab Repair






Building Slab Repair






Remaining Work to be Completed



- Complete asphalt paving
- Complete drainage improvements
- Complete building slab repairs
- Raise monitoring wells
- Prepare Remedial Action Closure Report
- Perform quarterly inspections and repairs



Schedule



- Mobilize and set up Temp Facilities January 2013
- Site Preparation and Debris Removal Jan-Apr 2013
- Building foundation repairs Feb-Apr 2013
- Rough grading Feb-Apr 2013
- Drainage improvements Mar-May 2013
- AB placement and Finish Grading Apr-May 2013
- Asphalt placement May-Jun 2013
- Quarterly O&M from Jun 2013 until transfer
- Draft RACR Aug 2013
- Final RACR Nov 2013
