

**U.S. Department of Transportation
Research and Special Programs Administration
John A. Volpe National Transportation Systems Center**

2003 JAN 23 PH 2:33

EPA REGION VIII
SUPERFUND BRANCH

PROGRESS REPORT IAG #DW69953792-01

**U.S. Environmental Protection Agency Region VIII
Environmental Compliance & Restoration Support**

Prepared by:

**John A. Volpe National Transportation Systems Center
Environmental Engineering Division, DTS-33
55 Broadway, Kendall Square
Cambridge, MA 02142-1093**

Prepared for:

**U.S. Environmental Protection Agency
Ecosystems Protection & Remediation
999 18th Street, Suite 500
Denver, CO 80202-2466**

January 17, 2002

PROGRESS REPORT
Environmental Compliance & Restoration Support

Libby, Montana Asbestos Project (N-2428, N-2079, N-2423)

A. Work Performed December 1-31, 2002

The following activities were completed during the December reporting period:

- Winterized the Screening Plant site
- Completed footbridges across Rainy Creek. Need to complete stairs for access
- Continued procuring services for various contracts
- Continued Millworks West site improvement work
- Continued to conduct investigative and sampling activities as requested by the OSCs
- Conducted remedial pre-design and design activities
- Continued to import and backfill clean agricultural fill at the Screening Plant
- Continued Millworks West site improvement work on Building 2
- Continued dust and air sampling at residential removal sites
- Communicated daily with OSCs, RPM and storefront regarding project status and needs
- Conducted bi-weekly schedule teleconferences with contractors
- Conducted community relations duties for removal actions
- Completed residential removal/restoration activities at the Beaulieu home
- Produced database queries and adhoc reports as requested by OSCs
- Performed database administration and system administration activities
- Entered and validated Field Sample information
- Entered analytical results
- Entered Chain-of-Custody information
- Entered IFF information
- Produced the Status report of samples and results in the database
- Reviewed and updated incorrect data in the database
- Continue to work with SRC as needed
- Updated the project schedule and database schema
- Completed the changes to the Data Entry application for the GIS/Location changes
- Completed the modifications to the Reports module to work with the GIS/Location database changes
- Continued coordination of analytical activities and weekly laboratory telecons
- Continued coordination of analytical activities and weekly laboratory telecons
- Worked with laboratories to clarify / verify various issues regarding reported results
- Continued analysis of USGS provided ISTM2 samples via various analytical methods, including SEM, TEM (2 methods), and PLM (3 methods)
- Analyzed EMSL prepared "Brown Soil Standards" via PLM using multiple Libby Team laboratories
- Coordinated with and conducted/participated in a Technical Issues meeting in Denver to review ISTM2 results, analytical methods and procedures, and sample preparation procedures

- Worked with CDM, EPA and laboratories to document modifications and clarifications to a variety of analytical operating procedures
- Worked with EPA to prepare various data-related court exhibits
- Continued oversight of residential removal activities
- Met with RPM to discuss project status, budget and future plans
- Participated and coordinate with EPA a Technical Issues meeting in Denver
- Provided documents to WR Grace in support of litigation activities, as required
- Conducted administrative and accounting activities
- Conducted contract and project management activities

B. Work Planned for January 1-31, 2003

The following activities are planned for the January reporting period:

- Provide documents to WR Grace in support of litigation activities, as required
- Conduct administrative and accounting activities
- Conduct contract and project management activities
- Continue oversight of residential removal activities
- Continue procuring services for various contracts
- Complete Millworks West site improvement work on Building 2
- Continue to conduct investigative and sampling activities as requested by the OSCs
- Continue dust and air sampling at residential removal sites
- Communicate daily with OSCs, RPM and storefront regarding project status and needs
- Complete residential restoration activities at the Beaulieu home
- Continue oversight of removal/restoration activities by EPA's contractor ER
- Conducted remedial pre-design and design activities
- Continue database queries and adhoc reports as requested by OSCs
- Continue database administration and system administration activities
- Continue to enter and validate Field Sample information
- Continue to enter analytical results
- Continue to enter Chain-of-Custody information
- Continue to enter IFF information
- Continue to load GIS information
- Produce Status report of samples and results in the database
- Continue to review and correct incorrect data in the database
- Prepare for the database meeting
- Continue to work with SRC as needed
- Update the project schedule
- Work with the Libby team to install the Report Module
- Continue coordination of laboratory support activities, including weekly telecons
- Assist EPA in the cost recovery trial with W.R. Grace
- Travel to Denver to meet with RPM to complete budget report planning, discuss contract actions and remedial technical activities
- Continue coordination of laboratory support activities, including weekly telecons

- Work with EPA and others on a variety of action items resulting from the December Denver Technical Issues Meeting, including follow-up test analysis, modifications to analytical SOPs, EDDs, and sample preparation procedures

C. Last Period's Outstanding Issues/Discussion Items

D. Current Period's Outstanding Issues/Discussion Items

E. Schedules (see Attachment 1)

F. Cost Summary (see Attachment 2)

Aspen Park Solvents Project (N-2332)

A. Work Performed December 1-30, 2002

The following activities were completed during the December reporting period:

- Conducted as needed maintenance activities.

B. Work Planned for January 1-31, 2002

The following activities are planned for the January reporting period:

- Conduct as needed maintenance activities.
- Specifically repairs to the water treatment system at the residence of Ken Gerbrendt will be made.

C. Last Period's Outstanding Issues/Discussion Items

- It was necessary to modify the contract so MWH will provide payment for the rental of the source removal system building.
- It was necessary to extend the period of performance from 9/12/02 - 1/31/03 to 2/1/03 - 3/12/03.
- It was necessary to fully fund TO 0005

D. Current Period's Outstanding Issues/Discussion Items

- It is necessary to begin future budgeting as current funds are running out
- The contractor has expressed some concern that the residential water treatment systems are reaching the age where many of systems will need to be serviced.

E. Cost Summary (see Attachment 2)

Libby Sister Sites (N-2097, N-2094, N-2088)

A. Work Performed December 1-31, 2002

The following activities were completed during the December reporting period at the former Intermountain Insulation Plant (Salt Lake City, UT):

- Finalizing a complete written Site Investigation Report describing activities and illustrating sample locations and results on GIS.
- Volpe and EPA are developing a plan for the Scope of Work for activities to be performed at SLC1 and SLC2 during the spring construction season.

No activities were completed during the December reporting period at the former Robinson Insulation Plant (Minot, ND).

No activities were completed during the December reporting period at the former Western Minerals (Denver, CO).

A. Work Planned for January 1-31, 2003

The following activities are planned for the January reporting period at the former Intermountain Insulation Plant (Salt Lake City, UT):

- Coordinate with EPA the scope of work to be performed during the Spring construction season.
- Provide preliminary cost data for soil and air sampling efforts
- Provide a completed written Site Investigation Report describing activities and illustrating sample locations and results on GIS.

The following activities are planned for the January reporting period at the former Western Minerals (Denver, CO):

- Discuss air/soil sampling efforts required during removals occurring March/April period

Libby Asbestos Site – RI/FS (N-2211)

A. Work Performed December 1-31, 2002

The following activities were completed during the December reporting period:

- Continued activities on the CSS (data analysis)
- Coordinated with RPM and CDM Fed regarding ongoing RI/FS Plans
- Prepared Scope of Work, Cost Estimate, and RFP to conduct RI analytical tasks
- Conducted PE tasks for CSS specific analytical methods

B. Work Planned for January 1-31, 2003

The following activities are planned for the January reporting period:

- Continue CSS data analysis tasks
- Begin development of plan for remedial action activities

C. Last Period's Outstanding Issues/Discussion Items

D. Current Period's Outstanding Issues/Discussion Items

E. Cost Summary (see Attachment 2)

**ATTACHMENT 1
(SCHEDULES)**

Removal Action Schedule

ID	Task Name	Removal Action Schedule																
		Start	Finish	% Complete	J	F	M	A	M	J	J	A	S	O	N	D	J	2001
1	LIBBY ASBESTOS PROJECT - REMOVAL ACTION	Tue 1/2/01	Mon 6/2/03	83%														
2	Removal 00 Documentation Close-out	Tue 1/2/01	Tue 3/6/01	100%														
6	Removal 01 Planning & Engineering	Tue 1/2/01	Tue 5/15/01	100%														
12	Screening Plant	Mon 3/4/02	Sat 5/31/03	96%														
13	Remove Winter Erosion Control Measures	Mon 6/17/02	Sat 6/22/02	100%														
14	North Side Agricultural Fill	Sat 6/1/02	Mon 7/29/02	100%														
17	Import and Backfill Agricultural Fill	Tue 7/9/02	Fri 11/22/02	100%														
18	Import and Backfill Clean Agricultural Fill	Tue 7/9/02	Fri 11/22/02	100%														
19	Final Grading	Tue 10/15/02	Fri 11/22/02	100%														
20	Rip/Till Soil on the N & South Sides	Mon 12/2/02	Sat 12/7/02	0%														
21	Road Construction	Mon 9/9/02	Sat 12/7/02	100%														
22	Import Structural Fill	Mon 9/9/02	Wed 9/18/02	100%														
23	Move Structural Fill to Flyway	Tue 10/29/02	Wed 11/6/02	100%														
24	Construct Roads	Mon 1/1/02	Sat 12/7/02	100%														
25	Install Culverts under roads	Mon 10/21/02	Fri 11/22/02	100%														
26	Screening Plant Utilities	Mon 9/23/02	Tue 12/3/02	98%														
27	Install Waterlines	Mon 9/23/02	Wed 11/13/02	100%														
28	Install Septic Tanks	Mon 12/2/02	Tue 12/3/02	0%														
29	Run Underground Electrical Lines	Mon 10/14/02	Wed 11/20/02	100%														
30	Install Pumps at River	Wed 11/13/02	Fri 11/15/02	100%														
31	Test Existing Well and Pump	Wed 10/2/02	Thu 10/10/02	100%														
32	Install Sprinklers	Sat 10/15/02	Fri 10/11/02	100%														
33	Install Frost-free Faucet	Sat 10/12/02	Sat 10/12/02	100%														
34	Rainy Creek and Riverbank Restoration Design	Mon 3/4/02	Tue 9/24/02	100%														
37	Rainy Creek	Mon 9/23/02	Sat 5/31/03	91%														
38	Reconstruct Creek Banks, Step Pools	Mon 9/23/02	Thu 10/24/02	100%														
39	Construct and install pedestrian foot bridges across creek	Wed 10/30/02	Sat 5/31/03	90%														
40	Revegetate Rainy Creek	Thu 5/1/03	Thu 5/1/03	0%														
41	Riverbanks	Wed 9/4/02	Thu 5/1/03	99%														
42	Finalize rip rap placement along riverbanks	Wed 9/4/02	Wed 9/4/02	100%														
43	Remove Material Near House Foundations	Mon 9/30/02	Wed 10/2/02	100%														
44	Reconstruct Riverbanks	Mon 10/28/02	Sat 11/9/02	100%														
45	Revegetate Riverbanks	Thu 5/1/03	Thu 5/1/03	0%														
46	Construct and Install Fishing Dock	Thu 5/1/03	Thu 5/1/03	100%														
47	Riverbank near Guest House on N. Side of Property	Mon 11/18/02	Fri 11/22/02	100%														
48	Screening Plant Final Restoration	Mon 9/30/02	Sat 5/31/03	91%														

Project: Removal Action
Status: as of November 30, 2002
Date: Fri 1/17/03Task Progress Milestone Summary

Removal Action Schedule

ID	Task Name	Removal Action Schedule															
		2001					2002										
		Start	Finish	% Complete	J	F	M	A	M	J	J	A	S	O	N	D	J
49	Construct Stairways	Mon 9/30/02	Wed 11/13/02	100%													
50	Import Clean Topsoil	Thu 5/1/03	Thu 5/1/03	100%													
51	Hydro Seeding	Thu 5/1/03	Thu 5/1/03	0%													
52	Fencing and Gates	Tue 12/3/02	Sat 5/3/03	90%													
53	Plant Trees	Thu 5/1/03	Thu 5/1/03	0%													
54	Site Winterization	Mon 12/2/02	Fri 12/20/02	100%													
55	Spread Straw on South Side	Mon 12/2/02	Fri 12/20/02	100%													
56	Spread Straw on Rainy Creek Banks	Mon 12/9/02	Wed 12/11/02	100%													
57	Spread Straw on Riverbanks	Thu 12/12/02	Mon 12/16/02	100%													
58	Demobilize	Tue 12/17/02	Fri 12/20/02	100%													
59	Millworks West	Wed 9/26/02	Thu 5/1/03	42%													
60	Clean New Planer Building	Wed 9/26/02	Tue 10/8/02	100%													
61	Clean Old Planer Building and Equipment	Wed 10/9/02	Tue 10/22/02	100%													
62	Building 1 (Asphalt)	Mon 11/4/02	Thu 5/1/03	0%													
65	Building 2 (Concrete)	Wed 9/26/02	Fri 1/10/03	97%													
66	Move Contents (Owner)	Wed 9/26/02	Thu 9/26/02	100%													
67	Excavate Subgrade	Fri 9/27/02	Sat 10/5/02	100%													
68	Plumbing	Tue 10/1/02	Mon 11/18/02	100%													
69	Electrical	Tue 10/1/02	Tue 12/31/02	100%													
70	Place Subgrade	Tue 10/6/02	Wed 10/9/02	100%													
71	Form and Pour 1-2	Tue 10/22/02	Sat 10/26/02	100%													
72	Build Bathroom	Mon 10/28/02	Fri 1/10/03	90%													
73	Install Septic Tank	Wed 10/16/02	Wed 10/23/02	100%													
74	KDC Properties: Flyway	Tue 9/10/02	Tue 2/11/03	0%													
82	School/Public Properties	Tue 7/24/01	Mon 6/2/03	99%													
83	Balfield Equipment Room	Mon 6/10/02	Fri 6/14/02	100%													
88	High School Track	Tue 7/24/01	Mon 6/2/03	99%													
154	Middle School	Tue 8/14/01	Fri 9/27/02	100%													
187	Sleffie	Mon 6/4/01	Sat 9/14/02	97%													
188	Investigation	Mon 6/4/01	Thu 6/4/01	100%													
189	Planning	Thu 6/14/01	Mon 6/25/01	100%													
190	Inventory	Tue 7/10/01	Mon 10/1/01	100%													
194	Decontamination of Personal Property	Mon 8/13/01	Fri 9/14/01	100%													
195	Storage of Personal Items	Tue 8/14/01	Fri 9/14/01	100%													
196	Demolition of Structures	Mon 9/10/01	Mon 9/17/01	100%													
197	Removal of Contaminated Soils	Wed 9/26/01	Sat 9/29/01	100%													

Project: Removal Action

Status: as of November 30, 2002

Date: Fri 1/17/03

Page 2

Removal Action Schedule

ID	Task Name	Removal Action Schedule												2002														
		2001					2002							J	F	M	A	M	J	J	A	S	O	N	D			
		Start	Finish	% Complete	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D
198	Import and place fill	Mon 10/1/01	Sat 10/27/01	100%																								
199	Decontaminate Residence Interior	Mon 10/15/01	Thu 11/8/01	100%																								
200	Site Restoration	Fri 10/5/01	Sat 9/14/02	95%																								
201	Residential Removals	Mon 8/5/02	Fri 12/6/02	99%																								
202	First 6	Mon 8/5/02	Thu 10/17/02	100%																								
215	Head Start/Plummer Elementary School Removal	Tue 10/8/02	Thu 10/10/02	100%																								
216	Head Start/ Plummer Elementary School Restoration	Thu 10/10/02	Fri 10/11/02	100%																								
217	Libby Baseball/Softball Equipment	Mon 10/7/02	Thu 10/10/02	100%																								
218	Burshia Removal/Restoration	Thu 10/17/02	Fri 12/6/02	95%																								
219	Beaulieu Removal	Tue 11/12/02	Fri 12/6/02	99%																								

Project: Removal Action
Status: as of November 30, 2002
Date: Fri 11/7/03

Task Progress Milestone

Progress Milestone


Summary


Libby Schedule

ID	Market	Task Name	% Compl.	Duration	Start	Finish	2nd Half			1st Half			2nd Half									
							a Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	a Jun	Jul	Aug	Sep	Oct
1	No	Ongoing Support	56%	261 days	Tue 10/1/02	Tue 9/30/03																
2	No	Administrator System (ongoing)	26%	261 days	Tue 10/1/02	Tue 9/30/03																
3	No	Perform System Administration	26%	261 days	Tue 10/1/02	Tue 9/30/03																
4	No	Data Entry Support (ongoing)	26%	260 days	Tue 10/1/02	Tue 9/30/03																
5	No	Enter, Validate & File Field Sample Sheets	43%	261 days	Tue 10/1/02	Tue 9/30/03																
6	No	Load Lab Results	26%	261 days	Tue 10/1/02	Tue 9/30/03																
7	No	Enter & File COCs	26%	261 days	Tue 10/1/02	Tue 9/30/03																
8	No	Enter & File Survey Questionnaire	95%	261 days	Tue 10/1/02	Tue 9/30/03																
9	No	Query & Adhoc support (ongoing)	26%	261 days	Tue 10/1/02	Tue 9/30/03																
10	No	Biweekly Status Report	26%	261 days	Tue 10/1/02	Tue 9/30/03																
11	No	Queries on Demand	26%	261 days	Tue 10/1/02	Tue 9/30/03																
12	No	SRC Requirements (ongoing)	26%	261 days	Tue 10/1/02	Tue 9/30/03																
13	No	System Improvements	74%	261 days	Tue 10/1/02	Tue 9/30/03																
14	No	Update Defect List	26%	261 days	Tue 10/1/02	Tue 9/30/03																
15	No	Adhoc support as needed	26%	261 days	Tue 10/1/02	Tue 9/30/03																
16	No	Database changes	100%	10 days	Tue 10/1/02	Tue 9/30/03																
17	No	Data Entry Application	100%	261 days	Tue 10/1/02	Tue 9/30/03																
18	No	EDD Load	100%	261 days	Tue 10/1/02	Tue 9/30/03																
19	No	GIS Load	27%	261 days	Tue 10/1/02	Tue 9/30/03																
20	No	Test	80%	261 days	Tue 10/1/02	Tue 9/30/03																
21	No	Fix Bugs	0%	261 days	Tue 10/1/02	Tue 9/30/03																
22	No	Put into Production	0%	261 days	Tue 10/1/02	Tue 9/30/03																
23	No	Report Module	100%	261 days	Tue 10/1/02	Tue 9/30/03																
24	No	System Development	87%	364 days	Mon 6/30/02	Mon 10/27/03																
25	No	SEM	86%	279 days	Tue 10/1/02	Mon 10/27/03																
26	No	Requirements	90%	1 day	Tue 10/1/02	Tue 10/1/02																
27	No	DB and application changes for TEM version field	0%	10 days	Tue 10/1/02	Mon 10/14/02																
28	No	EDD Changes	90%	261 days	Tue 10/1/02	Tue 9/30/03																
29	No	Test	0%	1 day	Tue 9/30/03	Tue 9/30/03																
30	No	In Production	;	;	;	;																
31	No	QC Validation	72%	80 days	Mon 6/30/02	Mon 9/23/02																
32	No	QC Validation Requirements	95%	27 days	Mon 6/30/02	Tue 7/9/02																
33	No	Database Changes	90%	5 days	Mon 8/26/02	Fri 8/30/02																
34	No	Implement changes in production	90%	1 day	Mon 9/9/02	Mon 9/9/02																
35	No	QA/QC Load Program	0%	10 days	Tue 9/10/02	Mon 9/23/02																
36	No	GIS/Location Redesign	100%	46 days	Fri 9/27/02	Fri 11/29/02																
37	No	Report Module	100%	31 days	Mon 10/28/02	Mon 12/9/02																

Libby Schedule

ID	Marker	Task Name	% Compl.	Duration	Start	Finish	2nd Half				1st Half				2nd Half				
							a	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	e	Mar	Apr	a
58	No	Lab Job Query	20%	1 day	Tue 10/1/02	Tue 10/1/02													
59	✓	Requirements Doc	100%	1 day	Tue 10/1/02	Tue 10/1/02													
60	No	Code DataEntry	0%	1 day	Tue 10/1/02	Tue 10/1/02													
61	No	Test DateEntry	0%	1 day	Tue 10/1/02	Tue 10/1/02													
62	No	Bug Fixes	0%	1 day	Tue 10/1/02	Tue 10/1/02													
63	No	In Production	0%	1 day	Tue 10/1/02	Tue 10/1/02													

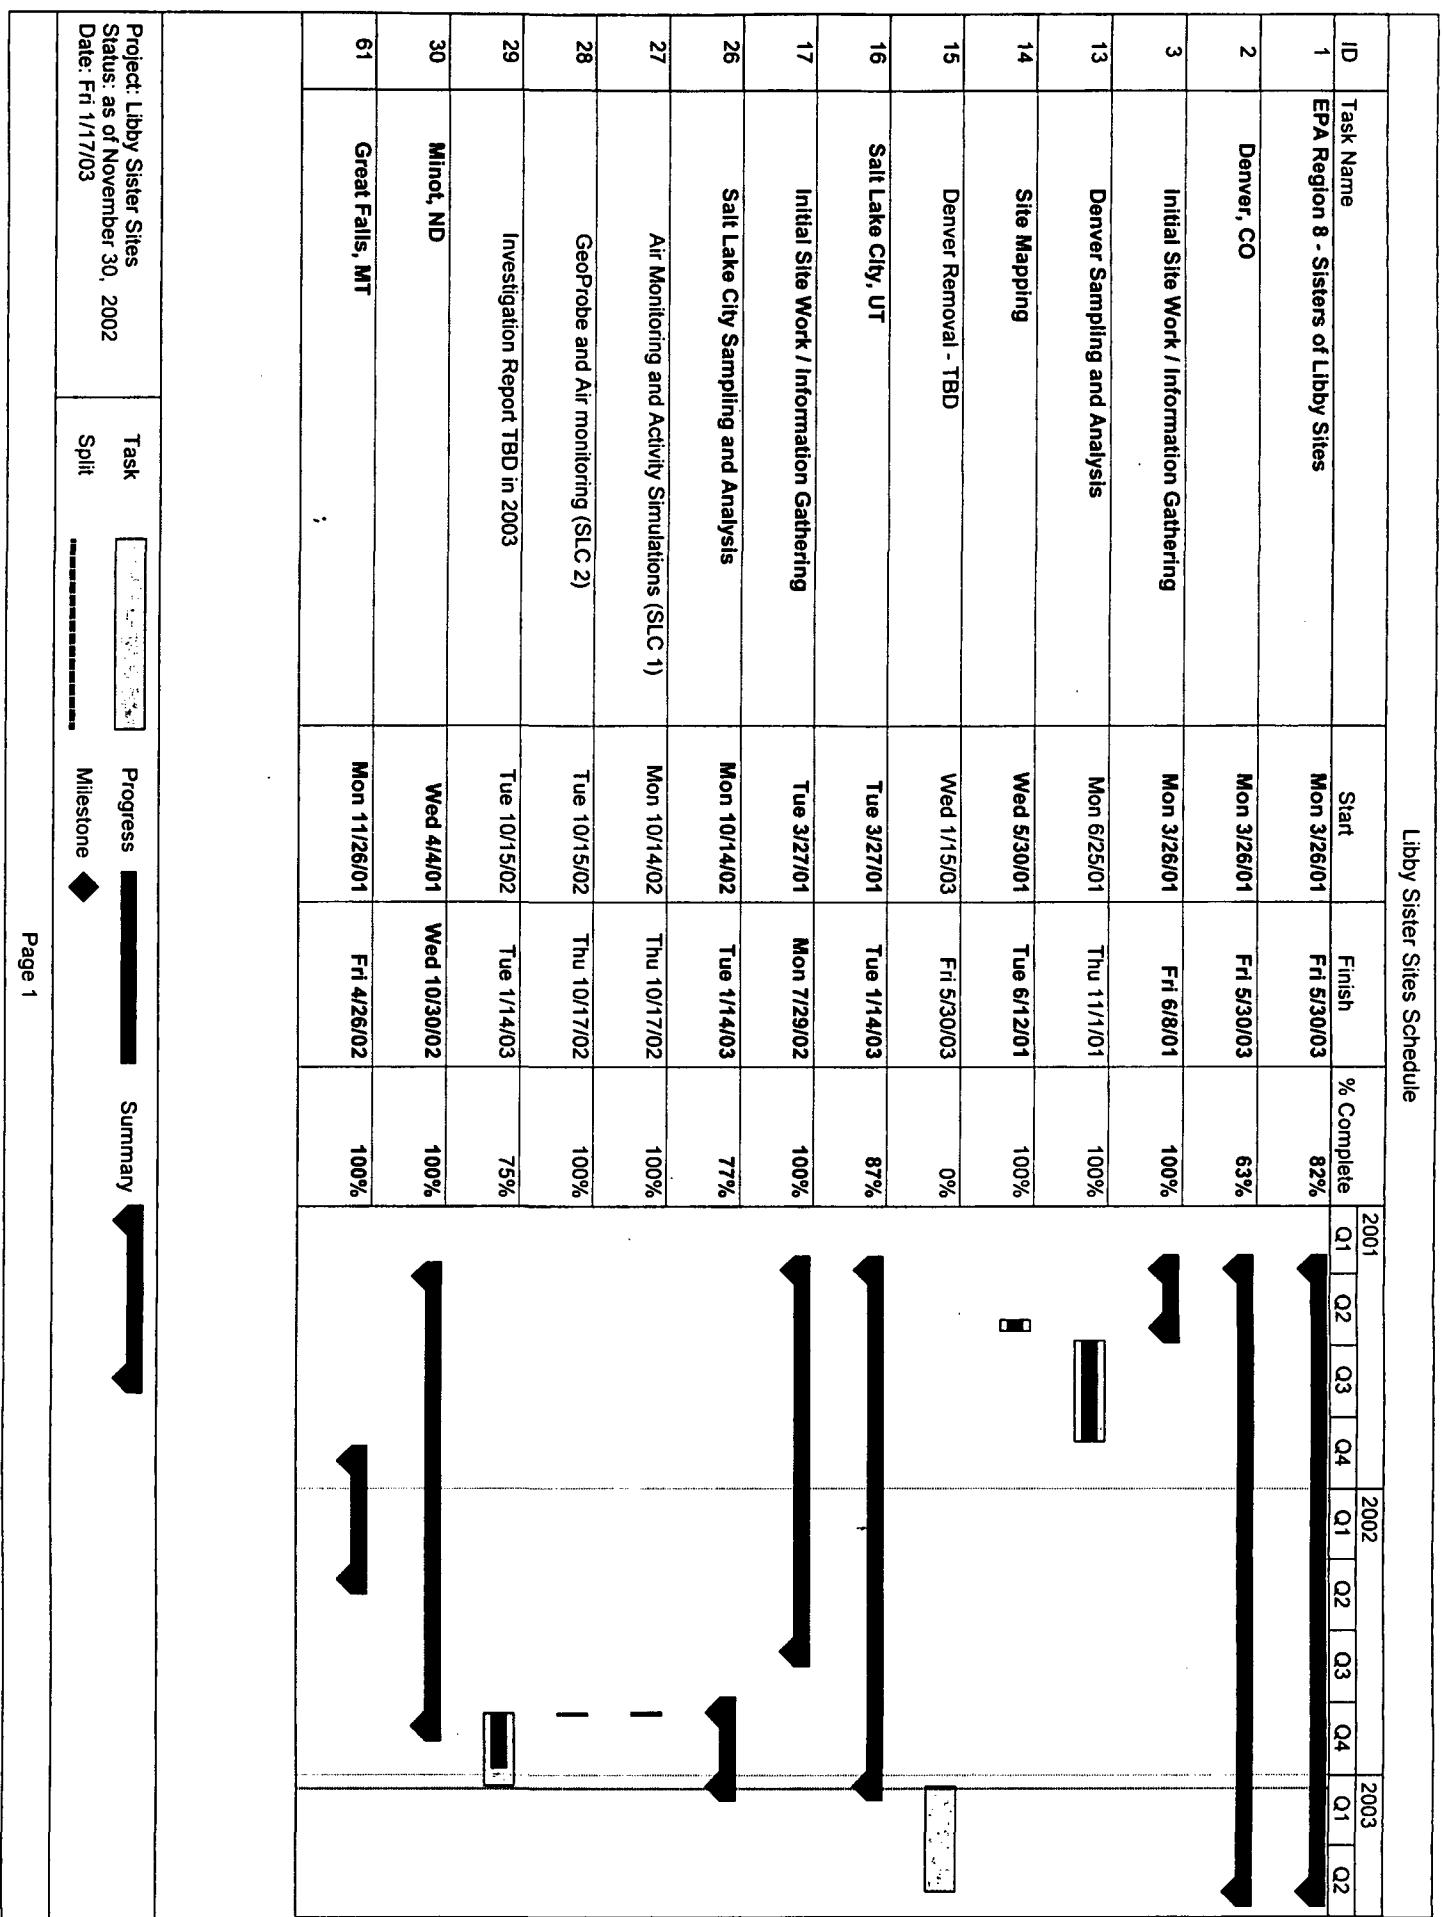

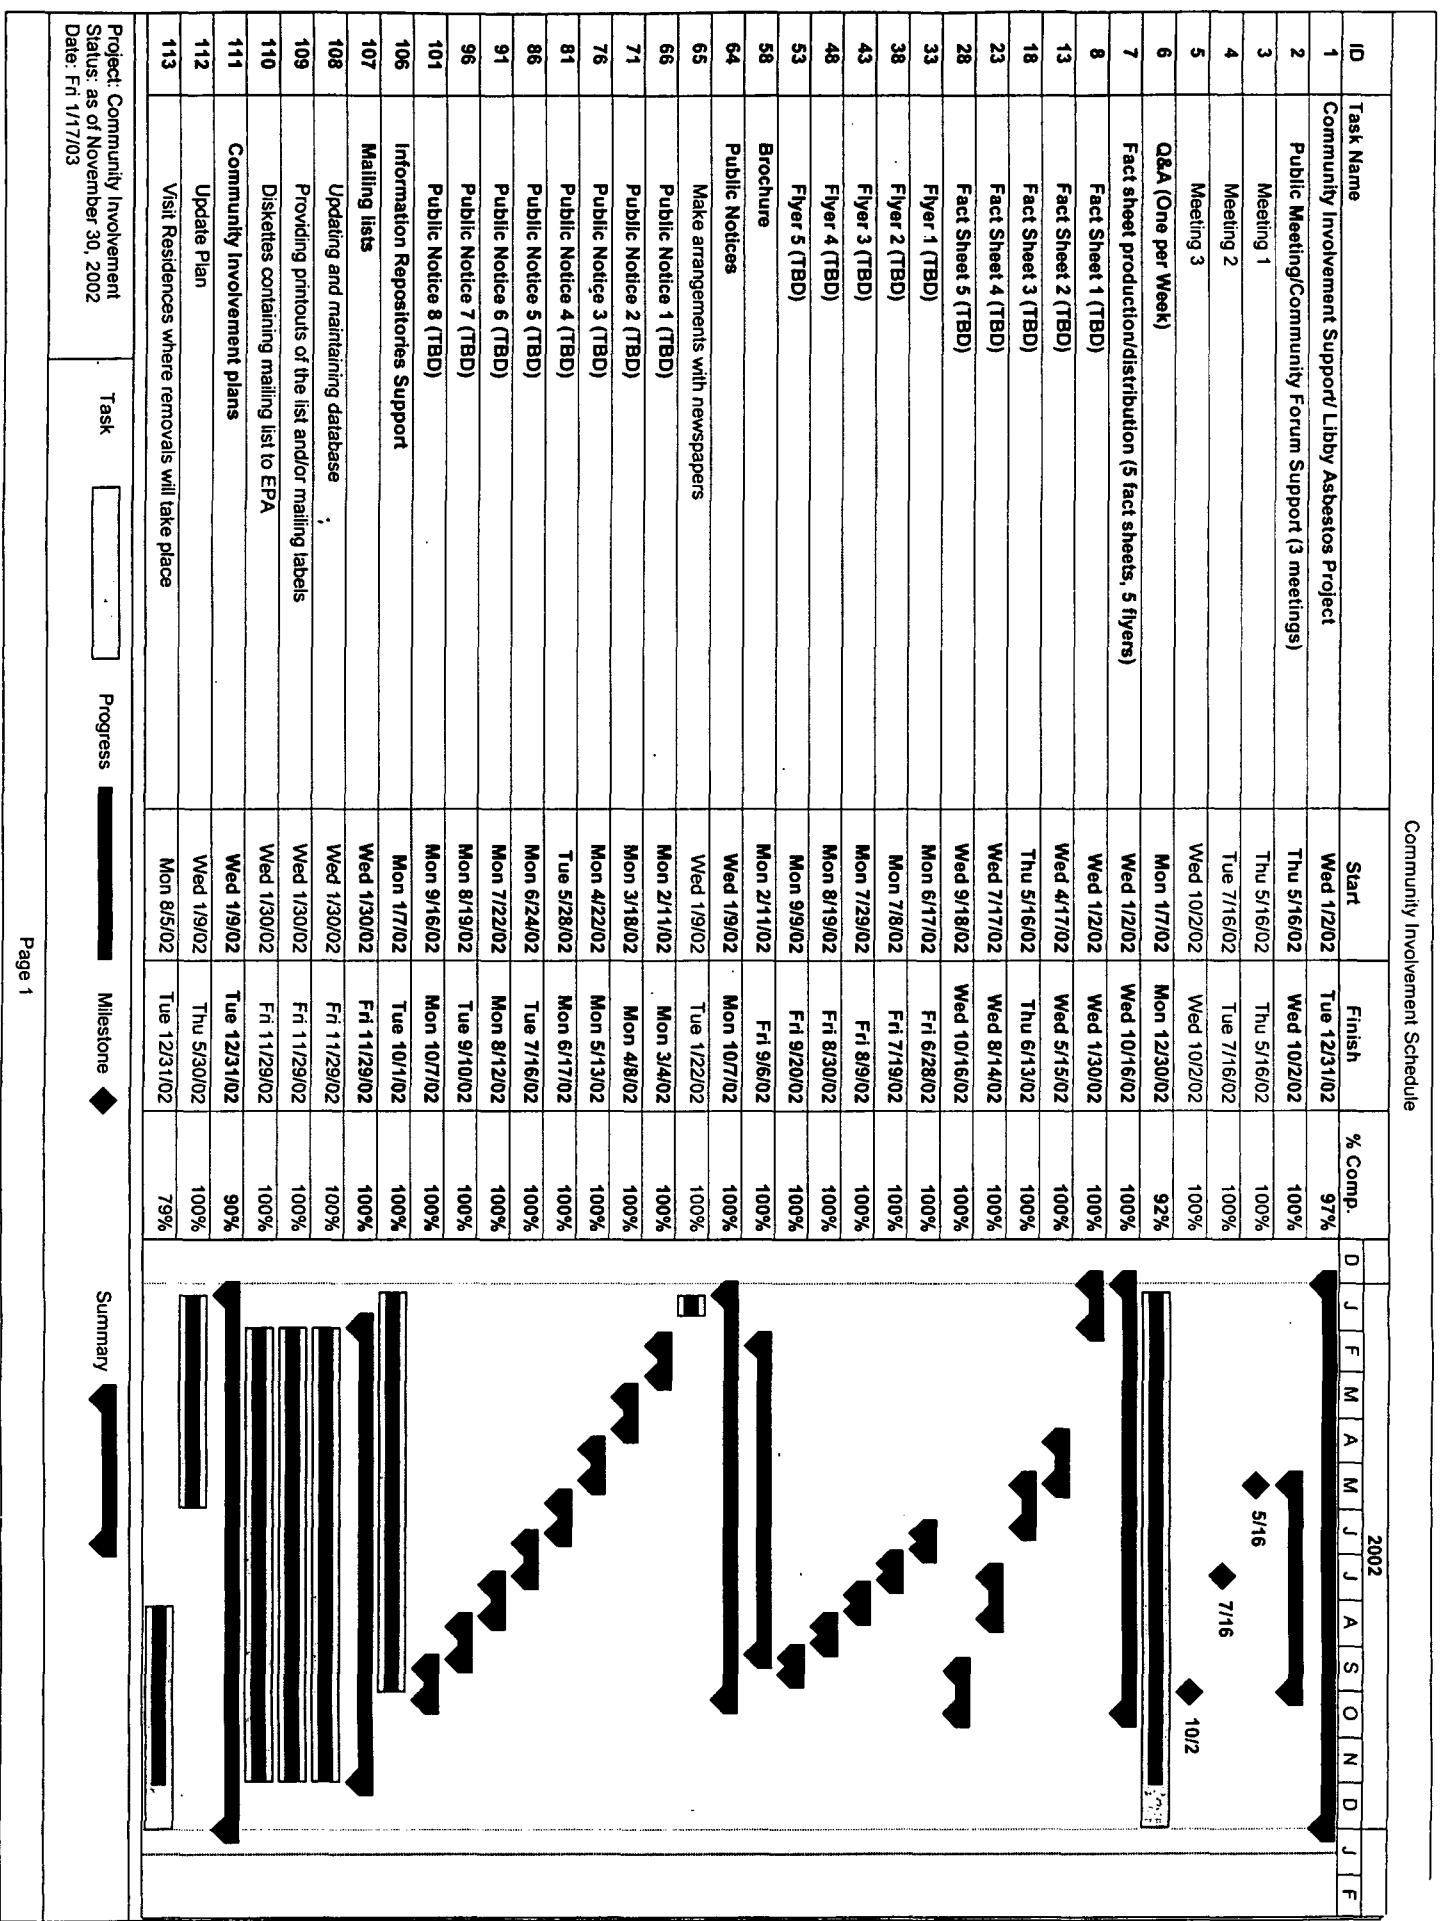


Project: Community Involvement
Status: as of November 30, 2002
Date: Fri 1/17/03

Task Progress Milestone

Summary

Community Involvement Schedule

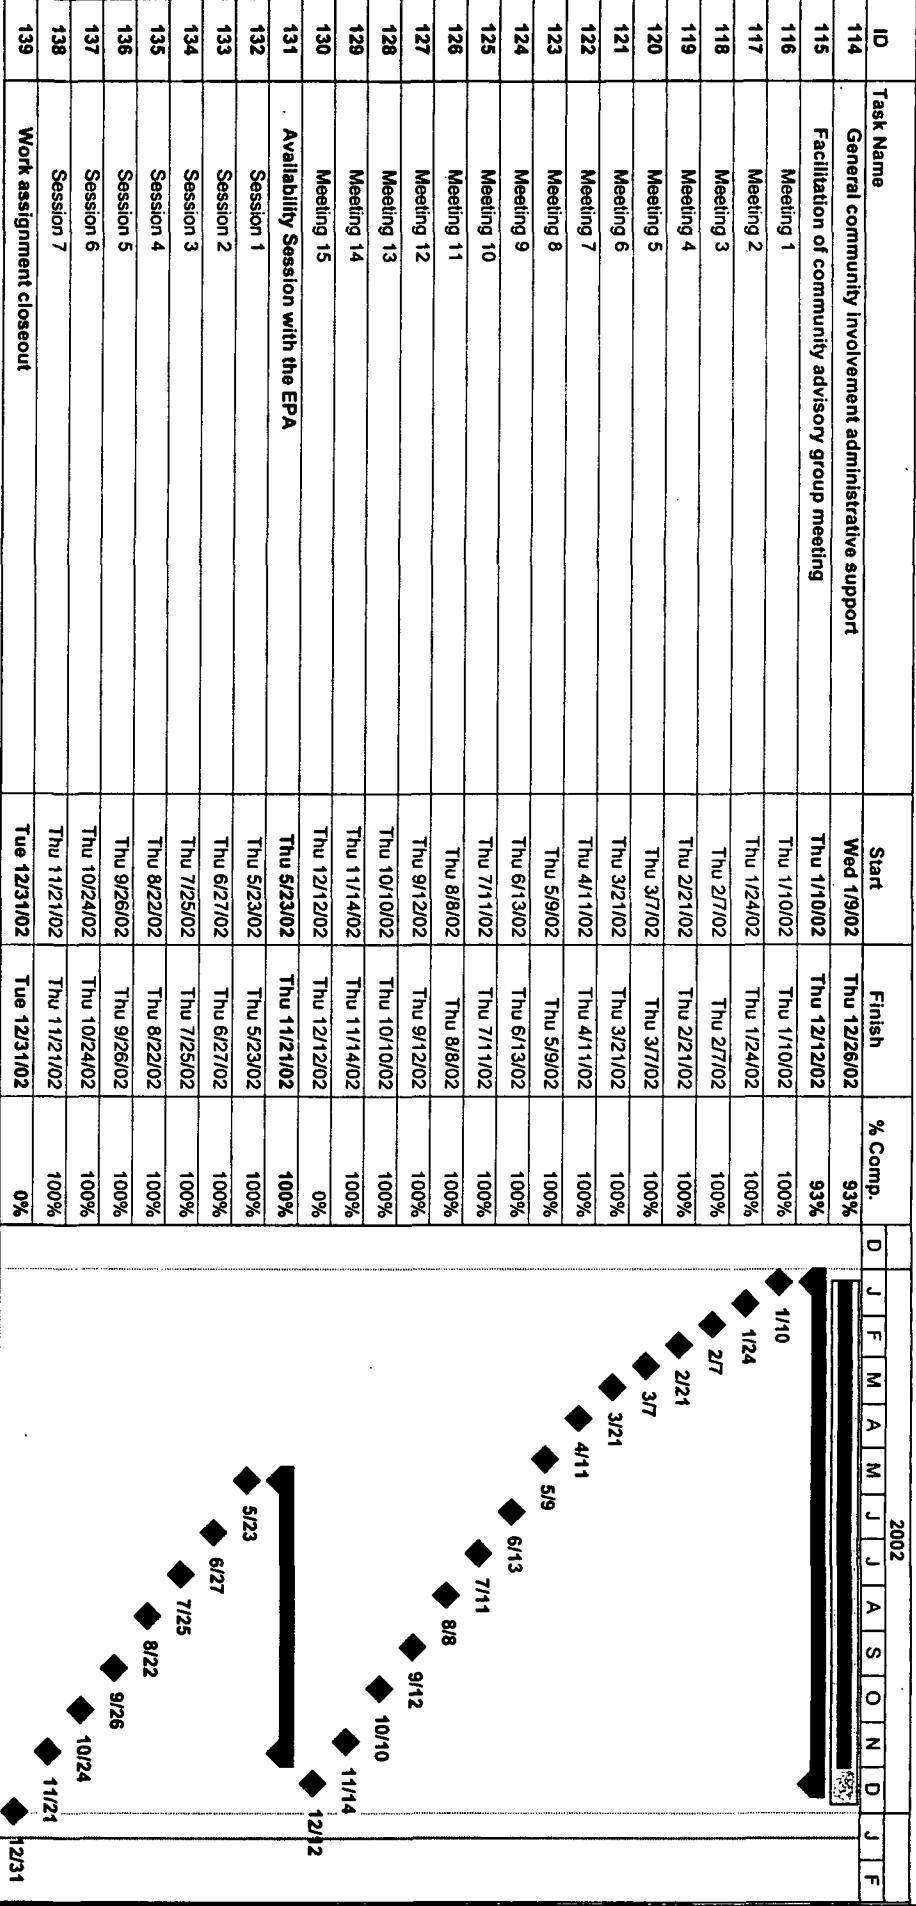

Project: Community Involvement
Status: as of November 30, 2002
Date: Fri 11/17/03

Task

Progress

Milestone

Summary

**ATTACHMENT 2
(COST SUMMARIES)**

PLANS, ADVANCES and EXPENDITURES SUMMARY

PLANS, ADVANCES and EXPENDITURES SUMMARY
Volpe IAG#DW69953792-01

PLANS - WAF HISTORY	DATE	WAF No. 1 Stockton Removal Action	WAF No. 2 Aspen Park Solvents Solvents	WAF No. 3 Counter Terrorism WP	WAF No. 4 Libby Asbestos Project Assessment	WAF No. 5 Lockwood Solvents	WAF No. 6 Libby Economic Analysis	WAF No. 7 Libby Asbestos Project - Export Plant	WAF No. 8 Libby Asbestos Proj - Removals	WAF No. 9 Asbestos Sampling/Site Assessments	WAF No. 10 Hazard Ranking System Documentation	WAF No. 11 Intermountain Insulation SLC, Utah	
99 T BALDE 50102D 0BVBGN00	11/25/2002		\$ (13,685)										
99 T BALDE 50102D 0B00BN00	11/25/2002					\$ (1,703)							
00 T BALDE 50102D 0BBCRV00	11/25/2002									\$ (18,083)			
01 T BALDE 50102D 0BBCHR00	11/25/2002										\$ (7,790)		
99 T BALDE 50102D 0BDVRV00	11/25/2002											\$ 7,515	
99 T BALDE 50102D 0B8CLT00	11/25/2002												
01 T BALDE 50102D 0B8CLT00	11/25/2002												
00 T BALDE 50102D 0B8CLT00	11/25/2002												
02 T BALDE 50102D 0B8CRV02	11/25/2002									\$ (882,500)			
02 T BALDE 50102D 0B8CRS00	11/25/2002					\$ 695,000							
99 T BALDE 50102D 0B8CRS00	11/25/2002					\$ 9,500							
02 T BALDE 50102D 0B8CRS00	11/25/2002					\$ 7,000							
02 T BALDE 50102D BCRV01	11/25/2002									\$ 165,000			
02 T BALDE 50102D 0B8CLT00	11/25/2002												
TOTAL WAFs		\$ 6,110,500	\$ 132,912	\$ 1,315	\$ 11,086,500	\$ 17,088	\$ 3,207	\$ 1,136,000	\$ 36,737,300	\$ 1,937	\$ 30,410	\$ 57,515	
BALANCE FOR WAFS													
COMMITMENTS		WAF No. 1 Stockton Removal Action	WAF No. 2 Aspen Park Solvents Solvents	WAF No. 3 Counter Terrorism WP	WAF No. 4 Libby Asbestos Project Assessment	WAF No. 5 Lockwood Solvents	WAF No. 6 Libby Economic Analysis	WAF No. 7 Libby Asbestos Project - Export Plant	WAF No. 8 Libby Asbestos Proj - Removals	WAF No. 9 Asbestos Sampling/Site Assessments	WAF No. 10 Hazard Ranking System Documentation	WAF No. 11 Intermountain Insulation SLC, Utah	
at 11/30/02		Nx329	Nx332:2x15	Nx350		Nx428		Nx388	Nx064	Nx423	Nx078	Nx131	Nx135
Volpe Engineering		\$ 418,998	\$ 7,926	\$ 1,315	\$ 2,078,992	\$ 3,175	\$ 3,207	\$ 34,086	\$ 1,659,125	\$ 1,286	\$ 386	\$ 9,230	
Contracts		\$ 5,450,404	\$ 115,367	\$ -	\$ 8,307,333	\$ 13,208	\$ -	\$ 1,045,407	\$ 32,938,465	\$ -	\$ 29,000	\$ 42,538	
Equip/supplies		\$ 31,768	\$ -	\$ -	\$ 147,198	\$ 27	\$ -	\$ 8,642	\$ 108,303	\$ 620	\$ -	\$ 505	
G&A		\$ 209,320	\$ 4,480	\$ -	\$ 328,217	\$ 492	\$ -	\$ 39,355	\$ 1,223,525	\$ 22	\$ 1,025	\$ 1,659	
TOTAL COMMITMENTS		\$ 6,110,490	\$ 127,773	\$ 1,315	\$ 10,861,741	\$ 16,903	\$ 3,207	\$ 1,127,791	\$ 35,929,418	\$ 1,937	\$ 30,410	\$ 53,930	
CURRENT MONTH COMMITMENTS		\$ -	\$ 8,210	\$ -	\$ 255,256	\$ -	\$ -	\$ 948	\$ 874,644	\$ -	\$ -	\$ 271	
Balance to Commit (WAFs less commitments)		\$ 10	\$ 5,139	\$ 0	\$ 224,759	\$ 185	\$ (0)	\$ 8,209	\$ 807,882	\$ (0)	\$ (0)	\$ 3,585	
ADVANCES	DATE	WAF No. 1 Stockton Removal Action	WAF No. 2 Aspen Park Solvents Solvents	WAF No. 3 Counter Terrorism WP	WAF No. 4 Libby Asbestos Project Assessment	WAF No. 5 Lockwood Solvents	WAF No. 6 Libby Economic Analysis	WAF No. 7 Libby Asbestos Project - Export Plant	WAF No. 8 Libby Asbestos Proj - Removals	WAF No. 9 Asbestos Sampling/Site Assessments	WAF No. 10 Hazard Ranking System Documentation	WAF No. 11 Intermountain Insulation SLC, Utah	
at 11/30/02													
Inv 03802348	02/19/1999	\$ 100,000											
Inv 03802564	05/26/1999	\$ 200,000											
Inv 03802635	06/22/1999	\$ 2,000,000											
Inv 03802740	08/26/1999	\$ 910,000	\$ 75,000	\$ 15,000									
Inv 03802893	10/28/1999	\$ 1,000,000											
Inv 03802935	12/14/1999	\$ 1,500,000											
Inv 03803145	03/28/2000	\$ 108,000				\$ 382,000							
Inv 03803267	05/23/2000					\$ 500,000							
Inv 03803365	07/12/2000					\$ 500,000			\$ 100,000	\$ 308,000			
Inv 03803405	09/18/2000									\$ 230,000	\$ 20,000		
Inv 03803435	09/22/2000	\$ 300,000				\$ 300,000							
Inv 03803460	09/30/2000												
Inv 03803494	11/22/2000												
Inv 03803550	12/13/2000					\$ 200,000			\$ 100,000	\$ 1,000,000			
Inv 03803571	01/22/2001	\$ (15,000)				\$ (10,000)	\$ 400,000	\$ (20,000)	\$ (1,793)	\$ 50,000	\$ 546,793		
March advance	March '01					\$ 485,000				\$ 100,000	\$ 400,000	\$ 5,000	
Inv 03803997	06/20/2001												
Inv 03804053	07/19/2001					\$ 605,000							
Inv 03804055	07/23/2001												
Inv 03804117	08/24/2001												
Inv 03804130	09/10/2001					\$ 350,000			\$ 150,000			\$ 50,000	
Inv 03804161	09/11/2001					\$ 1,000,000							
Inv 03804182	09/21/2001												
November advance	November 01	\$ (64,500)				\$ 1,200,000							
April advance	April 02	\$ 25,000				\$ 1,380,800			\$ 121,000	\$ 5,500,000	\$ (11,800)	\$ 10,000	
July advance	July 03					\$ 962,912	\$ 32,088	\$ 5,000					
Inv 03804417	09/14/2002												
Inv 03800475	09/29/2002					\$ 750,000							
Inv 03800514	09/30/2002					\$ 350,000							
Reverse 03800417													
Reverse 03800476						\$ (750,000)							
Reverse 03800514						\$ (350,000)							
Inv 3800577		\$ 5,000											
Inv 3800574						\$ 1,500,000							
Inv 3800875													
TOTAL ADVANCES		\$ 6,038,500	\$ 105,000	\$ 5,000	\$ 9,755,712	\$ 12,088	\$ 3,207	\$ 1,131,000	\$ 34,036,982	\$ 20,000	\$ 38,200	\$ 57,515	
Balance to Advance (WAFs less advances)		\$ 72,000	\$ 27,912	\$ (3,685)	\$ 1,330,788	\$ 5,000	\$ -	\$ 5,000	\$ 2,700,338	\$ (18,063)	\$ (7,780)	\$ -	
EXPENDITURES		Stockton Removal Action	Aspen Park Solvents Solvents	Counter Terrorism WP	Libby Asbestos Project Assessment	Lockwood Solvents	Libby Economic Analysis	Libby Asbestos Project - Export Plant	Libby Asbestos Proj - Removals	Asbestos Sampling/Site Assessments	Hazard Ranking System Documentation	Intermountain Insulation SLC, Utah	
at 11/30/02													
Volpe Engineering		\$ 418,998	\$ 7,926	\$ 1,315	\$ 2,054,890	\$ 3,175	\$ 3,207	\$ 34,086	\$ 1,614,227	\$ 1,296	\$ 386	\$ 9,230	
Contracts		\$ 5,218,901	\$ 93,550	\$ -	\$ 7,372,172	\$ 8,393	\$ -	\$ 813,619	\$ 30,180,165	\$ -	\$ 26,739	\$ 5,249	
Equip/supplies		\$ 31,768	\$ -	\$ -	\$ 145,782	\$ 27	\$ -	\$ 42	\$ 87,712	\$ 620	\$ -	\$ 5	
G&A		\$ 209,320	\$ 4,171	\$ -	\$ 327,298	\$ 492	\$ -	\$ 39,355	\$ 1,213,718	\$ 22	\$ 1,025	\$ 1,640	
TOTAL EXPENDITURES		\$ 5,878,987	\$ 105,848	\$ 1,315	\$ 9,900,151	\$ 12,088	\$ 3,207	\$ 887,103	\$ 33,105,823	\$ 1,937	\$ 28,150	\$ 18,124	
CURRENT MONTH EXPEND.		\$ -	\$ 2,321	\$ -	\$ 148,793	\$ -	\$ -	\$ 137,843	\$ 1,700,017	\$ -	\$ -	\$ 424	
Advances less Expenditures		\$ 159,513	\$ (648)	\$ 3,685	\$ (144,439)	\$ 0	\$ (0)	\$ 243,897	\$ 931,139	\$ 18,083	\$ 10,050	\$ 41,391	

PLANS, ADVANCES and EXPENDITURES SUMMARY

PLANS - WAF HISTORY	WAF No. 12 Robinson Insulation Minot, ND	WAF No. 13 Western Minerals Denver, CO	WAF 14 Pablo Tire Fire	WAF 15 Great Falls MT Insulation Site	WAF 16 Libby Litigation Support	WAF 17 Remedial Investigation	TOTAL
at 11/31/02							
997BALOEFAX082XRV00						\$ 475,000	
997BALOEFAX082XWQ00						\$ 1,000,000	
997BALOEFAX086DRV00						\$ 25,000	
997BALOEFAX086WQBN00						\$ 15,000	
997BALOEFAX086WQBCD0						\$ 250,000	
997BALOEFAX086BCRS00						\$ 350,000	
997BALOEFAX082XWQ00						\$ 4,625,000	
997BALOEFAX086DRV00						\$ 80,000	
997BALOEFAX086AKR00						\$ 20,000	
997BALOEFAX082XRV00						\$ 400,000	
997BALOEFAX086AKR00						\$ 20,000	
997BALOEFAX086BCBN00						\$ 200,000	
997BALOEFAX086BCR00						\$ 1,700,000	
997BALUFEAX0800BN00						\$ 5,000	
99 T BALOE 50201D 08BCRV01						\$ 200,000	
99 T BALOE 50201D 08BCRV02						\$ 1,200,000	
99 T BALOE 50102D 08BCRV02						\$ 143,000	
99 T BALOE 50102D 08BCRV02						\$ 750,000	
00 T BALOE 50102D 08BCRV02						\$ 2,600,000	
00 T BALOE 50102D 08BCRV00						\$ 20,000	
00 T BALOE 50102D 08BCRV01						\$ 300,000	
00 T BALOE 50102D 08BCRV00						\$ 500,000	
00 T BALOE 50102D 08BCRV02						\$ 800,000	
00 T BALOE 50102D 08BCRV00						\$ 500,000	
00 T BALOE 50102D 082XRV00						\$ (300,000)	
00 T BALOE 50102D 08BCRV02						\$ 1,680,000	
00 T BALOE 50102D 08BCRV00						\$ 1,500,000	
00 T BALOP 50102D 08BCRV00						\$ 50,000	
99 T BALOE 50102D 08DBRS00						\$ 10,000	
99 T BALOE 50102D 08DCRS00	\$ 45,000					\$ 45,000	
99 T BALOE 50102D 08DARS00		\$ 45,000				\$ 45,000	
00 T BALOP 50102D 08BCRV02						\$ 1,500,000	
00 T BALOP 50102D 08BCRV02						\$ 200,000	
99 T BALOE 50102D 08BCRV02						\$ (550,000)	
99 T BALOE 50102D 08BCRV02						\$ 608,000	
01 T BALOP 50102D 08BCRS00						\$ 550,000	
01 T BALOE 50102D 08BCRV02						\$ 3,500,000	
01 T BALOP 50102D 08BCRS00						\$ 1,500,000	
01 T BALOE 50102D 08BCRV02						\$ 1,500,000	
99 T BALOE 50102D 08BCRV00						\$ (700,000)	
01 T BALOP 50102D 08BCRS00						\$ 700,000	
99 T BALOE 50102D 08DCRS00	\$ 50,000					\$ 50,000	
99 T BALOE 50102D 08DARS00		\$ 50,000				\$ 50,000	
99 T BALOE 50102D 08BCRV00						\$ 600,000	
01 T BALOE 50102D 08BCRV02						\$ 2,700,000	
01 T BALOE 50102D 08DARS00		\$ 70,000				\$ 70,000	
01 T BALOE 50102D 08DARV00		\$ 70,000				\$ 70,000	
01 T BALOE 50102D 08WQDBRS00						\$ 20,000	
01 T BALOE 50102D 08DCRS00	\$ 70,000					\$ 70,000	
01 T BALOE 50102D 08DCRV00		\$ 70,000				\$ 70,000	
01 T BALOE 50102D 08BCRV02						\$ 4,000,000	
01 T BALOE 50102D 08BCRS00						\$ 125,000	
01 T BALOE 50102D 08BCRV02						\$ 1,200,000	
01 T BALOE 50102D 08BCRV02						\$ 3,840,000	
01 T BALOE 50102D 08BCHR00						\$ 50,000	
01 T BALOE 50102D 08EHHRV00						\$ 10,000	
01 T BALOE 50102D 08DARV00			\$ 10,000			\$ 10,000	
01 T BALOE 50102D 08ELERS00			\$ (15,000)			\$ (15,000)	
01 T BALOE 50102D 08BCRV00					\$ 15,000		
01 T BALOE 50102D 08BCRV00						\$ 400,000	
01 T BALOE 50102D 08BCRV01						\$ 100,000	
01 T BALOE 50102D 08EHRV00						\$ (10,000)	
01 T BALOE 50102D 08EKR00					\$ 10,000		
01 T BALOE 50102D 08BCRV01						\$ 15,000	
02 T BALOE 50102D 08BCRV02						\$ 1,850,000	
02 T BALOE 50102D 08BCRV02						\$ 4,750,000	
01 T BALOE 50102D 08BCRS00						\$ 500,000	\$ 500,000
99 T BALOE 50102D 08AKR00						\$ 27,912	
99 T BALOE 50102D 086DRV00						\$ 27,912	
99 T BALOE 50102D 082XRV00						\$ (89,500)	
02 T BALOE 50102D 08BCRS00						\$ 1,900,000	
99 T BALOE 50102D 08AKR00						\$ 5,000	
01 T BALOE 50102D 08BCRV01						\$ 71,000	
02 T BALOE 50102D 08BCRV02						\$ 3,100,000	
01 T BALOE 50102D 08BCRV02						\$ 600	
01 T BALOE 50102D 08BCHR00						\$ (61,800)	
01 T BALOE 50102D 08DBRS00						\$ (10,000)	
01 T BALOE 50102D 08DCRV00						\$ (15,000)	
01 T BALOE 50102D 08DARV00			\$ (20,000)			\$ (20,000)	
01 T BALOE 50102D 08EKR00				\$ (10,000)		\$ (10,000)	
01 T BALOE 50102D 08ELERS00				\$ 45,000		\$ 45,000	
01 T BALOE 50102D 08BCLT00					\$ 30,000		\$ 30,000
02 T BALOE 50102D 08BCCO04						\$ 500,000	\$ 500,000
02 T BALOE 50102D 08BCRV00						\$ 800,000	
02 T BALOE 50102D 08DCRV00						\$ 120,000	
02 T BALOE 50102D 08BCRV02						\$ 1,250,000	
02 T BALOE 50102D 08BCRS00						\$ 25,000	
02 T BALOE 50102D 08BCRV00						\$ 5,000	
02 T BALOE 50102D 08BCRV00						\$ 5,000	
02 T BALOE 50102D 08BCRV00						\$ 10,000	
02 T BALOE 50102D 08BCRS00						\$ 500,000	
02 T BALOE 50102D 08BCRV01						\$ 150,000	
99 T BALOE 50102D 08DCRV00						\$ 69,000	
99 T BALOE 50102D 08DCB00						\$ 6,000	
02 T BALOE 50102D 08BCLT00						\$ 10,000	
02 T BALOE 50102D 08DBRV00						\$ 21,000	
02 T BALOE 50102D 08DCRV00						\$ 35,000	
02 TC BALOE 50102D 08BCCO04						\$ 2,613,000	\$ 2,613,000
02 T BALOE 50102D 08BCRS00						\$ (500,000)	\$ (500,000)
02 T BALOE 50102D 08DBRV00						\$ 9,000	
02 T BALOE 50102D 08BCRV02						\$ 1,850,000	
02 T BALOE 50102D 08BCRV02						\$ 500,000	
02 T BALOE 50102D 08DCRV00						\$ 12,000	

PLANS, ADVANCES and EXPENDITURES SUMMARY
Volpe IAG#DW69953792-01

PLANS - WAF HISTORY	WAF No. 12 Robinson Insulation Minot ND	WAF No. 13 Western Minerals Denver, CO	WAF 14 Pablo Tire Fire	WAF 15 Great Falls MT Insulation Site	WAF 16 Libby Litigation Support	WAF 17 Remedial Investigation	TOTAL
99 T BALDE 501020 08VCBN00							\$ (13,685)
99 T BALDE 501020 0800BN00							\$ (1,783)
00 T BALDE 501020 08BCRV00							\$ (18,063)
01 T BALDE 501020 08BCHR00							\$ (7,780)
99 T BALDE 501020 08DBRV00							\$ 7,515
99 T BALDE 501020 08BCLT00					\$ 7,983		\$ 7,983
01 T BALDE 501020 08BCLT00					\$ 7,780		\$ 7,780
00 T BALDE 501020 08BCLT00					\$ 18,063		\$ 18,063
02 T BALDE 501020 08BCRV02							\$ (882,500)
02 T BALDE 501020 08BCRS00							\$ 665,000
99 T BALDE 501020 08BCRS00							\$ 9,500
02 T BALDE 501020 08BCRS00							\$ 7,000
02 T BALDE 501020 BCRV01							\$ 165,000
02 T BALDE 501020 08BCLT00					\$ 22,000		\$ 22,000
TOTAL WAFs	\$ 487,000	\$ 200,000	\$ -	\$ 60,000	\$ 115,816	\$ 3,113,000	\$ 59,290,500

BALANCE FOR WAWS							\$ 1,500
	WAF No. 12	WAF No. 13	WAF 14	WAF 15	WAF 16	WAF 17	
COMMITMENTS	Robinson Insulation Minot ND	Western Minerals Denver, CO	Pablo Tire Fire	Great Falls MT Insulation Site	Libby Litigation Support	Remedial Investigation	TOTAL
at 11/30/02	Nx084	Nx088		Nx177	Nx192		Nx211
Volpe Engineering	\$ 66,470	\$ 34,778	\$ -	\$ 5,048	\$ 105,206	\$ 18,361	\$ 4,447,600
Contracts	\$ 396,391	\$ 123,918	\$ -	\$ 30,000	\$ -	\$ 2,947,449	\$ 51,439,479
Equip/supplies	\$ 2,351	\$ 1,797	\$ -	\$ -	\$ 6,228	\$ -	\$ 307,740
G&A	\$ 15,054	\$ 4,459	\$ -	\$ 1,154	\$ 656	\$ 113,890	\$ 1,943,407
TOTAL COMMITMENTS	\$ 480,266	\$ 164,953	\$ -	\$ 36,202	\$ 112,090	\$ 3,079,800	\$ 58,138,226
CURRENT MONTH COMMITMENTS	\$ 68	\$ 339	\$ -	\$ -	\$ 1,826	\$ 7,178	\$ 1,148,740
Balance to Commit (WAWS less committ)	\$ 6,734	\$ 35,047	\$ -	\$ 23,798	\$ 3,726	\$ 33,200	\$ 1,152,274

WAWS	WAF No. 12	WAF No. 13	WAF 14	WAF 15	WAF 16	WAF 17	
ADVANCES	Robinson Insulation Minot ND	Western Minerals Denver, CO	Pablo Tire Fire	Great Falls MT Insulation Site	Libby Litigation Support	Remedial Investigation	TOTAL
at 11/30/02							
Inv 03802348							\$ 100,000
Inv 03802564							\$ 200,000
Inv 03802635							\$ 2,000,000
Inv 03802740							\$ 1,000,000
Inv 03802893							\$ 1,000,000
Inv 03802895							\$ 1,500,000
Inv 03803145							\$ 500,000
Inv 03803267							\$ 500,000
Inv 03803365							\$ 908,000
Inv 03803409							\$ 250,000
Inv 03803435							\$ 600,000
Inv 03803460							\$ 1,000,000
Inv 03803494							\$ 1,000,000
Inv 03803550							\$ 1,300,000
Inv 03803571							\$ 950,000
March advance	\$ 5,000	\$ 5,000					\$ 1,000,000
Inv 03803997							\$ 1,000,000
Inv 03804053	\$ 20,000	\$ 20,000					\$ 1,000,000
Inv 03804065							\$ 1,050,000
Inv 03804117							\$ 2,100,000
Inv 03804130	\$ 125,00	\$ 125,000					\$ 800,000
Inv 03804161							\$ 2,106,000
Inv 03804162							\$ 3,500,000
November advance				\$ 15,000			\$ 8,525,000
April advance	\$ 70,000	\$ 50,000		\$ 45,000	\$ 30,000		\$ 7,200,000
July advance							\$ 1,000,000
Inv 03800417							\$ 3,500,000
Inv 03800476							\$ 750,000
Inv 03800514						\$ 1,150,000	\$ 1,500,000
Reverse 03800417							\$ (3,500,000)
Reverse 03800476							\$ (750,000)
Reverse 03800514						\$ (1,150,000)	\$ (1,500,000)
Inv 3800577							\$ 6,340,000
Inv 3800574	\$ 267,000				\$ 85,816	\$ 3,113,000	\$ 4,250,000
Inv 3800675							\$ 2,500,000
TOTAL ADVANCES	\$ 487,000	\$ 200,000	\$ -	\$ 60,000	\$ 115,816	\$ 3,113,000	\$ 55,179,000

Balance to Advance (WAWS less advanced) \$ - \$ - \$ - \$ - \$ - \$ - \$ - \$ 4,111,500

EXPENDITURES	Robinson Insulation Minot ND	Western Minerals Denver, CO	Pablo Tire Fire	Great Falls MT Insulation Site	Libby Litigation Support	Remedial Investigation	TOTAL
at 11/30/02							
Volpe Engineering	\$ 66,470	\$ 34,778	\$ -	\$ 5,048	\$ 105,206	\$ 17,151	\$ 4,377,390
Contracts	\$ 267,305	\$ 122,918	\$ -	\$ 26,889	\$ -	\$ 2,023,153	\$ 46,169,055
Equip/supplies	\$ 451	\$ 1,797	\$ -	\$ -	\$ 5,478	\$ -	\$ 273,693
G&A	\$ 15,435	\$ 4,459	\$ -	\$ 1,154	\$ 627	\$ 113,890	\$ 1,932,305
TOTAL EXPENDITURES	\$ 349,161	\$ 163,953	\$ -	\$ 33,091	\$ 111,311	\$ 2,154,285	\$ 52,752,442
CURRENT MONTH EXPEND.	\$ 68	\$ 339	\$ -	\$ -	\$ 1,047	\$ 438,800	\$ 2,430,651
Advances less Expenditures	\$ 137,739	\$ 36,047	\$ -	\$ 26,908	\$ 4,505	\$ 958,705	\$ 2,426,558

EPA SUMMARY

USEPA/Nolpe IAC (IAC HDW69953792-01)

At 12/31/02

Funds Authorized		FY00 Planned	FY01 Planned	FY02 Planned	FY03 Planned
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,350	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,085	\$ 53,727	\$ 53,727	\$ 13,349
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 26,538	\$ 13,685	\$ 13,685	\$ 13,2912
4) Libby Asbestos Proj Assessment (N-428)	\$ 30,440	\$ 33,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 11,086,500
6) Libby Economic Analysis (N- 064)	\$ 5,000	\$ 1,793	\$ 1,793	\$ 1,793	\$ 1,7088
7) Libby Asbestos Proj - Export Plant (N- 423)	\$ 500,000	\$ 507,637	\$ 234,458	\$ 234,458	\$ 3,207
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 171,077	\$ 5,493,000	\$ 5,014,168	\$ 1,136,000
9) Asbestos Sampling/Site Assessments(N- 131)	\$ -	\$ 20,415,372	\$ 18,098,394	\$ 36,713,300	\$ 1,937
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ 19,793	\$ 18,063	\$ 10,000	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 100,000	\$ 7,790	\$ 30,000	\$ 57,515
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 235,000	\$ 40,976	\$ 46,892	\$ 48,700
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 20,000
14) Pablo Tire Fire	\$ -	\$ 76,967	\$ 35,386	\$ 20,000	\$ -
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ -
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 16,204	\$ 11,816	\$ -
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,900	\$ 1,289,395	\$ 3,113,000	\$ -
Total EPA Funds Authorized (WAFS)	\$ 5,908,000	\$ 10,493,680	\$ 7,814,441	\$ 59,291,500	A
Unallocated Funds	\$ -	\$ 26,10,360	\$ 59,291,500	\$ 1,500	B-A B-B
<i>Costs Incurred</i>					
Description		FY00 Comm.	Current Month	FY01 Comm.	FY02 Comm.
Valpe Engineering:		FY00 Comm.	Current Month	FY01 Comm.	FY02 Comm.
1) Stockton Removal Action (N- 329)	Valpe Labor	\$ 163,009	\$ -	\$ 268,176	\$ -
2) Aspen Park Solvents (N- 332)	Overhead	\$ 104,376	\$ -	\$ 174,505	\$ -
3) Counter-Terrorism Work Plan (N- 350)	Valpe In-House Support	\$ -	\$ -	\$ 115,689	\$ -
4) Libby Asbestos Proj Assessment (N- 428)	Valpe Travel	\$ 35,038	\$ -	\$ 61,374	\$ -
5) Lockwood Solvents (N- 386)	Subtotal-Valpe Engineering	\$ 302,373	\$ -	\$ 511,614	\$ -
6) Libby Economic Analysis (N- 064)				\$ 1,210,835	\$ -
7) Libby Asbestos Proj - Export Plant (N- 423)				\$ 1,854,124	\$ -
8) Libby Asbestos Proj - Removals (N- 079)				\$ 1,392	\$ 1,392
9) Asbestos Sampling/Site Assessments(N- 131)				\$ 568,854	\$ 153,875
10) Hazard Rating System Documentation (N- 135)				\$ 4,447,600	\$ 153,237
11) Intermountian Insulation, SLC, Utah (N- 097)					
12) Robinson Insulation, Minot, ND (N- 094)					
13) Western Minerals, Denver, CO (N- 088)					
14) Pablo Tire Fire					
15) Great Falls MT Insulation Site (N- 177)					
16) Libby Litigation Support (N- 192)					
17) Remedial Investigation (N- 211)					
Subtotal-Contracts		\$ 4,390,391	\$ -	\$ 6,631,147	\$ -
Subtotal-Contracts		\$ 4,390,391	\$ -	\$ 18,400,069	\$ -
Equipment/Supplies/Other		\$ 10,288	\$ -	\$ 110,517	\$ -
Valpe Acq O&H (3.9% of Contracts)	Total Cost	\$ 171,576	\$ -	\$ 238,617	\$ -
		\$ 4,874,538	\$ -	\$ 656,361	\$ -
		\$ 171,576	\$ -	\$ 640,567	\$ -
		\$ 7,491,695	\$ -	\$ 18,757,640	\$ -
		\$ 20,352,186	\$ -	\$ 1,150,465	\$ 58,139,226
		\$ -	\$ (1724)	\$ 6,662,167	\$ 1,148,740
		\$ -	\$ -	\$ 1,152,274	A-C
		\$ -	\$ -	\$ 1,153,774	B-C
Available Authorized Funds					
Available Funds					

EPA SUMMARY

USEPA Noope IAC (IAC; #DW69953792-01)

Financial Summary

At 12/31/02

1) Stockton Removal Action (N- 329)
 Financial Summary
 At 12/31/02

<u>Funds Authorized</u>	<u>FY'99 Planned</u>	<u>FY'00 Planned</u>	<u>FY'01 Planned</u>	<u>FY'02 Planned</u>	<u>FY'03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 1,093,850	\$ 10 10	\$ 6,110,500	A
2) Aspen Park Solvents (N- 312 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,549	\$ 6,132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 0	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,310,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 22,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ (0)	\$ 3,207
7) Libby Asbestos Proj - Export Plant (N- 423)	\$ -	\$ 500,000	\$ 507,637	\$ 234,458	\$ 1,136,000	
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300
9) Asbestos Sampling/Site Assessments (N- 131)	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937	
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410	
11) Interim/Initial Insulation, SLC, Utah (N- 097)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000	
13) Western Minerals, Denver, CO (N- 088)	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000		
14) Pablo Tire Fire	\$ 10,000	\$ -	\$ -	\$ -	\$ -	
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000		
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816		
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,000	\$ 1,269,395	\$ 3,113,000		
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500
<u>Crosses Insured</u>						
<u>Description</u>	<u>FY'99 Comm.</u>	<u>Current Month</u>	<u>FY'00 Comm.</u>	<u>Current Month</u>	<u>FY'01 Comm</u>	<u>Current Month</u>
<i>Voice Engineering/Proj. Mgmt:</i>						
Voice Labor	\$ 162,208	\$ 59,757	\$ 5,107	\$ -	\$ 227,071	\$ -
Overhead	\$ 103,813	\$ 38,884	\$ 3,423	\$ -	\$ 146,120	\$ -
Voice Travel	\$ 35,038	\$ 10,769	\$ -	\$ -	\$ 45,807	\$ -
Subtotal-Voice Engineering	\$ 301,058	\$ 109,410	\$ 8,330	\$ -	\$ 418,998	\$ -
<u>Contracts:</u>						
Initial Site Walks	\$ 4,519	\$ -	\$ -	\$ -	\$ 4,519	\$ -
Soil Transport & Disposal	\$ 993,399	\$ 702,423	\$ -	\$ -	\$ 1,695,822	\$ -
Plans/Site Office	\$ 65,467	\$ 17,106	\$ -	\$ -	\$ 82,573	\$ -
Security	\$ 37,055	\$ 31,416	\$ -	\$ -	\$ 68,471	\$ -
Site Removal/Replacement	\$ 1,896,846	\$ 19,880	\$ -	\$ -	\$ 1,916,426	\$ -
Soil Treatment	\$ 899,398	\$ -	\$ -	\$ -	\$ 899,398	\$ -
Site Landscaping	\$ 414,967	\$ -	\$ -	\$ -	\$ 414,967	\$ -
Staging Area Restoration	\$ -	\$ 368,228	\$ -	\$ -	\$ 368,228	\$ -
Subtotal-Contracts	\$ 4,311,651	\$ 1,138,753	\$ -	\$ -	\$ 5,450,404	\$ -
<u>Equip/Supplies/Other:</u>						
Volpe Acq Off (3.9% of Contracts)	\$ 10,288	\$ 10,011	\$ 11,368	\$ -	\$ 31,768	\$ -
TOTAL COST	\$ 4,791,508	\$ 164,510	\$ 40,658	\$ 342	\$ 209,320	\$ -
TOTAL AVAILABLE FUNDS					\$ 6,110,490	B
					\$ 10	A-B

1) Stockton Removal Action (N- 329)

Financial Summary

Alt 12/31/02

2) Aspen Park Solvents (N-332)

Financial Summary

A4 12/31/02

	FY'99 Planned	FY'00 Planned	FY'01 Planned	FY'02 Planned	FY'03 Planned	Planned
1) Stockton Removal Action (N-329)	\$ 5,801,000	\$ 1,398,711	\$ 109,830	\$ 10	\$ 0	6,110,500
2) Aspen Park Solvents (N-332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 33,727	\$ 13,349	132,912
3) Counter-Terrorism Work Plan (N-350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	1,315
4) Libby Asbestos Proj. Assessment (N-428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	11,086,500
5) Octwood Solvents (N-386)	\$ 17,000	\$ 3,000,000	\$ 2,3542	\$ 185	\$ 185	17,088
6) Libby Economic Analysis (N-064)	\$ -	\$ 5,000	\$ 1,793	\$ (0)	\$ 0	3,207
7) Libby Asbestos Proj. - Export Plant (N-423)	\$ -	\$ 500,000	\$ 507,637	\$ 234,458	\$ 1,136,000	1,136,000
8) Libby Asbestos Proj. - Removals (N-079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 5,014,168	\$ 36,737,300	36,737,300
9) Asbestos Sampling/Site Assessments (N-151)	\$ -	\$ 20,000	\$ 18,063	\$ (0)	\$ 1,937	1,937
10) Hazard Ranking System Documentation (N-135)	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410	30,410
11) Intermountain Insulation, SLC, Utah (N-397)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	57,515
12) Robinson Insulation, Minot, ND (N-094)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000	487,000
13) Western Minerals, Denver, CO (N-088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000	200,000
14) Pablo Tire Fire	\$ 0,000	\$ -	\$ -	\$ -	\$ -	-
15) Great Falls MT Insulation Site (N-177)	\$ -	\$ 60,000	\$ 21,799	\$ -	\$ 60,000	60,000
16) Libby Litigation Support (N-192)	\$ -	\$ 60,000	\$ 16,204	\$ -	\$ 115,816	115,816
17) Remedial Investigation (N-211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 5	\$ 3,113,000	3,113,000
Total EPA Funds Authorized (WAFS)	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500
<u>Costs Incurred</u>						
Description	FY'99 Accrued	Current Month	FY'00 Accrued	Current Month	FY'01 Accrued	Current Month
Volpe Engineering:						
Volpe Labor	\$ -	\$ 2,364	\$ 413	\$ 1,071	\$ -	\$ 3,867
Overhead	\$ -	\$ 1,538	\$ 290	\$ 697	\$ -	\$ 2,525
Volpe Travel	\$ -	\$ -	\$ -	\$ 1,534	\$ -	\$ 1,534
Subtotal Volpe Engineering	\$ -	\$ 3,902	\$ -	\$ 3,302	\$ -	\$ 7,926
Contracts:						
MWH						
ECC	\$ 68,476	\$ -	\$ -	\$ 5,933	\$ 2,321	\$ 5,933
Subtotal Contracts	\$ 68,476	\$ -	\$ -	\$ 19,141	\$ -	\$ 87,617
Subtotal Contracts	\$ 68,476	\$ -	\$ -	\$ 25,074	\$ 2,321	\$ 93,550
Equip/Supplies/Other:						
Volpe Acq/Othr (1.3% of Contracts)	\$ 2,759	\$ -	\$ -	\$ 1,373	\$ -	\$ 4,171
TOTAL COST	\$ 71,274	\$ -	\$ 3,902	\$ 723	\$ 2,321	\$ 105,648
TOTAL AVAILABLE FUNDS						\$ 27,264

2) Aspen Park Solvents (N-332)
 Financial Summary
 A4 12/13/02

	FY99 Planned	FY00 Planned	FY01 Planned	FY02 Planned	FY03 Planned	Planned
1) Stockton Removal Action (N-329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N-332 and N-215)	\$ 75,000	\$ 13,655	\$ 26,538	\$ 13,349	\$ 0	\$ 132,912
3) Counter-Terrorism Work Plan (N-350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N-428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,112,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N-386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N-064)	\$ -	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ 3,207
7) Libby Asbestos Proj - Export Plant (N-423)	\$ -	\$ 500,000	\$ 507,637	\$ 234,458	\$ 1,136,000	\$ -
8) Libby Asbestos Proj - Removals (N-079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 5,014,168	\$ 36,737,300	\$ -
9) Asbestos Sampling/Site Assessments (N-131)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937
10) Hazard Ranking System Documentation (N-135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N-097)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	\$ -
12) Robinson Insulation, Minot, ND (N-094)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000	\$ -
13) Western Minerals, Denver, CO (N-088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ -
14) Public Tire Fire	\$ -	\$ 10,000	\$ -	\$ -	\$ -	\$ -
15) Great Falls MT Insulation Site (N-177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ -	\$ -
16) Libby Litigation Support (N-192)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816	\$ -	\$ -
17) Remedial Investigation (N-211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000	\$ -	\$ -
Total EPA Funds Authorized (WAFS)	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500
Costs Incurred						
Description	FY99 Disburse Current Month	FY00 Disburse Current Month	Y01 Disbursed	Current Month	Y02 Disbursed	Current Month
<i>Volpe Engineering:</i>						
Volpe Labor	\$ -	\$ -	\$ 2,364	\$ -	\$ 433	\$ -
Overhead	\$ -	\$ -	\$ 1,538	\$ -	\$ 290	\$ -
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ 1,111	\$ -
<i>Subtotal-Volpe Engineering</i>	\$ -	\$ -	\$ 3,902	\$ -	\$ 723	\$ -
<i>Contracts:</i>						
MWHS						
ECC	\$ 68,476	\$ -	\$ -	\$ -	\$ -	\$ -
Subtotal-Contracts	\$ 68,476	\$ -	\$ -	\$ -	\$ -	\$ -
<i>Equip/Supp/Other:</i>						
Volpe Acq O&I (3.3% of Contracts)	\$ 2,799	\$ -	\$ -	\$ -	\$ 1,373	\$ -
TOTAL COST	\$ 71,274	\$ -	\$ 3,902	\$ -	\$ 723	\$ -
TOTAL AVAILABLE FUNDS						
						\$ 52,761
						<i>Cumulative Disbursed Costs Current Month</i>

<u>Funds Authorized</u>		<u>FY00 Planned</u>		<u>FY01 Planned</u>		<u>FY02 Planned</u>		<u>FY03 Planned</u>	
1) Stockton Removal Action (N- 132)	\$ 5,301,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 10	\$ 6,110,500	\$ 6,110,500		
2) Aspen/Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,349	\$ 132,912	\$ 132,912		
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ -	\$ 30,440	\$ 13,685	\$ 0	\$ 1,315	\$ 1,315		
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500	\$ 11,086,500		
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088	\$ 17,088		
6) Libby Economic Analysis (N- 364)	\$ -	\$ 5,000	\$ 1,793	\$ 0	\$ 0	\$ 3,207	\$ 3,207		
7) Libby Asbestos Proj - Export Plant (N- 423)	\$ -	\$ 500,000	\$ 171,077	\$ 507,637	\$ 1,136,000	\$ 1,136,000			
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 5,493,000	\$ 18,098,894	\$ 5,014,68	\$ 36,737,500	\$ 36,737,500			
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ 20,000	\$ 18,063	\$ 0	\$ 1,937	\$ 1,937			
10) Hazard Ranking Documentation (N- 135)	\$ -	\$ 19,793	\$ 7,790	\$ 0	\$ 30,410	\$ 30,410			
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 100,000	\$ 40,876	\$ 46,882	\$ 57,515	\$ 57,515			
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 30,000	\$ 358,423	\$ 29,881	\$ 487,000	\$ 487,000			
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 233,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ 200,000			
14) Pablo Tire Fire	\$ -	\$ 235,000	\$ -	\$ -	\$ -	\$ -			
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ 10,000	\$ 21,799	\$ 60,000	\$ 60,000	\$ 60,000			
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816	\$ 115,816	\$ 115,816			
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000			
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500			
<u>Costs Incurred</u>									
<u>Description</u>		<u>FY99 Comm.</u>		<u>Current Month</u>		<u>FY00 Comm.</u>		<u>Current Month</u>	
<u>Vulpe Engineering:</u>									
Vulpe Engineering:									
Vulpe Labor	\$ 802	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 802	\$ -
Vulpe Overhead	\$ 513	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 513	\$ -
Vulpe Travel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Subtotal-Vulpe Engineering	\$ 1,315	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,315	\$ -
<u>Contracts:</u>									
Subtotal-Contracts									
Subtotal-Vulpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
TOTAL COST	\$ 1,315	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,315	\$ -
<u>Equip/Supplies(Other):</u>									
Vulpe Acq O/H (3.9% of Contracts)									
TOTAL AVAILABLE FUNDS									

Annual Summary

Financial Summary
At 12/31/02

At 12/31/02

5) Lockwood Solvents (N-386)
Financial Summary
At 12/31/02

<u>Funds Authorized</u>		<u>FY99 Planned</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N-329)	\$ 5,801,000	\$ 1,398,711	\$ 1,098,850	\$ 109,850	\$ 10	\$ 10	\$ 6,110,500
2) Counter-Terrorism Work Plan (N-322 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,349	\$ 0	\$ 132,912
3) Counter-Terrorism Work Plan (N-350)	\$ 15,000	\$ 30,440	\$ 11,685	\$ 13,685	\$ 0	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N-428)	\$ -	\$ 32,841	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 110,086,500	A
5) Lockwood Solvents (N-386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 17,085	\$ 17,088	
6) Libby Economic Analysis (N-064)	\$ -	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ 3,207	
7) Libby Asbestos Proj - Export Plant (N-423)	\$ -	\$ 500,000	\$ 507,657	\$ 234,438	\$ 1,136,000		
8) Libby Asbestos Proj - Reno vals (N-079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 5,014,168	\$ 36,731,300		
9) Asbestos Sampling/Site Assessments (N-131)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ 1,937		
10) Hazard Ranking System Documentation (N-135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ 30,410		
11) Internumin Insulation (SLC, Utah (N-197)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515		
12) Robinson Insulation, Minot, ND (N-094)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000		
13) Western Minerals, Denver, CO (N-088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000		
14) Pablo Tire Fire	\$ -	\$ 10,000	\$ -	\$ -	\$ -		
15) Great Falls MT Insulation Site (N-177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ -		
16) Libby Litigation Support (N-192)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816			
17) Remedial Investigation (N-211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000			
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500	
<u>Costs Incurred</u>							
Description		FY99 Comm.	Current Month	FY00 Comm.	Current Month	FY01 Comm.	Current Month
Volpe Engineering:							
Volpe Labor	\$ -	\$ 1,654	\$ -	\$ 266	\$ -	\$ -	\$ 1,920
Overhead	\$ -	\$ 1,076	\$ -	\$ 179	\$ -	\$ -	\$ 1,255
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Subtotal-Volpe	\$ -	\$ 2,730	\$ -	\$ 445	\$ -	\$ -	\$ 3,175
Contracts:							
Culligan Water	\$ 6,888	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 6,888
Pioneer Water	\$ -	\$ -	\$ 6,320	\$ -	\$ -	\$ -	\$ 6,320
Subtotal-Contracts	\$ 6,888	\$ -	\$ 6,320	\$ -	\$ -	\$ -	\$ 13,208
Equipment/Supplies/Other:							
Volpe Acq OH (3.5% of Contract)	\$ 268	\$ -	\$ 277	\$ -	\$ -	\$ 27	\$ -
TOTAL COST	\$ 7,156	\$ -	\$ 9,302	\$ -	\$ 445	\$ 492	\$ -
TOTAL AVAILABLE FUNDS						\$ 16,903	B
						\$ 185	A-B

5) Lockwood Solvents (N- 386)
Financial Summary
At 12/31/02

Funds Authorized	FY00 Planned			FY01 Planned			FY02 Planned			FY03 Planned			Planned
	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,391,711	\$ 1,093,850	\$ 109,850	\$ 10	\$ 10	\$ 53,727	\$ 53,727	\$ 53,727	\$ 13,349	\$ 13,349	\$ 13,349	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 26,538	\$ 0	\$ 0	\$ 13,685	\$ 13,685	\$ 13,685	\$ 0	\$ 0	\$ 0	\$ 132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 4,819,210	\$ 4,819,210	\$ 4,122,447	\$ 4,122,447	\$ 1,110,725	\$ 1,110,725	\$ 1,110,725	\$ 1,110,725	\$ 1,110,725	\$ 1,110,725	\$ 11,086,500
4) Libby Asbestos Proj. Assessment (N- 428)	\$ -	\$ 32,844	\$ 23,542	\$ 23,542	\$ 185	\$ 185	\$ 1,793	\$ 1,793	\$ 1,793	\$ (0)	\$ (0)	\$ (0)	\$ 17,088
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 5,000	\$ 5,000	\$ 171,077	\$ 171,077	\$ 507,637	\$ 507,637	\$ 507,637	\$ 234,458	\$ 234,458	\$ 234,458	\$ 3,207
6) Libby Economic Analysis (N- 064)	\$ -	\$ 500,000	\$ 5,495,000	\$ 5,495,000	\$ 20,415,372	\$ 20,415,372	\$ 18,098,894	\$ 18,098,894	\$ 18,098,894	\$ 5,014,168	\$ 5,014,168	\$ 5,014,168	\$ 36,737,300
7) Libby Asbestos Proj. - Export Plant (N- 423)	\$ -	\$ -	\$ 19,793	\$ 19,793	\$ 18,063	\$ 18,063	\$ (0)	\$ (0)	\$ (0)	\$ 1,937	\$ 1,937	\$ 1,937	\$ 1,937
8) Libby Asbestos Proj. - Removals (N- 079)	\$ -	\$ -	\$ 100,000	\$ 100,000	\$ 7,790	\$ 7,790	\$ (0)	\$ (0)	\$ (0)	\$ 30,410	\$ 30,410	\$ 30,410	\$ 30,410
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ -	\$ 30,000	\$ 30,000	\$ 40,876	\$ 40,876	\$ 46,882	\$ 46,882	\$ 46,882	\$ 57,515	\$ 57,515	\$ 57,515	\$ 57,515
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ -	\$ 225,000	\$ 225,000	\$ 76,967	\$ 76,967	\$ 358,423	\$ 358,423	\$ 358,423	\$ 487,000	\$ 487,000	\$ 487,000	\$ 487,000
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ -	\$ 10,000	\$ 10,000	\$ -	\$ -	\$ 35,386	\$ 35,386	\$ 35,386	\$ 200,000	\$ 200,000	\$ 200,000	\$ 200,000
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ -	\$ 60,000	\$ 60,000	\$ 60,000	\$ 60,000	\$ 21,799	\$ 21,799	\$ 21,799	\$ 60,000	\$ 60,000	\$ 60,000	\$ 60,000
13) Western Minerals, Denver, CO (N- 083)	\$ -	\$ -	\$ 16,204	\$ 16,204	\$ 115,816	\$ 115,816	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000
14) Pabco Tire Fire	\$ -	\$ -	\$ 26,210,860	\$ 26,210,860	\$ 26,533,497	\$ 26,533,497	\$ 7,814,441	\$ 7,814,441	\$ 7,814,441	\$ 59,290,500	\$ 59,290,500	\$ 59,290,500	\$ 59,290,500
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
16) Libby Litigation Support (N- 192)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
17) Remedial Investigation (N- 211)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Total EPA Funds Authorized	\$ 5,908,000		\$ 10,493,680		\$ 26,210,860		\$ 26,533,497		\$ 7,814,441		\$ 59,290,500		\$ 59,290,500

Costs Incurred

Description	FY00 Accrued			Current Month			FY01 Accrued			Current Month			FY02 Accrued			Current Month			FY03 Accrued			Current Month			Cumulative Accrued Costs			Current Month			
	Volpe Engineering:	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering	Volpe Labor	Overhead	Volpe Travel	Subtotal-Volpe Engineering		
<i>Contracts:</i>																															
<i>Subtotal-Contracts</i>					\$ 2,073	\$ 1,054	\$ 1,076	\$ 2,730	\$ 445	\$ 266	\$ 179	\$ 179	\$ 445	\$ 1,920	\$ 1,255	\$ 1,255	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	\$ 3,175	
<i>Equip/Supplies/Other:</i>																															
<i>Subtotal-Equip/Other:</i>					\$ 2,073	\$ 6,320	\$ 6,320	\$ 6,320	\$ -	\$ 225	\$ 225	\$ 225	\$ -	\$ 2,073	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320	\$ 6,320		
<i>Volpe Accr D/H (3.9% of Contracts)</i>					\$ 2,468	\$ 1,154	\$ 1,154	\$ 1,154	\$ -	\$ 445	\$ 445	\$ 445	\$ -	\$ 2,468	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154	\$ 1,154		
TOTAL AVAILABLE FUNDS					\$ 2,341					\$ 2,302					\$ 445					\$ 445					\$ 12,088				\$ 5,000		

Financial Summary

Financial Summary

	FY'99 Planned	FY'00 Planned	FY'01 Planned	FY'02 Planned	FY'03 Planned	Planned
1) Stockton Removal Action (N- 329)	\$ 3,801,000	\$ 1,398,711	\$ 109,830	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park and N-215	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 0	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ 3,207	\$ -
7) Libby Asbestos Proj - Export Plan (N- 423)	\$ -	\$ 500,000	\$ 171,077	\$ 507,637	\$ 234,458	\$ 1,136,000
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 5,491,000	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,200
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	\$ -
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 235,000	\$ 338,423	\$ 29,881	\$ 487,000	\$ -
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ -
14) Pablo Tie Five	\$ -	\$ 10,000	\$ -	\$ -	\$ -	\$ -
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ -	\$ 60,000	\$ 21,799	\$ 60,000	\$ -
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816	\$ -	\$ -
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000	\$ -	\$ -
Total EPA Funds Authorized \$	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,531,497	\$ 7,814,441	\$ 59,290,500
Costs Incurred						
Description	FY'99 Accrued	Current Month	FY'00 Accrued	Current Month	FY'01 Accrued	Cumulative
Volpe Engineering:						Current Month
Volpe Labor \$	- \$	- \$	- \$	- \$	- \$	\$ 1,943
Overhead \$	- \$	- \$	- \$	- \$	- \$	\$ 1,264
Volpe Travel \$	- \$	- \$	- \$	- \$	- \$	\$ -
Subtotal-Volpe Engineering \$	- \$	- \$	- \$	- \$	- \$	\$ 3,207
Contracts:						
Subtotal-Contracts \$	- \$	- \$	- \$	- \$	- \$	\$ -
Equip/Supplies/Other:						
Volpe Acq OH (3.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
TOTAL COST \$	- \$	- \$	- \$	- \$	- \$	\$ 3,207
TOTAL AVAILABLE FUNDS						

7) Libby Asbestos Proj - Export Plant (N- 4123)
 Financial Summary

At 12/31/02

<u>Funds Authorized</u>		<u>FY'99 Planned</u>	<u>FY'00 Planned</u>	<u>FY'01 Planned</u>	<u>FY'02 Planned</u>	<u>FY'03 Planned</u>	<u>Planned</u>			
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10,10	\$ 10	\$ 6,110,500	\$ 6,110,500			
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,685	\$ 51,727	\$ 1,349	\$ 1,349	\$ 132,912	\$ 132,912			
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 26,538	\$ 13,685	\$ 1,349	\$ 1,349	\$ 1,315	\$ 1,315			
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 30,440	\$ 13,685	\$ 1,349	\$ 1,349	\$ 11,086,500	\$ 11,086,500			
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 4,122,447	\$ 1,110,725	\$ 1,110,725			
6) Libby Economic Analysis (N- 664)	\$ -	\$ 5,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088	\$ 17,088			
7) Libby Asbestos Proj - Export Plant (N- 4123)	\$ 500,000	\$ 1,793	\$ 1,793	\$ (0)	\$ (0)	\$ 3,207	\$ 3,207			
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 171,077	\$ 507,637	\$ 234,458	\$ 234,458	\$ 1,136,000	\$ 1,136,000			
9) Asbestos Sampling/Site Assessments (N- 111)	\$ -	\$ 5,493,000	\$ 18,098,894	\$ 5,014,168	\$ 5,014,168	\$ 36,737,300	\$ 36,737,300			
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ 20,000	\$ 18,063	\$ (0)	\$ (0)	\$ 1,937	\$ 1,937			
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ (0)	\$ 30,410	\$ 30,410			
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 46,882	\$ 57,515	\$ 57,515			
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 215,000	\$ 358,423	\$ 29,881	\$ 29,881	\$ 487,000	\$ 487,000			
14) Pablo Tire Fire	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 35,386	\$ 200,000	\$ 200,000			
15) Great Falls MT Insulation Site (N- 177)	\$ 10,000	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -			
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ 60,000	\$ 60,000	\$ 60,000			
17) Remedial Investigation (N- 211)	\$ -	\$ 60,000	\$ 16,204	\$ 115,816	\$ 115,816	\$ -	\$ -			
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,880	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 3,113,000	\$ 3,113,000			
<u>Costs Incurred</u>						\$ 59,290,500				
Description		<u>FY'99 Comm.</u>	<u>Current Month</u>	<u>FY'00 Comm.</u>	<u>Current Month</u>	<u>FY'01 Comm.</u>	<u>Current Month</u>	<u>Cumulative</u>	<u>Committed Costs</u>	<u>Current Month</u>
<i>Volpe Engineering:</i>										
Volpe Labor	\$ -	\$ 3,130	\$ -	\$ 9,583	\$ -	\$ 2,154	\$ -	\$ 3,947	\$ 575	\$ 575
Overhead	\$ -	\$ -	\$ 2,037	\$ -	\$ 6,424	\$ -	\$ 1,403	\$ 2,565	\$ 374	\$ 374
Volpe Travel	\$ -	\$ -	\$ -	\$ 2,845	\$ -	\$ -	\$ -	\$ -	\$ 2,845	\$ -
<i>Subtotal-Volpe Engineering</i>	\$ -	\$ 5,166	\$ -	\$ 18,852	\$ -	\$ 3,556	\$ -	\$ 6,512	\$ 948	\$ 948
<i>Contracts:</i>										
Markor	\$ -	\$ -	\$ -	\$ 28,311	\$ -	\$ -	\$ -	\$ -	\$ 28,311	\$ -
Kuo	\$ -	\$ -	\$ -	\$ 150,000	\$ -	\$ 181,489	\$ -	\$ 331,489	\$ -	\$ -
CDM	\$ -	\$ 312,687	\$ -	\$ 102,744	\$ -	\$ 418,487	\$ -	\$ 30,000	\$ 685,607	\$ -
<i>Subtotal-Contracts</i>	\$ -	\$ 312,687	\$ -	\$ 102,744	\$ -	\$ 418,487	\$ -	\$ 211,489	\$ -	\$ 1,045,407
<i>Equip/Supplies/Other:</i>										
Volpe Acq DMH (3.9% of Contracts)	\$ -	\$ 11,059	\$ -	\$ 8,900	\$ -	\$ 42	\$ -	\$ 42	\$ 8,942	\$ -
<i>TOTAL COST</i>	\$ -	\$ 328,923	\$ -	\$ 134,440	\$ -	\$ 16,992	\$ -	\$ 8,248	\$ 39,355	\$ -
TOTAL AVAILABLE FUNDS										
						\$ 8,209		\$ 1,127,791	\$ 948	B

7) Libby Asbestos Proj - Export Plant (N- 423)

Financial Summary

- At 12/31/02

8) Libby Asbestos Proj - Removals (N- 079)
 Financial Summary
 At 12/31/02

<u>Funds Authorized</u>		<u>FY'99 Planned</u>	<u>FY'00 Planned</u>	<u>FY'01 Planned</u>	<u>FY'02 Planned</u>	<u>FY'03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,301,000	\$ 1,398,711	\$ 1,098,850	\$ 10	\$ 10	\$ 6,110,500	
2) Asper Park Solvents (N- 215)	\$ 75,000	\$ 13,885	\$ 26,538	\$ 53,727	\$ 53,349	\$ 132,912	
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 0	\$ 0	\$ 1,315	
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500	
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ -	\$ 3,000,000	\$ 185	\$ 185	\$ 17,088	
6) Libby Economic Analysis (N- 064)	\$ -	\$ 5,000	\$ 23,342	\$ (0)	\$ (0)	\$ 3,207	
7) Libby Asbestos Proj - Export Plant (N- 423)	\$ -	\$ 500,000	\$ 1,793	\$ 507,637	\$ 224,458	\$ 1,136,000	
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 171,077	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300	
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ 5,493,000	\$ 20,000	\$ 18,063	\$ (0)	\$ 1,937	
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410	
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	
12) Robinson insulation, Minot, ND (N- 094)	\$ -	\$ 235,000	\$ 235,000	\$ 358,433	\$ 29,881	\$ 487,000	
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 76,967	\$ 76,967	\$ 35,386	\$ 200,000		
14) Pablo Tire Fire	\$ -	\$ -	\$ 10,000	\$ 60,000	\$ 23,799	\$ 60,000	
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ 60,000	\$ 60,000	\$ 16,204	\$ 115,816		
16) Libby Litigation Support (N- 192)	\$ -	\$ 3,113,000	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000		
17) Remedial Investigation (N- 211)	\$ -	\$ 26,533,497	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500		
Total EPA Funds Authorized	\$ 5,508,000		\$ 10,493,680		\$ 26,210,860		
<u>Costs Incurred</u>							
<u>Description</u>		<u>FY'99 Comm. Current Month</u>	<u>FY'00 Comm. Current Month</u>	<u>FY'01 Comm. Current Month</u>	<u>FY'02 Comm. Current Month</u>	<u>FY'03 Comm. Current Month</u>	<u>Cumulative Committed Costs Current Month</u>
<u>Volpe Engineering:</u>							
Volpe Labor	\$ -	\$ 47,269	\$ 251,836	\$ 360,173	\$ 104,003	\$ 333,333	\$ 33,333
Overhead	\$ -	\$ 30,758	\$ 168,806	\$ 234,616	\$ 67,602	\$ 21,666	\$ 21,666
Volpe In-House Support	\$ -	\$ 1,440	\$ 38,710	\$ 91,472	\$ 22,164	\$ 203,786	\$ -
Volpe Travel	\$ -	\$ 13,814	\$ 78,639	\$ 74,901	\$ 1,322	\$ 22,862	\$ 190,276
Subtotal-Volpe Engineering	\$ -	\$ 93,141	\$ 537,991	\$ 761,153	\$ 1,392	\$ 266,639	\$ 12,392
<u>Contracts:</u>							
New Contractors (Competitive and 95%)	Marcor	\$ -	\$ 2,364,167	\$ 9,087,025	\$ 3,782,743	\$ 387,111	\$ 15,621,047
Kuo		\$ -	\$ -	\$ 25,000	\$ 25,000	\$ 50,000	\$ -
MWH		\$ -	\$ 603,329	\$ 1,431,547	\$ 870,131	\$ (30,152)	\$ 2,905,007
LHC re Middle School/New Contract (High School)		\$ -	\$ 18,214	\$ 18,214	\$ 18,214	\$ 18,214	\$ (50,152)
Topsoil/Fill/Riprap (Multiple)	Crookstank	\$ -	\$ 819,103	\$ 1,407,284	\$ 291,000	\$ 2,517,387	\$ -
Relocations (Multiple)	City of Libby	\$ -	\$ 8,985	\$ 8,985	\$ 8,985	\$ 8,985	\$ -
Appraisal Support		\$ -	\$ 24,200	\$ 19,745	\$ 54,989	\$ (1,500)	\$ 98,914
Security Guard Services (Multiple)	ECC	\$ -	\$ 29,259	\$ 100,228	\$ 20,000	\$ 20,000	\$ (1,500)
CDM		\$ -	\$ 873,969	\$ 1,317,683	\$ 21,444	\$ 25,000	\$ 25,000
Subtotal-Contracts		\$ -	\$ 3,291,596	\$ 14,521,176	\$ 3,066,658	\$ 3,218,514	\$ 154,482
Equip/Supplies/Other:		\$ -	\$ 28,385	\$ 10,943,357	\$ (1,500)	\$ 3,782,336	\$ 1,931,884
Volpe Acq/Ops (3.9% of Contracts)		\$ -	\$ 2,076	\$ 70,912	\$ 6,770	\$ 90	\$ 108,303
TOTAL COST		\$ -	\$ 116,615	\$ 426,795	\$ (59)	\$ 150,590	\$ 1,223,575
		\$ -	\$ 3,503,628	\$ 16,017,277	\$ 12,202,226	\$ 30,360	\$ 30,301
TOTAL AVAILABLE FUNDS				\$ 807,882		\$ 35,929,418	\$ 874,644 B

8) Libby Asbestos Proj - Removals (N-079)
 Financial Summary
 A1 12/31/02

	<u>Funds Authorized</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N-329)	\$ 5,801,000	\$ 1,398,711	\$ 109,830	\$ 10	\$ 10	\$ 6,10,500
2) Aspen Park Solvents (N-332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 51,727	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N-350)	\$ 15,000	\$ 20,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N-428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N-386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N-064)	\$ -	\$ 5,000	\$ 1,793	\$ (0)	\$ (0)	\$ 3,207
7) Libby Asbestos Proj - Export Plant (N-423)	\$ -	\$ 500,000	\$ 171,077	\$ 507,537	\$ 234,458	\$ 1,136,000
8) Libby Asbestos Proj - Removals (N-079)	\$ -	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300	\$ 61,188
9) Asbestos Sampling/Site Assessments (N-131)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937
10) Hazard Ranking System Documentation (N-135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N-097)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	\$ -
12) Robinson Insulation, Minot, ND (N-094)	\$ -	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000	\$ -
13) Western Minerals, Denver, CO (N-088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ -
14) Pablo Tire Fire	\$ -	\$ 10,000	\$ -	\$ -	\$ -	\$ -
15) Great Falls MT Insulation Site (N-177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ -	\$ -
16) Libby Litigation Support (N-192)	\$ -	\$ 3,113,000	\$ 16,204	\$ 115,816	\$ -	\$ -
17) Remedial Investigation (N-211)	\$ -	\$ 3,129,395	\$ 3,113,000	\$ 3,113,000	\$ -	\$ -
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500
<i>Costs Incurred</i>						
Description	<u>FY99 Accrued</u>	<u>Current Month</u>	<u>FY00 Accrued</u>	<u>Current Month</u>	<u>FY01 Accrued</u>	<u>Current Month</u>
<i>Voice Engineering:</i>						
Voice Labor	\$ -	\$ -	\$ 47,269	\$ -	\$ 251,836	\$ -
Overhead	\$ -	\$ -	\$ 30,758	\$ -	\$ 168,806	\$ -
Voice In-House Support	\$ -	\$ -	\$ 1,440	\$ -	\$ 38,710	\$ -
Voice Travel	\$ -	\$ -	\$ 13,974	\$ -	\$ 78,639	\$ -
<i>Subtotal-Voice Engineering</i>	\$ -	\$ 93,741	\$ -	\$ 537,991	\$ -	\$ 74,901
<i>Contracts:</i>						
New Contractors (Competitive and 8A)	\$ -	\$ -	\$ 2,364,167	\$ -	\$ 9,058,934	\$ -
Kuon	\$ -	\$ -	\$ -	\$ -	\$ 597,607	\$ -
MWHLIC re Middle School/New Contract High School Topsou/Fill/RipRap (Multiple)	\$ -	\$ -	\$ -	\$ -	\$ 1,401,738	\$ -
Crookshank	\$ -	\$ -	\$ -	\$ -	\$ 18,035	\$ -
Relocations (Multiple)	\$ -	\$ -	\$ 24,200	\$ -	\$ 45,281	\$ -
City of Libby Appraisal Support	\$ -	\$ -	\$ -	\$ -	\$ 1,427,752	\$ -
Security Guard Services (Multiple)	\$ -	\$ -	\$ 27,459	\$ -	\$ 8,985	\$ -
ECC	\$ -	\$ -	\$ -	\$ -	\$ 33,997	\$ -
CDM	\$ -	\$ -	\$ 873,969	\$ -	\$ 2,918,537	\$ -
<i>Subtotal-Contracts</i>	\$ -	\$ 3,289,796	\$ -	\$ 14,835,578	\$ -	\$ 10,599,142
<i>Equip/Supplies/Other:</i>						
Vope Acq OH (3.9% of Contracts)	\$ -	\$ 2,076	\$ 25,244	\$ -	\$ 55,662	\$ -
		\$ 116,615	\$ -	\$ 329,525	\$ (59)	\$ 47,730
TOTAL COST	\$ -	\$ 3,501,228	\$ -	\$ 15,928,338	\$ -	\$ 11,842,762
TOTAL AVAILABLE FUNDS						\$ 3,631,477

Financial Summary
At 12/31/02

At 12/31/02

At 12/31/02

- At [2/3] /()

10) Libby Hazard Ranking System Documentation (N- 135)
 Financial Summary
 At 12/31/02

	<u>FY99 Planned</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,830	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,685	\$ 53,727	\$ 5	\$ 13,349	\$ 132,912
3) Counter-Terrorist Work Plan (N- 350)	\$ 15,000	\$ 26,538	\$ 13,685	\$ 5	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 30,440	\$ 13,685	\$ 5	\$ 0	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ -	\$ 3,000,000	\$ 23,542	\$ 5	\$ 185	\$ (0)
7) Libby Asbestos Proj - Export Plan (N- 423)	\$ -	\$ 5,000	\$ 1,793	\$ 5	\$ 0	\$ 3,207
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 500,000	\$ 171,077	\$ 5	\$ 234,458	\$ 1,136,000
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ 5,493,000	\$ 18,098,894	\$ 5	\$ 5,014,168	\$ 36,737,300
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ 20,000	\$ 19,793	\$ 5	\$ (0)	\$ 1,937
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 100,000	\$ 7,790	\$ 5	\$ (0)	\$ 30,410
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 30,000	\$ 40,876	\$ 5	\$ 46,882	\$ 57,515
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 225,000	\$ 358,423	\$ 5	\$ 29,881	\$ 487,000
14) Pablo Tire Fire	\$ -	\$ 235,000	\$ 76,967	\$ 5	\$ 35,386	\$ 200,000
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ 10,000	\$ -	\$ 5	\$ -	\$ -
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 60,000	\$ 5	\$ 23,799	\$ 60,000
17) Remedial Investigation (N- 211)	\$ -	\$ 60,000	\$ 16,204	\$ 5	\$ 115,816	\$ -
Total EPA Funds Authorized \$	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500
<u>Costs Incurred</u>						
<u>1) Voice Engineering:</u>						
<u>FY99 Accrued</u>	<u>Current Month</u>	<u>FY00 Accrued</u>	<u>Current Month</u>	<u>FY01 Accrued</u>	<u>Current Month</u>	<u>FY02 Accrued</u>
Voice Labor \$	\$ -	\$ -	\$ -	\$ 231	\$ -	\$ -
Overhead \$	\$ -	\$ -	\$ -	\$ 155	\$ -	\$ -
Voice Travel \$	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
<u>Subtotal Voice Engineering</u> \$	\$ -	\$ -	\$ -	\$ 386	\$ -	\$ -
<u>Contracts:</u>						
<u>FY99 Accrued</u>	<u>Current Month</u>	<u>FY00 Accrued</u>	<u>Current Month</u>	<u>FY01 Accrued</u>	<u>Current Month</u>	<u>FY02 Accrued</u>
CDM \$	\$ -	\$ -	\$ -	\$ 26,739	\$ -	\$ -
<u>Subtotal Contracts</u> \$	\$ -	\$ -	\$ -	\$ 26,739	\$ -	\$ -
<u>Equip/Supplies/Other:</u>						
<u>FY99 Accrued</u>	<u>Current Month</u>	<u>FY00 Accrued</u>	<u>Current Month</u>	<u>FY01 Accrued</u>	<u>Current Month</u>	<u>FY02 Accrued</u>
Total Cost \$	\$ -	\$ -	\$ -	\$ 1,025	\$ -	\$ -
<u>TOTAL AVAILABLE FUNDS</u>						
	\$ 28,150	\$ -	\$ -	\$ -	\$ 28,150	\$ -
					\$ 2,260	

II) Intermountain Insulation, SLC, Utah (N-097)
 Financial Summary
 A 12/23/02

	FY99 Planned	FY00 Planned	FY01 Planned	FY02 Planned	FY03 Planned	Planned
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 0	\$ 6,110,500
2) Aspen Park Solvents (N- 322 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 51,727	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ -	\$ 5,000	\$ 1,793	\$ (0)	\$ (0)	\$ 3,207
7) Libby Asbestos Proj - Export Plant (N- 421)	\$ -	\$ 500,000	\$ 171,077	\$ 507,637	\$ 234,458	\$ 1,136,000
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ -	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300
9) Asbestos Sampling/Site Assessments (N- 131)	\$ 5,493,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937	\$ 1,937
10) Hazard Ranking System (N- 135)	\$ 20,000	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410	\$ 30,410
II) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,515	A
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 215,000	\$ 358,423	\$ 29,881	\$ 487,000	
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 255,000	\$ 76,967	\$ 35,386	\$ 200,000	
14) Pablo Tire Fire	\$ -	\$ 10,000	\$ -	\$ -	\$ -	
15) Great Falls MT. Insulation Site (N- 177)	\$ -	\$ 60,000	\$ 23,799	\$ 60,000	\$ 115,816	
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ 16,204	\$ 3,113,000	\$ 3,113,000	
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,000	\$ 1,289,395	\$ 7,814,441	\$ 59,290,500	
Total EPA Funds Authorized \$	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 78,144,441	
<i>Costs Incurred</i>						
Description	FY99 Comm.	Current Month	FY00 Comm.	Current Month	FY01 Comm	Cumulative
<i>Voice Engineering:</i>						Current Month
Voice Labor	\$ -	\$ -	\$ -	\$ -	\$ 1,766	164
Overhead	\$ -	\$ -	\$ -	\$ -	\$ 530	4,358
Voice Travel	\$ -	\$ -	\$ -	\$ -	\$ 1,190	\$ 1,150
Subtotal-Voice Engineering	\$ -	\$ -	\$ -	\$ -	\$ 723	\$ 107
<i>Contracts:</i>						
CDM	\$ -	\$ -	\$ -	\$ -	\$ 3,689	\$ 1,510
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 271
<i>Equip/Supplies/Other:</i>						
Upfr Acq/DHI (1.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ 5249	\$ 3,249
TOTAL COST \$	\$ -	\$ -	\$ -	\$ -	\$ 9,124	\$ 1,510
TOTAL AVAILABLE FUNDS						
					\$ 3,585	A-B

11) Intermountain Insulation, SLC, Utah (N-097) •
Financial Summary

At 12/31/02

<u>Costs Incurred</u>												
Description	FY'99 Accrued		Current Month		FY'00 Accrued		Current Month		FY'01 Accrued		Current Month	
	FY'99 Planned	FY'00 Planned	FY'00 Actual	FY'00 Actual	FY'00 Planned	FY'00 Actual	FY'01 Actual	FY'01 Actual	FY'01 Planned	FY'01 Actual	FY'02 Actual	FY'02 Actual
<i>Voice Engineering:</i>												
Voice Labor	\$ -	\$ 5,801,000	\$ -	\$ 1,398,711	\$ -	\$ 109,830	\$ -	\$ 10	\$ 10	\$ 10	\$ 6,110,500	\$ 6,110,500
Voice Overhead	\$ -	\$ 75,000	\$ -	\$ 13,685	\$ -	\$ 26,518	\$ -	\$ 51,727	\$ 51,727	\$ 51,727	\$ 132,912	\$ 132,912
Voice Travel	\$ -	\$ 15,000	\$ -	\$ 30,440	\$ -	\$ 13,685	\$ -	\$ 13,685	\$ 13,685	\$ 13,685	\$ 1,315	\$ 1,315
<i>Subtotal-Voice Engineering</i>	\$ -	\$ 17,000	\$ -	\$ 32,844	\$ -	\$ 4,819,210	\$ -	\$ 4,122,447	\$ 4,122,447	\$ 4,122,447	\$ 11,086,500	\$ 11,086,500
<i>Contracts:</i>												
CDM	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,000,000	\$ -	\$ 23,542	\$ 23,542	\$ 23,542	\$ 17,088	\$ 17,088
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,000	\$ -	\$ 1,793	\$ 1,793	\$ 1,793	\$ 3,207	\$ 3,207
<i>Equip/Supplies/Other:</i>												
Voice Act/Off (3.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 500,000	\$ -	\$ 171,077	\$ 171,077	\$ 171,077	\$ 1,136,000	\$ 1,136,000
TOTAL COST	\$ -	\$ 5,908,000	\$ -	\$ 10,493,680	\$ -	\$ 26,210,360	\$ -	\$ 26,533,497	\$ 26,533,497	\$ 26,533,497	\$ 781,441	\$ 781,441
TOTAL AVAILABLE FUNDS	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 9,124	\$ -	\$ 1,510	\$ 1,510	\$ 1,510	\$ 59,290,500	\$ 59,290,500

<u>Funds Authorized</u>	<u>FY'99 Planned</u>	<u>FY'00 Planned</u>	<u>FY'01 Planned</u>	<u>FY'02 Planned</u>	<u>FY'03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N-332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N-350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N-428)	\$ 5	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,10,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,342	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ 3,207	\$ -
7) Libby Asbestos Proj - Export Plant (N- 423)	\$ 500,000	\$ 17,077	\$ 507,637	\$ 234,438	\$ 1,136,000	\$ -
8) Libby Asbestos Proj - Removals (N- 079)	\$ 5,493,000	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300	\$ -
9) Asbestos Sampling/Site Assessments (N- 131)	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937	\$ -
10) Hazard Ranking System Documentation (N- 135)	\$ 100,000	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410	\$ -
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ 30,000	\$ 40,876	\$ 46,882	\$ 57,151	\$ -	\$ -
12) Robinson Insulation, Minot, ND (N- 094)	\$ 235,000	\$ 358,473	\$ 29,881	\$ 487,000	\$ A	\$ -
13) Western Minerals, Denver, CO (N- 088)	\$ 235,000	\$ 76,967	\$ 35,366	\$ 200,000	\$ -	\$ -
14) Pablo Tire Fire	\$ 10,000	\$ -	\$ -	\$ -	\$ -	\$ -
15) Great Falls MT Insulation Site (N- 177)	\$ 60,000	\$ 60,000	\$ 23,799	\$ 60,000	\$ -	\$ -
16) Libby Litigation Support (N- 192)	\$ 60,000	\$ 16,204	\$ 115,816	\$ -	\$ -	\$ -
17) Remedial Investigation (N- 211)	\$ 3,113,000	\$ 1,299,395	\$ 3,113,000	\$ -	\$ -	\$ -
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,531,497	\$ 7,814,441	\$ 59,290,500
<u>Costs Incurred</u>						
Description	<u>FY'99 Comm.</u>	<u>Current Month</u>	<u>FY'00 Comm.</u>	<u>Current Month</u>	<u>FY'01 Comm.</u>	<u>Current Month</u>
<u>Volpe Engineering:</u>						
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ 17,637	\$ 41
Overhead	\$ -	\$ -	\$ -	\$ -	\$ 534	\$ 31,145
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ 347	\$ 27
Subtotal-Volpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ 27	\$ 20,532
Contracts:					\$ 14,792	\$ 27
C DM	\$ -	\$ -	\$ -	\$ -	\$ 68	\$ -
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ 66,470	\$ 68
<u>Equip/Supplies/Other:</u>						
Volpe Acq OH (3.2% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
TOTAL COST	\$ -	\$ -	\$ 116,577	\$ -	\$ 23,147	\$ 68
<u>TOTAL AVAILABLE FUNDS</u>					\$ 480,266	\$ 68
					\$ 6,734	B
					A-B	

Initial Jump

AI 12/31/02

AI 12/31/02

	<u>FY99 Authorized</u>	<u>FY99 Planned</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,830	\$ 10 10	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 13,349	\$ 132,912	
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315	
4) Libby Asbestos Proj Assessment (N- 428)	\$ 32,844	\$ 3,000,000	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500	
5) Lockwood Solvents (N- 186)	\$ 17,000	\$ 5,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088	
6) Libby Economic Analysis (N- 064)	\$ -	\$ 500,000	\$ 1,793	\$ (0)	\$ 3,207		
7) Libby Asbestos Proj. Export Plant (N- 423)	\$ -	\$ 171,077	\$ 507,637	\$ 224,438	\$ 1,136,000		
8) Libby Asbestos Proj. Removals (N- 079)	\$ 5,493,000	\$ 20,415,372	\$ 18,096,894	\$ 5,014,168	\$ 36,737,300		
9) Asbestos Sampling/Site Assessments (N- 131)	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937		
10) Hazard Ranking System Documentation (N- 135)	\$ 100,000	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410		
11) Intermountain Insulation, SLC, Utah (N- 057)	\$ 30,000	\$ 30,000	\$ 48,876	\$ 46,882	\$ 57,515		
12) Robinson Insulation, Minot, ND (N- 094)	\$ 235,000	\$ 235,000	\$ 358,423	\$ 29,881	\$ 487,000		
13) Western Minerals, Denver, CO (N- 088)	\$ 10,000	\$ 76,967	\$ 35,386	\$ 200,000			
14) Pablo Tire Fire							
15) Great Falls MT Insulation Site (N- 177)	\$ 60,000	\$ 60,000	\$ 23,799	\$ 60,000			
16) Libby Irrigation Support (N- 192)	\$ 60,000	\$ 60,000	\$ 16,204	\$ 115,816			
17) Remedial Investigation (N- 211)	\$ 3,113,000	\$ 3,113,000	\$ 1,289,395	\$ 3,113,000			
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,290,500	
<u>Costs Incurred</u>							
	<u>FY99 Comm.</u>	<u>Current Month</u>	<u>FY00 Comm.</u>	<u>Current Month</u>	<u>FY01 Comm.</u>	<u>Current Month</u>	<u>FY02 Comm.</u>
							<u>Committed Costs</u>
							<u>Cumulative</u>
							<u>Current Month</u>
<i>Volpe Engineering:</i>							
<i>Volpe Engineering:</i>							
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ 11,940	\$ 1746	\$ 205
Overhead	\$ -	\$ -	\$ -	\$ -	\$ 8,003	\$ 5,046	\$ 205
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ 1,528	\$ 177	\$ 133
<i>Subtotal-Volpe Engineering</i>	\$ -	\$ -	\$ -	\$ -	\$ 21,471	\$ -	\$ 133
<i>Contracts:</i>							
<i>CDM Contracts</i>	\$ -	\$ -	\$ -	\$ -	\$ 98,095	\$ 25,822	\$ -
<i>Subtotal-Contracts</i>	\$ -	\$ -	\$ -	\$ -	\$ 98,095	\$ 25,822	\$ 121,918
<i>Equip/Supplies/Other:</i>							
<i>Volpe Acq OH (3.2% of Contracts)</i>	\$ -	\$ -	\$ -	\$ -	\$ 3,466	\$ 1,797	\$ -
TOTAL COST	\$ -	\$ -	\$ -	\$ -	\$ 123,033	\$ 41,581	\$ 164,953
TOTAL AVAILABLE FUNDS					\$ 35,047	\$ 339	A-B

Funds Authorized																	
1) Stockton Removal Action (N-1329)	\$ 5,801,000																
2) Aspen Park Solvents (N-1215)	\$ 13,685																
3) Counter-Terrorism Work Plan (N-1350)	\$ 15,000																
4) Libby Asbestos Proj Assessment (N-428)	\$ 30,440																
5) Lockwood Software (N-386)	\$ 32,844																
6) Libby Economic Analysis (N-064)	\$ 4,819,210																
7) Libby Asbestos Proj - Export Plan (N-423)	\$ 23,542																
8) Libby Asbestos Proj - Removals (N-079)	\$ 185																
9) Asbestos Sampling/Site Assessments (N-131)	\$ 1,793																
10) Hazard Rating System Documentation (N-135)	\$ 1,793																
11) Intermountain Insulation, SLC, Utah (N-097)	\$ 507,637																
12) Robinson Insulation, Minot, ND (N-094)	\$ 234,458																
13) Western Minerals, Denver, CO (N-088)	\$ 5,014,168																
14) Pablo Tire Fire	\$ 0																
15) Great Falls MT Insulation Site (N-177)	\$ 30,410																
16) Libby Litigation Support (N-192)	\$ 57,515																
17) Remedial Investigation (N-211)	\$ 1,136,000																
Total EPA Funds Authorized	\$ 5,998,000																
Costs Incurred																	
Volpe Engineering:																	
FY22 Accrued																	
Volpe Engineering:																	
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 11,940	\$ -	\$ 7,746	\$ -	\$ 205	\$ 205	\$ 19,891	\$ 205	\$ 205	
Overhead	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 8,003	\$ -	\$ 5,046	\$ -	\$ 133	\$ 133	\$ 13,182	\$ 133	\$ 133	
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,528	\$ -	\$ 177	\$ -	\$ -	\$ -	\$ 1,705	\$ -	\$ -	
Subtotal Volpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 21,471	\$ -	\$ 12,669	\$ -	\$ 339	\$ 339	\$ 34,778	\$ 339	\$ 339	
Contracts:																	
CDM	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 98,096	\$ -	\$ 24,822	\$ -	\$ -	\$ -	\$ 122,918	\$ -	\$ -	
Subtotal Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 98,096	\$ -	\$ 24,822	\$ -	\$ -	\$ -	\$ 122,918	\$ -	\$ -	
Equip/Supplies/Other:																	
Volpe Acq O/H (3.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 3,466	\$ -	\$ 1,797	\$ -	\$ -	\$ -	\$ 1,797	\$ -	\$ -	
TOTAL COST	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 123,033	\$ -	\$ 339	\$ -	\$ 339	\$ 339	\$ 163,933	\$ 339	\$ 36,047	
TOTAL AVAILABLE FUNDS																	
FY22 Planned	\$ 1,98,711																
FY23 Planned	\$ 109,850																
FY24 Planned	\$ 10																
FY22 Accrued																	
Current Month																	
FY22 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	
Current Month																	
FY24 Accrued																	
Current Month																	
FY23 Accrued																	

At 12/31/02

	Funds Authorized									
	FY99 Planned		FY00 Planned		FY01 Planned		FY02 Planned		FY03 Planned	
1) Stockton Removal Action (N-329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 5,10	\$ 10	\$ 6,110,500	\$ 110,500	\$ 132,912	\$ 132,912
2) Aspen Park Solvents (N-332 and N-215)	\$ 15,000	\$ 13,685	\$ 26,538	\$ 53,727	\$ 0	\$ 0	\$ 13,349	\$ 0	\$ 1,315	\$ 1,315
3) Counter-Terrorism Work Plan (N-350)	\$ -	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 0	\$ 0	\$ 0	\$ 1,110,725	\$ 1,106,500
4) Libby Asbestos Proj Assessment (N-428)	\$ 5	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 5	\$ 5	\$ 185	\$ 185	\$ 17,088	\$ 17,088
5) Lockheed Solvents (N-386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 1,793	\$ 5	\$ 5	\$ 0	\$ 0	\$ 3,207	\$ 3,207
6) Libby Economic Analysis (N-364)	\$ 5	\$ 5,000	\$ 1,793	\$ 171,077	\$ 5	\$ 5	\$ 507,637	\$ 523,458	\$ 1,136,000	\$ 1,136,000
7) Libby Asbestos Proj - Export Plant (N-423)	\$ -	\$ 500,000	\$ 20,415,372	\$ 18,098,879	\$ 5	\$ 5	\$ 5,014,168	\$ 5,014,168	\$ 36,737,300	\$ 36,737,300
8) Libby Asbestos Proj - Removals (N-079)	\$ 5	\$ 5,493,000	\$ 18,063	\$ 19,793	\$ 5	\$ 5	\$ 18,063	\$ 18,063	\$ 1,937	\$ 1,937
9) Asbestos Sampling/Site Assessments (N-131)	\$ 20,000	\$ 100,000	\$ 7,790	\$ 7,790	\$ 5	\$ 5	\$ (0)	\$ 30,410	\$ 46,832	\$ 57,515
10) Hazard Ranking System Documentation (N-135)	\$ 5	\$ 30,000	\$ 40,876	\$ 40,876	\$ 5	\$ 5	\$ 358,423	\$ 29,881	\$ 487,000	\$ 487,000
11) Intermountain Insulation, SLC, Utah (N-097)	\$ 5	\$ 235,000	\$ 235,000	\$ 235,000	\$ 5	\$ 5	\$ 76,967	\$ 35,386	\$ 200,000	\$ 200,000
12) Robinson Insulation, Minot, ND (N-094)	\$ 5	\$ 275,000	\$ 10,000	\$ 10,000	\$ 5	\$ 5	\$ 60,000	\$ 23,799	\$ 69,000	\$ 69,000
13) Western Minerals, Denver, CO (N-088)	\$ 5	\$ 60,000	\$ 60,000	\$ 60,000	\$ 5	\$ 5	\$ 16,204	\$ 16,204	\$ 115,816	\$ 115,816
14) Pablo Tire Fire	\$ 5	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000	\$ 5	\$ 5	\$ 1,289,395	\$ 3,113,000	\$ 3,113,000	\$ 3,113,000
15) Great Falls MT Insulation Site (N-177)	\$ 5	\$ 26,210,860	\$ 26,533,497	\$ 26,533,497	\$ 5	\$ 5	\$ 7,814,441	\$ 59,280,500	\$ 59,280,500	\$ 59,280,500
16) Libby Litigation Support (N-192)	\$ 5	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
17) Remedial Investigation (N-211)	\$ 5	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,280,500	\$ -	\$ -	\$ -	\$ -
<i>Costs Incurred</i>										
<i>Voice Engineering:</i>										
FY99 Comm.	Current Month	FY00 Comm.	Current Month	FY01 Comm.	Current Month	FY02 Comm.	Current Month	FY03 Comm.	Current Month	Cumulative
Voice Labor	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 2,923	\$ -	\$ -	\$ 2,923	\$ -
Overhead	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,904	\$ -	\$ -	\$ 1,904	\$ -
Voice Travel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 222	\$ -	\$ -	\$ 222	\$ -
<i>Subtotal-Voice Engineering</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,048	\$ -	\$ -	\$ 5,048	\$ -
<i>Contracts:</i>										
CDM Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 30,000	\$ -	\$ -	\$ 30,000	\$ -
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 30,000	\$ -	\$ -	\$ 30,000	\$ -
<i>Equip/Supplies/Other:</i>										
Voice Acq O/H (1.9% of Contracts)	\$ 5	\$ -	\$ -	\$ -	\$ -	\$ 1,154	\$ -	\$ -	\$ 1,154	\$ -
TOTAL COST	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 36,202	\$ -	\$ -	\$ 36,202	\$ -
TOTAL AVAILABLE FUNDS	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 23,799	\$ -	\$ -	\$ 23,799	\$ -

15) Great Falls MT Insulation Site (N- 177)
 Financial Summary
 At 12/31/02

<u>Funds Authorized</u>	<u>FY99 Planned</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,683	\$ 26,538	\$ 13,327	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 1,315
4) Libby Asbestos Proj. Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,900,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ -	\$ 5,000	\$ 1,793	\$ 1,793	\$ (0)	\$ 3,207
7) Libby Asbestos Proj. - Export Plant (N- 423)	\$ -	\$ 500,000	\$ 171,077	\$ 507,657	\$ 234,458	\$ 1,136,000
8) Libby Asbestos Proj. - Removals (N- 079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 36,737,300
9) Asbestos Sampling/Site Assessments (N- 111)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ 30,000	\$ 235,000	\$ 40,876	\$ 46,882	\$ 57,515
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 235,000	\$ 235,000	\$ 38,423	\$ 29,881	\$ 487,000
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 10,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ -
14) Pablo Tire Fire	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
15) Great Falls MT Insulation Site (N- 177)	\$ -	\$ -	\$ -	\$ -	\$ 60,000	\$ 60,000
16) Libby Litigation Support (N- 192)	\$ -	\$ -	\$ 60,000	\$ 23,799	\$ 16,204	\$ 115,816
17) Remedial Investigation (N- 211)	\$ -	\$ -	\$ 3,113,000	\$ 1,239,395	\$ 3,113,000	\$ -
Total EPA Funds Authorized \$	\$ 9,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,533,497	\$ 7,814,441	\$ 59,229,500
<u>Costs Incurred</u>						
Description	FY99 Accrued	Current Month	FY00 Accrued	Current Month	FY01 Accrued	Current Month
<i>Volpe Engineering:</i>						
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ 2,923	\$ 2,923
Overhead	\$ -	\$ -	\$ -	\$ -	\$ 1,904	\$ 1,904
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ 222	\$ 222
Subtotal, Volpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ 5,048	\$ -
<i>Contracts:</i>						
CDM	\$ -	\$ -	\$ -	\$ -	\$ 26,889	\$ 26,889
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ 26,889	\$ -
Equip/Supplies/Other:						
Volpe Acq/DHI (1.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ 1,154	\$ 1,154
TOTAL COST \$	\$ -	\$ -	\$ -	\$ -	\$ 33,091	\$ 33,091
TOTAL AVAILABLE FUNDS					\$ 26,909	
					<u>Cumulative Accrued Costs</u>	<u>Current Month</u>

16) Libby Litigation Support (N- 192)
Financial Summary

AT12/23/02

		FY99 Planned				FY00 Planned				FY01 Planned				FY02 Planned				FY03 Planned				Planned		
		\$ 3,801,000	\$ 75,000	\$ 15,000	\$ 17,000	\$ -	\$ 500,000	\$ 1,398,711	\$ 30,440	\$ 32,844	\$ 3,000,000	\$ 500,000	\$ 171,077	\$ 507,637	\$ 109,850	\$ 53,727	\$ 13,685	\$ 4,819,210	\$ 23,542	\$ 1,793	\$ 224,458	\$ 10,500	\$ 10,500	
1) Stockton Removal Action (N- 329)																								
2) Aspen Park Solvents (N- 332 and N-215)																								
3) Counter-Terrorism Work Plan (N- 350)																								
4) Libby Asbestos Proj Assessment (N- 428)																								
5) Lockwood Solvents (N- 386)																								
6) Libby Economic Analysis (N- 064)																								
7) Libby Asbestos Proj - Export Plant (N- 423)																								
8) Libby Asbestos Proj - Removals (N- 079)																								
9) Asbestos Sampling/Site Assessments (N- 131)																								
10) Hazard Ranking System Documentation (N- 135)																								
11) Intermountain insulation, SLC, Utah (N- 097)																								
12) Robinson Insulation, Minot, ND (N- 094)																								
13) Western Minerals, Denver, CO (N- 088)																								
14) Pablo Tire Fire																								
15) Great Falls MT Insulation Site (N- 177)																								
16) Libby Litigation Support (N- 192)																								
17) Remedial Investigation (N- 211)																								
Total EPA Funds Authorized		\$ 5,908,000						\$ 10,493,680							\$ 26,210,860									
C costs incurred																								
Description		FY99 Comm. Current Month				FY00 Comm. Current Month				FY01 Comm. Current Month				FY02 Comm. Current Month				FY03 Comm. Current Month				Cumulative		
Volpe Engineering:																							Current Month	
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 50,144	\$ -	\$ 6,995	\$ 635	\$ 57,139	\$ 635	\$ 6,10,500	\$ 6,10,500			
Overhead	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 32,664	\$ -	\$ 4,547	\$ 412	\$ 37,210	\$ 412	\$ 132,912	\$ 132,912			
Volpe In-House Support	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 10,668	\$ -	\$ 152	\$ -	\$ 10,819	\$ -	\$ 1,315	\$ 1,315			
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 38	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 1,086,500	\$ 1,086,500			
Subtotal-Volpe Engineering Contracts:															\$ 93,513	\$ -	\$ 11,693	\$ 1,047	\$ 105,206	\$ 1,047	\$ 17,088	\$ 17,088		
Equip/Supplies/Other:																								
Volpe Acq/OH (3.9% of Contracts)																								
TOTAL COST		\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,478	\$ -	\$ 750	\$ 750	\$ 6,228	\$ 750	\$ 112,090	\$ 112,090	A		
TOTAL AVAILABLE FUNDS																								

16) Libby Litigation Support (N- 192)
 Financial Summary
 A1 12/31/02

<i>Funds Authorized</i>		<u>FY99 Planned</u>	<u>FY00 Planned</u>	<u>FY01 Planned</u>	<u>FY02 Planned</u>	<u>FY03 Planned</u>	<u>Planned</u>						
1) Stockton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,850	\$ 50	\$ 10	\$ 10	\$ 6,110,500						
2) Aspen Park Solvents (N- 332 and N-215)	\$ 5,75,000	\$ 13,685	\$ 26,538	\$ 55,727	\$ 13,349	\$ 132,912	\$ 132,912						
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 13,685	\$ 0	\$ 0	\$ 1,315						
4) Libby Asbestos Proj Assessment (N- 428)	\$ 32,844	\$ 3,000,000	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 1,110,725	\$ 11,086,500						
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 5,000	\$ 23,542	\$ 185	\$ 185	\$ 185	\$ 17,088						
6) Libby Economic Analysis (N- 064)	\$ 1,793	\$ 1,793	\$ 1,793	\$ (0)	\$ (0)	\$ (0)	\$ 3,207						
7) Libby Asbestos Proj Export Plant (N- 423)	\$ 500,000	\$ 171,077	\$ 507,637	\$ 234,458	\$ 5	\$ 5	\$ 1,136,000						
8) Libby Asbestos Proj Removals (N- 079)	\$ 5,493,000	\$ 20,000	\$ 20,415,372	\$ 18,098,894	\$ 5,014,168	\$ 5	\$ 36,737,300						
9) Asbestos Sampling/Site Assessments (N- 131)	\$ 19,793	\$ 100,000	\$ 18,063	\$ (0)	\$ (0)	\$ 5	\$ 1,917						
10) Hazard Ranking System Documentation (N- 135)	\$ 10,000	\$ 40,876	\$ 7,790	\$ (0)	\$ (0)	\$ 5	\$ 30,410						
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ 30,000	\$ 235,000	\$ 46,882	\$ 46,882	\$ 5	\$ 5	\$ 57,515						
12) Robinson Insulation, Minn, ND (N- 094)	\$ 235,000	\$ 358,423	\$ 29,881	\$ 29,881	\$ 5	\$ 5	\$ 487,000						
13) Western Minerals, Denver, CO (N- 088)	\$ 235,000	\$ 76,967	\$ 35,386	\$ 35,386	\$ 5	\$ 5	\$ 200,000						
14) Pablo Tire Fire	\$ 10,000	\$ 60,000	\$ 23,799	\$ 23,799	\$ 5	\$ 5	\$ -						
15) Great Falls MT Insulation Site (N- 177)	\$ 60,000	\$ 60,000	\$ 60,000	\$ 60,000	\$ 5	\$ 5	\$ 60,000						
16) Libby Litigation Support (N- 192)	\$ 3,119,000	\$ 16,204	\$ 1,289,395	\$ 1,289,395	\$ 115,816	\$ 5	\$ 115,816						
17) Remedial Investigation (N- 211)	\$ 3,119,000	\$ 26,210,860	\$ 26,533,397	\$ 7,814,441	\$ 5	\$ 5	\$ 59,290,500						
<i>Total EPA Funds Authorized</i>	\$ 5,908,000		\$ 10,493,680										
<i>Const Incurred</i>													
Description		<u>FY99 Accrued</u>	<u>Current Month</u>	<u>FY00 Accrued</u>	<u>Current Month</u>	<u>FY01 Accrued</u>	<u>Current Month</u>	<u>FY02 Accrued</u>	<u>Current Month</u>	<u>FY03 Accrued</u>	<u>Current Month</u>	<u>Cumulative Accrued Costs</u>	<u>Current Month</u>
<i>Volpe Engineering:</i>													
<i>Volpe Engineering:</i>													
<i>Volpe Labor</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 50,144	\$ -	\$ 6,995	\$ 635	\$ 57,139	\$ -	\$ 635	
<i>Overtime</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 32,664	\$ -	\$ 4,347	\$ 412	\$ 37,210	\$ -	\$ 412	
<i>In-House Support</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 10,668	\$ -	\$ 152	\$ -	\$ 10,819	\$ -	\$ -	
<i>Volpe Travel</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 38	\$ -	\$ -	\$ -	\$ 38	\$ -	\$ -	
<i>Subtotal Volpe Engineering</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 93,513	\$ -	\$ 11,693	\$ 1,047	\$ 105,206	\$ -	\$ 1,047	
<i>Contracts:</i>													
<i>Subtotal Contracts</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	
<i>Equip/Supplies/Other:</i>													
<i>Volpe Acq/OH (3.9% of Contracts)</i>	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 5,478	\$ -	\$ 5,478	\$ 5,478	\$ 5,478	\$ -	\$ -	
TOTAL COST	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 99,612	\$ -	\$ 11,699	\$ 1,047	\$ 111,311	\$ -	\$ 1,047	
TOTAL AVAILABLE FUNDS						\$ 4,505							

Financial Summary

A1 12/31/02

		FY99 Planned		FY00 Planned		FY01 Planned		FY02 Planned		FY03 Planned		Planned
		\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	
<i>Funds Authorized</i>												
1) Stockton Removal Action (N-329)	\$	\$5,801,000	\$	\$1,398,711	\$	\$109,850	\$	\$10	\$	\$10	\$	\$6,110,500
2) Aspen Park Solvents (N-312 and N-215)	\$	75,000	\$	13,685	\$	53,277	\$	\$13,349	\$	\$13,349	\$	\$13,2912
3) Counter-Terrorism Work Plan (N-350)	\$	15,000	\$	30,440	\$	13,685	\$	\$13,685	\$	\$13,685	\$	\$13,15
4) Libby Asbestos Proj. Assessment (N-428)	\$		\$	32,844	\$	4,819,210	\$	4,122,447	\$	\$1,110,725	\$	\$11,086,500
5) Lockheed Solvents (N-386)	\$	17,000	\$	3,000,000	\$	23,542	\$	\$185	\$	\$185	\$	\$17,988
6) Libby Economic Analysis (N-664)	\$		\$	5,000	\$	1,793	\$	\$0	\$	\$0	\$	
7) Libby Asbestos Proj. - Export Plant (N-422)	\$		\$	500,000	\$	171,077	\$	507,637	\$	\$234,538	\$	\$1,136,000
8) Libby Asbestos Proj. - Removals (N-079)	\$		\$	5,493,000	\$	20,415,372	\$	18,098,824	\$	\$5,014,168	\$	\$36,731,300
9) Asbestos Sampling/Site Assessments (N-131)	\$		\$	20,000	\$	19,793	\$	18,063	\$	\$0	\$	\$1,937
10) Hazard Ranking System Documentation (N-135)	\$		\$	100,000	\$	7,790	\$	\$0	\$	\$0	\$	\$30,410
11) Intermountain Insulation, SLC, Utah (N-097)	\$		\$	30,000	\$	40,836	\$	46,882	\$	\$5,715	\$	
12) Robinson Insulation, Minot, ND (N-094)	\$		\$	233,000	\$	338,423	\$	29,381	\$	\$0	\$	\$48,7,000
13) Western Minerals, Denver, CO (N-088)	\$		\$	233,000	\$	76,967	\$	35,186	\$	\$0	\$	\$20,000
14) Pablo Tire Fire	\$		\$	10,000	\$	10,000	\$	10,000	\$	\$0	\$	
15) Great Falls MT Insulation Support (N-177)	\$		\$	60,000	\$	23,799	\$	60,000	\$	\$0	\$	
16) Libby Litigation Support (N-192)	\$		\$	60,000	\$	16,204	\$	115,816	\$	\$0	\$	
17) Remedial Investigation (N-211)	\$		\$	3,113,000	\$	1,289,395	\$	3,113,000	\$	\$0	\$	
<i>Total EPA Funds Authorized</i>	\$	\$ 5,908,000	\$	\$ 10,493,680	\$	\$ 26,210,860	\$	\$ 26,533,497	\$	\$ 7,814,441	\$	\$ 59,290,500
<i>Costs Incurred</i>												
Description	FY99 Comm.	Current Month	FY00 Comm.	Current Month	FY01 Comm.	Current Month	FY02 Comm.	Current Month	FY03 Comm.	Current Month	Cumulative	
Volpe Engineering:											Committed Costs	Current Month
Volpe Labor	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 9,899	\$ 3,617
Overhead	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 6,439	\$ 2,351
Volpe In-House Support	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 4,269	\$ 2,351
Volpe Travel	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 1,210	\$ 1,210
<i>Subtotal Volpe Engineering</i>	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 2,024	\$ 1,210
Contracts:												
CDM	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 18,361	\$ 7,178
<i>Subtotal Contracts</i>	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 12,046	\$ 7,178
<i>Equip/Supplies/Other:</i>												
<i>Subtotal O/H (3.9% of Contracts)</i>	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$	\$ 6,316	\$ 7,178
TOTAL COST	\$	\$	\$ 1,750,000	\$ 2,947,449								
TOTAL AVAILABLE FUNDS	\$	\$	\$ 1,823,605	\$ 7,178								
											\$ 1,256,195	\$ 3,079,800
											\$ 113,390	\$ 7,178
											A	B
											\$ 33,200	

17) Remedial Investigation (N- 211)
Financial Summary
A 11/23/02

	FY'99 Planned	FY'00 Planned	FY'01 Planned	FY'02 Planned	FY'03 Planned	Planned
1) Stuckton Removal Action (N- 329)	\$ 5,801,000	\$ 1,398,711	\$ 109,550	\$ 10	\$ 10	\$ 6,110,500
2) Aspen Park Solvents (N- 332 and N-215)	\$ 75,000	\$ 13,885	\$ 26,538	\$ 53,727	\$ 13,349	\$ 132,912
3) Counter-Terrorism Work Plan (N- 350)	\$ 15,000	\$ 30,440	\$ 13,685	\$ 0	\$ 0	\$ 1,315
4) Libby Asbestos Proj Assessment (N- 428)	\$ -	\$ 32,844	\$ 4,819,210	\$ 4,122,447	\$ 1,110,725	\$ 11,086,500
5) Lockwood Solvents (N- 386)	\$ 17,000	\$ 3,000,000	\$ 23,542	\$ 185	\$ 185	\$ 17,088
6) Libby Economic Analysis (N- 064)	\$ 5,000	\$ 5,000	\$ 1,793	\$ (0)	\$ (0)	\$ 3,207
7) Libby Asbestos Proj - Export Plan (N- 422)	\$ -	\$ 500,000	\$ 171,077	\$ 507,637	\$ 234,438	\$ 1,136,000
8) Libby Asbestos Proj - Removals (N- 079)	\$ -	\$ 5,493,000	\$ 20,415,372	\$ 18,058,894	\$ 5,014,168	\$ 36,737,300
9) Asbestos Sampling/Site Assessments (N- 131)	\$ -	\$ 20,000	\$ 19,793	\$ 18,063	\$ (0)	\$ 1,937
10) Hazard Ranking System Documentation (N- 135)	\$ -	\$ -	\$ 100,000	\$ 7,790	\$ (0)	\$ 30,410
11) Intermountain Insulation, SLC, Utah (N- 097)	\$ -	\$ -	\$ 30,000	\$ 40,836	\$ 46,882	\$ 57,515
12) Robinson Insulation, Minot, ND (N- 094)	\$ -	\$ 215,000	\$ 158,473	\$ 29,881	\$ 29,881	\$ 487,000
13) Western Minerals, Denver, CO (N- 088)	\$ -	\$ 235,000	\$ 76,967	\$ 35,386	\$ 200,000	\$ -
14) Pablo Tire Five	\$ -	\$ 10,000	\$ -	\$ -	\$ -	\$ -
15) Great Falls, MT Insulation Site (N- 177)	\$ -	\$ -	\$ 60,000	\$ 21,799	\$ 60,000	\$ -
16) Libby Litigation Support (N- 192)	\$ -	\$ 60,000	\$ -	\$ 16,204	\$ 115,816	\$ -
17) Remedial Investigation (N- 211)	\$ -	\$ 3,113,000	\$ 1,269,395	\$ 3,113,000	\$ 7,814,441	\$ 59,290,500
Total EPA Funds Authorized	\$ 5,908,000	\$ 10,493,680	\$ 26,210,860	\$ 26,513,497	\$ 7,814,441	\$ 958,705
<i>Costs Incurred</i>						
Description	FY'99 Accrued	Current Month	FY'00 Accrued	Current Month	FY'01 Accrued	Current Month
Volpe Engineering:						
Volpe Labor	\$ -	\$ -	\$ -	\$ -	\$ 3,332	\$ -
Volpe Overhead	\$ -	\$ -	\$ -	\$ -	\$ 2,170	\$ -
Volpe In-House Support	\$ -	\$ -	\$ -	\$ -	\$ -	\$ 4,269
Volpe Travel	\$ -	\$ -	\$ -	\$ -	\$ 814	\$ -
Subtotal-Volpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ 6,316	\$ -
Contracts:						
CDM	\$ -	\$ -	\$ -	\$ -	\$ 10,836	\$ -
Subtotal-Contracts	\$ -	\$ -	\$ -	\$ -	\$ 5,968	\$ -
Subtotal-Volpe Engineering	\$ -	\$ -	\$ -	\$ -	\$ 17,151	\$ -
Equip/Supplies/Other:						
Volpe Acq/OH (3.9% of Contracts)	\$ -	\$ -	\$ -	\$ -	\$ 814	\$ -
TOTAL COST	\$ -	\$ -	\$ -	\$ -	\$ 491,368	\$ 439,800
TOTAL AVAILABLE FUNDS						
