

October 30, 2013

**CERTIFIED MAIL: 7010 3090 0003 3945 3201**

**Return Receipt Requested**

U.S. Environmental Protection Agency Region 7  
Attn: Chief, RCRA Corrective Action and Permits Branch  
Air, RCRA and Toxics Division  
11201 Renner Boulevard  
Lenexa, Kansas 66219

**RE: 3rd QUARTER 2013 QUARTERLY PROGRESS REPORT; OCCIDENTAL  
CHEMICALS CORPORATION, WICHITA PLANT; USEPA ID# KSD007482029**

Dear Sir:

Enclosed please find the Quarterly Progress Report, as required by Occidental Chemical Corporation's RCRA hazardous waste permit number KSD007482029. This report summarizes the activities conducted for Part II of the Facility's RCRA Permit during the third quarter of 2013. In addition, please find enclosed the most recent version of the RFI Schedule, which is dated October 28, 2013, for your review and use. If you have any questions, please call Lisa R. Thurman at 316/529-7204.

Sincerely,



Steve Hieger  
Plant Manager

L1310067

Enclosure

c.c.: Mostafa Kamal; KDHE  
Brad Roberts, USEPA Region VII  
Juan Somoano; GSHI  
Lisa Thurman; OCC  
Bruce Clegg; CRA

**CERTIFIED MAIL: 7010 3090 0003 3945 3188**

**CERTIFIED MAIL: 7010 3090 0003 3945 3195**

RCRA



527615

**RECEIVED**

**NOV 04 2013**

**AWMD/WRAP-KNRP**

## **Occidental Chemical Corporation, Quarterly Progress Report July 1, 2013 through September 30, 2013**

Pursuant to Occidental Chemical Corporation's (OCC) hazardous waste permit KSD007482029, Part II, Section C.13, OCC is submitting this quarterly progress report. This report updates the progress of RCRA Corrective Action activities conducted during the third quarter of 2013.

- Submitted the first 2013 Semiannual Groundwater Monitoring report.
- A quarterly building monitoring and inspection event was completed. The completed reporting form was submitted to EPA.
- Completed the Phase II On-Site Groundwater RFI field investigation.
- Commenced subsurface DNAPL delineation and source area evaluation.
- Completed the Inorganics Area Phase III field investigation work.
- Installed two additional extraction wells (IW45 and IW46) in areas southwest of the Facility. Installed piezometers proximate to the new interceptor wells IW45 and IW46.
- Commenced construction of a wastewater treatment plant (activated carbon beds) for IW45 and IW46.
- Continued operation of the interceptor well network for groundwater control around Occidental's Wichita plant.
- Continued with the implementation of modifications to the groundwater extraction and treatment system.
- Conducted the Community Interest Group meeting at the Facility.
- There have been no releases of hazardous materials to report.



Work scheduled for the fourth quarter of 2013 includes:

- Complete the second 2013 semiannual groundwater monitoring event.
- Submit the Phase II On-Site Groundwater RFI Summary Report.
- Submit the Phase III Inorganics Area Summary Report.
- Continue operation of the interceptor well network for groundwater control around Occidental's Wichita plant.
- Continue with the implementation of modifications to the groundwater extraction and treatment system, including modifications to the piping conveyance system and construction of an additional treatment system.
- Conduct and report a quarterly building inspection and pressure monitoring event.
- Submit the NPDES permit modifications application.

Notifications:

- None.



CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
07/07/2008	Draft Work Plan for Indoor Soil Gas Sampling
07/07/2008	Comments to QAPP Addendum 04/18/08
07/07/2008	Spring 2008 Neighbor Results
07/11/2008	Request for Interim Measures for Railroad Tracked Areas
07/25/2008	Revised Asbestos Surface Impoundment SWMU Interim Corrective Measure Implementation Report
07/28/2008	2008 2nd Quarter Progress Report
08/05/2008	Comments to Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
08/08/2008	Notice of Plug & Abandonment of DW #4
08/08/2008	Request for Extension of QAPP Comment Response
08/15/2008	Response to Railroad Tracked Areas Interim Measures Letter
08/18/2008	Interim Corrective Measures Implementation Report for Asbestos Surface Impoundment SWMU
09/03/2008	Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
09/19/2008	Revised Draft Work Plan for Indoor Soil Gas Sampling
09/22/2008	Comments to Draft Work Plan for Indoor Soils Gas Sampling
09/30/2008	Approval Letter for Work Plan for Indoor Soils Gas Sampling
10/03/2008	Comments to Draft Work Plan for Collection & Analysis of Groundwater Samples (Appendix 9)
10/30/2008	Appendix IX Semi-Annual Groundwater Monitoring Report
11/03/2008	Draft Work Plan for Collection & Analysis of Groundwater Samples
11/21/2008	Off-Site Soils Gas Sampling Data Evaluation Report
11/21/2008	Off-Site Geoprobe Groundwater Investigation Report
01/05/2009	Draft QAPP
01/19/2009	Indoor Soils Gas Sampling Report
01/23/2009	Sub-Slab Soils Gas Sampling
01/28/2009	Semi-Annual Neighbor Well Data
01/28/2009	4 <sup>th</sup> Quarter Corrective Action Report
02/10/2009	Direct Push Investigation Comments to EPA
02/12/2009	Off-Site Geoprobe Groundwater Investigation Report
02/20/2009	Soil Gas Sampling Data Evaluation Comments to EPA
03/19/2009	Soils Gas Sampling Data Evaluation
03/26/2009	2009 Ongoing Activities Cost Estimate



DATE	CORRECTIVE ACTION CHRONOLOGY EVENT
04/20/2009	Off-Site Geoprobe Report
04/21/2009	Email responding to QAPP Comments
04/30/2009	Semi-Annual Groundwater Report
04/30/2009	Monitor Well Inspection Summary Report
05/08/2009	Response to Comments for Sub-Slab Soils Gas Sampling Report
06/08/2009	Final QAPP and SAP Reports
06/30/2009	RFI Investigation Work Plan for Landfill, Hex Pits, and Brine Ponds
06/30/2009	ICM Effectiveness Evaluation Report
08/26/2009	Revised RFI Work Plan for Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
09/14/2009	Response to EPA's Comments letter dated July 9, 2009 regarding on-Site vapor intrusion
09/14/2009	On-Site Vapor Intrusion Investigation, Assessment and Interim Corrective Measures Implementation Report
11/30/2009	Draft Penta Area and Shipping RFI Work Plan
12/14/2009	Response to EPA Comments & Submission of Revised Interceptor Well ICM Effectiveness Evaluation Report
12/22/2009	Supplemental Off-Site Soil Gas Sample Collection and Analysis, 1 <sup>st</sup> Quarterly, letter submission
12/30/2009	Preliminary Draft Phase I Summary/Phase II Recommendations letter report
01/15/2010	Response to EPA Comments – On-Site VI, Assessment & Interim ICM Implementation Report
02/12/2010	Final Revision to Interceptor Well ICM Effectiveness Report
02/12/2010	Second 2009 Semiannual Groundwater Monitoring Report
02/16/2010	Received comments from EPA for Penta Area and Shipping RFI Work Plan
02/19/2010	Phase I Summary/Phase II Recommendations Letter Report (final), Alpha Cake Landfill, Hex Waste Pits and Brine Ponds RFI Work Plan
04/30/2010	Response to EPA Comments – Penta Area and Shipping RFI Work Plan
04/30/2010	Revised Penta Area and Shipping RFI Work Plan
05/17/2010	Resampling of MW137S1 Letter to EPA
05/28/2010	Inorganics Area RFI Work Plan
07/09/2010	Received comments from EPA for Inorganics Area RFI Work Plan
08/11/2010	Response to EPA Comments – Inorganics Area RFI Work Plan
08/11/2010	Revised Inorganics Area RFI Work Plan
08/24/2010	First Semiannual Groundwater Monitoring Report

CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
09/23/2010	Groundwater Screening (near MW-140) Investigation Summary Letter
10/4/2010	Operation and Maintenance Plan for On-Site Vapor Intrusion ICM for on-Site buildings
10/15/2010	RFI Summary Report for the Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
10/29/2010	Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
12/20/2010	Response to EPA Comments on the Operation and Maintenance Plan for On-Site Vapor Intrusion ICM for on-Site buildings
12/16/2010	Received comments from EPA for Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
12/16/2010	Received comments from EPA for RFI Summary Report, Alpha Cake Landfill, Hex Waste Pits and Brine Ponds
12/30/2010	Comprehensive Well Survey letter submittal to EPA
1/4/2011	Penta Area and Shipping RFI Summary Report
1/17/2011	Response to EPA comments and revised Supplemental Quarterly Off-Site Soil Gas Monitoring Summary Report
1/18/2011	Response to EPA comments and revised RFI Summary Report – Landfill Areas
2/16/2011	Inorganic Area RFI Summary Report
2/23/2011	Second 2010 Semiannual Groundwater Monitoring Report
3/2/2011	Draft Conceptual Design Summary for Groundwater ICM Modifications
4/18/2011	Chloromethanes I, II, Perc and Hazwaste Areas RFI Work Plan
4/18/2011	Arkema Area Investigative Work Plan
4/29/2011	Response to EPA comments and revised RFI Summary Report – Penta Area and Shipping
4/29/2011	Response to EPA comments and revised RFI Summary Report – Inorganics Area
5/2/2011	On-Site Vapor Intrusion Mitigation ICM Construction Completion Report
6/17/2011	Response to EPA comments and revised Preliminary Conceptual Design Groundwater ICM Modifications Rpt
6/30/2011	On-Site Groundwater RFI Work Plan
6/30/2011	Vapor Intrusion ICM Inspection and Pressure Monitoring Record Report Form
7/20/2011	Response to EPA comments and revised Arkema Area Investigative Work Plan
8/1/2011	Response to EPA comments and revised On-Site Vapor Intrusion Mitigation ICM Construction Completion Rpt
8/18/2011	First 2011 Semiannual Groundwater Monitoring Report
8/22/2011	Response to EPA comments and revised Penta Area and Shipping RFI Summary Report
8/22/2011	Response to EPA comments and revised Chloromethanes I, II, Perc and Hazwaste Areas RFI Work Plan
8/26/2011	Response to EPA comments and revised Conceptual Design Groundwater ICM Modifications Report
9/12/2011	Response to EPA comments and revised Groundwater Monitoring Program Summary Table


CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
9/30/2011	Response to EPA comments and revised Arkema Investigative Work Plan
10/31/2011	Vapor Intrusion ICM Inspection and Pressure Monitoring Record Report Form
11/14/2011	Received EPA comments on On-Site Groundwater RFI Work Plan
11/14/2011	Received EPA approval letter for Arkema Area Investigative Work Plan
11/30/2011	Sampling and Analysis Plan
12/14/2011	Response to Comments and Revised On-Site Groundwater RFI Work Plan
1/5/2012	EPA Comments on Draft Sampling and Analysis Plan
1/27/2012	EPA Comments on On-Site Groundwater RFI Work Plan
2/8/2012	Response to Comments and Revised Sampling and Analysis Plan
2/20/2012	Second 2011 Semiannual Groundwater Monitoring Report
3/9/2012	Revised Sampling and Analysis Plan (SAP)
3/13/2012	Revised Standard Operating Procedures 4 for SAP
3/19/2012	Response to Comments and Revised On-Site Groundwater RFI Work Plan
3/21/2012	EPA Approval letter – On-Site Groundwater RFI Work Plan
4/17/2012	Stormwater Ponds Area RFI Work Plan
4/17/2012	Fuel Depot Area RFI Work Plan
8/6/2012	Penta Area and Shipping Phase II RFI Summary Report
8/6/2012	Chloromethanes I, II, Perc and Hazwaste Areas RFI and Arkema Area Investigation Summary Report
8/13/2012	Response to Comments and Revised Stormwater Ponds RFI Work Plan and Revised Fuel Depot RFI Work Plan
8/14/2012	Inorganics Area Supplemental Report
8/17/2012	Formal Notification of Additional SWMUs
8/24/2012	First 2012 Semiannual Groundwater Monitoring Report
11/14/2012	Class I Modification Letter for Additional SWMUs
11/15/2012	Phase I On-Site Groundwater Investigation RFI Summary Report
2/22/2013	Second 2012 Semiannual Groundwater Monitoring Report
3/7/2013	Response to EPA Comments and Revised Penta Area and Shipping Phase II RFI Summary Report
3/15/2013	Response to EPA Comments and Revised Phase I On-Site Groundwater RFI Summary Report
3/22/2013	Fuel Depot and Stormwater Ponds Area RFI Summary Report
4/19/2013	EPA approval letter – Revised Phase I On-Site Groundwater Summary Report and Revised Phase II Penta Area and Shipping RFI Summary Report

CORRECTIVE ACTION CHRONOLOGY	
DATE	EVENT
4/24/2013	Monitoring Well Abandonment and Replacement letter
4/25/2013	EPA approval letter – Fuel Depot and Stormwater Pond Area RFI Summary Report
8/22/2013	Second 2013 Semiannual Groundwater Monitoring Report



# Occidental Chemical Corporation


Wichita Facility  
DRAFT RFI Schedule  
October 28, 2013

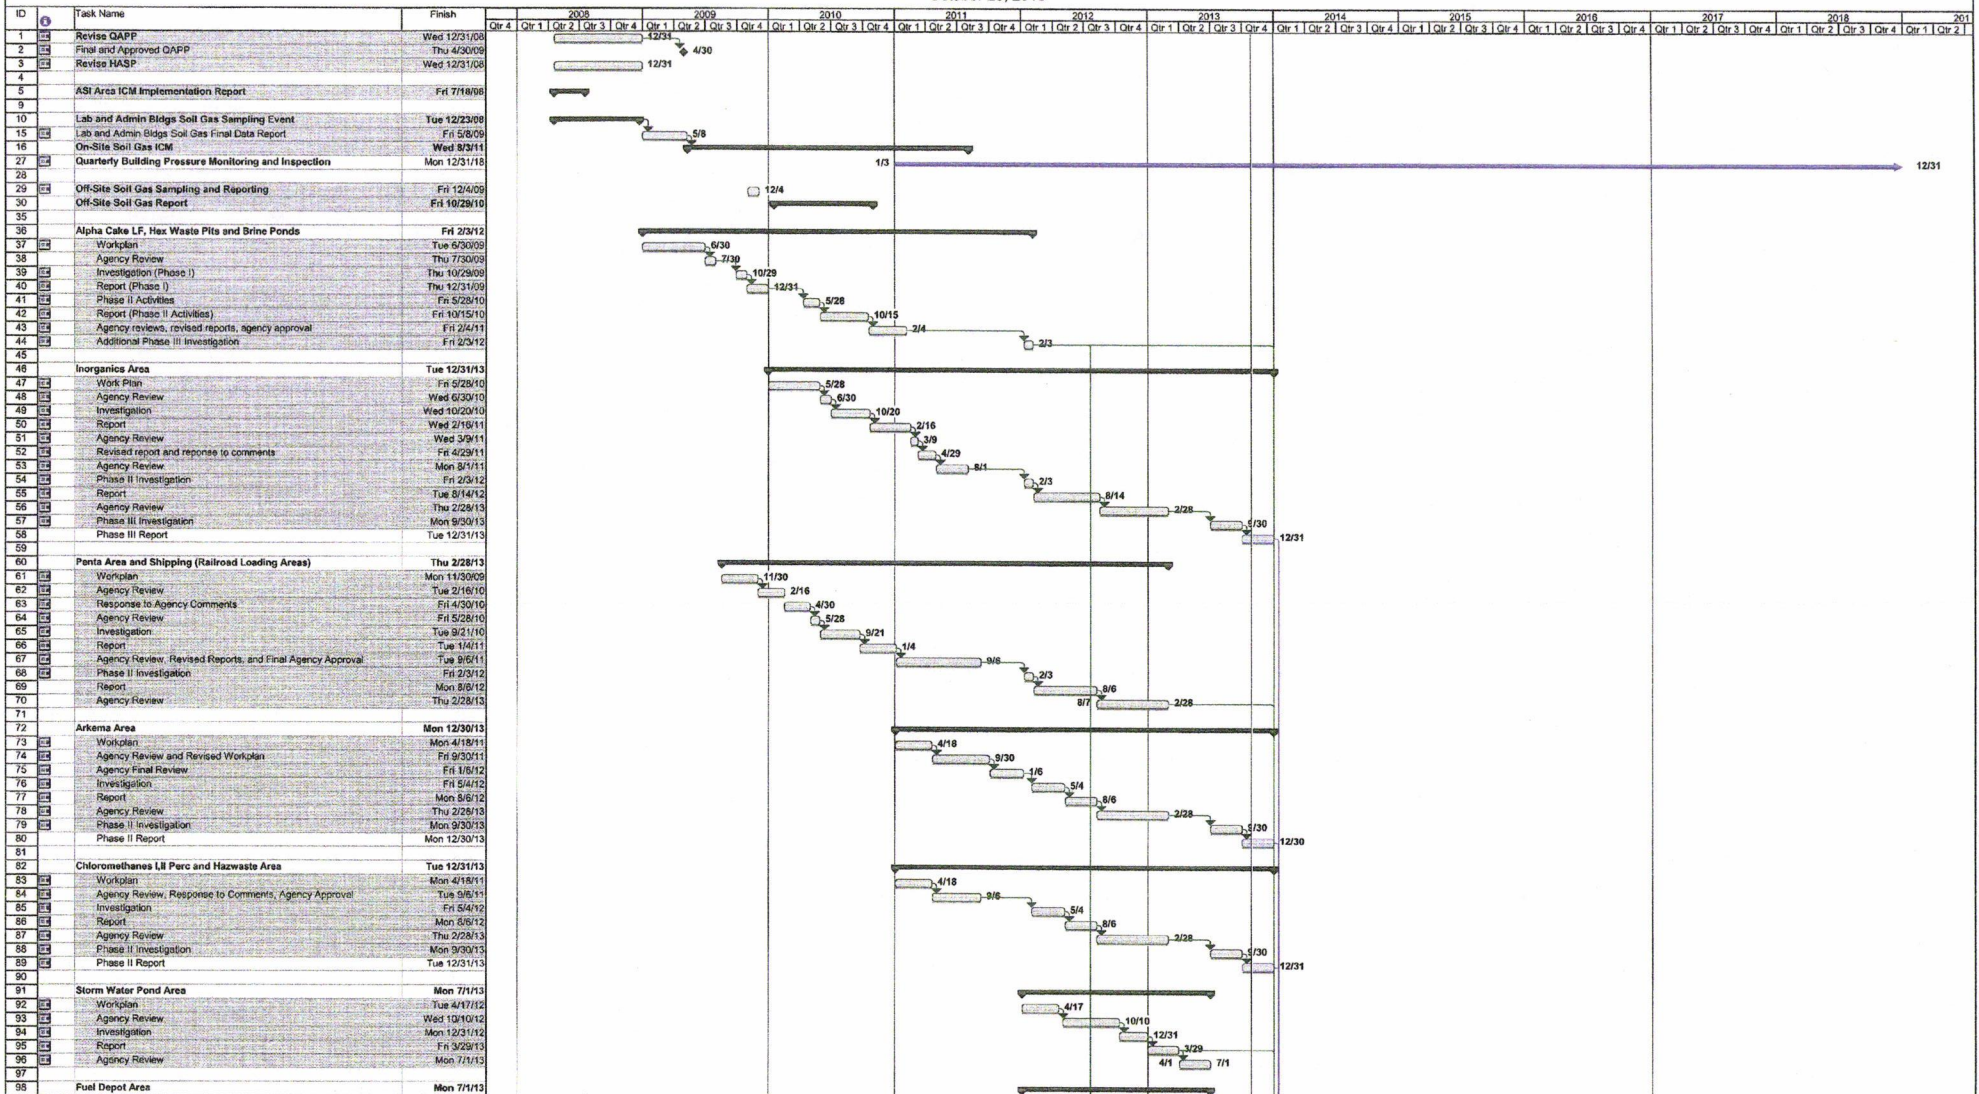

Task Critical Task Completed Task Progress Milestone Summary Rolled Up Task Rolled Up Critical Task Rolled Up Milestone Rolled Up Progress Split External Tasks Project Summary External Milestone Task Critical Task Progress

# Occidental Chemical Corporation

Wichita Facility  
DRAFT RFI Schedule  
October 28, 2013

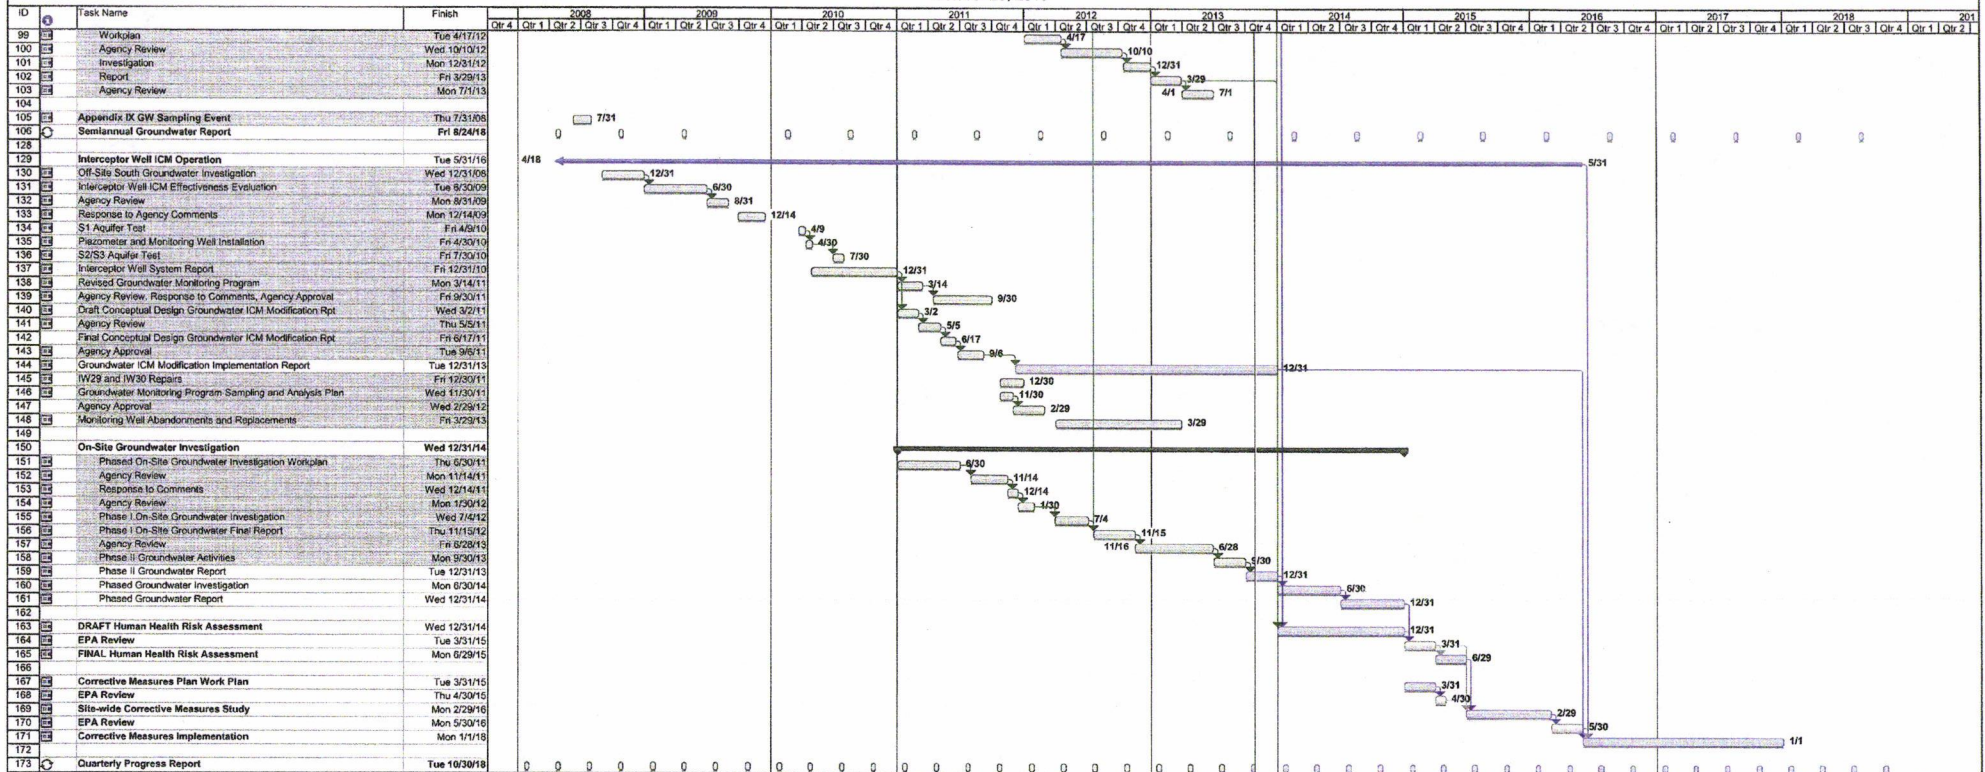

Task Completed Task Milestone Rolled Up Task Rolled Up Milestone Split Project Summary Critical Task  
Critical Task Progress Summary Rolled Up Critical Task Rolled Up Progress External Tasks External Milestone Task Progress
